
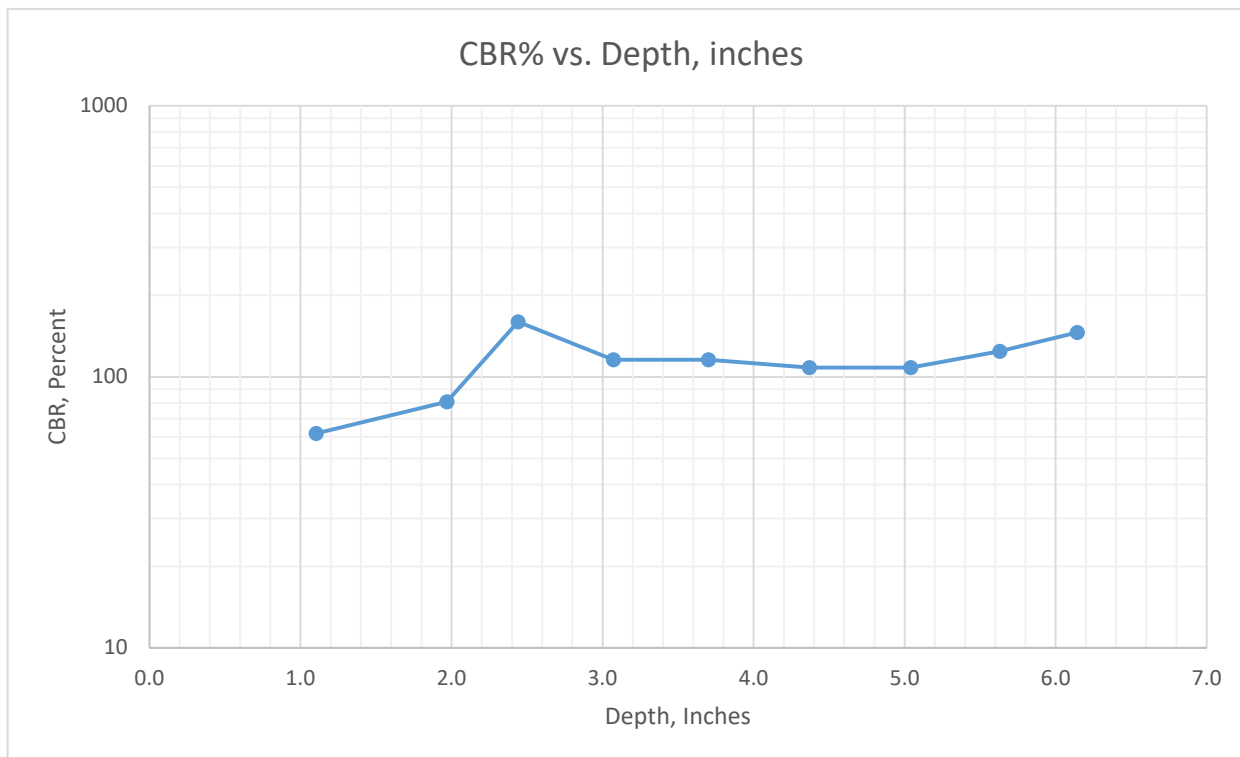


Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	8/27/2021 1:00pm
Station/ offset	Sta. H103+00 4'R	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	

Raw Data					DCP Index			
# of blows	Cumulative Penetration (mm)	Penetration Increase (mm)	Depth (mm)	Depth (in)	Penetration per blow -PR (mm)	Hammer Blow Factor	CBR%*	Notes:
0	355	0	0	0.0				
7	383	28	28.0	1.1	4.0	1	62	
7	405	22	50.0	2.0	3.1	1	81	
7	417	12	62.0	2.4	1.7	1	160	
7	433	16	78.0	3.1	2.3	1	116	
7	449	16	94.0	3.7	2.3	1	116	
7	466	17	111.0	4.4	2.4	1	108	
7	483	17	128.0	5.0	2.4	1	108	
7	498	15	143.0	5.6	2.1	1	124	
7	511	13	156.0	6.1	1.9	1	146	

*292/(PR^1.12)

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	8/27/2021 1:00pm
Station/ offset	Sta. H 152+00 10' R	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	

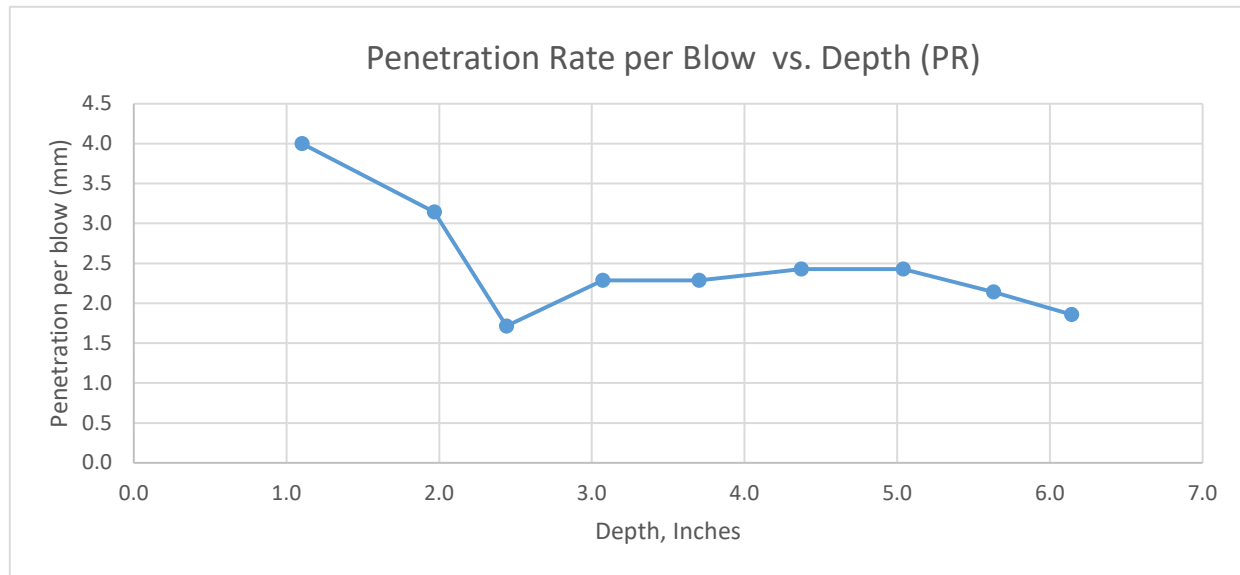

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date:/Time	8/27/2021 1:00pm
Station/ offset	Sta. H 152+00 10' R	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	0

