

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	8/27/2021 1:00pm
Station/ offset	Sta. H132+00 10' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	



Raw Data					DCP Index			
# of blows	Cumulative Penetration (mm)	Penetration Increase (mm)	Depth (mm)	Depth (in)	Penetration per blow -PR (mm)	Hammer Blow Factor	CBR%*	Notes:
0	356	0	0	0.0				
7	400	44	44.0	1.7	6.3	1	37	
7	432	32	76.0	3.0	4.6	1	53	
7	459	27	103.0	4.1	3.9	1	64	
7	484	25	128.0	5.0	3.6	1	70	
7	499	15	143.0	5.6	2.1	1	124	
7	516	17	160.0	6.3	2.4	1	108	

*292/(PR^1.12)



Reviewed by:

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	8/27/2021 1:00pm
Station/ offset	Sta. H132+00 10' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	0

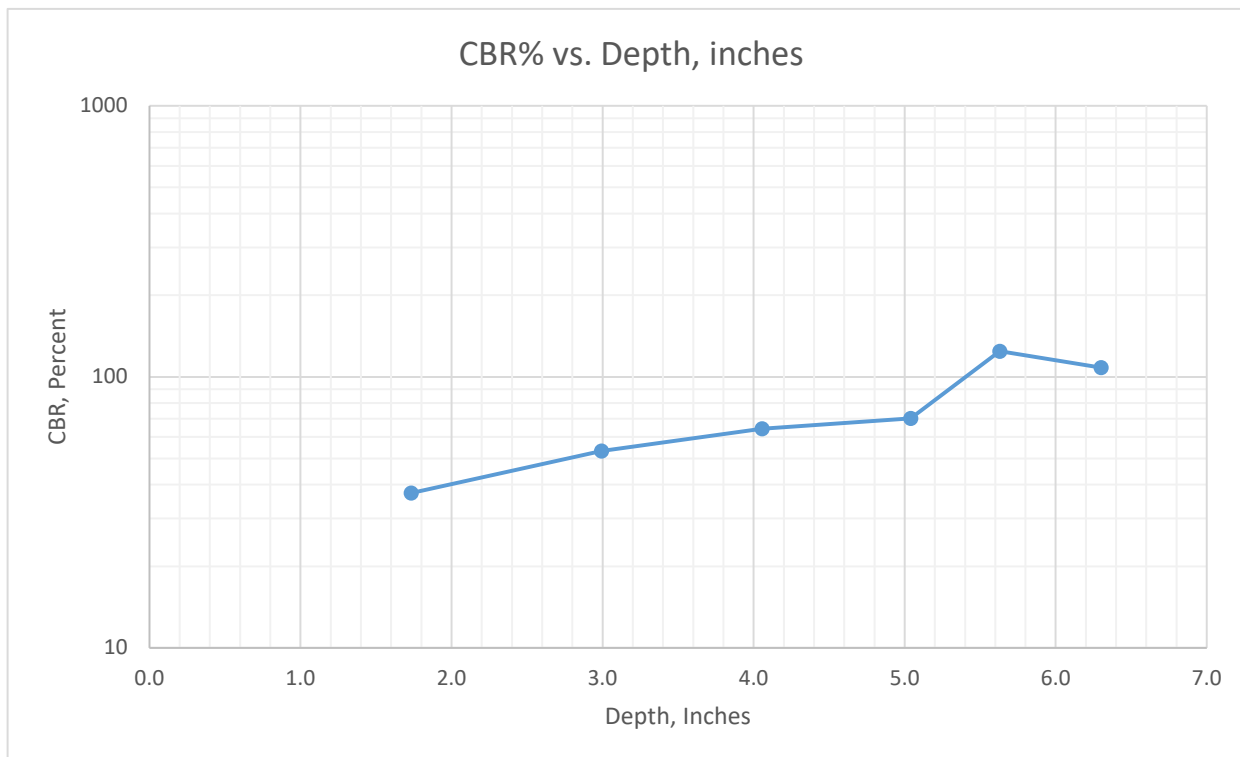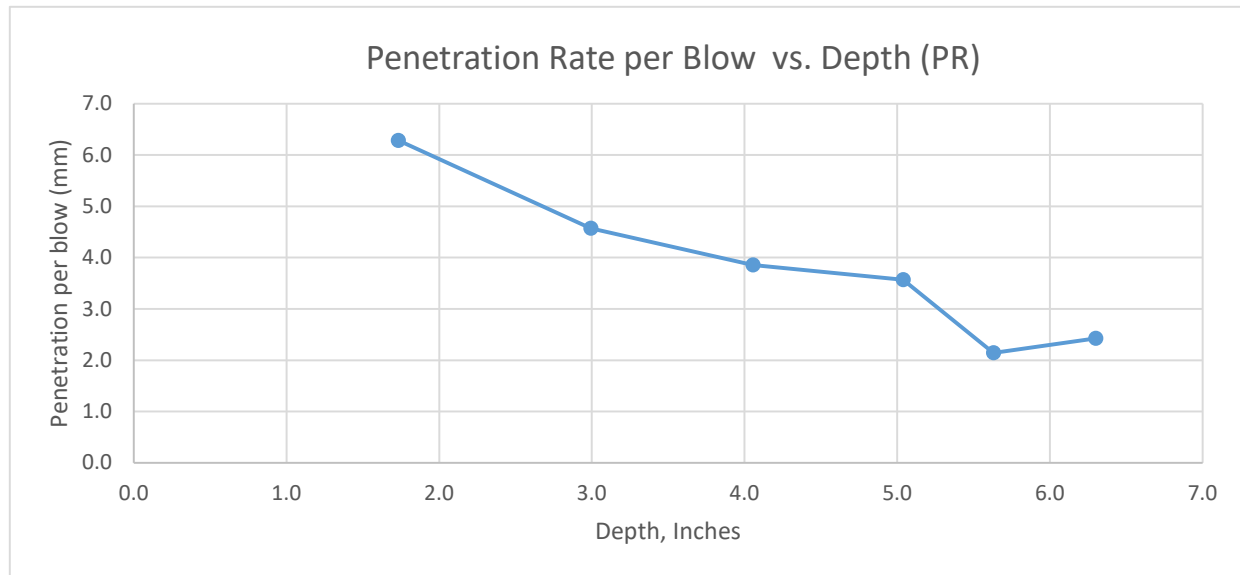

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date:/Time	8/27/2021 1:00pm
Station/ offset	Sta. H132+00 10' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	0

