
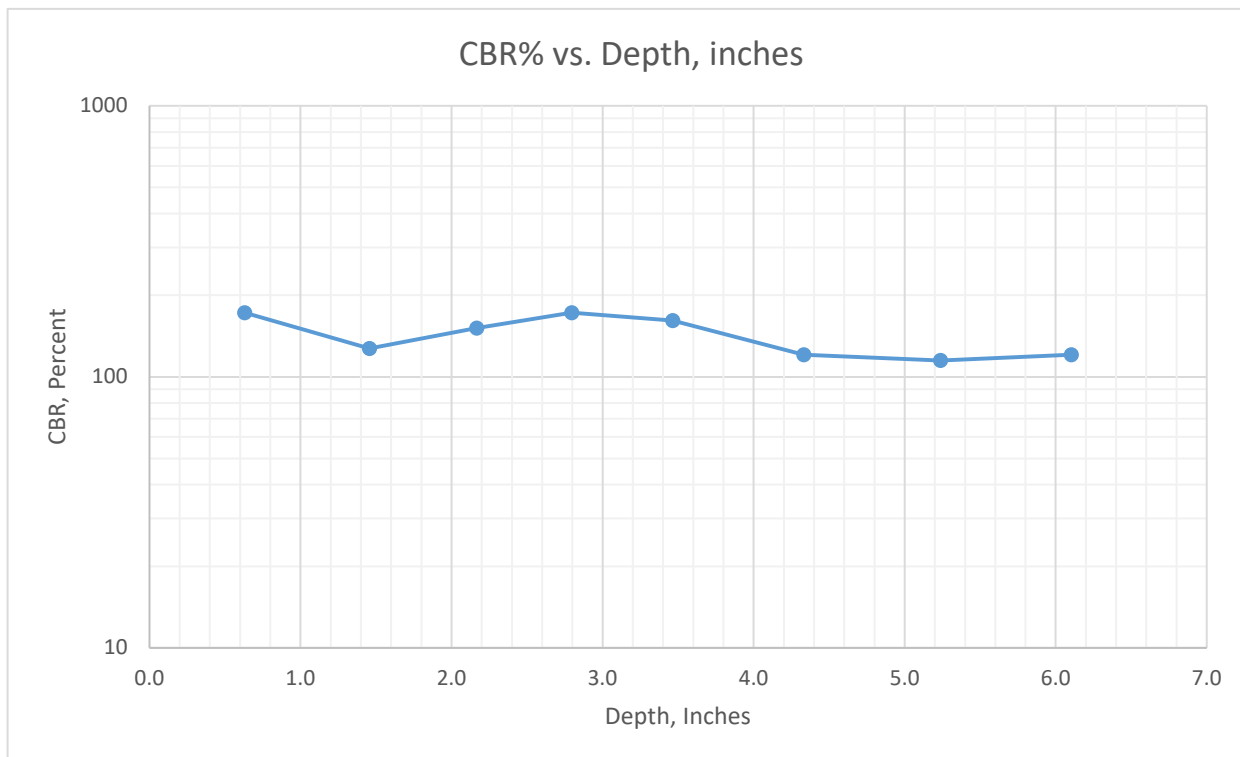


Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	8/27/2021 1:00pm
Station/ offset	Sta. H 132+00 10'R	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	

Raw Data					DCP Index			
# of blows	Cumulative Penetration (mm)	Penetration Increase (mm)	Depth (mm)	Depth (in)	Penetration per blow -PR (mm)	Hammer Blow Factor	CBR%*	Notes:
0	365	0	0	0.0				
10	381	16	16.0	0.6	1.6	1	172	
10	402	21	37.0	1.5	2.1	1	127	
10	420	18	55.0	2.2	1.8	1	151	
10	436	16	71.0	2.8	1.6	1	172	
10	453	17	88.0	3.5	1.7	1	161	
10	475	22	110.0	4.3	2.2	1	121	
10	498	23	133.0	5.2	2.3	1	115	
10	520	22	155.0	6.1	2.2	1	121	

*292/(PR^1.12)

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	8/27/2021 1:00pm
Station/ offset	Sta. H 132+00 10'R	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	0

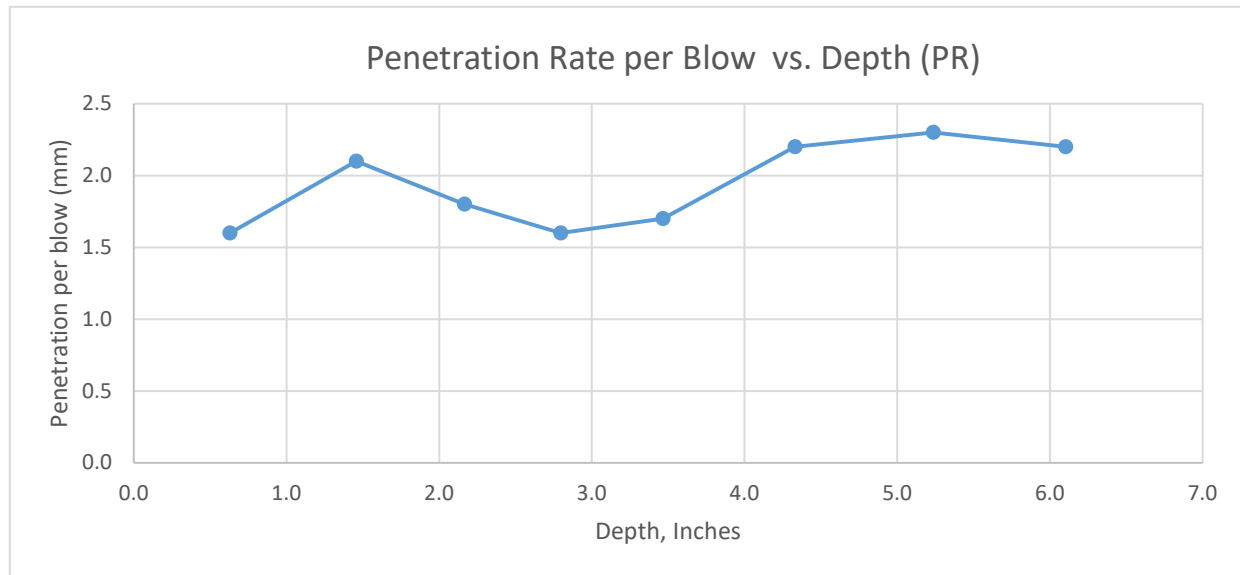

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date:/Time	8/27/2021 1:00pm
Station/ offset	Sta. H 132+00 10'R	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	0

