
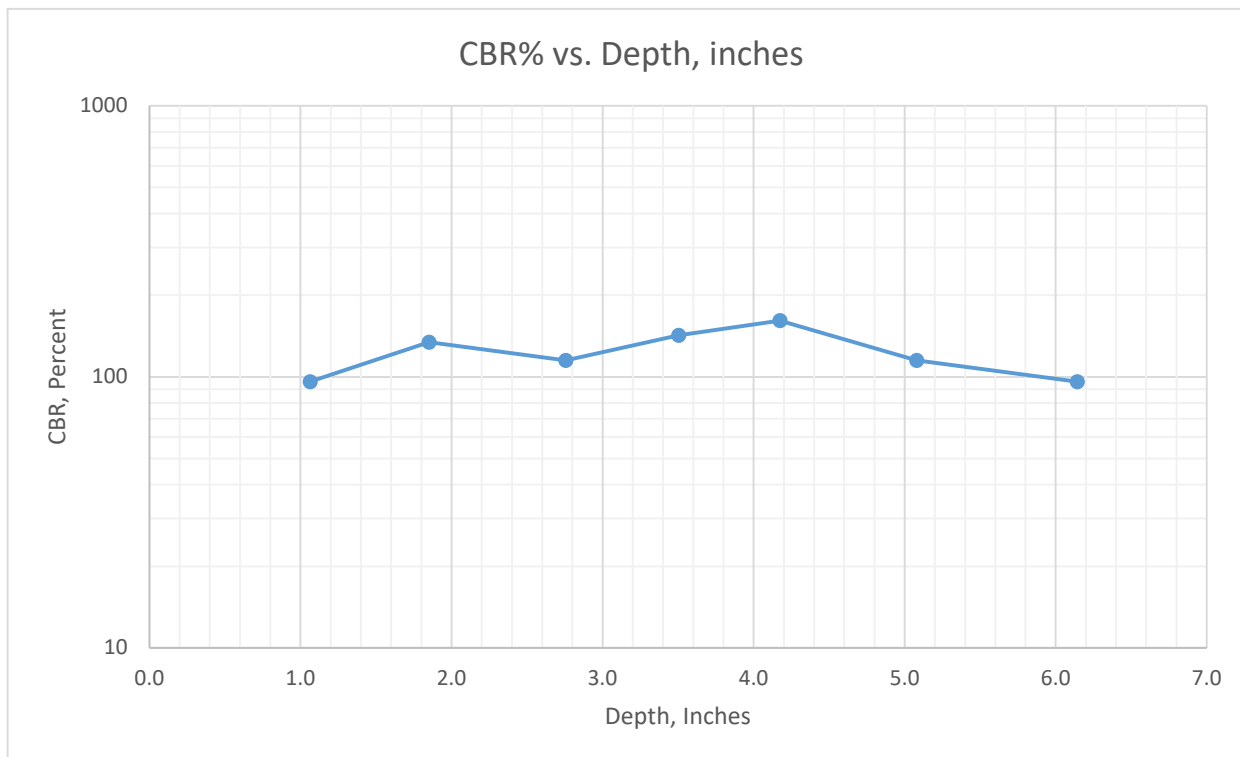


Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	8/27/2021 1:00pm
Station/ offset	Sta. H 152+00 4' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	

Raw Data					DCP Index			
# of blows	Cumulative Penetration (mm)	Penetration Increase (mm)	Depth (mm)	Depth (in)	Penetration per blow -PR (mm)	Hammer Blow Factor	CBR%*	Notes:
0	371	0	0	0.0				
10	398	27	27.0	1.1	2.7	1	96	
10	418	20	47.0	1.9	2.0	1	134	
10	441	23	70.0	2.8	2.3	1	115	
10	460	19	89.0	3.5	1.9	1	142	
10	477	17	106.0	4.2	1.7	1	161	
10	500	23	129.0	5.1	2.3	1	115	
10	527	27	156.0	6.1	2.7	1	96	

*292/(PR^1.12)

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	8/27/2021 1:00pm
Station/ offset	Sta. H 152+00 4' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	0

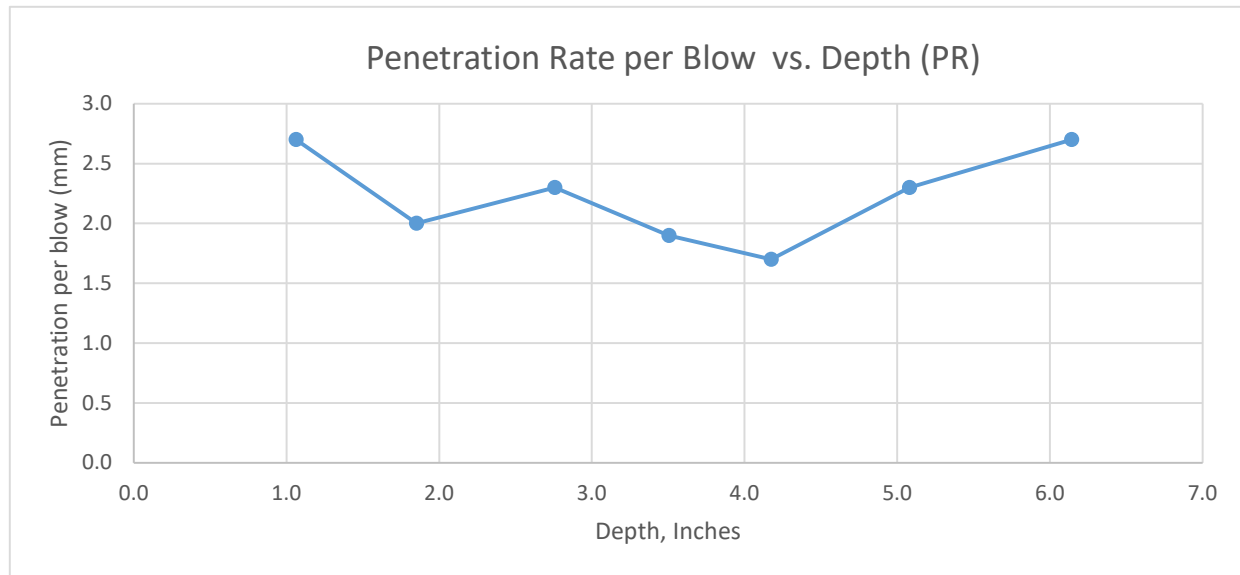

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date:/Time	8/27/2021 1:00pm
Station/ offset	Sta. H 152+00 4' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	0

