
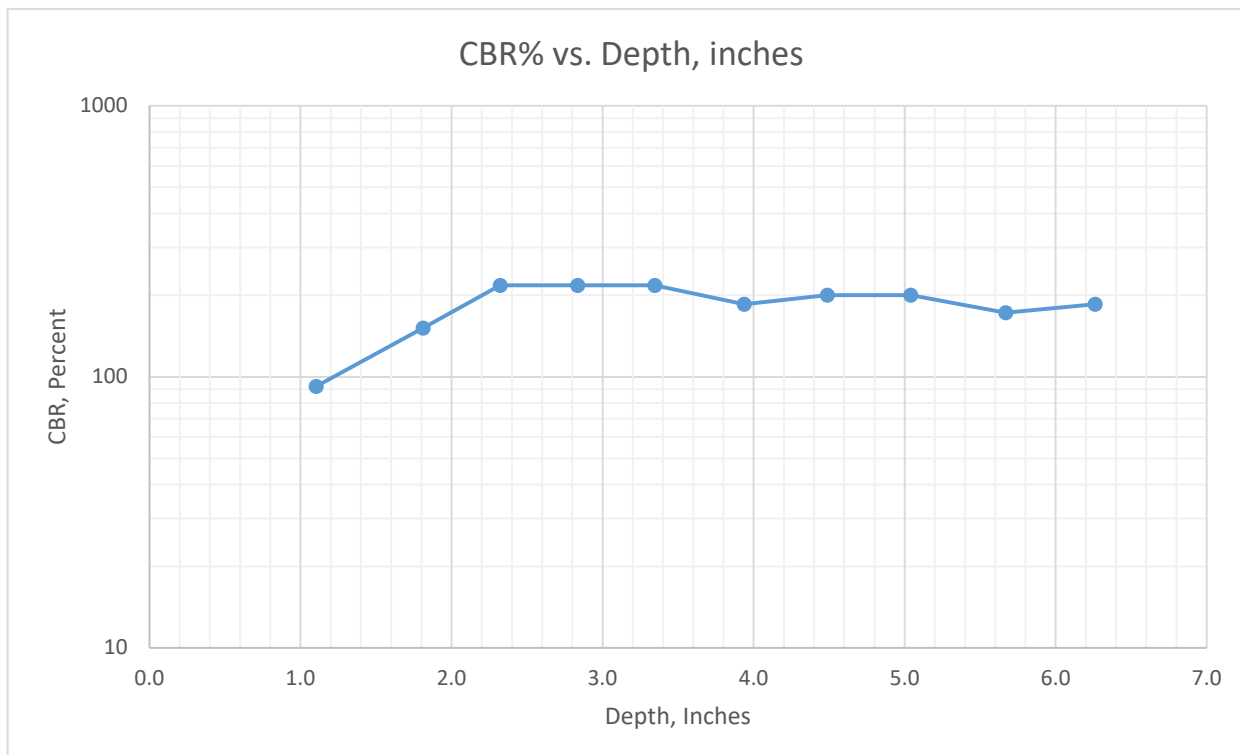


Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	9/1/2021 8:30AM
Station/ offset	Sta. M10+00 10'L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Sunny

Raw Data					DCP Index			
# of blows	Cumulative Penetration (mm)	Penetration Increase (mm)	Depth (mm)	Depth (in)	Penetration per blow -PR (mm)	Hammer Blow Factor	CBR%*	Notes:
0	356	0	0	0.0				
10	384	28	28.0	1.1	2.8	1	92	
10	402	18	46.0	1.8	1.8	1	151	
10	415	13	59.0	2.3	1.3	1	218	
10	428	13	72.0	2.8	1.3	1	218	
10	441	13	85.0	3.3	1.3	1	218	
10	456	15	100.0	3.9	1.5	1	185	
10	470	14	114.0	4.5	1.4	1	200	
10	484	14	128.0	5.0	1.4	1	200	
10	500	16	144.0	5.7	1.6	1	172	
10	515	15	159.0	6.3	1.5	1	185	

*292/(PR^1.12)

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	9/1/2021 8:30AM
Station/ offset	Sta. M10+00 10'L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Sunny

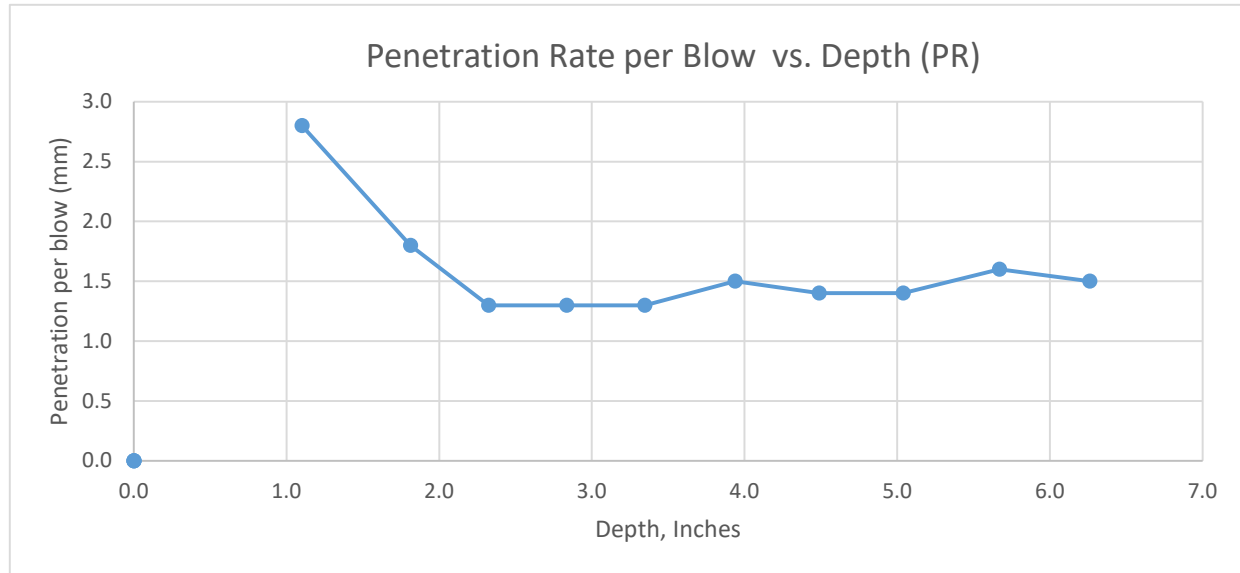

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date:/Time	9/1/2021 8:30AM
Station/ offset	Sta. M10+00 10'L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Sunny

