
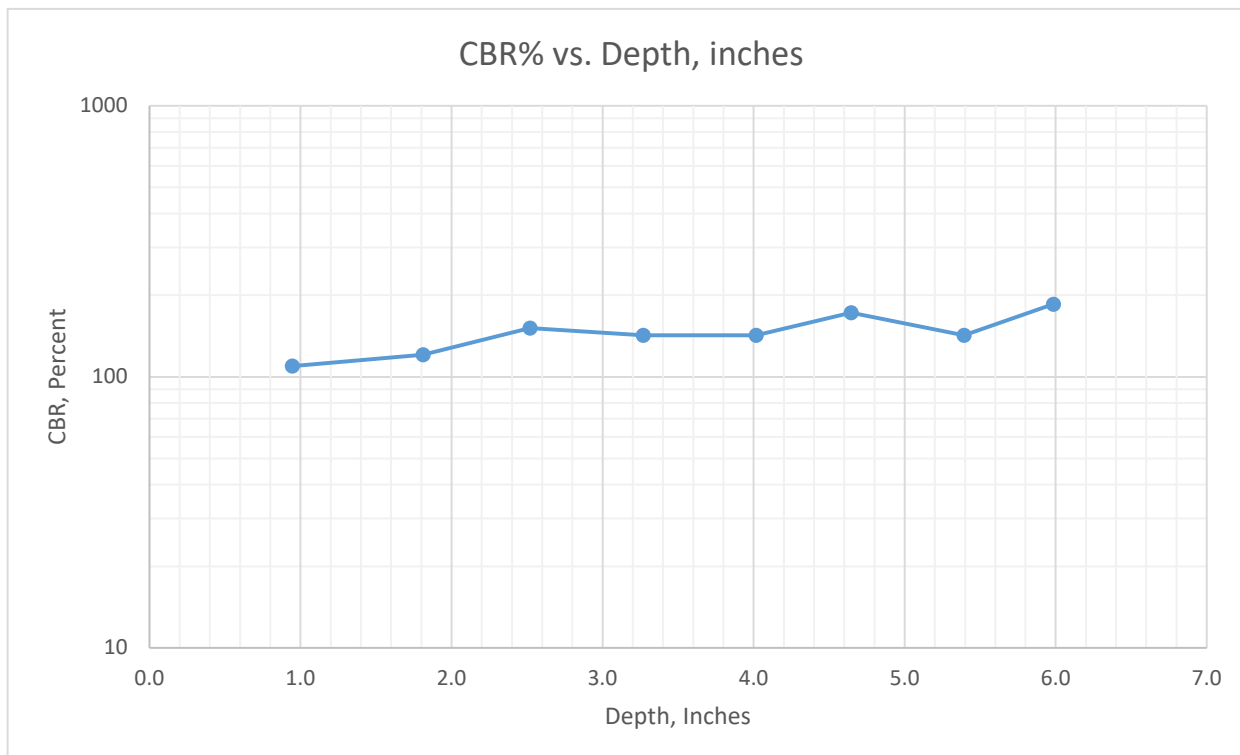


Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	9/1/2021 8:30am
Station/ offset	Sta. M10+00 4'L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Partly sunny, Hot

Raw Data					DCP Index			
# of blows	Cumulative Penetration (mm)	Penetration Increase (mm)	Depth (mm)	Depth (in)	Penetration per blow -PR (mm)	Hammer Blow Factor	CBR%*	Notes:
0	363	0	0	0.0				
10	387	24	24.0	0.9	2.4	1	110	
10	409	22	46.0	1.8	2.2	1	121	
10	427	18	64.0	2.5	1.8	1	151	
10	446	19	83.0	3.3	1.9	1	142	
10	465	19	102.0	4.0	1.9	1	142	
10	481	16	118.0	4.6	1.6	1	172	
10	500	19	137.0	5.4	1.9	1	142	
10	515	15	152.0	6.0	1.5	1	185	

*292/(PR^1.12)

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	9/1/2021 8:30am
Station/ offset	Sta. M10+00 4'L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Partly sunny, Hot

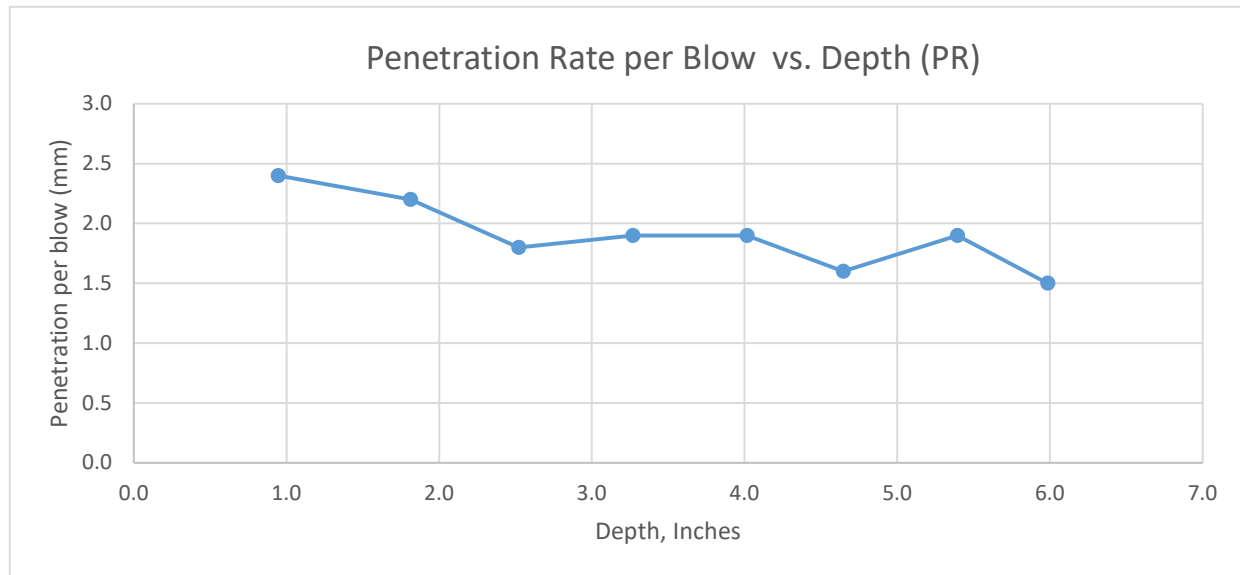

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date:/Time	9/1/2021 8:30am
Station/ offset	Sta. M10+00 4'L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Partly sunny, Hot

