
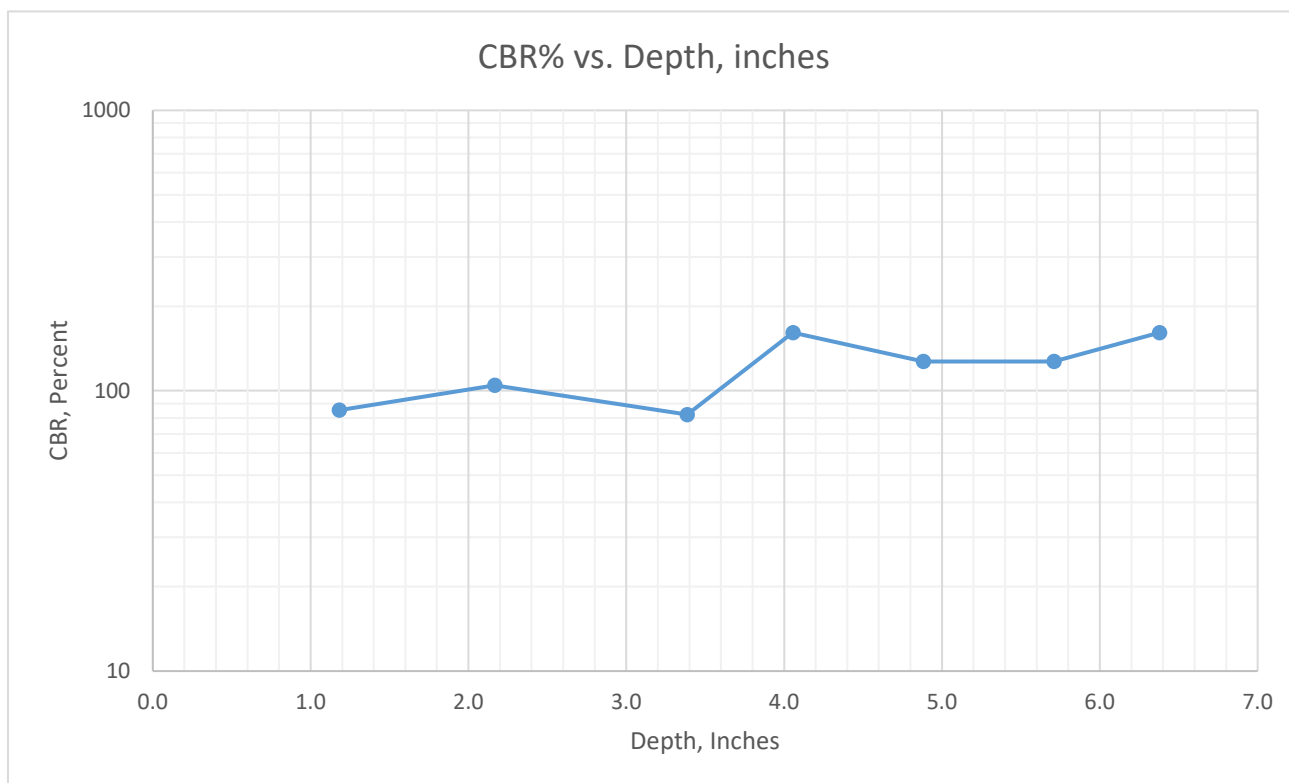


Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date:/Time	9/13/2021 8:30am
Station/ offset	Sta. M 114+00, 4' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Partly sunny, Hot

Raw Data					DCP Index			
# of blows	Cumulative Penetration (mm)	Penetration Increase (mm)	Depth (mm)	Depth (in)	Penetration per blow -PR (mm)	Hammer Blow Factor	CBR%*	Notes:
0	365	0	0	0.0				
10	395	30	30.0	1.2	3.0	1	85	
10	420	25	55.0	2.2	2.5	1	105	
10	451	31	86.0	3.4	3.1	1	82	
10	468	17	103.0	4.1	1.7	1	161	
10	489	21	124.0	4.9	2.1	1	127	
10	510	21	145.0	5.7	2.1	1	127	
10	527	17	162.0	6.4	1.7	1	161	

*292/(PR^{1.12})

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date:/Time	9/13/2021 8:30am
Station/ offset	Sta. M 114+00, 4' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Partly sunny, Hot

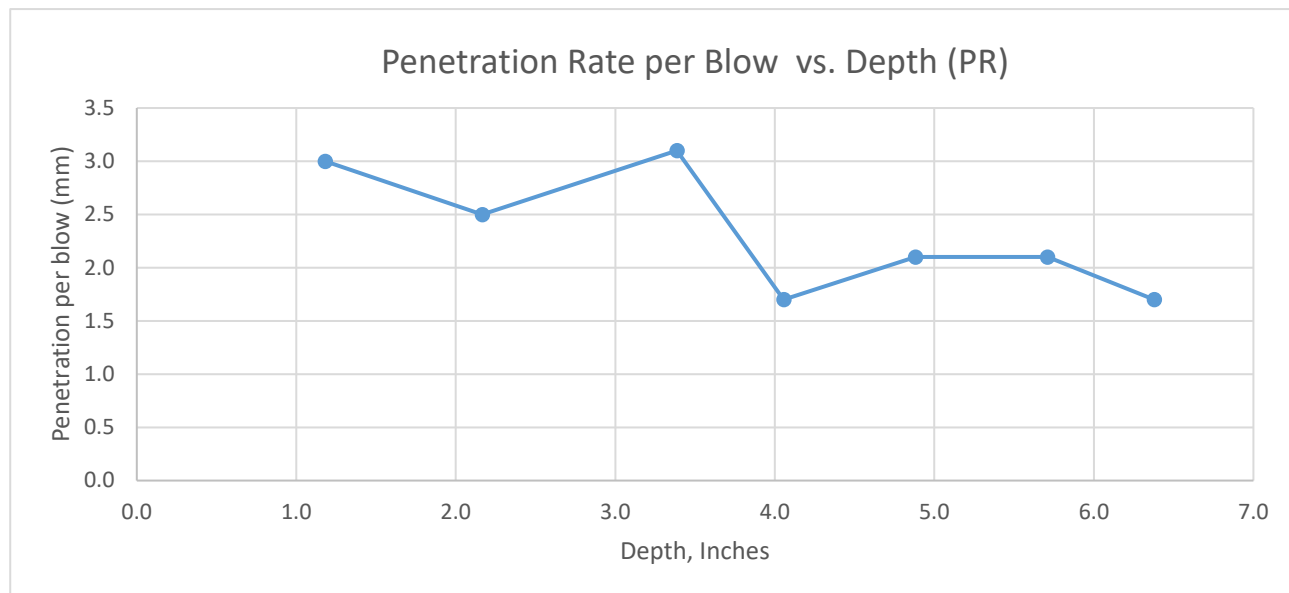

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date:/Time	9/13/2021 8:30am
Station/ offset	Sta. M 114+00, 4' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Partly sunny, Hot

