
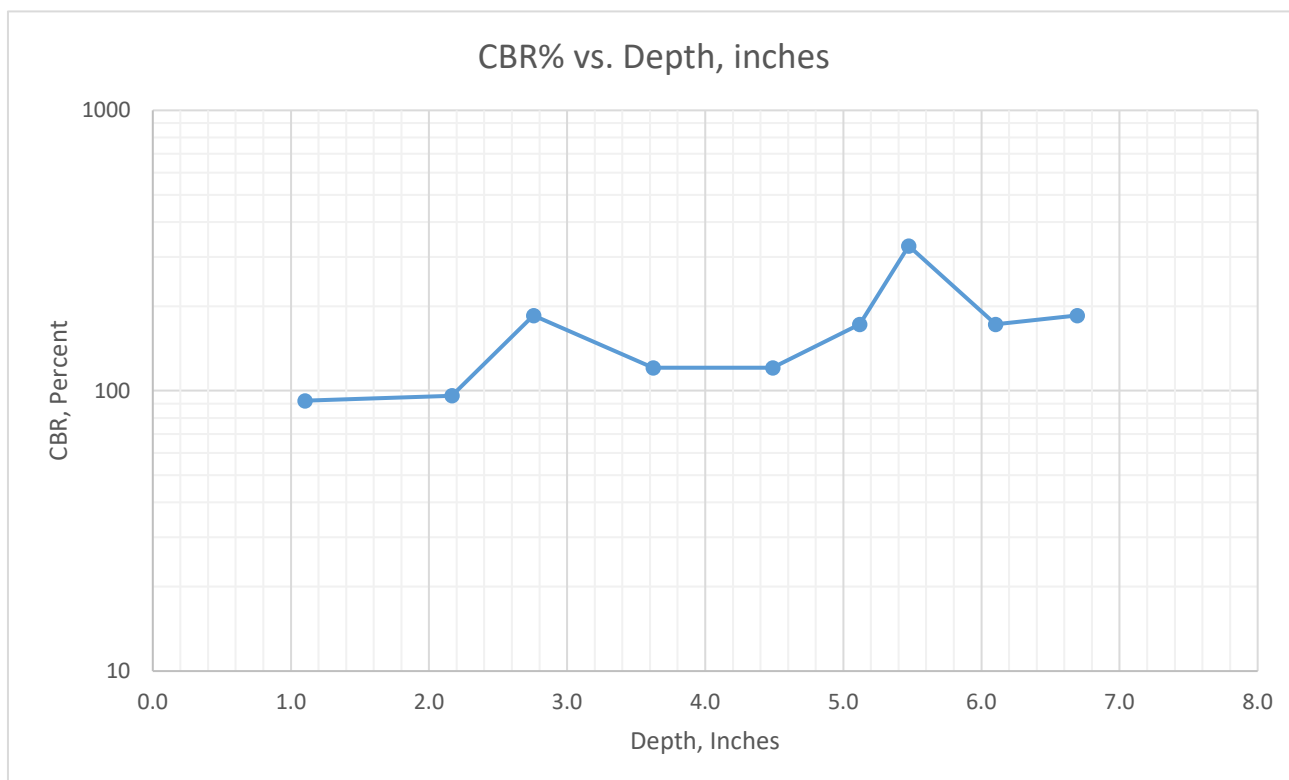


Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	9/13/2021 8:30am
Station/ offset	Sta. M 150+00, 10' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Partly sunny, Hot

Raw Data					DCP Index			
# of blows	Cumulative Penetration (mm)	Penetration Increase (mm)	Depth (mm)	Depth (in)	Penetration per blow -PR (mm)	Hammer Blow Factor	CBR%*	Notes:
0	370	0	0	0.0				
10	398	28	28.0	1.1	2.8	1	92	
10	425	27	55.0	2.2	2.7	1	96	
10	440	15	70.0	2.8	1.5	1	185	
10	462	22	92.0	3.6	2.2	1	121	
10	484	22	114.0	4.5	2.2	1	121	
10	500	16	130.0	5.1	1.6	1	172	
10	509	9	139.0	5.5	0.9	1	329	
10	525	16	155.0	6.1	1.6	1	172	
10	540	15	170.0	6.7	1.5	1	185	

*292/(PR^1.12)

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	9/13/2021 8:30am
Station/ offset	Sta. M 150+00, 10' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Partly sunny, Hot

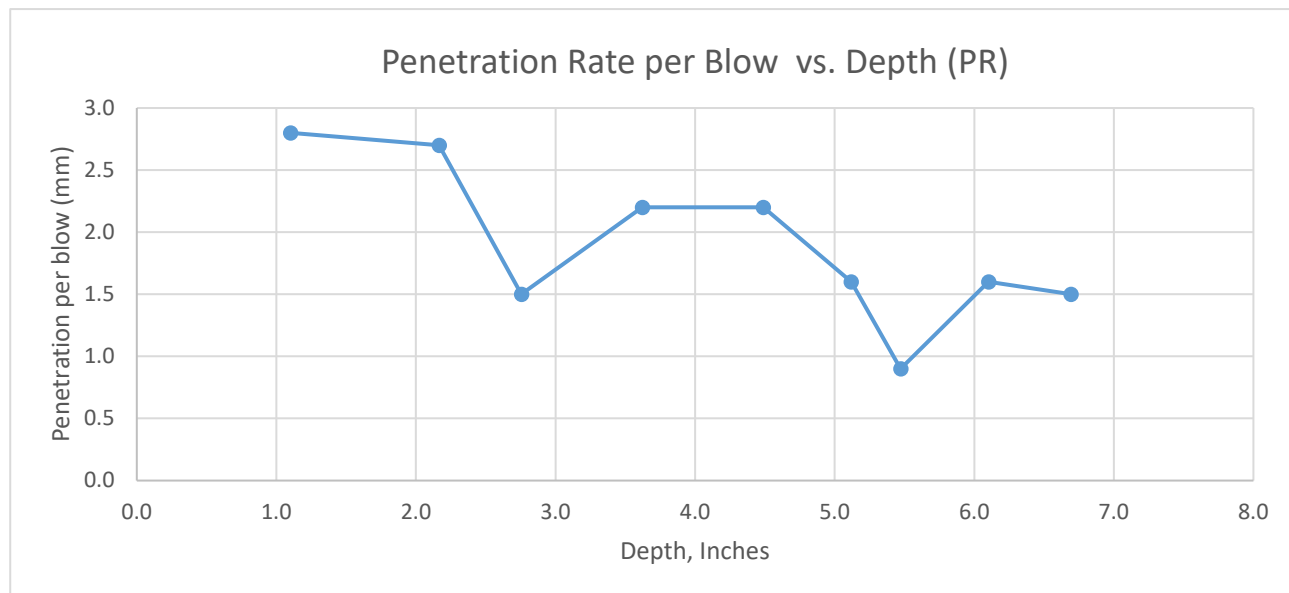

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	9/13/2021 8:30am
Station/ offset	Sta. M 150+00, 10' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Partly sunny, Hot

