
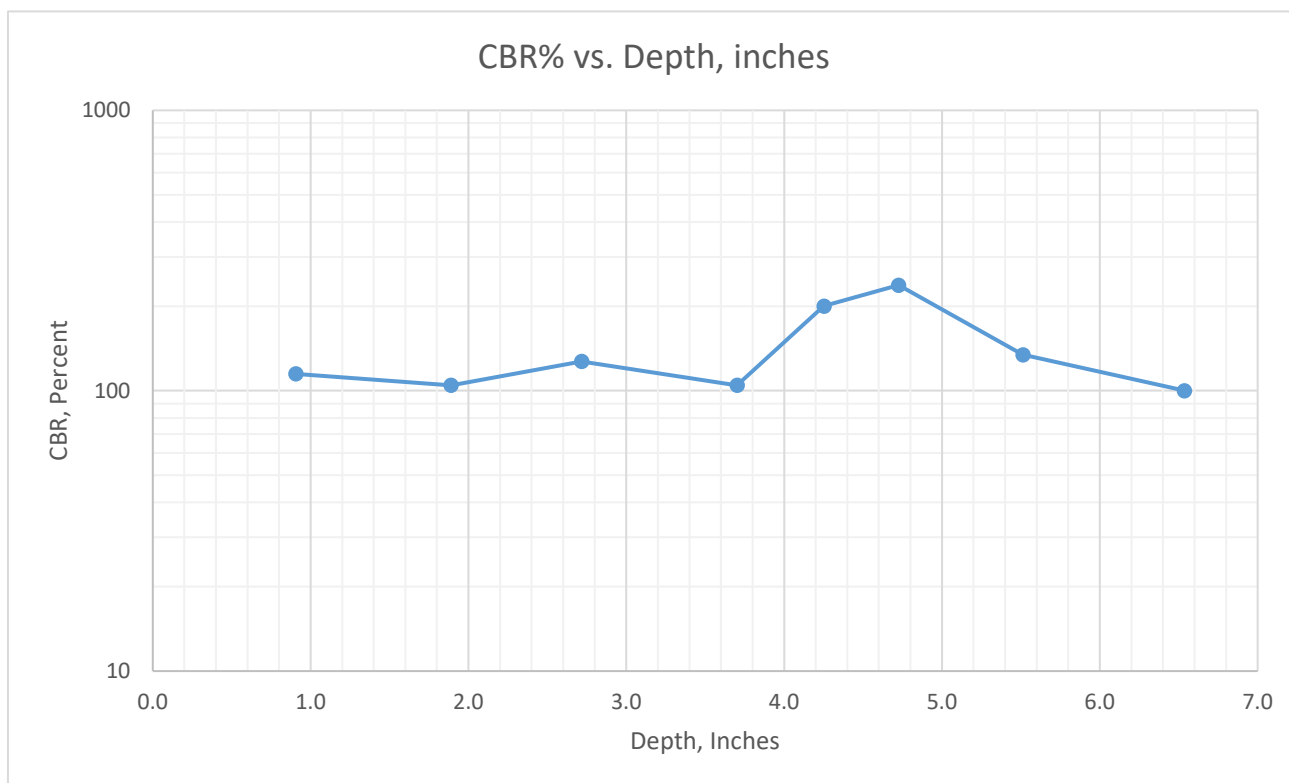


Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	9/13/2021 8:30am
Station/ offset	Sta. M 94+00, 10' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Partly sunny, Hot

Raw Data					DCP Index			
# of blows	Cumulative Penetration (mm)	Penetration Increase (mm)	Depth (mm)	Depth (in)	Penetration per blow -PR (mm)	Hammer Blow Factor	CBR%*	Notes:
0	361	0	0	0.0				
10	384	23	23.0	0.9	2.3	1	115	
10	409	25	48.0	1.9	2.5	1	105	
10	430	21	69.0	2.7	2.1	1	127	
10	455	25	94.0	3.7	2.5	1	105	
10	469	14	108.0	4.3	1.4	1	200	
10	481	12	120.0	4.7	1.2	1	238	
10	501	20	140.0	5.5	2.0	1	134	
10	527	26	166.0	6.5	2.6	1	100	

*292/(PR^{1.12})

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date/Time	9/13/2021 8:30am
Station/ offset	Sta. M 94+00, 10' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Partly sunny, Hot

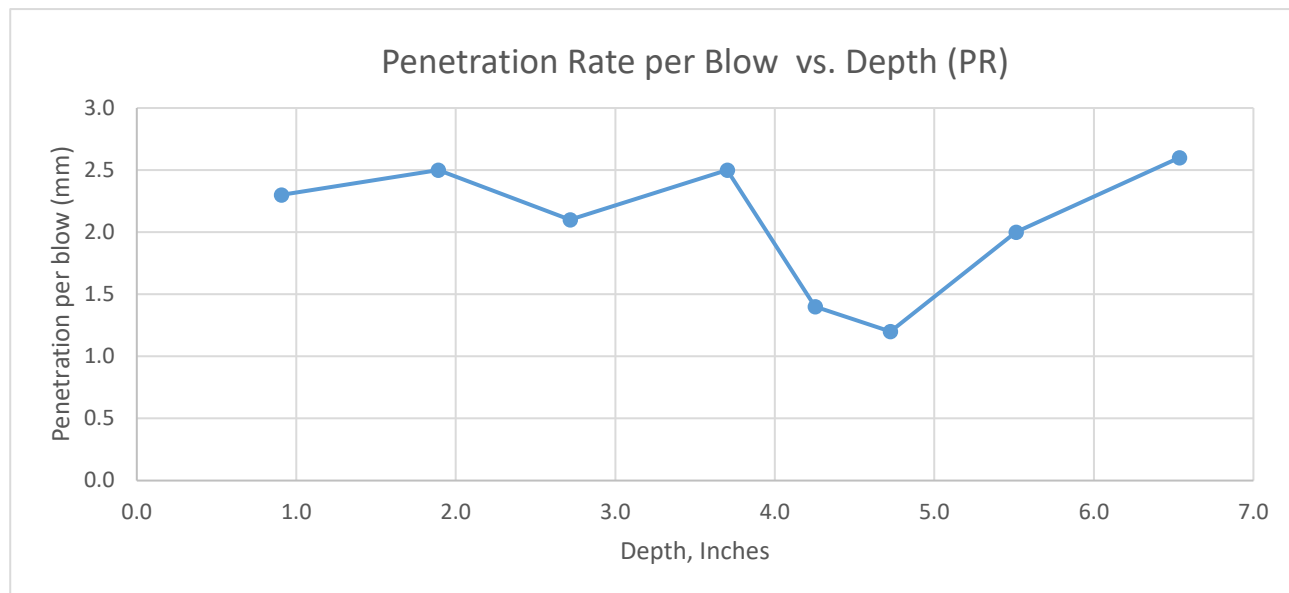

Project:	21-0561 Johnson-Morrisville STP 2919(1)	Date:/Time	9/13/2021 8:30am
Station/ offset	Sta. M 94+00, 10' L	Soil Type:	FDR
Tech:	M. Kingery	Weather/ Temp:	Partly sunny, Hot

