



FINAL REPORT

SPS-5 PROJECT 4005
ASPHALT REHABILITATION STUDY
US-62 WESTBOUND - COMANCHE COUNTY, OKLAHOMA

FHWA/LTPP
SOUTHERN REGION COORDINATION OFFICE

October 1998

Research Div.
Library

TE251.5
.S27
1998x
OKDOT
Library



FINAL REPORT

**SPS-5 PROJECT 4005
ASPHALT REHABILITATION STUDY
US-62 WESTBOUND - COMANCHE COUNTY, OKLAHOMA**

**FHWA/LTPP
SOUTHERN REGION COORDINATION OFFICE**

October 1998

**Research Div.
Library**

TABLE OF CONTENTS

<u>Section</u>	<u>Page</u>
INTRODUCTION	1
SPS-5 General Experiment Design	1
Selection/Nomination of US-62, Westbound	1
Specific Experiment Design for US-62	4
PRECONSTRUCTION MONITORING	4
Pavement Surface Distress	4
Structural Capacity	4
Surface Roughness	5
Materials Sampling and Testing	5
CONSTRUCTION MONITORING	5
POSTCONSTRUCTION MONITORING	7
Materials Sampling and Testing	7
SUMMARY	7
APPENDICES	
APPENDIX A. SITE NOMINATION FORMS, APPROVAL CORRESPONDENCE AND OTHER PERTINENT INFORMATION	A.1
APPENDIX B. PRECONSTRUCTION DISTRESS SURVEYS	B.1
APPENDIX C. DEFLECTION PLOTS	C.1
APPENDIX D. MATERIAL SAMPLING AND TESTING PLAN	D.1
APPENDIX E. REHABILITATION CONSTRUCTION PLANS AND DATA FORMS	E.1
APPENDIX F. ROD AND LEVEL PROFILE DATA	F.1
APPENDIX G. PHOTOGRAPHS	G.1

LIST OF FIGURES

<u>Figure</u>	<u>Page</u>
1. SPS-5, Rehabilitation of Asphalt Concrete Pavements	3

LIST OF TABLES

<u>Table</u>	<u>Page</u>
1. Key Products of SPS-5	2
2. Profile Readings	6

FINAL REPORT - SPS-5 PROJECT 4005
ASPHALT REHABILITATION STUDY
US-62, WESTBOUND
COMANCHE COUNTY, OKLAHOMA

INTRODUCTION

As part of the Strategic Highway Research Program's (SHRP) Long Term pavement Performance (LTPP) Study, sections of highway are being selected to apply very specific treatments to study various facets of construction (both new and rehabilitated). These projects are referred to as Specific Pavement Studies (SPS). This particular project, on US-62 in Comanche County, Oklahoma, was identified as a potential candidate for inclusion in the evaluations of asphalt concrete rehabilitation (SPS-5).

SPS-5 General Experiment Design

The anticipated products of the SPS-5 experiment are included in table 1. The overall intent of the experiment is to evaluate some of the more common asphalt rehabilitation techniques currently used by State Highway Agencies (SHAs). This general evaluation is intended to include condition of the pavement prior to overlay (both structurally and functionally), the loading conditions the project is exposed to (including both environment and traffic) and finally, the various treatment applications. The standard SPS-5 experiment design consists of nine 500' test sections (as shown in figure 1). The standard SPS-5 experiment includes four test sections which are subjected to intensive surface preparation (milling) prior to overlay vs. four test sections which will undergo minimal surface preparation, four test sections utilizing recycled mix vs. four with virgin mix and thin overlays (approximately 2") vs. thick overlays (approximately 5"). The eight test sections represent combinations of the above mentioned features and are placed adjacent to the control section (which receives no rehabilitation) for comparison purposes. Minimal surface preparation will include patching only and/or crack sealing. Intensive surface preparation includes 2" of milling to be conducted along with patching, if necessary.

As part of the experiment, it was designated that the recycled mixture contain 30% of the Recycled Asphalt Pavement (RAP) and that the RAP material shall be the millings from the intensive surface preparation sections.

Selection/Nomination of US-62, Westbound

The Oklahoma SPS-5 site location was identified through efforts of the personnel from the Oklahoma Department of Transportation (ODOT). The ODOT reviewed anticipated rehabilitation programs to determine potential candidates.

Table 1. Key Products of SPS-5

1. Comparisons and development of empirical prediction models for performance of AC pavements with different intensities of surface preparation, with thin and thick AC overlays, and with virgin and recycled AC overlay mixtures.
2. Evaluation and field verification of the AASHTO Guide design procedures for rehabilitation of existing AC pavements with AC overlays, and other analytical overlay design procedures for AC pavements.
3. Determination of appropriate timing to rehabilitate AC pavements in relation to existing condition and type of rehabilitation procedures.
4. Development of procedures to verify and update the pavement management and life-cycle cost concepts in the AASHTO Guide using the performance prediction models developed for rehabilitated AC pavements.
5. Development of a comprehensive database on the performance of rehabilitation AC pavements for use by state and provincial engineers and other researchers.

REHABILITATION PROCEDURES		
S P U R R E F P A C E	O M V A E T R E L R A I Y A L	O T V H E I R C L K A N Y E S S
Routine Maint. (Control)		0"
M I N I M U M	Recycled	2"
	AC	5"
	Virgin	2"
	AC	5"
I N T E N S E	Recycled	2"
	AC	5"
	Virgin	2"
	AC	5"

FACTORS FOR MOISTURE, TEMPERATURE, AND PAVEMENT CONDITION															
WET								DRY							
FREEZE				NO FREEZE				FREEZE				NO FREEZE			
FAIR	POOR			FAIR	POOR			FAIR	POOR			FAIR	POOR		
												X			
												X			
												X			
												X			
												X			
												X			
												X			
												X			
												X			
												X			

Subgrade Soil: Fine
Traffic: > 280 KESAL/Year
X = Sections on 400500

Figure 1. SPS-5, Rehabilitation of Asphalt Concrete Pavements

As a result, an SPS-5 candidate project was nominated by the State of Oklahoma on 30 May 1996. Nomination forms, correspondence and site information is included in appendix A. The project site is located on US-62, approximately 0.5 miles west of SH-115. This particular project site was representative of generally fine-grained soils. Traffic levels for this particular site were estimated at approximately 280 KESALs/year in the design lane. The project was let for construction in July 1996 and construction began in June 1997.

Specific Experiment Design for US-62

The layout and typical sections are included in appendix A. The subgrade for this project is a silty clay corresponding to fine-grained soil. The site was considered in fair condition, even with transverse cracks of moderate severity. This project includes nine core experiment test sections along with one supplemental test section selected by the ODOT, to evaluate a varied overlay thickness for further use in future rehabilitation.

PRECONSTRUCTION MONITORING

A number of preconstruction monitoring measurements were performed on US-62 to establish the condition prior to rehabilitation. Each preconstruction monitoring endeavor will be discussed separately in the following text.

Pavement Surface Distress

Prior to rehabilitation, each test section was marked with paint and signs, etc., to allow for the collection of pavement surface distress data. Each test section was rated manually using the SHRP Distress ID Manual. The predominant distress throughout all test sections was bleeding in the wheel paths and moderate severity transverse cracking. Appendix B contains the preconstruction distress surveys. The severity of the transverse cracks gave rise to concerns about the effects on the overlay. The transverse crack width did not meet the $\frac{3}{4}$ " requirements for patching, but did have depressions along the crack. Initially a level-up was not deemed necessary; however, when paving began, it was the only method available to prevent bumps in the roadway for sections 400502 and 400505. It was decided to remove the SS-1 from the crack area and place and compact HMAC material along the crack to improve the ride quality for the two sections.

Structural Capacity

Deflection measurements were performed beginning on 16 June 1997, in conjunction with the distress surveys, and concluded 18 June 1997. Deflection measurements were obtained using the SHRP Falling Weight Deflectometer (FWD) to evaluate the structural capacity of each of these test sections. Deflection measurements were recorded from a series of varying weights in a set pattern at 25' intervals to measure the subsurface response (deflection) of the structural layers in that highway segment. Results of the deflection testing are included in appendix C.

Surface Roughness

Profilometer testing was performed on 4 June 1997. Profilometer measurements were taken in m/km and the profile readings (see table 2) were taken for both the inside and outside wheel paths. The average for each section is indicated as well as an overall average for the project. This measurement is called the International Roughness Index (IRI) and is used widely by various agencies.

Materials Sampling and Testing

Materials sampling and testing was performed on 16 June 1997 by one of the subcontractors, following a Material Sampling and Testing Guide established specifically for this project (see appendix D). The subcontractors furnished a drill rig for completing the augering, shoulder probes, subgrade sampling and coring.

The cores extracted during the preconstruction sampling indicated that up to two distinct layers were present along the SPS-5 sections. The existing pavement contained 4" HMAC over 8" of hot sand. This appeared to be consistent throughout the project length. A set of the construction plans are included in appendix E. It should be noted that their layer thicknesses indicated in the MSTP incorrectly indicate 8" of existing HMAC.

CONSTRUCTION MONITORING

Following are details of the construction event relating to the asphalt rehabilitation on US-62 in the westbound lane in Comanche County, Oklahoma. This SPS-5 rehabilitation project included ten 500' test sections.

At the preconstruction meeting on 5 November 1996, the contractor noted that they wanted to start in February 1997. No significant concerns were expressed regarding the construction of these test sections.

One and one-half inches of cold-milling was performed on sections 06, 07, 08, 09 and 60 on 27 June 1997. The milling machine was a D1100 SMI with a 12' cutting bit. The sections were open to traffic from the time of milling to the beginning of paving operations on 30 June 1997.

Paving operations always began with sweeping of the lanes and application of a tack coat at a rate of 0.03 gal./sq. yd. The mix was laid using a Blaw-Knox PF-510 paver. The material was compacted using a Hypac vibratory, a Ferguson pneumatic roller and a Caterpillar steel-wheel finishing roller.

The ODOT provided a surface and binder design for the HMAC layer. These were called BH and AH, respectively. The BH (surface mix) was laid as one final 1½" lift. The AH (binder mix) was laid in sections receiving milling and/or a 5" overlay. Lifts varying in thickness from 1.5 to 3 inches were laid, depending on the designs. Detailed information on the

**Table 2. Profile Readings
International Roughness Index (IRI) in m/km**

Preconstruction - Date Surveyed: 4 June 1997

Section	Left	Right	Average
400501	1.724	1.410	1.567
400502	2.857	2.12	2.535
400503	2.182	1.926	2.054
400504	1.800	1.733	1.766
400505	1.740	1.445	1.592
400506	2.461	1.686	2.073
400507	2.375	2.212	2.293
400508	2.315	1.888	2.102
400509	1.089	1.083	1.086
400560	Unknown	Unknown	Unknown
Average	2.060	1.733	1.896

Postconstruction - Date Surveyed: 14 January 1998

Section	Left	Right	Average
400501	1.294	1.340	1.317
400502	1.280	1.015	1.147
400503	1.131	0.866	0.998
400504	1.118	1.026	1.072
400505	1.153	0.878	1.016
400506	1.061	0.935	0.998
400507	0.938	0.825	0.882
400508	1.077	0.786	0.932
400509	1.074	0.756	0.915
400560	0.752	0.685	0.719
Average	1.088	0.911	1.000

laydown procedures can be located in Appendix E. The initial steel-wheel applied one coverage, the pneumatic applied two to three coverages and the finishing steel-wheel applied one to two coverages.

The plant was located at Station 990+00, approximately ¼ mile from the project, off US-62. The plant was an Aztec batch plant, which provided all of the virgin and recycled mix. The RAP contained 30% recycled. The initial batch of recycled laid on the test strip contained an AC content that was too high. This was reduced and met specifications.

Elevations were taken on the milled surface and every subsequent overlay. Thickness information and cross-profiles of each section is provided in appendix F.

Section 400501 received only minor maintenance (crack sealing) and will serve as the control section. The nine sections receiving minor and major rehabilitation did not receive crack sealing. As mentioned previously in this report, a level-up using the specified hot-mix (virgin or recycled) was applied along the few transverse cracks that existed in sections 400502 and 400505, to improve ride quality. The site will provide valuable information on the comparison of the different rehabilitation methods.

POSTCONSTRUCTION MONITORING

Following the completion of all rehabilitation applications, postconstruction sampling was initiated. These monitoring activities consisted of similar types of sampling activities that took place prior to construction, as well as manual surveys, FWD testing, and profilometer testing. LTPP directives indicate that the manual surveys and profilometer testing need to be performed biennially. FWD testing is to be performed annually. Postconstruction transverse profiles using Dipstick® and visual distress surveys were conducted Wednesday, 23 July 1997. Postconstruction FWD testing was conducted on 3 December 1997, and is included in appendix C. Profilometer testing was conducted on 14 January 1998, and will continue quarterly.

Materials Sampling and Testing

The postconstruction sampling and testing (coring of 4" cores) was performed the day after construction of each section. Coring was performed 25' from the approach and leave end of each test section according to the layout diagram in the Material Sampling Plan prepared for this experiment. Sampling was conducted by the subcontracted laboratory. Testing is currently under-way and near completion, utilizing SHRP test protocols.

SUMMARY

Having completed the observations of the construction for this SPS-5 project, located on US-62 west of Lawton, Oklahoma, it appears that this project will contribute significantly to the LTPP objectives by providing valuable information about the rehabilitation of asphalt pavements. The efforts of the ODOT, and their willingness to participate in this study, are greatly appreciated. Special thanks go to Kathleen Toney, David Ooten, and Don Farrow.

Monitoring is underway and we will continue noting changes in the surface distress, surface profile and structural capacity, and compare those data with other projects of this nature around the country in an attempt to improve on existing asphalt pavement rehabilitation design methods.

APPENDIX A

**SITE NOMINATION FORMS, APPROVAL CORRESPONDENCE
AND
SITE INFORMATION**

Brent Rauhut Engineering Inc.



24 May 1996

Mr. David Ooten
Engineering Manager, Research
Oklahoma Department of Transportation
200 N.E. 21st Street, Room 2A2
Oklahoma City, Oklahoma 73105-3204

Subject: Nomination of SPS Project

Dear David,

Enclosed are the nomination guidelines for Experiment SPS-1, "Strategic Study of Structural Factors for Flexible Pavements" and Experiment SPS-5, "Rehabilitation of Asphalt Concrete Pavements".

Please do not hesitate to call should you have any questions during the completion of the nomination forms. I will be certain to do everything in my power to get these nominations processed as quickly as possible to facilitate incorporation in the project you have underway. I look forward to hearing from you soon.

Sincerely,

A handwritten signature in black ink, appearing to read 'Jerry Daleiden', with a long horizontal flourish extending to the right.

Jerry F. Daleiden, P.E.
Project Engineer, SRCO

JFD:dmj

Enclosures: As stated.

c.w/o Enc: Morris Reinhardt, RE/SRCO
Mark Gardner, SRCO/File

RECEIVED JUN - 4 1996



NAME	INFO	ACTN	COPY
BR			
WG			
MR			
<i>PD</i>		<i>✓</i>	

File: _____

Dear Mr. Daleiden:

The Oklahoma Department of Transportation is requesting that the project NH-215(60) on U.S. 62 west of Lawton be considered for SPS-1 and SPS-5 sites in the SHRP LTPP study. The plans have been submitted and this project is scheduled to be let in July 1996. In the interest of time, we will send the required information as it is collected so that you may begin processing the nominations. A set of plans is enclosed for your review. If I may be of further assistance please contact myself or Ginger McGovern at (405) 521-2671.


Jack D. Telford
Materials Engineer

Enclosures

AN EQUAL OPPORTUNITY EMPLOYER

Brent Rauhut Engineering Inc.



5 June 1996

Mr. Monte Symons
Pavement Performance Division - LTPP (HNR-40)
Federal Highway Administration
Turner-Fairbanks Highway Research Center
6300 Georgetown Pike, Room F-215
McLean, Virginia 22101

Subject: Nomination of SPS Projects from the Oklahoma DOT

Dear Monte,

The Oklahoma DOT has expressed an interest in constructing test sections for incorporation in the SPS-1 and SPS-5 experiments (see attached letter and nomination forms). It is proposed that these test sections be built side-by-side. They have an existing portion of US-62 just west of Cache, Oklahoma that has an existing two-lane undivided facility. The planned construction will widen this facility to a four-lane divided highway. The SPS-1 sections would be incorporated in the new construction and the SPS-5 sections would be incorporated in the rehabilitation of the existing facility.

Although we have not yet collected soil samples at this particular location, it is our understanding that the subgrade here is a sandy clay (based on the information provided by the state and materials sampling conducted previously at LTPP test sections in Altus, Oklahoma on US-62 to the west of this particular location, and near Lawton, Oklahoma on US-62 just east of this particular location). These sections would, of course, be in the dry no-freeze environmental zone. From review of the plans for upcoming construction and the plans of original construction of the two-lane undivided facility, we believe that ample space will be available to satisfactorily locate all of the test sections in the same vicinity, with comparable traffic and earthwork.

It should be noted that this project is scheduled to be let for construction in six weeks. With this in mind, it is being asked that this section be given your earliest possible consideration. We believe that we can assist the Oklahoma DOT in incorporating these test sections in this project, and believe that these will be very desirable test sections. However, we will need a fairly prompt response to bring these sections to fruition.

Please feel free to contact me if you have any questions on the information provided, or if we can be of any further assistance in your review of these nominations. Thank you for your consideration.

Sincerely,

A handwritten signature in black ink, appearing to read "Jerry Daleiden". The signature is fluid and cursive, with a long horizontal stroke at the end.

Jerry F. Daleiden, P.E.
Project Engineer, SRCO

JFD:dmj

Attachments: As stated.

c.w/Att: Ginger McGovern, OKDOT
 John Stites, FHWA-OK Div.

John Miller, PCS/LAW
Morris Reinhardt, RE/SRCO

SHEET A. SPS-5 CANDIDATE PROJECT NOMINATION AND INFORMATION FORM

STATE OK

PROJECT LOCATION

ROUTE NUMBER U.S. 62ROUTE SIGNING ☐ Interstate ☒ U.S. ☐ State ☐ County

Other _____

PROJECT LOCATION Start Milepost _____ End Milepost _____

Start Station _____ End Station _____

PROJECT LOCATION DESCRIPTION Approx. 0.5 miles west of S.H. 115 and
approx. 1.0 miles east of S.H. 54

COUNTY

Comanche

HIGHWAY AGENCY DISTRICT NUMBER

7

SHRP ENVIRONMENTAL ZONE

☐ WET FREEZE ☐ WET NO-FREEZE ☐ DRY FREEZE ☒ DRY NO-FREEZE

SIGNIFICANT DATES

LATEST DATE OF APPROVAL NOTIFICATION FROM SHRP

CONTRACT LETTING DATE

7-96

ESTIMATED CONSTRUCTION START DATE

9-96

PROJECT DESCRIPTION

YEAR OPENED TO TRAFFIC

1973

NUMBER OF LANES (One Direction)

2☒ Divided-when completed ☐ Undivided

OUTSIDE LANE WIDTH (Feet)

12.0

OUTSIDE SHOULDER TYPE

☐ Turf ☐ Granular ☒ Asphalt Concrete ☐ Surface Treatment☐ PCC ☐ Curb and Gutter Other _____

OUTSIDE SHOULDER WIDTH (Feet)

10.0SUBSURFACE EDGE DRAINS ☐ Placed at initial construction ☒ Not Used☐ Retrofitted

Retrofit Date _____

ASSESSMENT OF PRESENT PAVEMENT CONDITION

☒ Fair☐ Poor

PREDOMINATE DISTRESSES

☐ Fatigue Cracking ☒ Other Cracking ☐ Potholes/Patches ☒ RuttingComments Transverse cracking is most prevalent distress; also haveapprox. 3/4" rutting.

SHEET B. SPS-5 CANDIDATE PROJECT NOMINATION AND INFORMATION FORM

STATE _____

PAVEMENT STRUCTURE LAYER DESCRIPTIONS

LAYER ¹ NO.	LAYER ² DESCRIPTION CODE	MATERIAL TYPE ³ CLASS CODE	THICKNESS ⁴ (INCHES)	STRUCTURAL ⁵ COEFFICIENT
1	SUBGRADE (7)	<u>5</u> <u>2</u>	— — —	— — —
2	<u>0</u> <u>6</u>	<u>4</u> <u>2</u>	— — —	0. — —
3	<u>0</u> <u>5</u>	<u>2</u> <u>8</u>	— <u>8</u> . <u>0</u>	0. — —
4	<u>0</u> <u>4</u>	<u>0</u> <u>1</u>	— <u>3</u> . <u>0</u>	0. — —
5	<u>0</u> <u>3</u>	<u>0</u> <u>1</u>	— <u>1</u> . <u>5</u>	0. — —
6	— —	— —	— — —	0. — —
7	— —	— —	— — —	0. — —
8	— —	— —	— — —	0. — —
9	— —	— —	— — —	0. — —

NOTES

1. Layer 1 is the natural occurring subgrade soil. The existing surface will have the largest assigned layer number.

2. Layer description codes:

Overlay	01	Base Layer	05	Porous Friction Course ..	09
Seal Coat	02	Subbase Layer	06	Surface Treatment	10
Original Surface ..	03	Subgrade	07	Embankment (Fill)	11
Subsurface HMAC ..	04	Interlayer	08		

3. Refer to Tables 1 through 4 for material class codes.

4. If subgrade depth to a rigid layer is known, enter this depth for subgrade, otherwise leave blank for subgrade layer.

5. Enter AASHTO structural layer coefficient used in pavement design or typical coefficient used by agency for this material. For the subgrade, enter either AASHTO soil support value or estimated resilient modulus.

SHEET C. SPS-5 CANDIDATE PROJECT NOMINATION AND INFORMATION FORM

STATE OK

TRAFFIC DATA

ANNUAL AVERAGE DAILY TRAFFIC (TWO DIRECTION)	<u>4000</u>
% HEAVY TRUCKS AND COMBINATIONS (OF AADT)	<u>13%</u>
COUNT YEAR OF AADT ESTIMATE	<u>1994</u>
TRAFFIC GROWTH RATE SINCE PROJECT OPENED TO TRAFFIC (%/YR)	<u>1.58%</u>
18K ESAL RATE IN PROPOSED STUDY LANE (1,000 ESAL/YR)	<u>280.617</u>
YEAR OF ESAL RATE ESTIMATE	<u>1994</u>
ESTIMATED TOTAL 18K ESAL APPLICATIONS IN STUDY LANE ¹	<u>8,418,511</u>

REHABILITATION INFORMATION²PRIMARY CAUSE FOR REHABILITATION Widening to 4 lane divided highway

OVERLAY	Thickness (Inches)	Material Type Class Code
Surface Course	<u>2</u>	<u>01</u>
Binder Course	<u>1 1/2</u>	<u>01</u>

SURFACE PREPARATION PRIOR TO OVERLAY

☐ Patching ☐ Crack Sealing ☒ Milling Depth of Mill 1 inch
 Other Fog Seal & Fabric Reinforcement

OTHER CONSTRUCTION ACTIVITIES TO BE PERFORMED DURING REHABILITATION

Remove 6' of the existing 10' left shoulder.

NOTES

1. Leave blank if estimate is not available.
2. This information concerns the planned rehabilitation work to be performed by the agency on the non-experimental portions of the project.

SHEET D. SPS-5 CANDIDATE PROJECT NOMINATION AND INFORMATION FORM

STATE _____

TEST SECTION LAYOUT

NUMBER OF TEST SECTIONS ENTIRELY ON: FILL _____ CUT _____

SHORTEST TRANSITION BETWEEN CONSECUTIVE TEST SECTIONS (Feet) _____

COMMENTS ON DEVIATIONS FROM DESIRED SITE LOCATION CRITERIA _____

OTHER SHRP TEST SECTIONS

DOES PROJECT CONFORM TO GPS-1 OR GPS-2 PROJECT CRITERIA? ☐ YES ☐ NODOES AGENCY APPLIED TREATMENT QUALIFY FOR GPS-6B? ☐ YES ☐ NOIS PROJECT SUITABLE FOR SPS-3 TEST SECTIONS? ☐ YES ☐ NOIS AGENCY INTERESTED IN USE OF PROJECT AS SPS-3 SITE? ☐ YES ☐ NODISTANCE TO NEAREST GPS TEST SECTION ON SAME ROUTE (Miles) 9.5TEST SECTION NUMBER OF NEAREST GPS SECTION 404162

SUPPLEMENTAL TEST SECTIONS

IF SUPPLEMENTAL EXPERIMENTAL TEST SECTIONS ARE PROPOSED, COMPLETE THE FOLLOWING

TOTAL NUMBER OF SUPPLEMENTAL TEST SECTIONS _____

FACTORS TO BE INVESTIGATED _____

Brent Rauhut Engineering Inc.



27 August 1997

Mr. Monte Symons
Pavement Performance Division - LTPP
Federal Highway Administration
Turner-Fairbanks Highway Research Center
6300 Georgetown Pike, Room F-215
McLean, Virginia 22101

Subject: Addition of Oklahoma SPS-5 Test Section to the IMS

Dear Monte,

We were notified this morning, Wednesday, 27 August 1997, that the SPS-5 supplemental test section 400560 on US-62 in Comanche County, Oklahoma was not included in the original submission of Form 1s for this project. Attached is a Form 1 requesting that this test section be included in the IMS tables.

Thank you for your assistance in this matter. If you have any questions, please feel free to contact me.

Sincerely,

Timothy J. Martin
Graduate Engineer, SRCO

TJM:dmj

Attachment: As stated.

c.w/Att: Barbara Ostrom, FHWA/LTPP-PPD
Rick Cale, SAIC
John Brunken, SRCO
Jerry Daleiden, SRCO

Jonathan Groeger, PCS/LAW
Peter Jordahl, SRCO
Hank Usher, SRCO
Mark Gardner, SRCO/File: 5.1.10

CHANGE REQUEST FOR FHWA/LTPP IMS CRITICAL TABLES

Requester [Timothy J. Martin] Region [Southern]

Date Submitted [0 8 / 2 7 / 9 7]

STATE CODE [40]

SHRP ID [0560]

```
Type of Change Requested ..... [1]
1 - Add a section
2 - Change section status
3 - Change assign date
4 - Change experiment
5 - Delete section
6 - Other change
```

If adding a section, check that nomination forms are attached []
Assign Date [0 1 / 0 1 / 8 7]

If changing section status, proposed new status .. [___] O - Out of study
(Fill out comments below for explanation) R - Released
Deassign Date [__ __ / __ __ / __ __]

If changing assignment date, proposed new date ... [__ __ / __ __ / __ __]
(Fill out comments below for explanation) old date ... [__ __ / __ __ / __ __]

```

If changing experiment, check that documentation is attached ..... [ ]
Existing Experiment ..... [ ]
Deassign Date ..... [__ __ / __ __ / __ __]
Proposed Experiment ..... [ ]

```

If deleting a section, check that documentation is attached [___]
(Fill out comments below for explanation)

If 'Other Change' is requested, check that documentation is attached. [____]
(Fill out comments below for explanation)

Comments:

Approved By: _____ Date: _____ (FHWA/LTPP)
 _____ (PCS/LAW)

Oklahoma Department of Transportation

DATE: April 19, 1996

TO: Roadway Design Engineer


FROM: Pavement Engineer

SUBJ: Pavement Design for Project Nh-215(58), J/P 04040(04),
Comanche Co., US-62, west of Cache

ADT (Present)	=	4000
ADT (30 year Future)	=	13,250
ADT (Design)	=	6625
Design PI	=	28
Design Rigid ESALs*	=	
Design Flex. ESALs*	=	8,418,511
Design Resilient Mod.=		14,628,061
% Heavy Trucks	=	13

On this day, a review was made on the subject project to establish a pavement design based on a final subgrade soil survey.

* A four-lane factor of 0.8 has been used in the calculations.


Tim M. Borg, P.E.
Pavement Engineer

cc: Rosemarie Case, Engineering Manager
Division File

THE:CCMAN62J

FINAL PAVEMENT RECOMMENDATION
COMANCHE COUNTY
Project Number NH-215(58)
J/P 04040(04)
US-62

Description: West of Cache, new construction eastbound;
overlay westbound.


This final pavement recommendation is made from a final subgrade soil survey.

The previous data indicate that the following depth of Asphalt Concrete (Section 411) or depth of Portland Cement Concrete (Section 414) will be required.

I. Flexible Pavement: 2" Type 'BH' AC
 6" Type 'AH' AC
 4" Open Graded Base
 6" Aggregate Base
 8" Lime Treated Subgrade

II. Rigid Pavement: 10" Dowel Jointed PCCP
 4" Open Graded Base
 6" Aggregate Base
 8" Lime Treated Subgrade

III. Flexible Overlay: 2" Type 'BH' AC
 1½" Type 'BH' AC
 Reinforcing Fabric



Tim M. Borg, P.E.
Pavement Engineer

cc: Rosemarie Case, Engineering Manager
Division File

THIS COMANCH 624

1986 AASHTO Pavement Design
DARWin(tm) Pavement Design System

A Proprietary AASHTOWARE(tm)
 Computer Software Product

Flexible Structural Design Module

NH-215(58), J/P 04040(04), COMANCHE CO.
 US-62, west of Cache, westward, EB lane

Flexible Structural Design Module Data

18-kip ESALs Over
 Initial Performance Period: 8,418,511
 Initial Serviceability: 4.5
 Terminal Serviceability: 2.5
 Reliability Level (%): 90
 Overall Standard Deviation: .45
 Roadbed Soil Resilient Modulus (PSI): 5,000
 Stage Construction: 1

Calculated Design Structural Number: 5.27

Specified Layer Design

Layer	Material Description	Struct. Coef. (A)	Drain. Coef. (M)	Thickness (D) (in)	Width (ft)	Calculated SN
1	Poly. Mod. Type 'B' AC	.44	1	2	38	.88
2	Type 'A' AC	.44	1	8	38	2.64
3	Open Graded Bit. Base	.12	1	4	38	.48
4	Aggregate Base	.22	1	8	38	1.32
5	Lime/Flyash Treat. Subg.	.12	1	8	38	.96
Total	-	-	-	26.00	-	6.28

Simple ESAL Calculation

Performance Period (years): 30
 Two-Way Daily Traffic (ADT): 4,000
 Percent Heavy Trucks (of ADT) FHWA
 Class 5 or Greater: 13
 Number of Lanes In Design Direction: 2
 Percent of All Trucks In Design Lane (%): 80
 Percent Trucks In Design Direction (%): 55
 Average Initial Truck Factor (ESALs/truck): 2.34
 Annual Truck Factor Growth Rate (%): 0
 Annual Truck Volume Growth Rate (%): 3
 Growth: Simple

Total Calculated Cumulative Esals: 8,418,511

Brent Rauhut Engineering Inc.



(Please Call 512/346-0870 If You Have Any Trouble Receiving This Transmission Or If You Did Not Receive The Number Of Pages Shown Below.)

FAX TRANSMITTAL WITH MESSAGE

TO: MONTE SYMONS, FHWA/LTPP-PPD **FROM:** JERRY DALEIDEN
INFO: JOHN MILLER, PCS/LAW **PROJECT ENGINEER, SRCO**
DATE: 2 JULY 1996
TOTAL NO. OF PAGES: 2

MESSAGE: Subject: Weigh-in-Motion (WIM) Traffic Data Collected for SPS Site near Cache, Oklahoma

Monte -

As noted in the attached letter, the Oklahoma DOT would like to use an existing WIM location for collecting data for the SPS-1 and SPS-5 projects to be built next spring. In discussing this subject with John Miller, we could not identify any significant reason for opposing this request (considering the information provided in Mr. Telford's letter). John did suggested, however, that we check with you before responding to the Oklahoma DOT.


Please feel free to contact me should you have any questions or comments regarding the information provided.

Jerry

Jerry

Attachment: As stated.

JFD:dmj



200 N. E. 21st Street
Oklahoma City, OK 73105-3204

APPENDIX B

PRECONSTRUCTION DISTRESS SURVEYS

RECEIVED JUN 3 0 1997

Revised December 1, 1992

SHEET 1

DISTRESS SURVEY

LTPP PROGRAM

STATE ASSIGNED ID

STATE CODE

SHRP SECTION ID

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR)

SURVEYORS: T J M, M J D PHOTOS, VIDEO, OR BOTH WITH SURVEY (P, V, B) B
PAVEMENT SURFACE TEMP - BEFORE 34°C; AFTER 38°C

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
CRACKING			
1. FATIGUE CRACKING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
2. BLOCK CRACKING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
3. EDGE CRACKING (Meters)	<u>0</u>	<u>0</u>	<u>0</u>
4. LONGITUDINAL CRACKING (Meters)			
4a. Wheel Path Length Sealed (Meters)	<u>0</u>	<u>0</u>	<u>0</u>
4b. Non-Wheel Path Length Sealed (Meters)	<u>14.5</u>	<u>0</u>	<u>0</u>
5. REFLECTION CRACKING AT JOINTS Number of Transverse Cracks	<u>0</u>	<u>0</u>	<u>0</u>
Transverse Cracking (Meters) Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
Longitudinal Cracking (Meters) Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
6. TRANSVERSE CRACKING Number of Cracks	<u>9</u>	<u>0</u>	<u>0</u>
Length (Meters) Length Sealed (Meters)	<u>27.2</u>	<u>0</u>	<u>0</u>

PATCHING AND POTHOLES

7. PATCH/PATCH DETERIORATION (Number) (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
8. Potholes (Number) (Square Meters)	<u>1</u>	<u>1</u>	<u>1</u>

ENLINED OCT 21 1997 J
REVIEWED JUL 21 1997 J D
REVIEWED JUL 17 1997 JP

Revised December 1, 1992

SHEET 2
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _ _ _ _

STATE CODE 40

SHRP SECTION ID 0501

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/16/97

SURVEYORS: I J M, M J D

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
SURFACE DEFORMATION			
9. RUTTING - REFER TO SHEET 3 FOR SPS-3 OR Form S1 from Dipstick Manual			
10. SHOVING (Number) (Square Meters)			<u>0</u> <u>0</u>
SURFACE DEFECTS			
11. BLEEDING (Square Meters)	<u>305.0</u>	<u>0</u>	<u>0</u>
12. POLISHED AGGREGATE (Square Meters)			<u>0</u>
13. RAVELING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
MISCELLANEOUS DISTRESSES			
14. LANE-TO-SHOULDER DROPOFF - REFER TO SHEET 3			
15. WATER BLEEDING AND PUMPING (Number) Length of Affected Pavement (Meters)			<u>0</u> <u>0</u>
16. OTHER (Describe) _____			

Revised May 29, 1992

SHEET 3
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _____
STATE CODE 40
SHRP SECTION ID 0501

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/16/97

SURVEYORS: TJM, M & D

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

ENL 1111 OCT 21 1997 J. B

9. RUTTING (FOR SPS-3 SITE SURVEYS)

INNER WHEEL PATH			OUTER WHEEL PATH		
Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)	Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)
1	0.	— — —	1	0.	— — —
2	15.25	— — —	2	15.25	— — —
3	30.5	— — —	3	30.5	— — —
4	45.75	— — —	4	45.75	— — —
5	61.	— — —	5	61.	— — —
6	76.25	— — —	6	76.25	— — —
7	91.5	— — —	7	91.5	— — —
8	106.75	— — —	8	106.75	— — —
9	122.	— — —	9	122.	— — —
10	137.25	— — —	10	137.25	— — —
11	152.5	— — —	11	152.5	— — —

SEE
DIPSTER
DATA

14. LANE-TO-SHOULDER DROPOFF


Point No.	Point Distance ¹ Meters	Lane-to-Shoulder Dropoff (mm)
1	0.	— — —
2	15.25	— — —
3	30.5	— — —
4	45.75	— — —
5	61.	— — —
6	76.25	— — —
7	91.5	— — —
8	106.75	— — —
9	122.	— — —
10	137.25	— — —
11	152.5	— — —

Note 1: "Point Distance" is the distance in meters from the start of the test section to the point where the measurement was made. The values shown are SI equivalents of the 50 ft spacing used in previous surveys.


State Assigned ID _____

State Code 40

SIIRP Section ID 0501

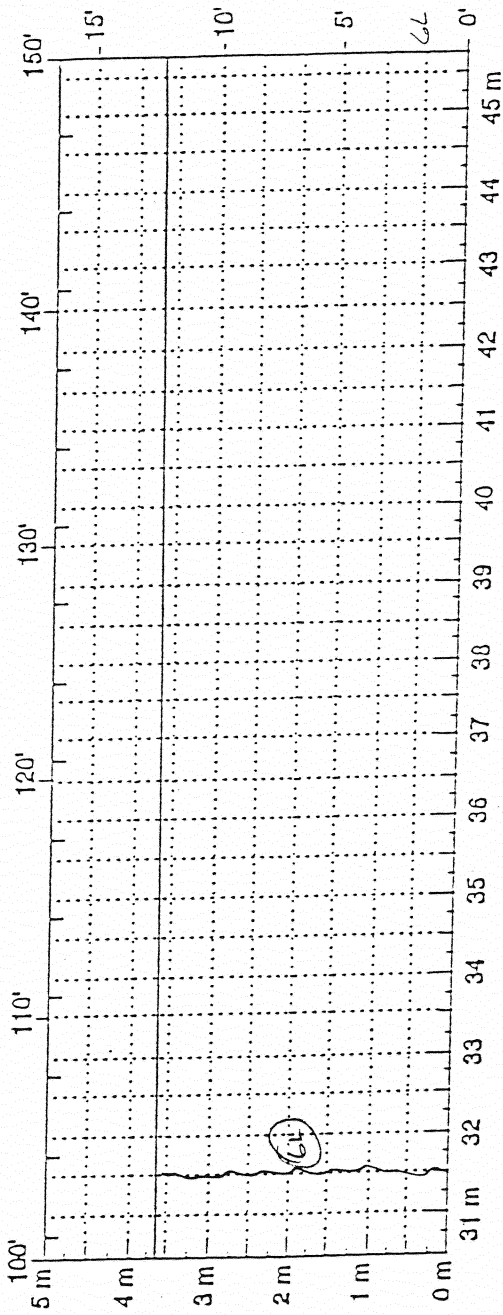


Comments: _____

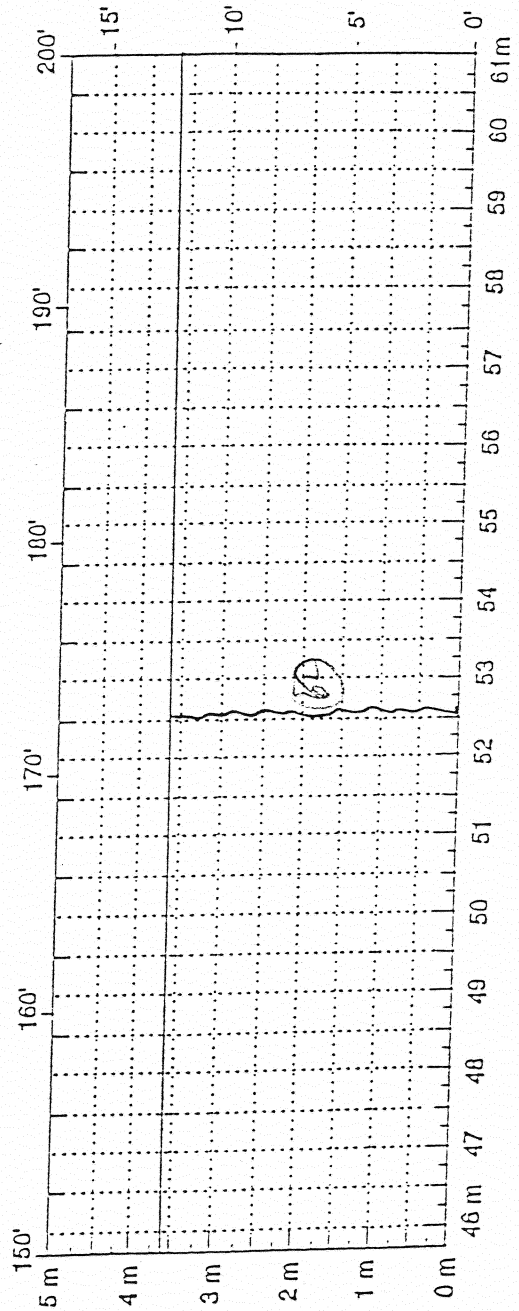


Comments: _____

State Assigned ID _____
 State Code 40
 SRRP Section ID 0501

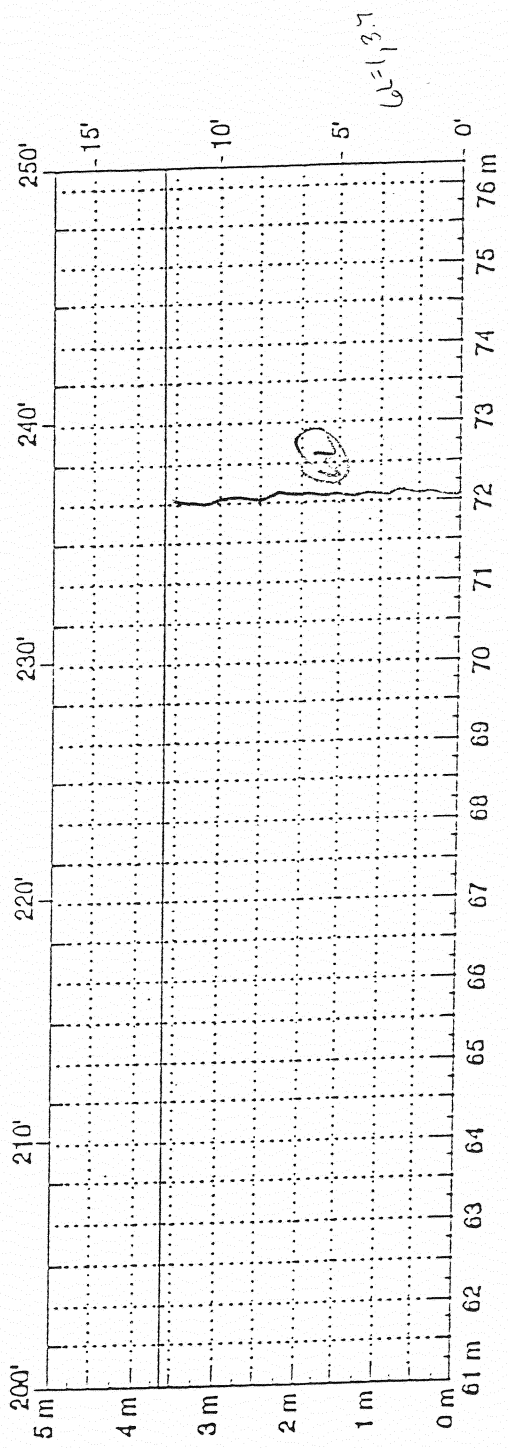

Comments: _____

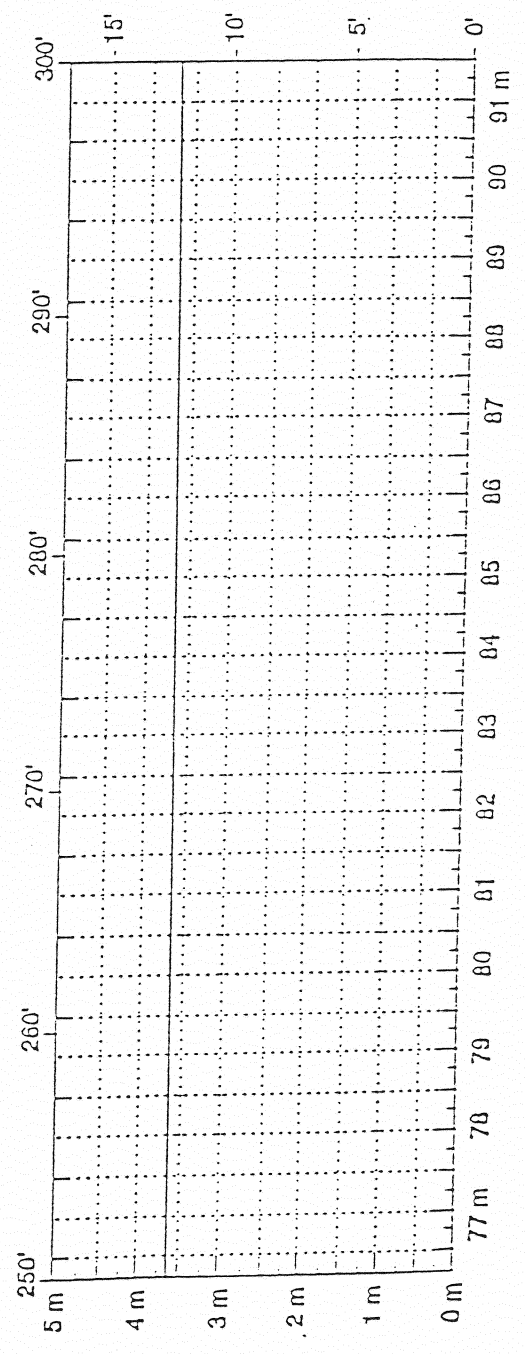


Comments: _____

State Assigned ID


40

State Code

SHRP Section ID 0501

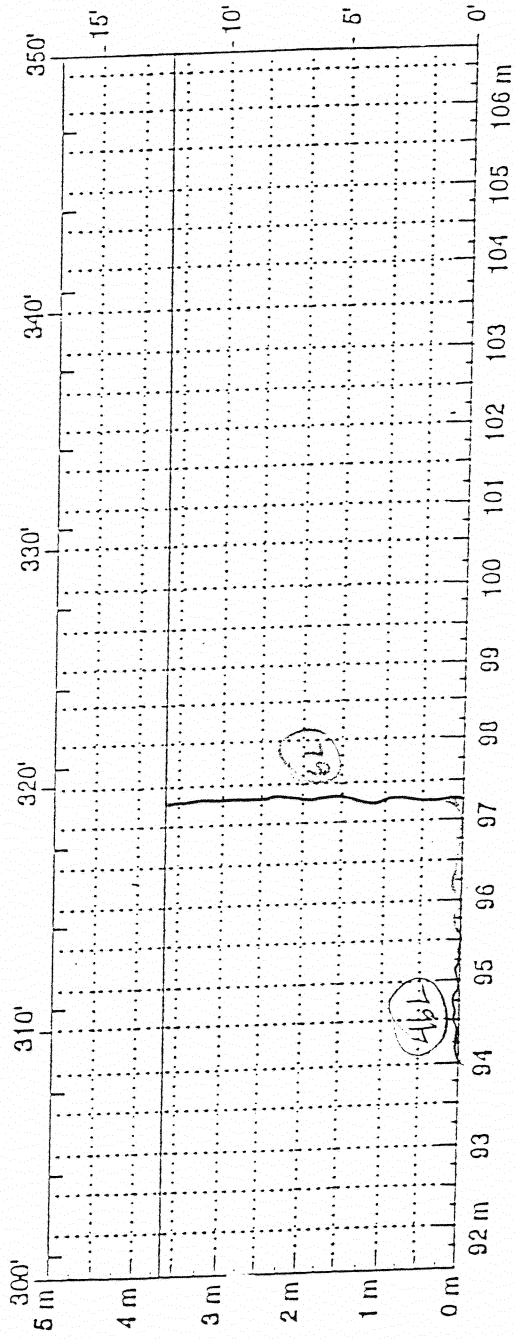

Comments:

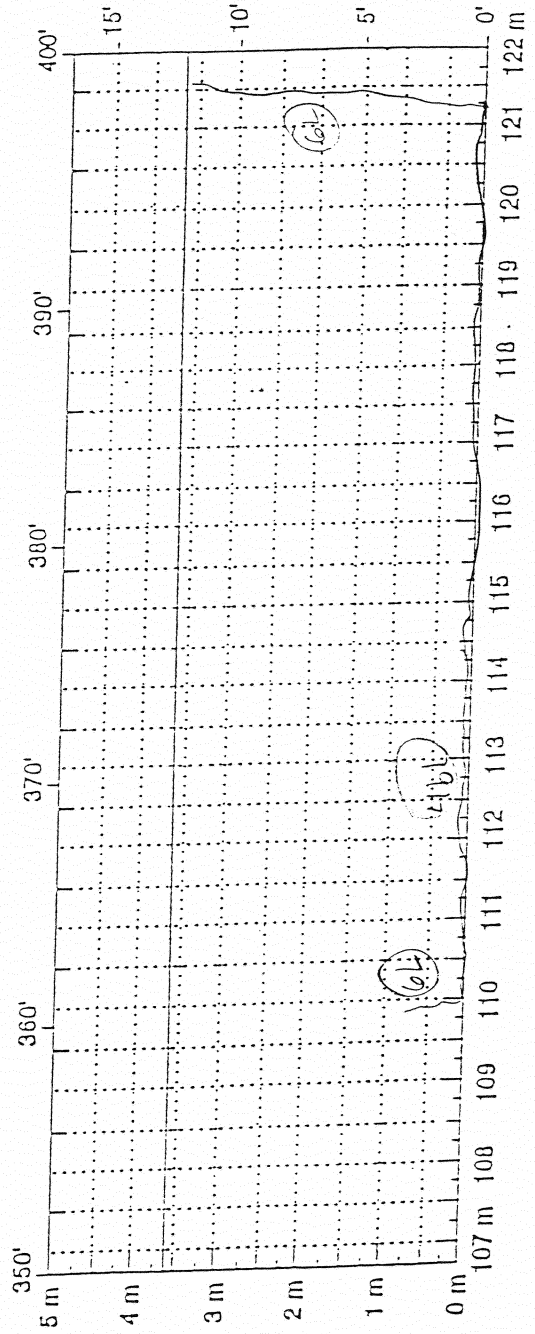

Comments:


State Assigned ID

40


State Code

0501

SNIP Section ID

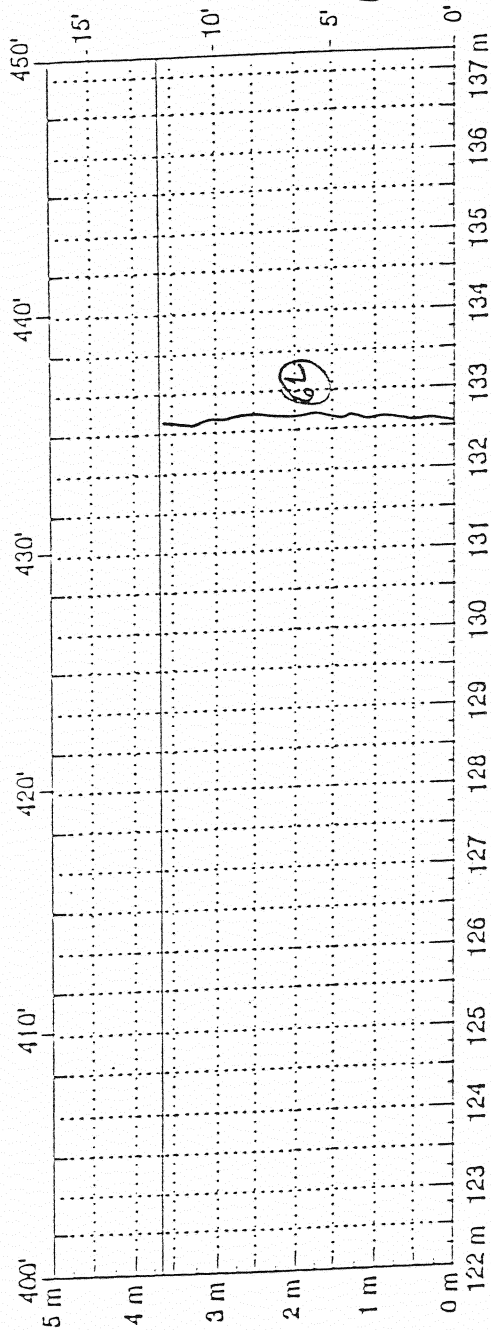

Comments:

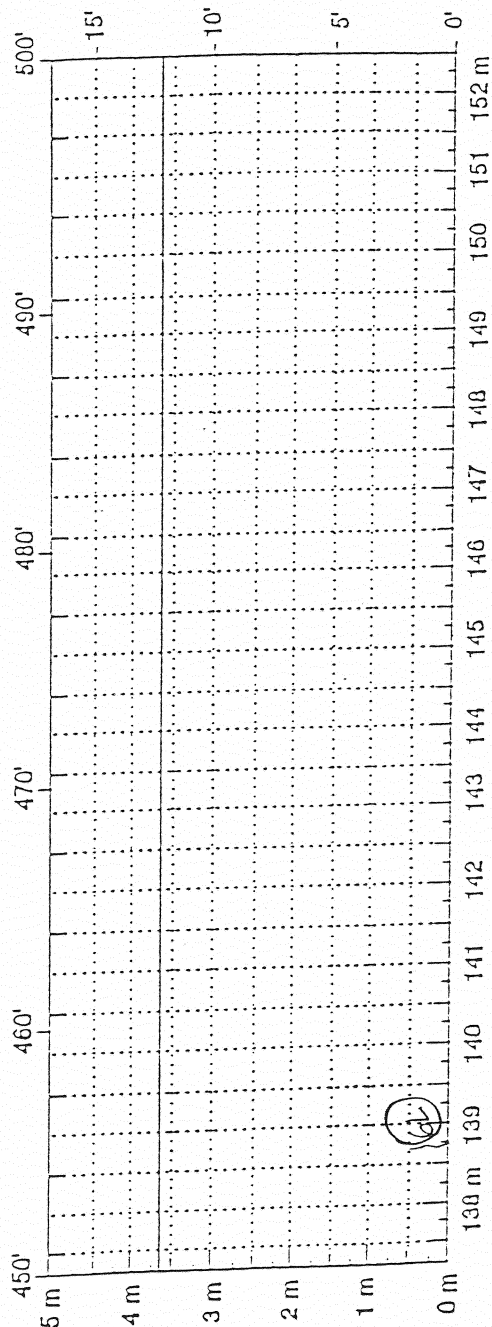

Comments:

LTPP Automated Dipstick Data Collection	State Code	[4 0]
Transverse Profile Form DS-11	LTPP Section ID	[0 5 0 1]
Zero and Calibration Checks	Date (dd/mm/yy)	[0 6 / 1 6 / 1 9 7]

Operator: Tim Martin

Employer: BRE

Dipstick Serial Number: 30023

Pre Measurement Checks

Time (military): 1 0 : 3 0

Automatic Zero Performed:

Calibration

Calibration Check	
Measurement	Reading (inches)
First Reading	.443
Second Reading on Calibration Block	.568
Second Reading - 0.125 - First Reading	.443

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Post Measurement Checks

Time (military): 1 1 : 1 0

Zero Check Acceptable: ✓

Calibration Check	
Measurement	Reading (inches)
First Reading	.442
Second Reading on Calibration Block	.569
Second Reading - 0.125 - First Reading	.443

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Comments

ENTRUSTED/661211-01997A-1114

OPERATOR: Tom Adams

RECORDED: Math Drake

DIPSTICK SERIAL NUMBER: 30023

ENTERED JUL 10 1997 A H

STATE CODE:

SIIRP SECTION I.D.: 0501

DIPSTICK READING														
LOCATION	1	2	3	4	5	6	7	8	9	10	11	12	TOTAL	SUM
0+00	-043	-104	106	255	131	047	-099	016	137	353	230	186		
0+50	44 ²¹	108 ⁵³	99 ²⁴	-250 ²²	131 ⁷	-42 ¹⁷	104 ¹²	-010 ⁷	-137 ¹	-353 ¹	-227 ¹	-188 ⁻²	.034	
(15m)	-043	-112	103	300	161	008	-114	026	180	319	228	209		
1+00	044 ⁷	106 ⁶	-113 ¹²	-292 ²²	-150 ¹¹	-000 ³	115 ⁻⁵	-033 ⁻⁶	-184 ¹	-308 ⁵	-233 ⁻⁴	-208 ¹	.007	
(30m)	044	-086	147	408	282	126	062	-013	155	445	290	182		
1+50	-044	089 ¹¹	-144 ⁴	-405 ¹	-285 ⁻²	-127 ¹	-064 ²	015 ⁴	-150 ²	-446 ⁻³	-291 ⁻²	-193 ⁻¹	.007	
(45m)	057	045	158	370	281	167	040	012	234	382	331	290		
(60m)	-57 ¹⁵	-044 ¹⁵	-148 ¹¹	-372 ⁴	-281 ⁶	-164 ⁶	-037 ³	-010 ⁰	-233 ⁻²	-302 ⁻³	-335 ⁻³	-289 ¹	.015	
(2+00)	-043	-50	095	311	313	189	025	-018	194	353	327	207		
(60m)	042 ¹⁰	+53 ¹⁷	-095 ¹¹	-310 ¹¹	-311 ¹⁵	-188 ¹¹	1023 ¹⁰	018 ⁸	-191 ⁸	-349 ⁵	-326 ¹	-207 ⁰	.016	
2+50	-011	-083	100	360	282	188	-071	-016	200	423	341	194		
(75m)	013	083 ⁶	-101 ⁶	-360 ⁷	-277 ⁷	-190 ²	075 ¹¹	017 ⁰	-197 ⁻¹	-422 ⁻⁴	-345 ⁻⁵	-195 ⁻¹	.800	
3+00	-009	-053	146	424	310	116	-102	-020	216	475	317	294		
(90m)	009 ¹¹	054 ¹¹	-144 ³	-423 ¹	-312 ⁰	-118 ²	106 ⁴	022 ⁰	-215 ⁻²	-475 ⁻³	-321 ⁻³	-293 ¹	.004	
3+50	102	-022	187	390	262	173	-041	.001	.187	432	365	260		
(105m)	-101 ⁷	022 ⁶	-186 ⁶	-386 ⁵	-264 ¹	-171 ³	042 ¹	-002 ⁰	-182 ¹	-443 ⁻¹	-365 ⁻³	-261 ⁻⁴	.007	
4+00	115	-079	217	522	337	074	-202	042	340	544	354	289		
(120m)	-119 ²⁶	085 ³⁰	-211 ²⁴	-521 ²¹	-335 ¹⁰	-066 ¹³	260 ¹⁰	-033 ¹²	-336 ³	-540 ⁻¹	-350 ⁻⁵	-290 ⁻¹	.026	
4+50	235	-016	191	415	280	208	-025	007	178	424	296	194		
(135m)	-235 ¹⁶	017 ¹⁶	-190 ¹⁵	-412 ¹⁴	-288 ¹¹	-200 ¹³	032 ¹¹	-008 ⁴	-177 ⁵	-419 ⁴	-294 ⁻¹	-197 ⁻³	.016	
5+00	167	001	212	361	312	136	037	054	196	375	293	212		
(150m)	-172 ¹¹	004 ¹¹	-212 ⁴	-365 ¹¹	-303 ⁸	-138 ⁻¹	-034 ¹	-054 ⁷	-196 ⁻²	-376 ⁻²	-292 ⁻¹	-214 ⁻²	.004	
COMMENTS														

COMMENTS

RECEIVED JUN 30 1997 STATE ASSIGNED ID _____

SHEET 1

DISTRESS SURVEY

STATE CODE 40

LTPP PROGRAM

SHRP SECTION ID 0502

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/16/97

SURVEYORS: T J M, M J D PHOTOS, VIDEO, OR BOTH WITH SURVEY (P, V, B)
PAVEMENT SURFACE TEMP - BEFORE 49°C; AFTER 53°C

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
CRACKING			
1. FATIGUE CRACKING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
2. BLOCK CRACKING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
3. EDGE CRACKING (Meters)	<u>0</u>	<u>0</u>	<u>0</u>
4. LONGITUDINAL CRACKING (Meters)			
4a. Wheel Path Length Sealed (Meters)	<u>0</u>	<u>0</u>	<u>0</u>
4b. Non-Wheel Path Length Sealed (Meters)	<u>0</u>	<u>0</u>	<u>0</u>
5. REFLECTION CRACKING AT JOINTS Number of Transverse Cracks	<u>0</u>	<u>0</u>	<u>0</u>
Transverse Cracking (Meters)	<u>0</u>	<u>0</u>	<u>0</u>
Length Sealed (Meters)	<u>0</u>	<u>0</u>	<u>0</u>
Longitudinal Cracking (Meters)	<u>0</u>	<u>0</u>	<u>0</u>
Length Sealed (Meters)	<u>0</u>	<u>0</u>	<u>0</u>
6. TRANSVERSE CRACKING Number of Cracks	<u>4</u>	<u>3</u>	<u>0</u>
Length (Meters)	<u>11.9</u>	<u>11.1</u>	<u>0</u>
Length Sealed (Meters)	<u>0</u>	<u>0</u>	<u>0</u>

PATCHING AND POTHOLES

7. PATCH/PATCH DETERIORATION (Number)	<u>0</u>	<u>0</u>	<u>0</u>
(Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
8. Potholes (Number)	<u>0</u>	<u>0</u>	<u>0</u>
(Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>

REVIEWED JUL 17 1997 J B
REVIEWED JUL 17 1997 J B

SHEET 2
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _ _ _ _

STATE CODE 40SHRP SECTION ID 0502DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/16/97SURVEYORS: TJM, MJD

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH

SURFACE DEFORMATION

9. RUTTING - REFER TO SHEET 3 FOR SPS-3 OR Form S1 from Dipstick Manual

10. SHOVING
(Number) 0
(Square Meters) 0

SURFACE DEFECTS

11. BLEEDING
(Square Meters) 305.0 0 0

12. POLISHED AGGREGATE
(Square Meters) 0

13. RAVELING
(Square Meters) 0 0 0

MISCELLANEOUS DISTRESSES

14. LANE-TO-SHOULDER DROPOFF - REFER TO SHEET 3

15. WATER BLEEDING AND PUMPING
(Number) 0
Length of Affected Pavement
(Meters) 0

16. OTHER (Describe) _____

Revised May 29, 1992

SHEET 3
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _____

STATE CODE 40

SHRP SECTION ID 0502

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/16/97

SURVEYORS: TJM, MJD

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

ENTERED OCT 21 1997 J. B

9. RUTTING (FOR SPS-3 SITE SURVEYS)

INNER WHEEL PATH			OUTER WHEEL PATH		
Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)	Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)
1	0.	— — —	1	0.	— — —
2	15.25	— — —	2	15.25	— — —
3	30.5	— — —	3	30.5	— — —
4	45.75	— — —	4	45.75	— — —
5	61.	— — —	5	61.	— — —
6	76.25	— — —	6	76.25	— — —
7	91.5	— — —	7	91.5	— — —
8	106.75	— — —	8	106.75	— — —
9	122.	— — —	9	122.	— — —
10	137.25	— — —	10	137.25	— — —
11	152.5	— — —	11	152.5	— — —

SEE
Distress
Data


14. LANE-TO-SHOULDER DROPOFF

Point No.	Point Distance ¹ Meters	Lane-to-Shoulder Dropoff (mm)
1	0.	— — —
2	15.25	— — —
3	30.5	— — —
4	45.75	— — —
5	61.	— — —
6	76.25	— — —
7	91.5	— — —
8	106.75	— — —
9	122.	— — —
10	137.25	— — —
11	152.5	— — —


Note 1: "Point Distance" is the distance in meters from the start of the test section to the point where the measurement was made. The values shown are SI equivalents of the 50 ft spacing used in previous surveys.

State Assigned ID _____
 State Code 40
 SHRP Section ID 0502

date: 6/16/97
 Surveyors: STM - MJD

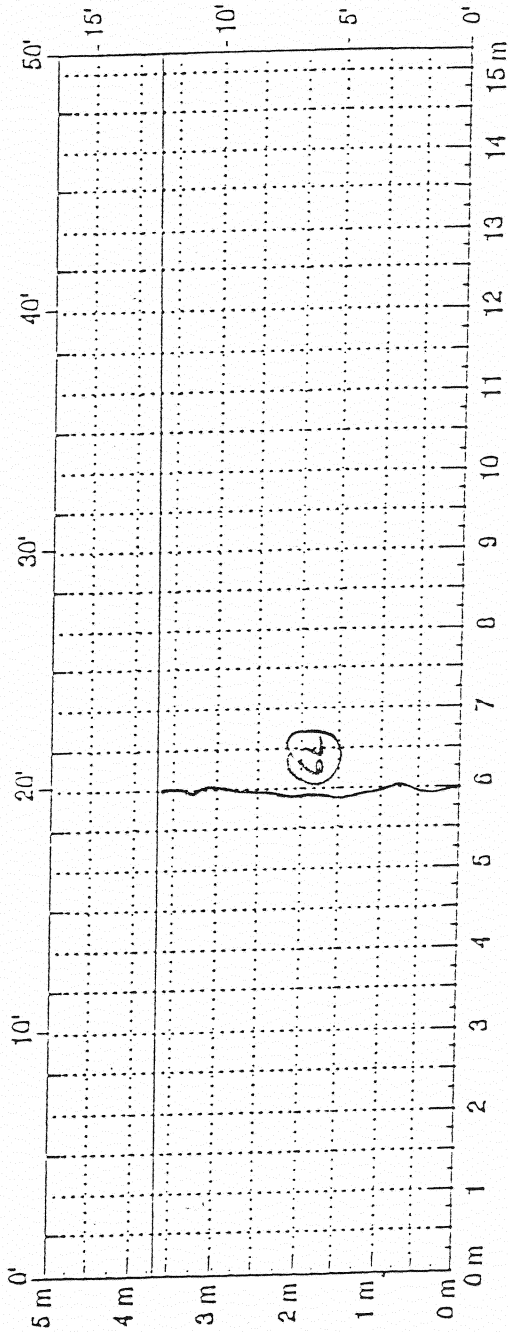

Comments: _____

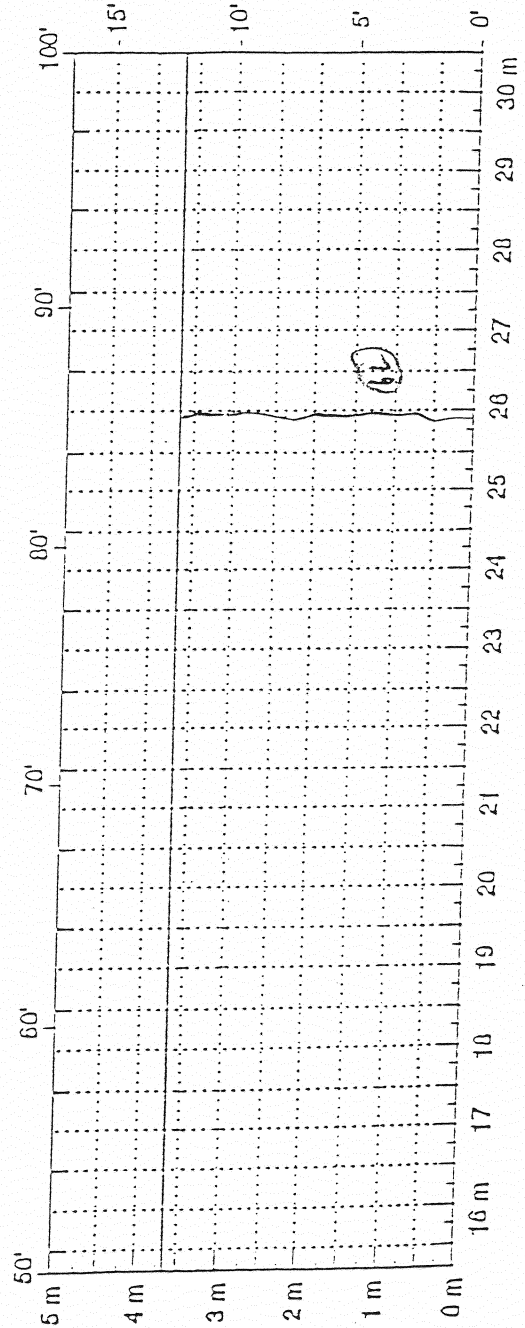


Comments: _____


State Assigned ID _____

State Code 40

SLIRP Section ID 0502

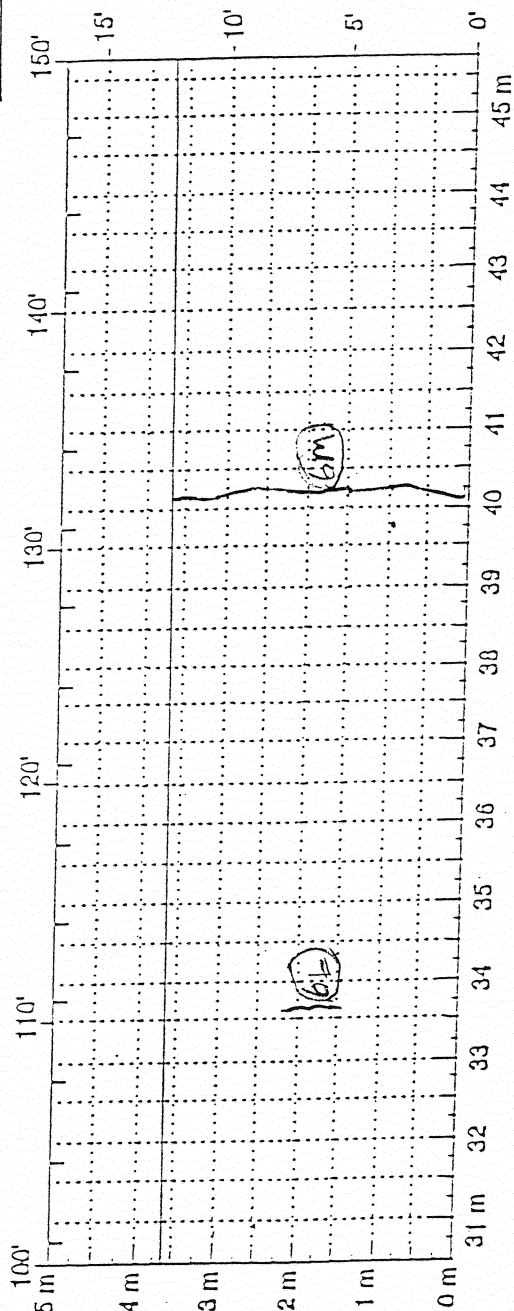

Comments: _____

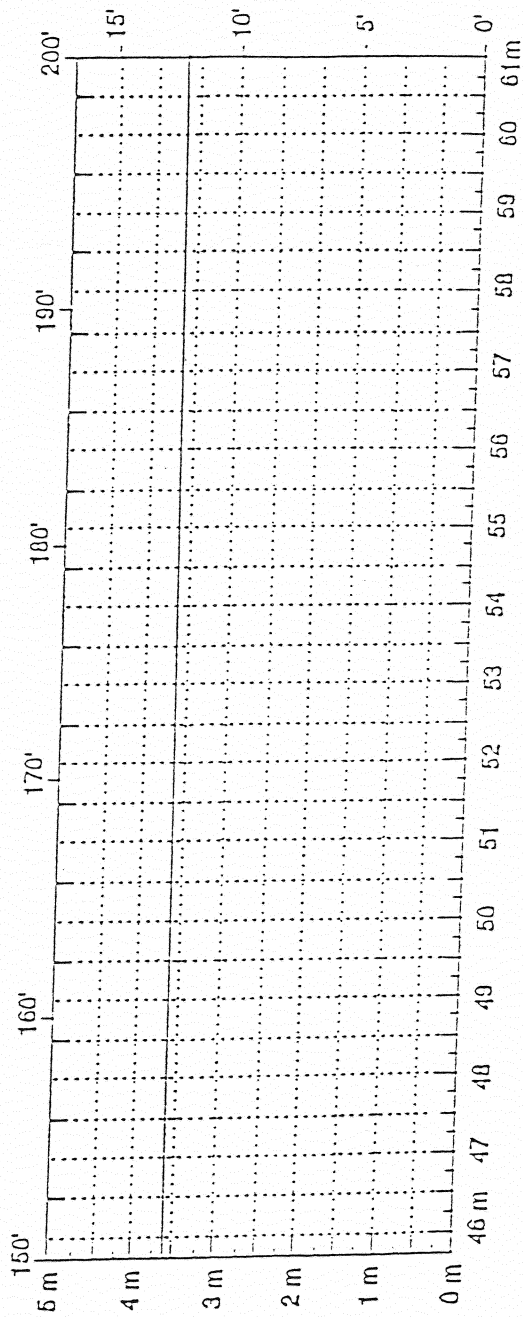


Comments: _____


State Assigned ID _____

State Code 40

SNIP Section ID 0502


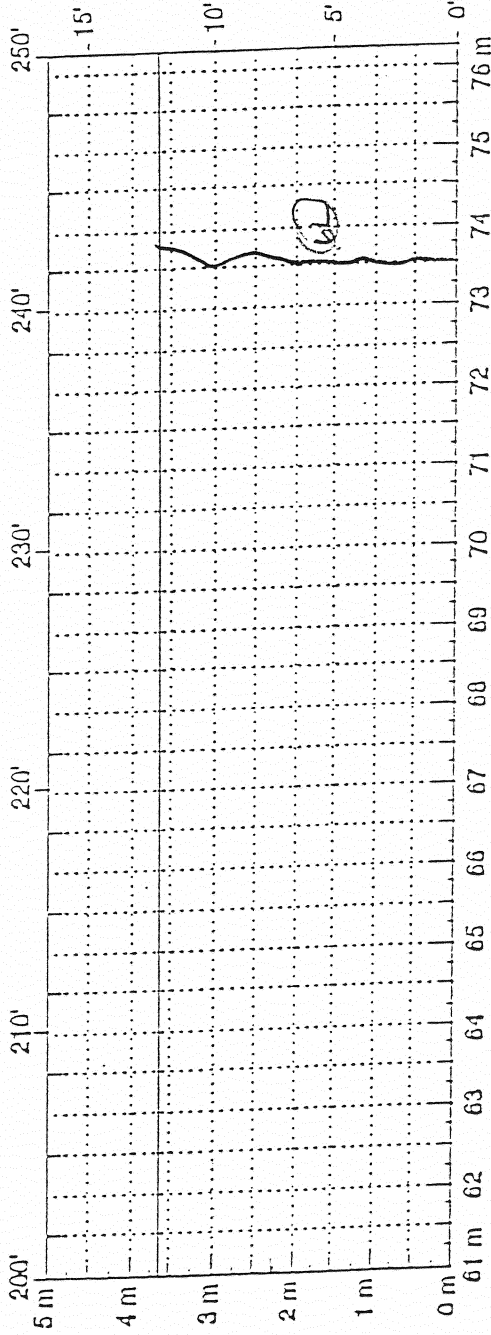


Comments: _____

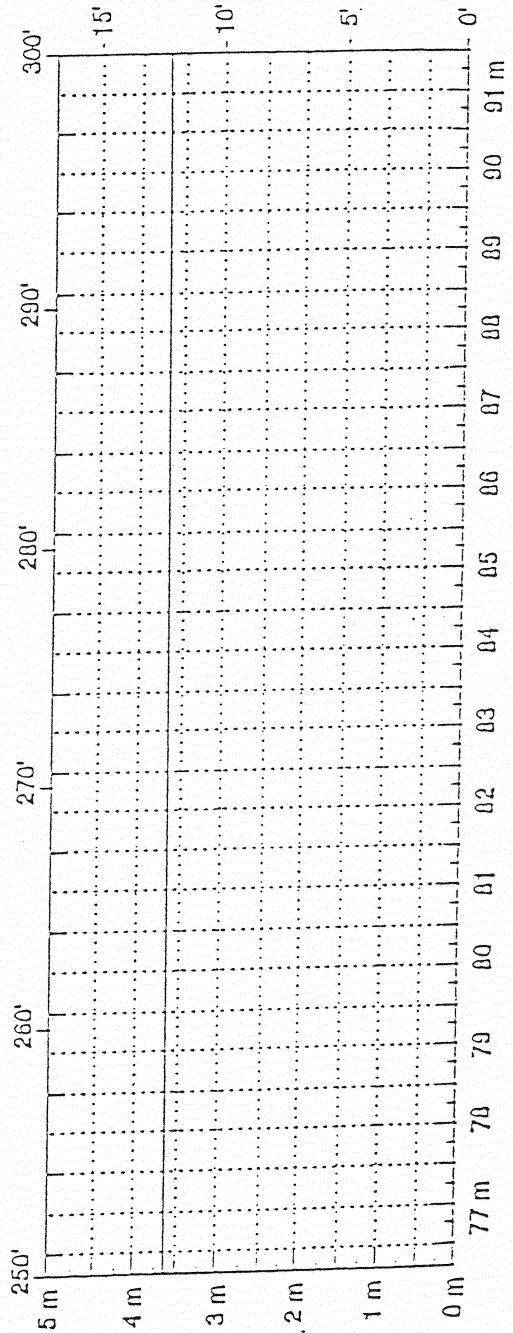


Comments: _____


State Assigned ID 40
 State Code 0502
 SIIRP Section ID 0502

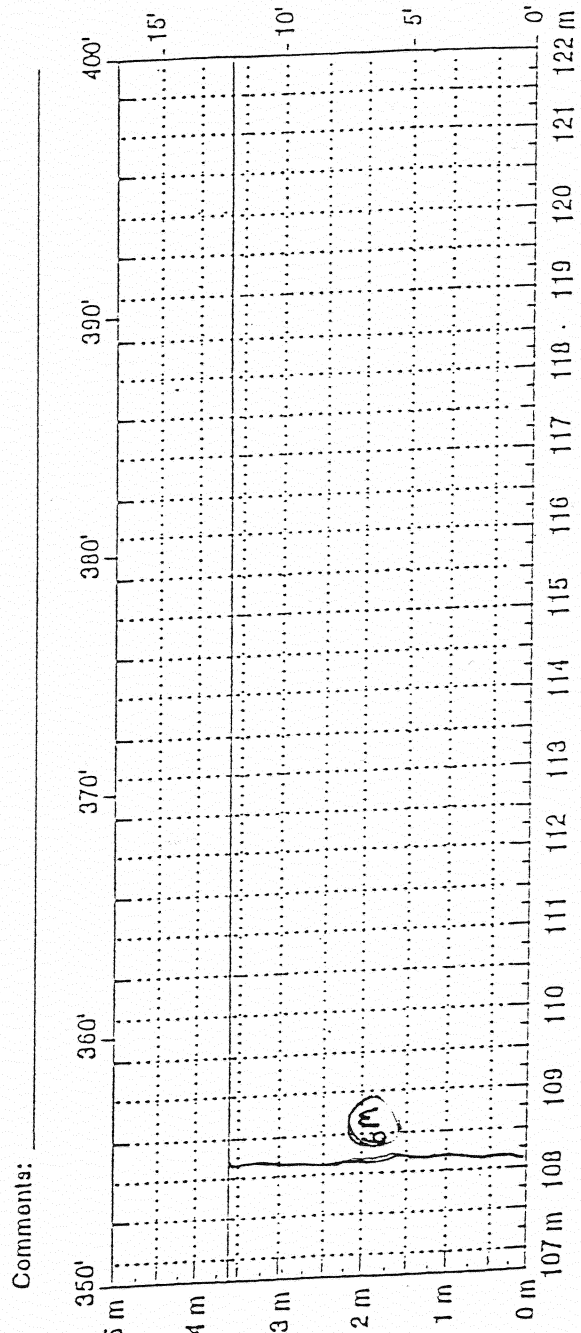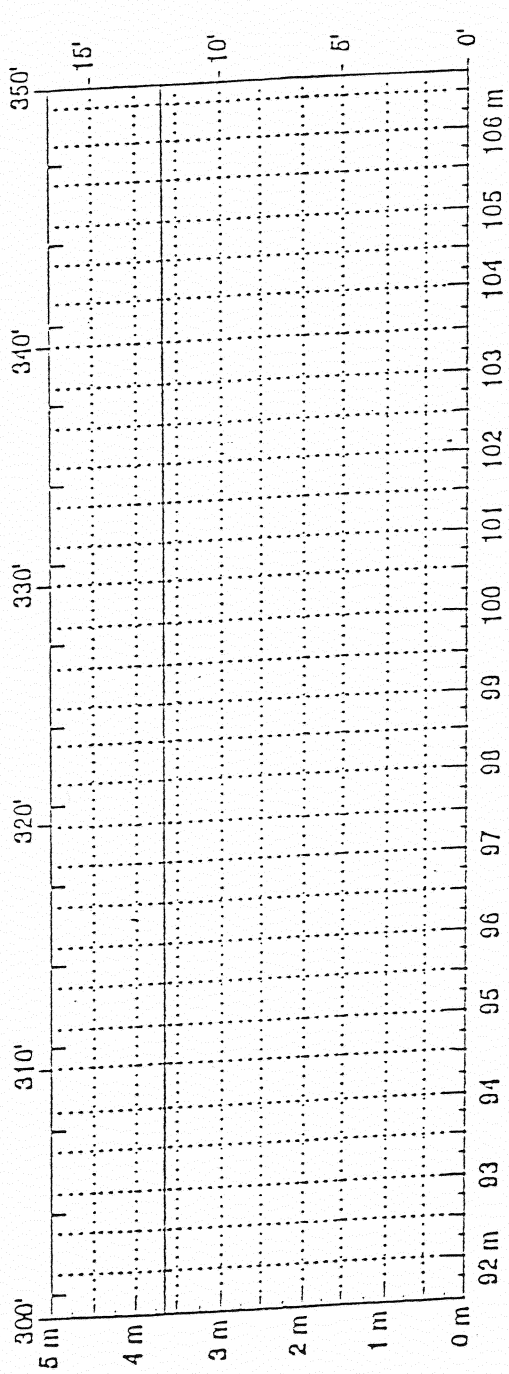

State Assigned ID 40
 State Code 0502
 SLIRP Section ID 0502

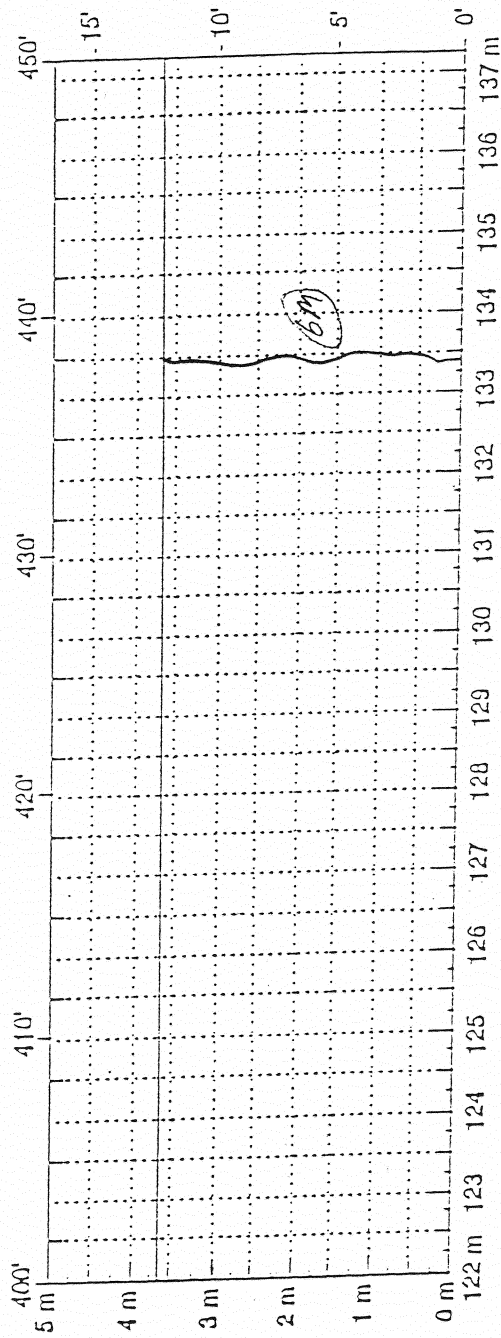

Comments: _____

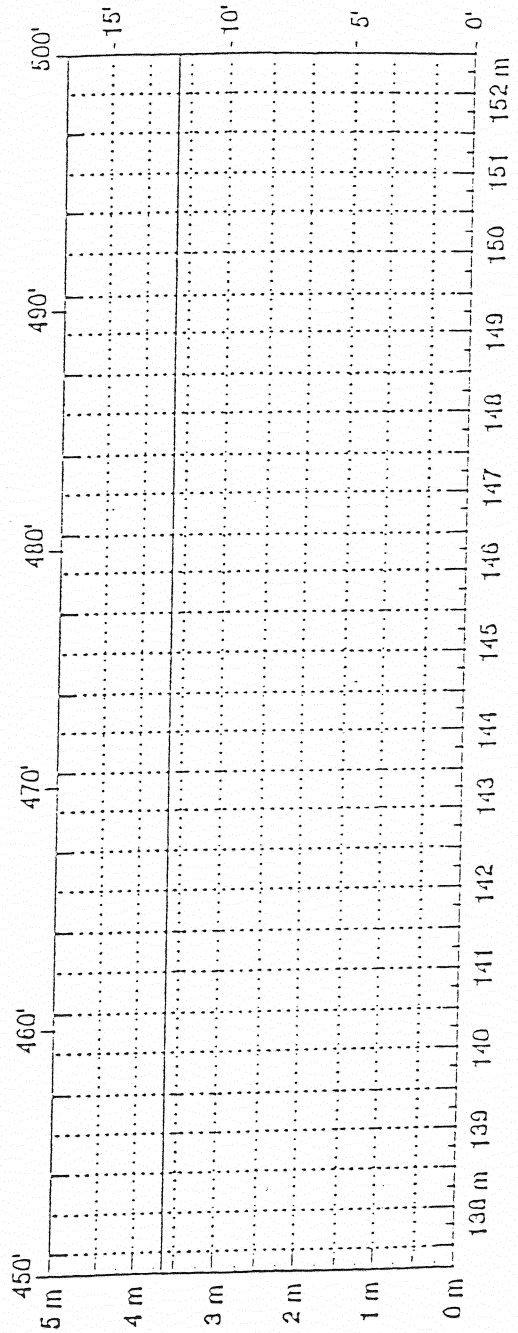

Comments: _____

LTPP Automated Dipstick Data Collection	State Code
Transverse Profile Form DS-11	LTPP Section ID
Zero and Calibration Checks	Date (dd/mm/yy)

Operator: Mark Duke Employer: BRE

Dipstick Serial Number: 30023

Pre Measurement Checks

Time (military): 14:10

Automatic Zero Performed:

Calibration

Calibration Check	
Measurement	Reading (inches)
First Reading	.192
Second Reading on Calibration Block	.318
Second Reading - 0.125 - First Reading	.126

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Post Measurement Checks

Time (military): 14:50

Zero Check Acceptable: ✓

Calibration Check	
Measurement	Reading (inches)
First Reading	.193
Second Reading on Calibration Block	.318
Second Reading - 0.125 - First Reading	.125

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Comments

DATE: 6/16/97

OPERATOR: Matt Cate

RECORDER: Tim Martin

DIPSTICK SERIAL NUMBER: 20023

EM VUL6800 Y 24897A NF

RECEIVED JUL 10 1997 A II

STATE CODE: 40

SURF SECTION I.D.: 0502

LOCATION	DIPSTICK READING												TOTAL	SUM
	1	2	3	4	5	6	7	8	9	10	11	12		
0+00	.085 ²⁴ -.084 ²⁴	-.032 ²³ +.033 ²³	.159 ¹² -.157 ¹²	.253 ²⁰ -.254 ²⁰	.178 ²⁶ -.169 ²⁶	.023 ¹⁷ +.017 ¹⁷	-.017 ¹⁰ +.018 ¹⁰	.030 ¹⁰ -.032 ¹⁰	.142 ¹² -.141 ¹²	.317 ¹¹ -.310 ¹¹	.272 ⁴ -.267 ⁴	.193 ¹ -.194 ¹		
0+50 (15m)	.1078 ⁶⁴ -.076 ⁶⁴	.049 ⁶² +.042 ⁶²	.125 ⁵⁵ -.120 ⁵⁵	.238 ⁵⁰ -.233 ⁵⁰	.224 ⁴⁵ -.223 ⁴⁵	.136 ³⁴ -.135 ³⁴	.048 ³² -.035 ³²	.031 ²⁵ -.020 ²⁵	.151 ¹⁴ -.156 ¹⁴	.331 ¹⁹ -.314 ¹⁹	.339 ² -.350 ²	.375 ¹³ -.362 ¹³	.064	.024
1+00 (30m)	.125 ⁴⁴ -.115 ⁴⁴	.026 ³⁴ -.035 ³⁴	.158 ⁴³ -.166 ⁴³	.312 ⁵¹ -.308 ⁵¹	.326 ⁴⁷ -.323 ⁴⁷	.129 ⁴⁴ -.130 ⁴⁴	.063 ¹¹⁵ -.048 ¹¹⁵	.049 ³⁰ -.050 ³⁰	.121 ³¹ -.120 ³¹	.223 ³⁰ -.230 ³⁰	.353 ³⁷ -.342 ³⁷	.360 ²⁶ -.334 ²⁶	.044	
1+50 (45m)	.293 ⁵² -.302 ⁵²	.052 ⁶¹ -.049 ⁶¹	.183 ⁵⁹ -.182 ⁵⁹	.311 ⁵⁷ -.316 ⁵⁷	.242 ⁶² -.228 ⁶²	.141 ⁴⁸ -.127 ⁴⁸	.073 ³⁴ -.066 ³⁴	.009 ²² +.010 ²²	.189 ³¹ -.190 ³¹	.331 ³² -.310 ³²	.335 ¹¹ -.335 ¹¹	.332 ¹¹ -.321 ¹¹	.052	
2+00 (60m)	.102 ²⁹ -.97 ²⁹	.085 ³⁴ -.085 ³⁴	.205 ³⁴ -.195 ³⁴	.279 ¹⁴⁴ -.278 ¹⁴⁴	.262 ¹⁴⁵ -.271 ¹⁴⁵	.150 ³⁶ -.155 ³⁶	.037 ³¹ -.043 ³¹	.022 ²³ -.027 ²³	.154 ²⁰ -.156 ²⁰	.238 ¹⁸ -.242 ¹⁸	.263 ¹⁴ -.274 ¹⁴	.295 ³ -.298 ³	.029	
2+50 (75m)	.051 ⁴² -.051 ⁴²	.068 ⁴² +.059 ⁴²	.172 ³⁵ -.176 ³⁵	.264 ³⁷ -.251 ³⁷	.253 ²⁴ -.255 ²⁴	.126 ²⁶ -.125 ²⁶	.131 ²⁵ -.134 ²⁵	.116 ²⁸ -.109 ²⁸	.222 ²¹ -.224 ²¹	.302 ²³ -.288 ²³	.346 ⁷ -.338 ⁷	.219 ¹ -.218 ¹	.042	
3+00 (90m)	.144 ¹⁷ -.140 ¹⁷	.055 ²¹ -.052 ²¹	.210 ²⁴ -.210 ²⁴	.265 ²⁴ -.263 ²⁴	.179 ²⁶ -.186 ²⁶	.074 ¹⁹ -.081 ¹⁹	.002 ¹² -.010 ¹²	.056 ⁴ -.058 ⁴	.199 ² -.201 ²	.268 ⁰ -.261 ⁰	.264 ⁷ -.268 ⁷	.216 ³ -.219 ³	.017	
3+50 (105m)	.187 ³⁵ -.183 ³⁵	.067 ³¹ -.072 ³¹	.259 ³⁶ -.248 ³⁶	.310 ³⁵ -.327 ³⁵	.237 ¹² -.232 ¹²	.087 ³⁷ -.081 ³⁷	-.021 ³¹ +.029 ³¹	.084 ²³ -.081 ²³	.238 ²⁰ -.231 ²⁰	.306 ¹³ -.302 ¹³	.243 ⁹ -.236 ⁹	.188 ² -.186 ²	.035	
4+00 (120m)	.087 ⁶⁴ -.091 ⁶⁴	.118 ⁶³ -.112 ⁶³	.208 ⁶² -.197 ⁶²	.265 ⁵¹ -.266 ⁵¹	.146 ⁵² -.143 ⁵²	.021 ¹⁰⁴ -.014 ¹⁰⁴	-.016 ⁴² +.025 ⁴²	.067 ³³ -.057 ³³	.190 ²³ -.185 ²³	.255 ¹⁸ -.251 ¹⁸	.220 ¹⁴ -.210 ¹⁴	.230 ⁴ -.226 ⁴	.064	
4+50 (135m)	.075 ⁵⁵ -.066 ⁵⁵	.101 ²⁶ -.114 ²⁶	.230 ³⁹ -.227 ³⁹	.292 ³⁶ -.292 ³⁶	.222 ³⁶ -.201 ³⁶	-.001 ¹⁵ -.004 ¹⁵	-.033 ²⁰ +.036 ²⁰	.071 ¹⁷ -.072 ¹⁷	.244 ¹⁸ -.243 ¹⁸	.296 ¹⁷ -.281 ¹⁷	.240 ² -.247 ²	.186 ⁹ -.177 ⁹	.035	
5+00 (150m)	.034 ⁸⁶ -.029 ⁸⁶	.047 ²¹ +.049 ²¹	.183 ²³ -.172 ²³	.241 ¹² -.250 ¹²	.170 ²¹ -.162 ²¹	.066 ¹³ -.073 ¹³	-.023 ²⁰ +.041 ²⁰	.067 ² -.082 ²	.169 ¹⁷ -.167 ¹⁷	.240 ¹⁵ -.237 ¹⁵	.191 ¹² -.193 ¹²	.096 ¹¹ -.082 ¹¹	.026	

COMMENTS

RECEIVED JUN 30 1997

SHEET 1

DISTRESS SURVEY

LTPP PROGRAM

STATE ASSIGNED ID

STATE CODE

SHRP SECTION ID

ENTERED OCT 21 1997 J. B

REVIEWED JUL 1 1997 J. B
REVIEWED JUL 17 1997 JP

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR)

06/16/97

SURVEYORS: T J M, N J D PHOTOS, VIDEO, OR BOTH WITH SURVEY (P, V, B) B
PAVEMENT SURFACE TEMP - BEFORE 5 °C; AFTER 5 °C

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
CRACKING			
1. FATIGUE CRACKING (Square Meters)	0	0	0
2. BLOCK CRACKING (Square Meters)	0	0	0
3. EDGE CRACKING (Meters)	0	0	0
4. LONGITUDINAL CRACKING (Meters)			
4a. Wheel Path Length Sealed (Meters)	0	0	0
4b. Non-Wheel Path Length Sealed (Meters)			
5. REFLECTION CRACKING AT JOINTS Number of Transverse Cracks			
Transverse Cracking (Meters)			
Length Sealed (Meters)			
Longitudinal Cracking (Meters)			
Length Sealed (Meters)			
6. TRANSVERSE CRACKING Number of Cracks	0	3	2
Length (Meters)	5	11.1	7.4
Length Sealed (Meters)		0	0
PATCHING AND POTHoles			
7. PATCH/PATCH DETERIORATION (Number)		0	0
(Square Meters)			
8. Potholes (Number)			
(Square Meters)			

Revised December 1, 1992

SHEET 2
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _ _ _ _

STATE CODE 40

SHRP SECTION ID 0503

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/18/97

SURVEYORS: T J M, M J D

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
SURFACE DEFORMATION			
9. RUTTING - REFER TO SHEET 3 FOR SPS-3 OR Form S1 from Dipstick Manual			
10. SHOVING (Number) (Square Meters)			<u>0</u> <u>0</u>
SURFACE DEFECTS			
11. BLEEDING (Square Meters)	<u>205.0</u>	<u>0</u>	<u>0</u>
12. POLISHED AGGREGATE (Square Meters)			<u>0</u>
13. RAVELING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
MISCELLANEOUS DISTRESSES			
14. LANE-TO-SHOULDER DROPOFF - REFER TO SHEET 3			
15. WATER BLEEDING AND PUMPING (Number) Length of Affected Pavement (Meters)			<u>0</u> <u>0</u>
16. OTHER (Describe)			

Revised May 29, 1992

SHEET 3
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _____
STATE CODE 40
SHRP SECTION ID 0503

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/18/97

SURVEYORS: T J M, M J D

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

ENTERED OCT 21 1997 J. B

9. RUTTING (FOR SPS-3 SITE SURVEYS)

INNER WHEEL PATH			OUTER WHEEL PATH		
Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)	Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)
1	0.	— — —	1	0.	— — —
2	15.25	— — —	2	15.25	— — —
3	30.5	— — —	3	30.5	— — —
4	45.75	— — —	4	45.75	— — —
5	61.	— — —	5	61.	— — —
6	76.25	— — —	6	76.25	— — —
7	91.5	— — —	7	91.5	— — —
8	106.75	— — —	8	106.75	— — —
9	122.	— — —	9	122.	— — —
10	137.25	— — —	10	137.25	— — —
11	152.5	— — —	11	152.5	— — —


SEE
DIPSTICK
DATA

14. LANE-TO-SHOULDER DROPOFF

Point No.	Point Distance ¹ Meters	Lane-to-Shoulder Dropoff (mm)
1	0.	— — —
2	15.25	— — —
3	30.5	— — —
4	45.75	— — —
5	61.	— — —
6	76.25	— — —
7	91.5	— — —
8	106.75	— — —
9	122.	— — —
10	137.25	— — —
11	152.5	— — —

Note 1: "Point Distance" is the distance in meters from the start of the test section to the point where the measurement was made. The values shown are SI equivalents of the 50 ft spacing used in previous surveys.

State Assigned ID _____
 date: 6/16/97
 State Code 40
 Surveyors: TIM, MID
 SIPP Section ID 0503

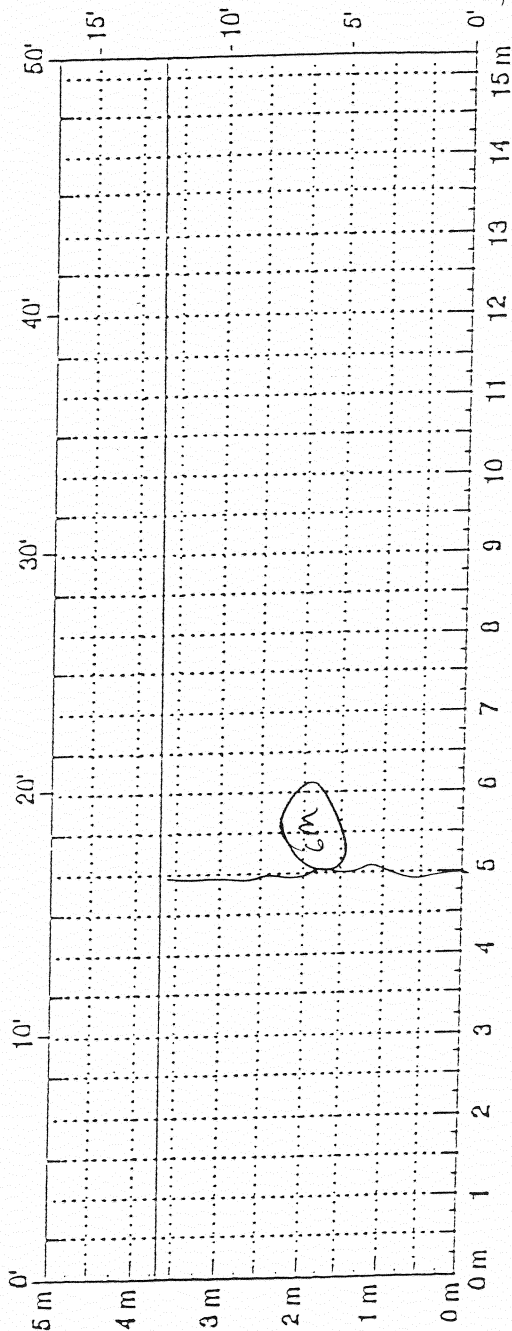


$U_{WN} = 1/3.7$

Totals:

Comments: Bleeding in the wheel-paths through section 11L

$CM = 11.1/4m$
 $CH = 2.7/4m$
 $HL = 20.5 sm$

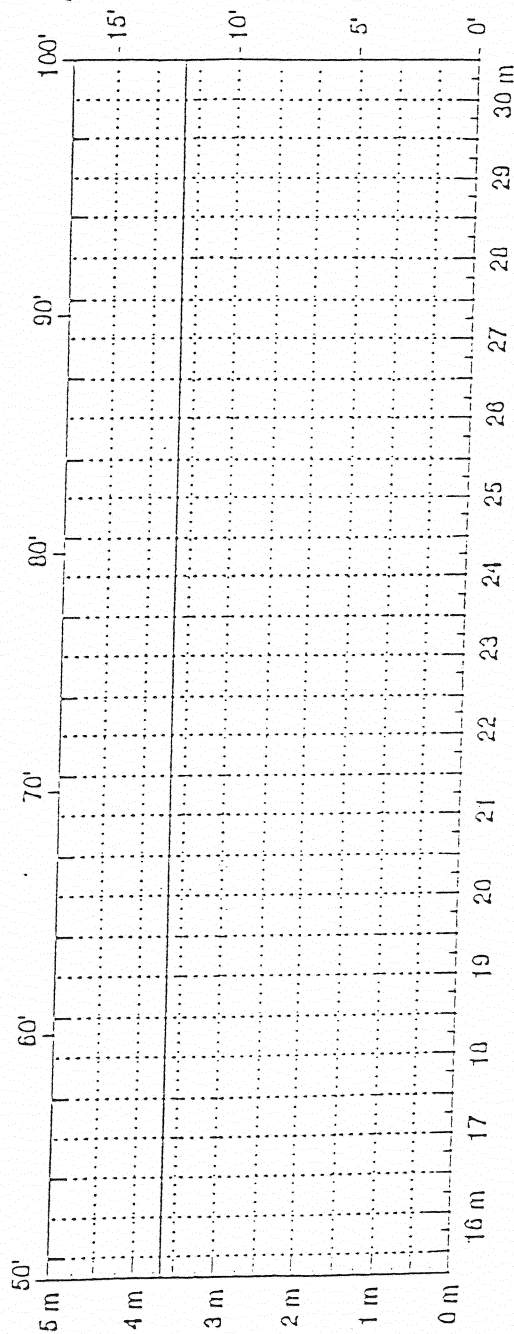


Comments: _____

State Assignment ID


40

State Code

SIIRP Section ID 0503

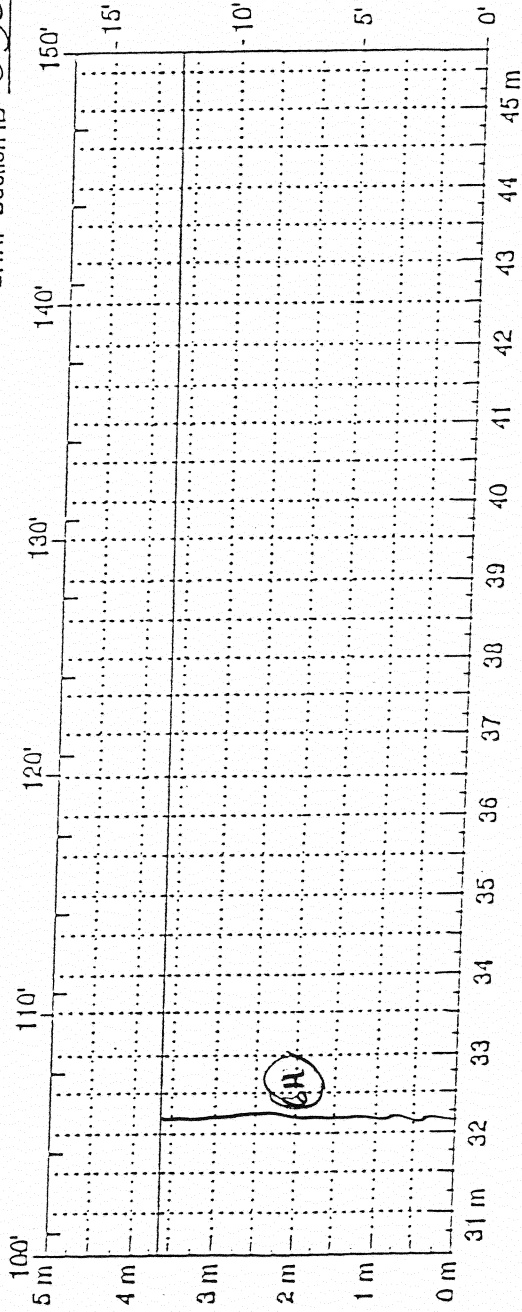


Comments:

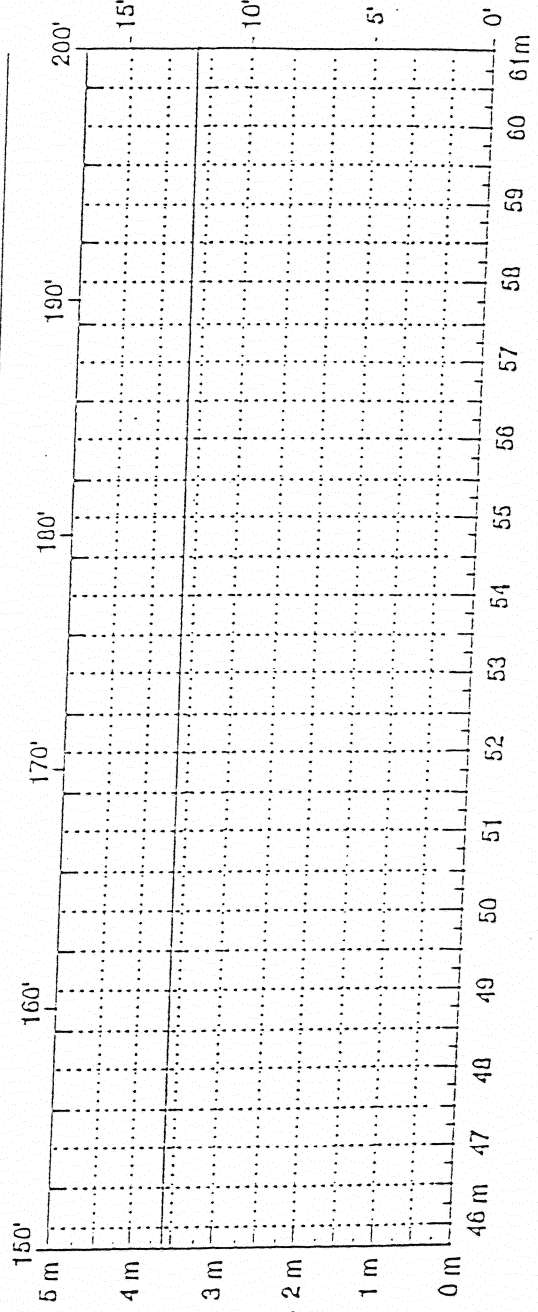


Comments:

State Assigned ID _____
 State Code 40
 SIIIP Section ID 0503

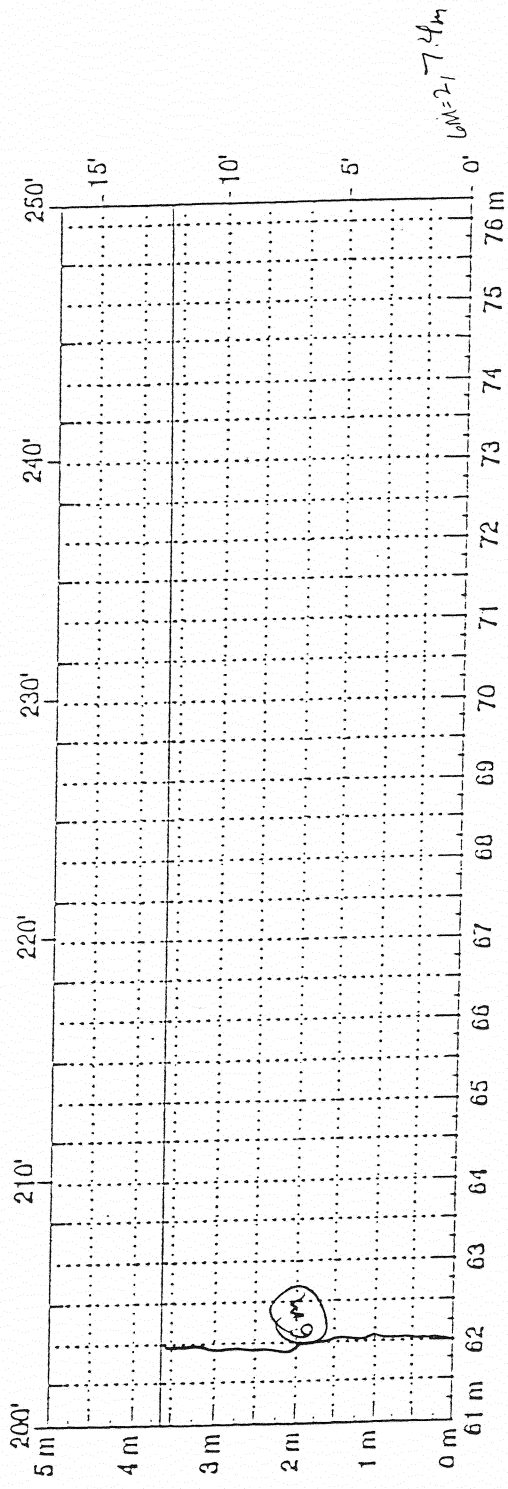

Comments: _____

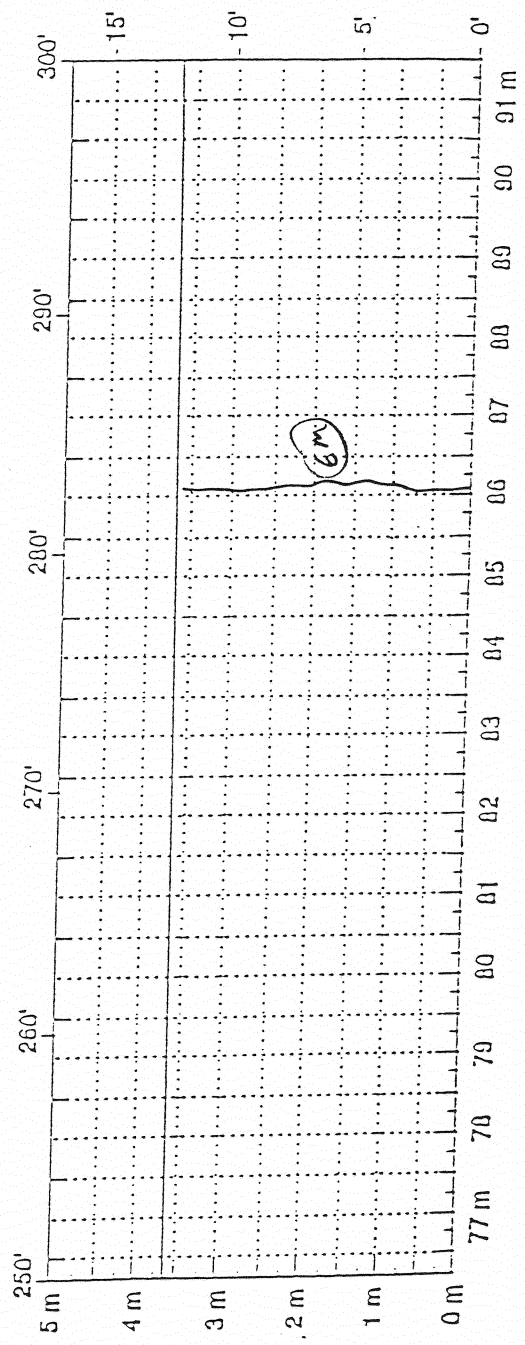


Comments: _____


State Assigned ID _____

State Code 40

SIIRP Section ID 0503

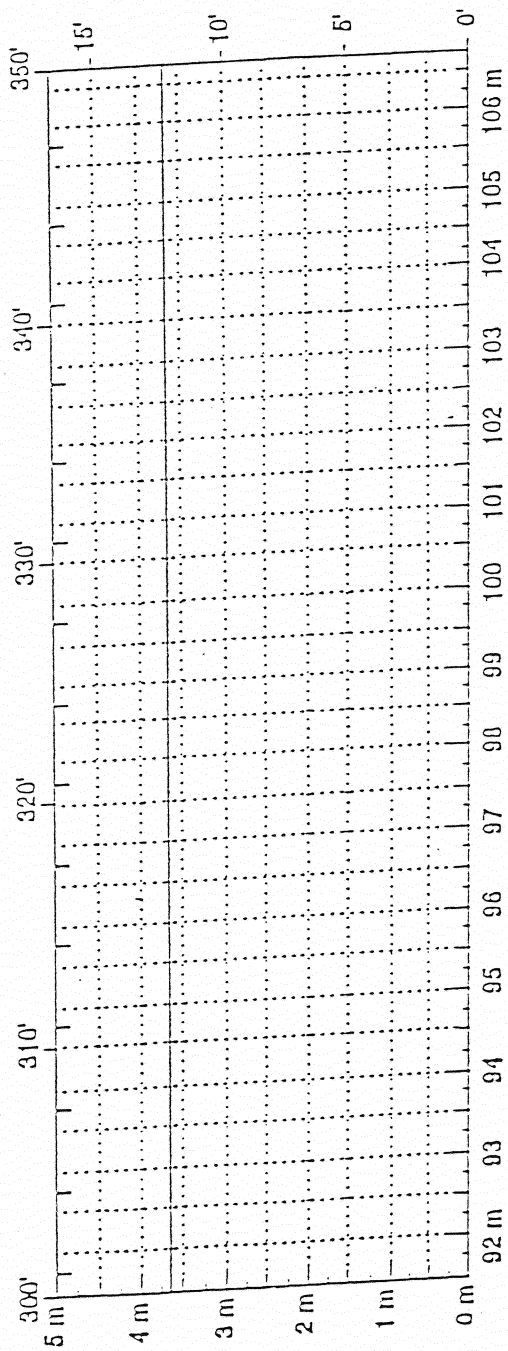


Comments: _____

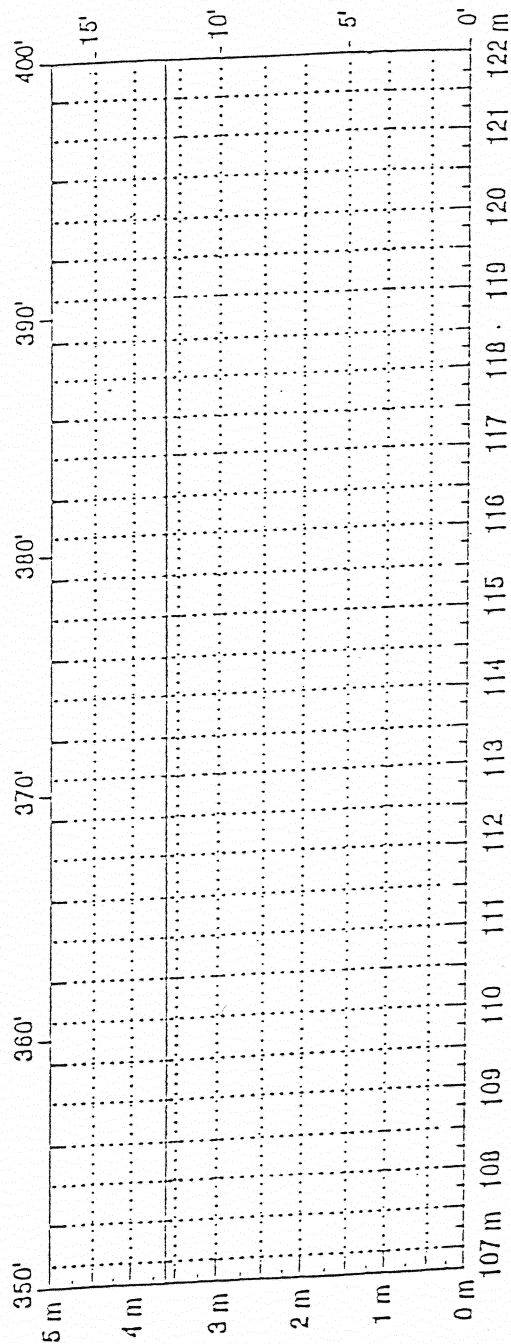


Comments: _____

State Assigned ID 40
 State Code 0503
 SIPP Section ID 0503

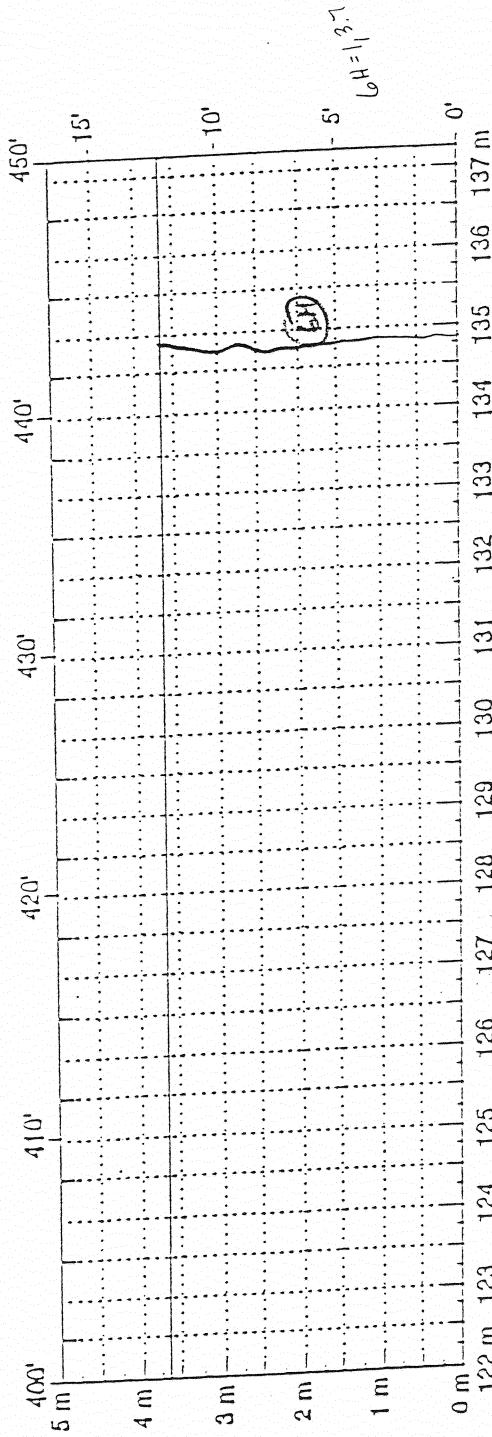

Comments:

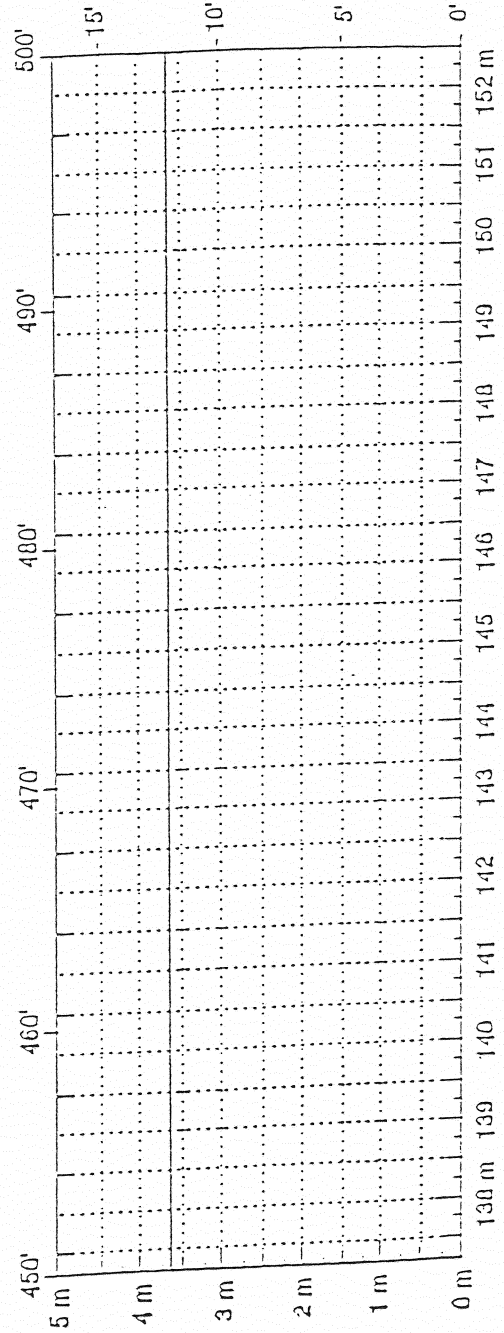

Comments:

LTPP Automated Dipstick Data Collection Transverse Profile Form DS-11 Zero and Calibration Checks	State Code [40] LTPP Section ID [0503] Date (dd/mm/yy) [06/17/97]
---	---

Operator: Tim Martin

Employer: BRE

Dipstick Serial Number: 30023

Pre Measurement Checks

Time (military): 09:45

Automatic Zero Performed:

Calibration

Calibration Check	
Measurement	Reading (inches)
First Reading	.214
Second Reading on Calibration Block	.339
Second Reading - 0.125 - First Reading	.214

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Post Measurement Checks

Time (military): 10:15

Zero Check Acceptable: ✓

Calibration Check	
Measurement	Reading (inches)
First Reading	-.221
Second Reading on Calibration Block	-.096
Second Reading - 0.125 - First Reading	-.221

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Comments

DATE: 6/17/97

OPERATOR: Tim M. G. +

RECORDED: M. K. D. K.

DIPSTICK SERIAL NUMBER: 30023

ENHANCED JUL 16 1997

STATE CODE: 40

SURF SECTION ID: 0503

LOCATION	1	2	3	4	5	6	7	8	9	10	11	12	TOTAL	SUM
0100	033	-032	071	198	150	-017	-062	-029	104	268	260	182		
0150	-033	030	-064	-198	-143	015	016	033	-101	-268	-254	-186	011	
(15m)	024	000	090	259	222	094	057	-029	103	343	240	263		
1100	-025	000	-089	-259	-220	-048	-55	029	-103	-342	-215	-263	005	
(30m)	033	-044	127	329	234	167	060	007	155	315	260	284		
1150	-040	055	-122	-327	-235	-165	055	-003	-155	-315	-253	-289	013	
(45m)	-011	058	123	240	161	056	-059	046	167	285	219	147		
(45m)	003	-058	-121	-240	-161	-057	010	-099	-168	-283	-219	-152	-012	
(2100)	-073	-005	115	256	182	100	-028	030	154	305	276	175		
(60m)	074	007	-111	-254	-183	-098	030	-029	-150	306	275	-175	017	
2150	021	046	116	246	174	060	-020	093	188	311	265	168		
(75m)	025	-044	-117	-247	-172	-054	019	-090	-182	-311	-266	-167	012	
3100	090	055	141	273	203	074	000	084	185	308	311	216		
(90m)	-014	055	-139	-273	-203	-072	002	-083	-183	-311	-314	-213	003	
3150	026	043	167	276	230	076	009	078	178	348	284	280		
(105m)	-047	-054	-168	-300	-230	-079	-008	-077	-181	-341	-292	-285	-017	
4100	-006	000	125	232	150	032	-032	052	138	268	261	374		
(120m)	000	-007	-121	-229	161	-023	051	-048	-130	-408	-261	-373	024	
4150	-090	000	106	185	123	-019	-064	-006	128	280	192	223		
(135m)	088	000	-103	-184	-122	017	070	001	-131	-269	-195	-222	012	
5100	-160	031	077	191	104	004	-087	007	125	254	156	158		
(150m)	096	-025	-076	-185	-106	002	093	-006	-125	-250	-160	153	017	

COMMENTS

RECEIVED JUN 30 1997

STATE ASSIGNED ID _____

SHEET 1

DISTRESS SURVEY

STATE CODE 40

LTPP PROGRAM

SHRP SECTION ID 05084

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR)

06/17/97

SURVEYORS: T J M, M J D PHOTOS, VIDEO, OR BOTH WITH SURVEY (P, V, B)
PAVEMENT SURFACE TEMP - BEFORE 21°C; AFTER 23°C

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
CRACKING			
1. FATIGUE CRACKING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
2. BLOCK CRACKING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
3. EDGE CRACKING (Meters)	<u>0</u>	<u>0</u>	<u>0</u>
4. LONGITUDINAL CRACKING (Meters)			
4a. Wheel Path Length Sealed (Meters)	<u>0.7</u>	<u>0</u>	<u>0</u>
4b. Non-Wheel Path Length Sealed (Meters)	<u>0</u>	<u>0</u>	<u>0</u>
5. REFLECTION CRACKING AT JOINTS Number of Transverse Cracks	<u>0</u>	<u>0</u>	<u>0</u>
Transverse Cracking (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
Longitudinal Cracking (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
6. TRANSVERSE CRACKING Number of Cracks	<u>3</u>	<u>5</u>	<u>1</u>
Length (Meters)	<u>1.9</u>	<u>18.5</u>	<u>1</u>
Length Sealed (Meters)	<u>0.0</u>	<u>0.0</u>	<u>1</u>
PATCHING AND POTHOLES			
7. PATCH/PATCH DETERIORATION (Number) (Square Meters)	<u>0</u>	<u>0</u>	<u>1</u>
8. Potholes (Number) (Square Meters)	<u>0</u>	<u>0</u>	<u>1</u>

RECEIVED JUL 17 1997 JP

ENTERED OCT 21 1997 J B
REVIEWED JUL 21 1997 J

Revised December 1, 1992

SHEET 2
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _ _ _ _

STATE CODE

40

SHRP SECTION ID

050~~4~~

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/17/97

SURVEYORS: T J M, M J D

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH

SURFACE DEFORMATION

9. RUTTING - REFER TO SHEET 3 FOR SPS-3 OR Form S1 from Dipstick Manual

10. SHOVING (Number)			<u>0</u>
(Square Meters)			<u>0.</u>

SURFACE DEFECTS

11. BLEEDING (Square Meters)	<u>305.0</u>	<u>0.</u>	<u>0.</u>
---------------------------------	--------------	-----------	-----------

12. POLISHED AGGREGATE (Square Meters)			<u>0.</u>
---	--	--	-----------

13. RAVELING (Square Meters)	<u>0.</u>	<u>0.</u>	<u>0.</u>
---------------------------------	-----------	-----------	-----------

MISCELLANEOUS DISTRESSES

14. LANE-TO-SHOULDER DROPOFF - REFER TO SHEET 3

15. WATER BLEEDING AND PUMPING (Number)	<u>0</u>
Length of Affected Pavement (Meters)	<u>0.</u>

16. OTHER (Describe) _____

Revised May 29, 1992

SHEET 3

DISTRESS SURVEY

LTPP PROGRAM

STATE ASSIGNED ID _____

STATE CODE 40

SHRP SECTION ID 05084

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/17/97

SURVEYORS: TJM, MJD

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

9. RUTTING (FOR SPS-3 SITE SURVEYS)

INNER WHEEL PATH			OUTER WHEEL PATH		
Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)	Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)
1	0.	— — —	1	0.	— — —
2	15.25	— — —	2	15.25	— — —
3	30.5	— — —	3	30.5	— — —
4	45.75	— — —	4	45.75	— — —
5	61.	— — —	5	61.	— — —
6	76.25	— — —	6	76.25	— — —
7	91.5	— — —	7	91.5	— — —
8	106.75	— — —	8	106.75	— — —
9	122.	— — —	9	122.	— — —
10	137.25	— — —	10	137.25	— — —
11	152.5	— — —	11	152.5	— — —

SEE
DIPSTICK
DATA

14. LANE-TO-SHOULDER DROPOFF

Point No.	Point Distance ¹ Meters	Lane-to-Shoulder Dropoff (mm)
1	0.	— — 0.
2	15.25	— — 1.
3	30.5	— — 1.
4	45.75	— — 1.
5	61.	— — 1.
6	76.25	— — 1.
7	91.5	— — 1.
8	106.75	— — 1.
9	122.	— — 1.
10	137.25	— — 1.
11	152.5	— — 1.


Note 1: "Point Distance" is the distance in meters from the start of the test section to the point where the measurement was made. The values shown are SI equivalents of the 50 ft spacing used in previous surveys.

ENL 100 OCT 21 1997 J. B

State Assigned ID _____
 State Code 40
 SIIRP Section ID 05084


date: 6/17/97

surveys: TJMT-MJD

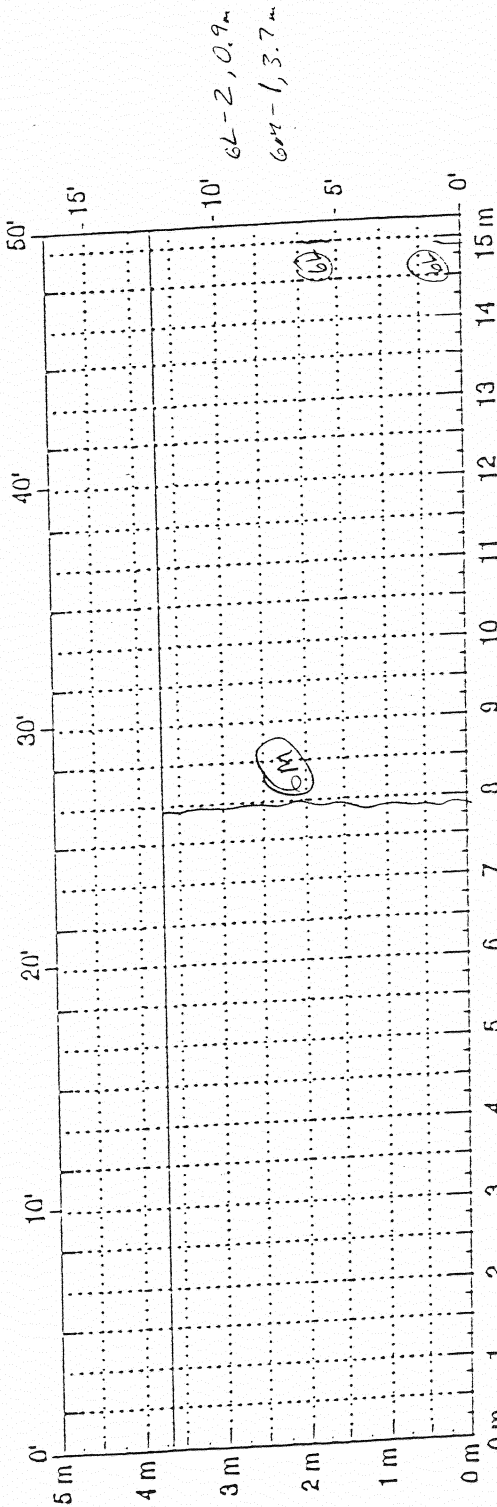


Tails
 216L - 0.7m
 6L - 3, 1.2m
 6M - 5, 18.5m
 11L - 305m

Comments: Bleeding throughout section in both wheel-paths.

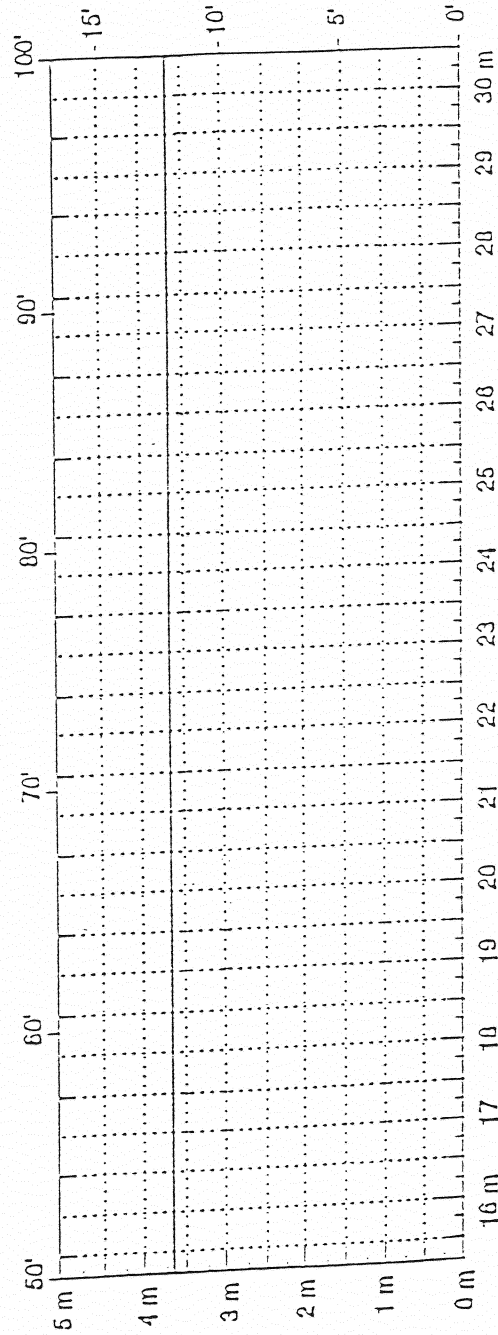


Comments: _____


State Ass[gnod ID _____
 State Code 40
 SIPP Section ID 05084

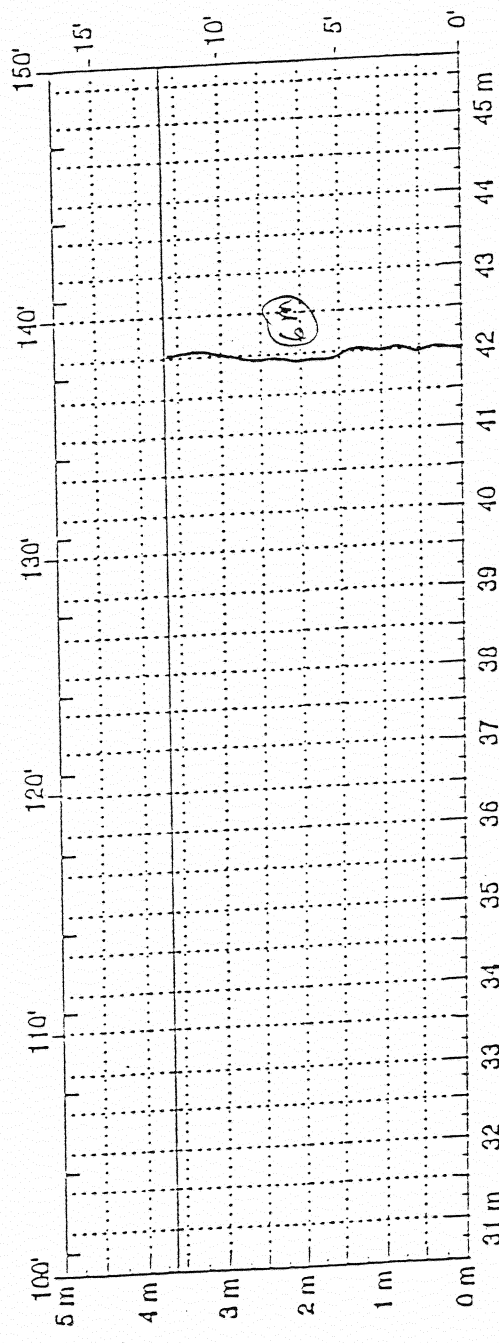


6.4m - 1, 3.7m

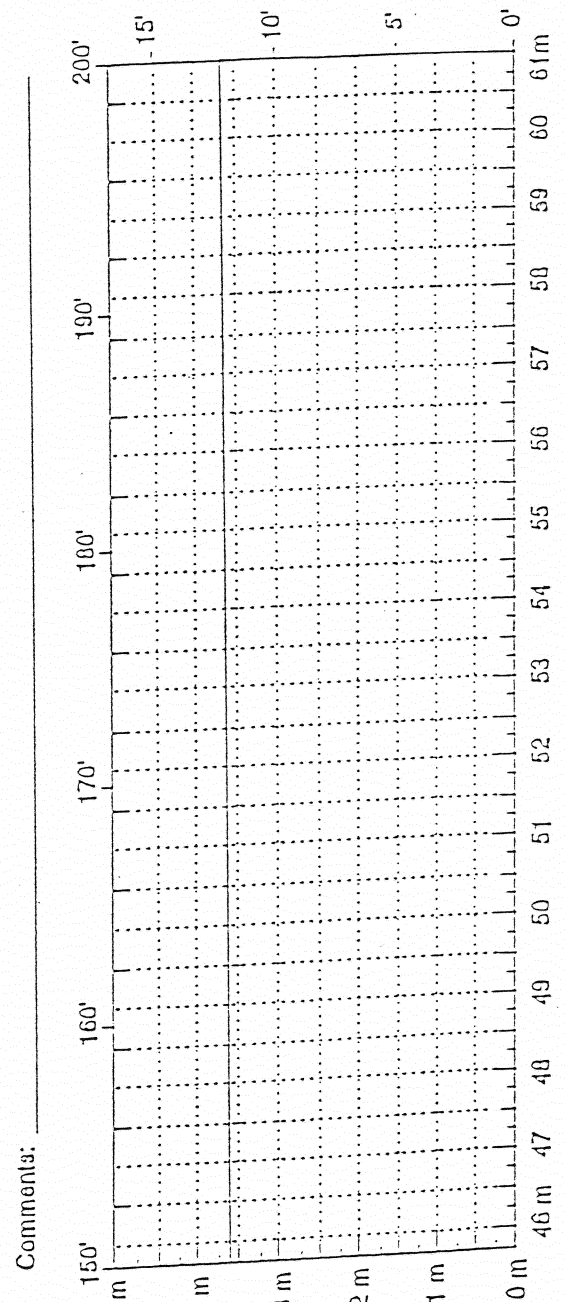

State Assigned ID _____
 State Code 40
 SHIP Section ID 05084

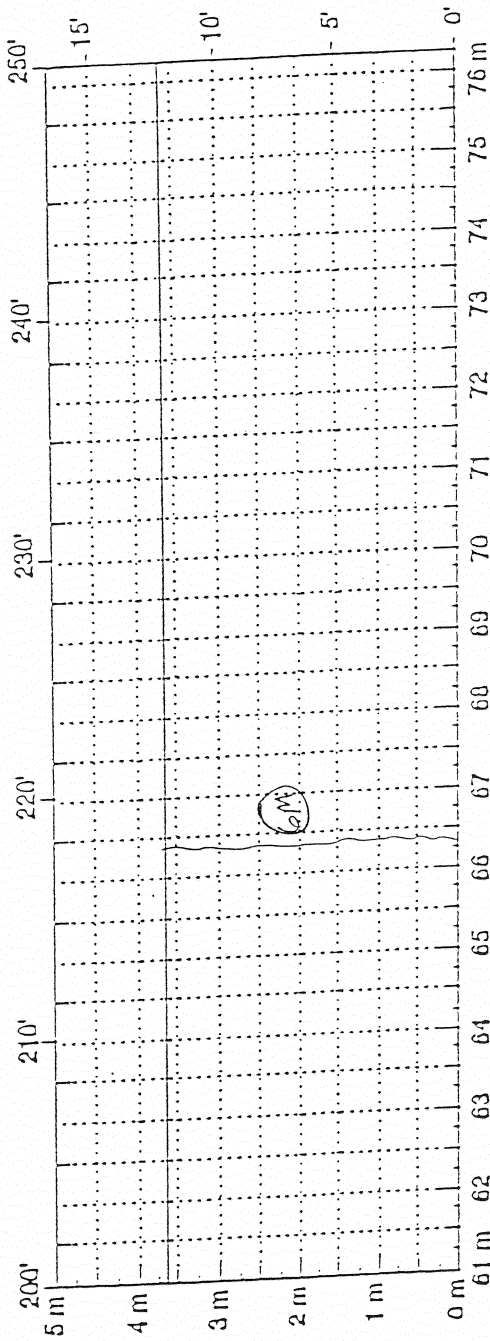

Comments: _____

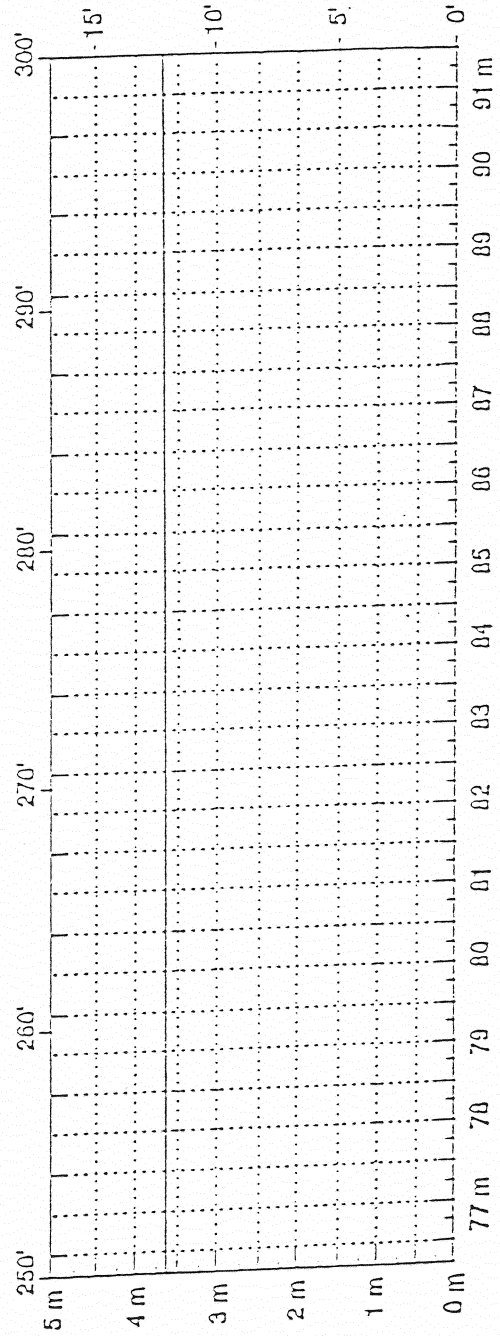


Comments: _____

State Assigned ID _____


State Code 40

SHRP Section ID 05084

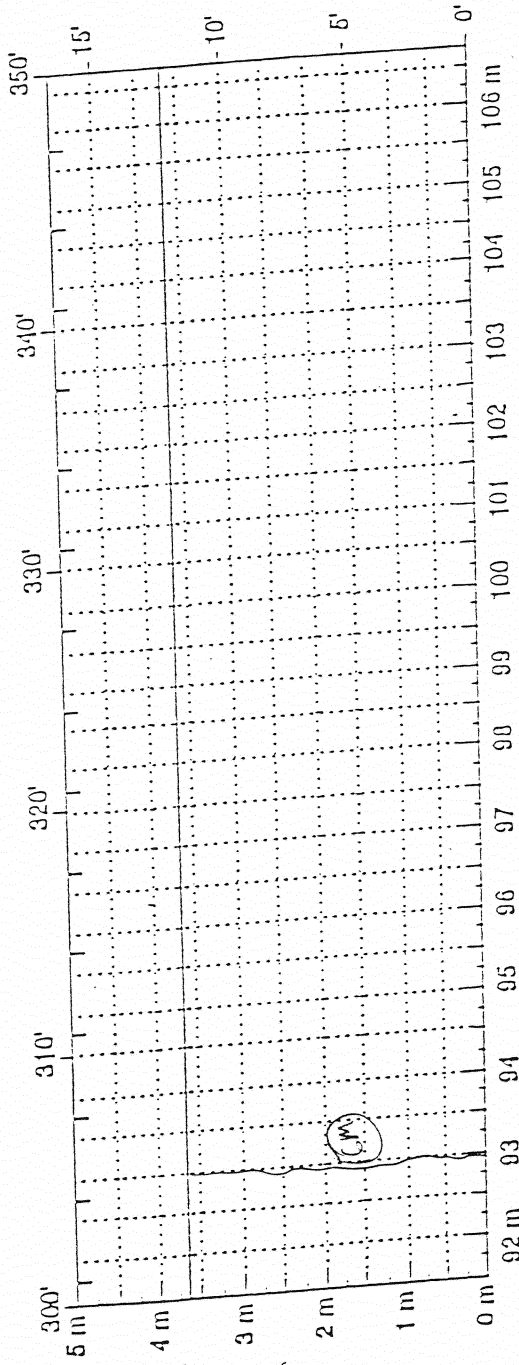


416L - 0.7m
6L - 1.1m
6M - 1, 3.7m

Comments: _____

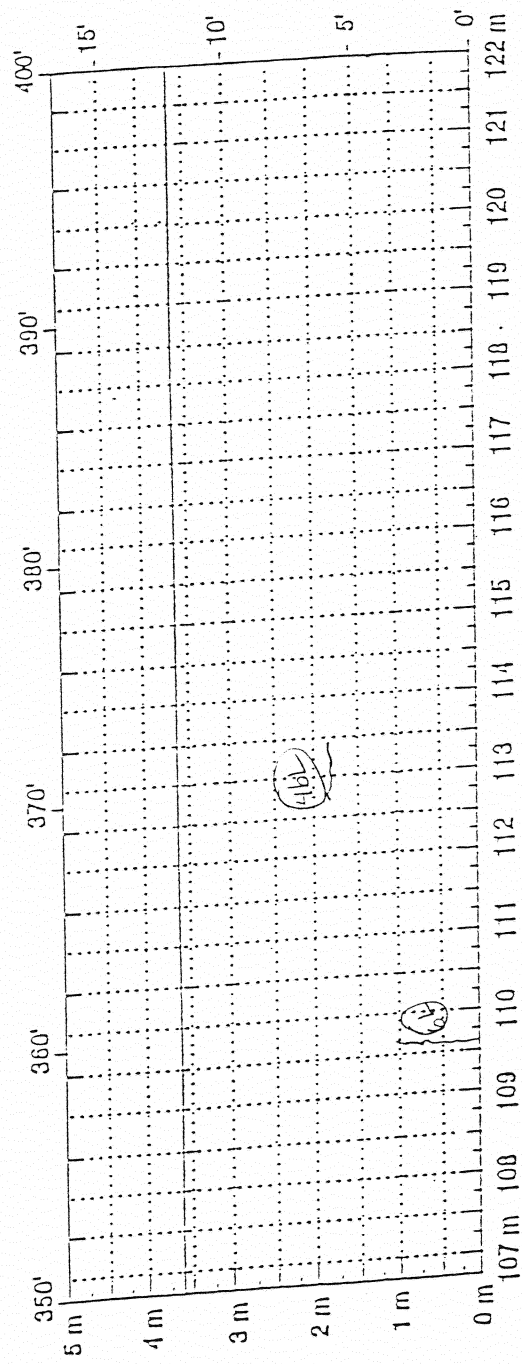


Comments: _____

State Assigned ID 40
 State Code 050
 SIPP Section ID 050

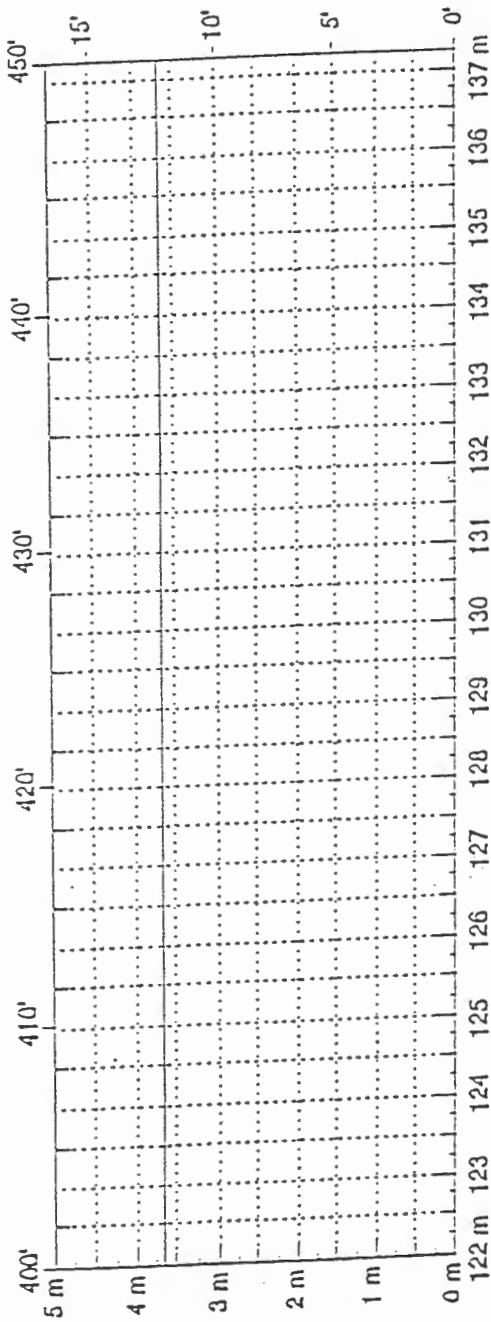

6 m, 1-3.7 m

Comments:

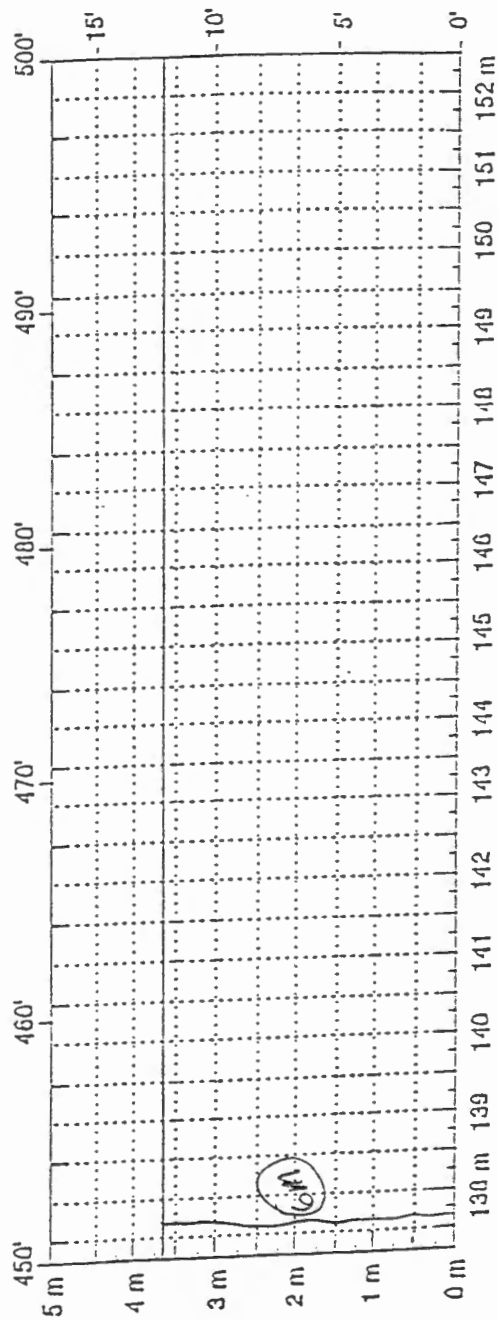

Comments:

LTPP Automated Dipstick Data Collection Transverse Profile Form DS-11 Zero and Calibration Checks	State Code [40] LTPP Section ID [0504] Date (dd/mm/yy) [6/17/97]
---	--

Operator: Tim Marth

Employer: BRE

Dipstick Serial Number: 30023

Pre Measurement Checks

Time (military): 17:50

Automatic Zero Performed:

Calibration

Calibration Check	
Measurement	Reading (inches)
First Reading	- 080
Second Reading on Calibration Block	- 206
Second Reading - 0.125 - First Reading	.125

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Post Measurement Checks

Time (military): 18:30

Zero Check Acceptable: ✓

Calibration Check	
Measurement	Reading (inches)
First Reading	.079
Second Reading on Calibration Block	.204
Second Reading - 0.125 - First Reading	.125

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Comments

DATE: 6/17/97

OPERATOR: Tim Martin

RECORDER: Matt Duke

DIPSTICK SERIAL NUMBER: 30023

EN. VIZGELUN 7 249974

ENTRANCED JUL 10 1997 A II

STATE CODE: 40

SHIP SECTION ID: 0504

DIPSTICK READING

LOCATION	1	2	3	4	5	6	7	8	9	10	11	12	TOTAL	SUM
0100	119	019	004	221	240	156	025	-026	005	240	345	248		
	-119 ¹⁵	025 ¹⁵	-003 ⁹	-219 ⁸	-236 ⁵	-155 ¹	-022 ⁶	030 ²³	-003 ⁷	-233 ²⁴	-356 ¹⁰	-253 ²⁵	015	
0150	079	004	060	303	310	105	087	014	090	357	407	295		
(15m)	-083 ²²	-009 ²¹	-051 ²⁶	-303 ¹⁷	-308 ¹⁷	-166 ¹⁵	-082 ¹⁶	+019 ¹¹	-083 ⁶	-356 ¹¹	403 ²²	-361 ¹⁶	017	
1100	020	054	046	218	250	142	070	028	065	286	368	225		
(30m)	-020 ²¹	-054 ²¹	-041 ²²	-213 ¹⁶	-248 ¹¹	-143 ⁹	-070 ¹¹	-040 ¹⁰	-053 ²²	-278 ¹¹	-366 ²²	-225 ²⁰	021	
1150	074	044	023	266	226	145	043	-082	090	360	351	269		
(45m)	-070	-047	-013	-263	-224	-138	-032 ²⁴	098 ²⁷	-087 ¹⁷	-349 ¹⁴	-347 ²³	-270 ²¹	061	
(2100)	026	055	050	245	226	160	022	-107	074	340	360	356		
(60m)	-034	-059 ⁴¹	-042 ⁴⁵	-241 ²⁷	-221 ²²	-158 ²⁹	-008 ²⁶	110 ¹²	-066 ⁹	-334 ¹	-364 ¹⁵	-357 ²¹	043	
2150	-039	-109	035	254	250	086	-037	-088	090	308	306	238		
(75m)	044	110	-034 ¹	-252 ¹²	-249 ¹³	-081 ¹¹	043 ²⁰	093 ¹⁰	-085 ⁹	-306 ¹¹	-304 ²²	-238	040	
3100	003	000	130	331	319	122	-007	-075	126	361	322	190		
(90m)	-003 ¹⁵	010 ¹⁰	-127 ²²	-331 ¹²	-313 ¹³	-419 ¹¹	014 ¹⁰	077 ¹¹	-123 ⁷	-336 ⁴	-341 ²²	-192 ²²	-018	
3150	108	018	062	384	364	154	-049	-071	140	408	435	321		
(105m)	-111 ¹⁶	-008 ¹¹	-056 ²¹	-382 ²¹	-363 ²¹	-150 ²⁰	055 ²⁶	082 ²⁰	-135 ²	-407 ¹⁴	-435 ²³	-318 ²³	046	
4100	030	-017	082	325	306	116	-022	-049	130	334	304	165		
(120m)	-034 ²¹	023 ²²	-076 ²²	-321 ²²	-309 ²²	-109 ¹¹	026 ¹⁶	047 ¹¹	-120 ¹⁶	-330 ¹⁶	-362 ²²	-105 ²⁰	034	
4150	024	049	081	312	255	092	045	-039	090	354	352	254		
(135m)	-026 ²²	053 ²²	-074 ²¹	-318 ¹⁴	-250 ²²	-90 ¹²	-052 ¹²	047 ²⁰	-090 ¹²	-352 ¹²	-342 ¹⁶	-254 ²⁰	023	
5100	085	023	057	278	226	117	-018	-043	123	275	271	263		
(150m)	087 ¹²	038 ¹⁵	-046 ²²	-281 ²²	-222 ²²	-117 ²²	023 ²⁸	053 ²²	-122 ²²	-270 ¹¹	-284 ¹⁶	-263 ²⁰	013	

COMMENTS

RECEIVED JUN 30 1997

STATE ASSIGNED ID _____

SHEET 1

DISTRESS SURVEY

STATE CODE 40

LTPP PROGRAM

SHRP SECTION ID 0505

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR)

06/17/97

SURVEYORS: JJM, MJD PHOTOS, VIDEO, OR BOTH WITH SURVEY (P, V, B) B
PAVEMENT SURFACE TEMP - BEFORE 39°C; AFTER 38°C

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
CRACKING			
1. FATIGUE CRACKING (Square Meters)	<u>0.3</u>	<u>0</u>	<u>0</u>
2. BLOCK CRACKING (Square Meters)	<u>0</u>	<u>1</u>	<u>1</u>
3. EDGE CRACKING (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
4. LONGITUDINAL CRACKING (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
4a. Wheel Path Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
4b. Non-Wheel Path Length Sealed (Meters)	<u>6.5</u> ^v <u>0</u>	<u>4.5</u> <u>0</u>	<u>1</u>
5. REFLECTION CRACKING AT JOINTS Number of Transverse Cracks	<u>0</u>	<u>0</u>	<u>1</u>
Transverse Cracking (Meters) Length Sealed (Meters)	<u>1</u> <u>1</u>	<u>1</u> <u>1</u>	<u>1</u> <u>1</u>
Longitudinal Cracking (Meters) Length Sealed (Meters)	<u>1</u> <u>1</u>	<u>1</u> <u>1</u>	<u>1</u> <u>1</u>
6. TRANSVERSE CRACKING Number of Cracks	<u>5</u>	<u>2</u>	<u>1</u>
Length (Meters) Length Sealed (Meters)	<u>12.8</u> <u>1.3</u>	<u>7.4</u> <u>0</u>	<u>1</u> <u>1</u>

PATCHING AND POTHOLES

7. PATCH/PATCH DETERIORATION (Number) (Square Meters)	<u>0</u> <u>1</u>	<u>0</u> <u>1</u>	<u>1</u> <u>1</u>
8. Potholes (Number) (Square Meters)	<u>1</u> <u>1</u>	<u>1</u> <u>1</u>	<u>1</u> <u>1</u>

REVIEWED JUL 7 1997 JP
REVIEWED JUL 7 1997 JP

FILED OCT 21 1997 JP

Revised December 1, 1992

SHEET 2
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _____

STATE CODE 40

SHRP SECTION ID 0505

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/17/97

SURVEYORS: TJM, MJD

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
SURFACE DEFORMATION			
9. RUTTING - REFER TO SHEET 3 FOR SPS-3 OR Form S1 from Dipstick Manual			
10. SHOving (Number) (Square Meters)			<u>0</u> <u>0</u>
SURFACE DEFECTS			
11. BLEEDING (Square Meters)	<u>305.0</u>	<u>0</u>	<u>0</u>
12. POLISHED AGGREGATE (Square Meters)			<u>0</u>
13. RAVELING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
MISCELLANEOUS DISTRESSES			
14. LANE-TO-SHOULDER DROPOFF - REFER TO SHEET 3			
15. WATER BLEEDING AND PUMPING (Number) Length of Affected Pavement (Meters)			<u>0</u> <u>0</u>
16. OTHER (Describe) _____			

Revised May 29, 1992

ENTERED OCT 21 1997

SHEET 3

DISTRESS SURVEY

LTPP PROGRAM

STATE ASSIGNED ID — — — —

STATE CODE 40

SHRP SECTION ID 0505

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/17/97

SURVEYORS: TJM, MJD

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

9. RUTTING (FOR SPS-3 SITE SURVEYS)

INNER WHEEL PATH			OUTER WHEEL PATH		
Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)	Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)
1	0.	— — —	1	0.	— — —
2	15.25	— — —	2	15.25	— — —
3	30.5	— — —	3	30.5	— — —
4	45.75	— — —	4	45.75	— — —
5	61.	— — —	5	61.	— — —
6	76.25	— — —	6	76.25	— — —
7	91.5	— — —	7	91.5	— — —
8	106.75	— — —	8	106.75	— — —
9	122.	— — —	9	122.	— — —
10	137.25	— — —	10	137.25	— — —
11	152.5	— — —	11	152.5	— — —

SEE
DIPSTICK
DATA

14. LANE-TO-SHOULDER DROPOFF


Point No.	Point Distance ¹ Meters	Lane-to-Shoulder Dropoff (mm)
1	0.	— — 0.
2	15.25	— — 5.
3	30.5	— — 5.
4	45.75	— — 5.
5	61.	— — 5.
6	76.25	— — 5.
7	91.5	— — 5.
8	106.75	— — 5.
9	122.	— — 5.
10	137.25	— — 5.
11	152.5	— — 5.

Note 1: "Point Distance" is the distance in meters from the start of the test section to the point where the measurement was made. The values shown are SI equivalents of the 50 ft spacing used in previous surveys.


State Assigned ID _____
 State Code 40
 date: 6/17/97
 Surveyors: TJM + MSD
 SIPP Section ID 0505

$T_1 = 39^\circ\text{C}$
 $T_2 = 38^\circ\text{C}$
Targets:
 1L - 0.3 m ✓
 1L = 305.5 m ✓
 4BL - 6.5 m ✓
 4BL - 4.5 m ✓
 6L - 5, 12.8 m, 1.3 m ✓
 6M - 2, 7.4 m ✓

4BL - 1.5 m ✓
 6M - 1, 3.7 m ✓

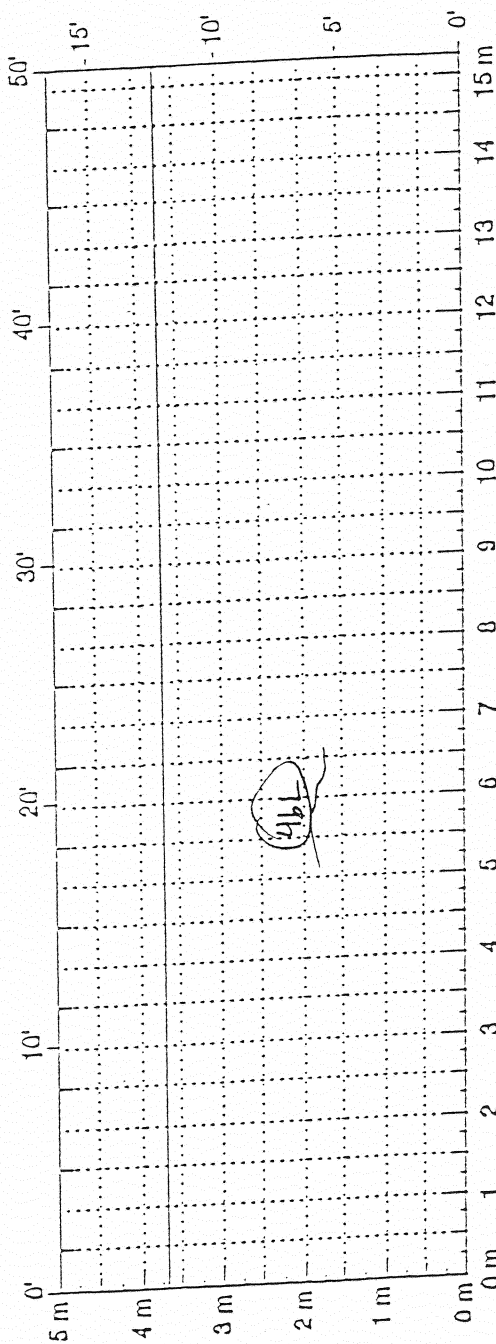


Comments: Bleeding throughout section in both wheel-paths, 11L

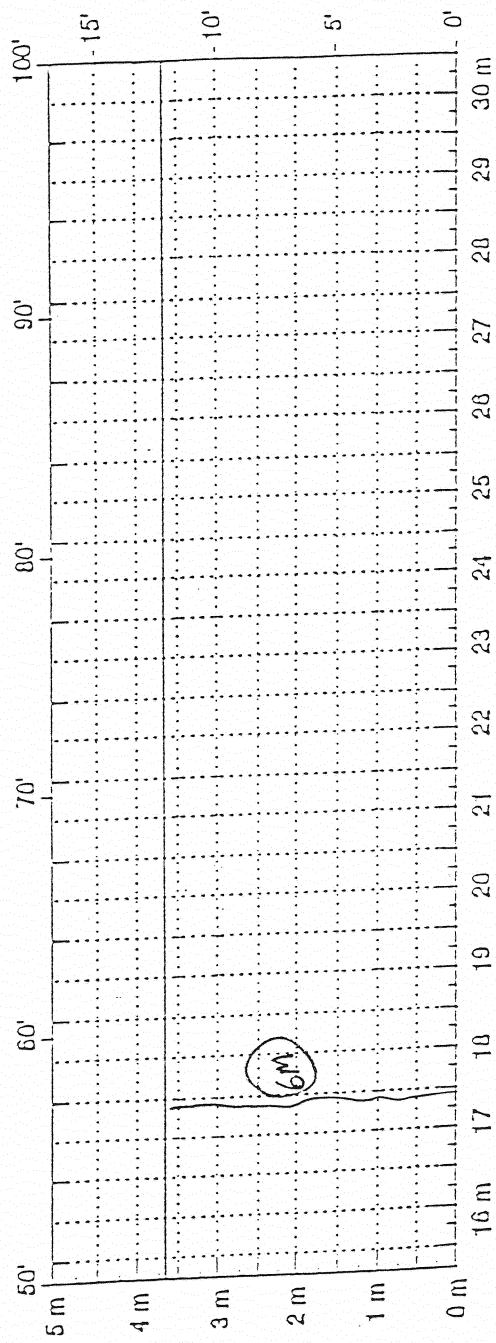


Comments:

State Assigned ID _____
 State Code 40
 SIIRP Section ID 0505

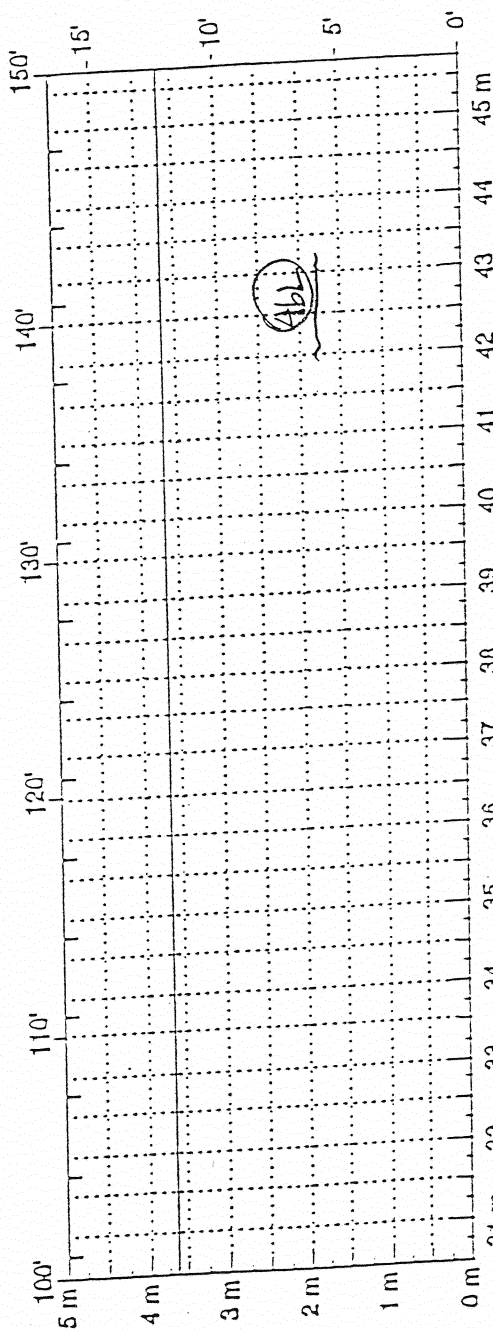


Comments: _____

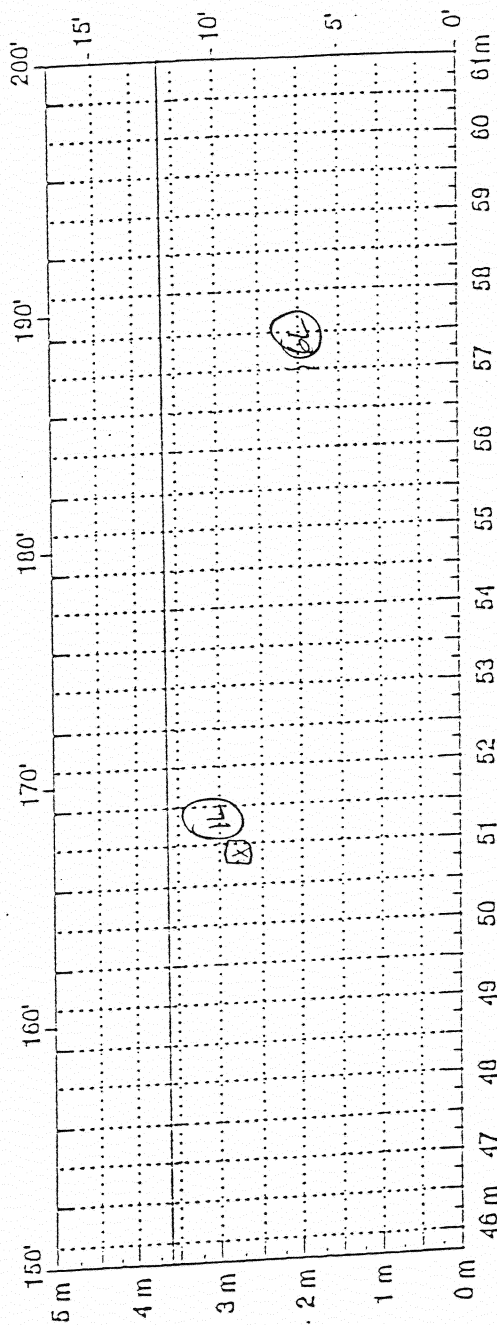


Comments: _____

State Assigned ID _____
 State Code 40
 SLIP Section ID 0505

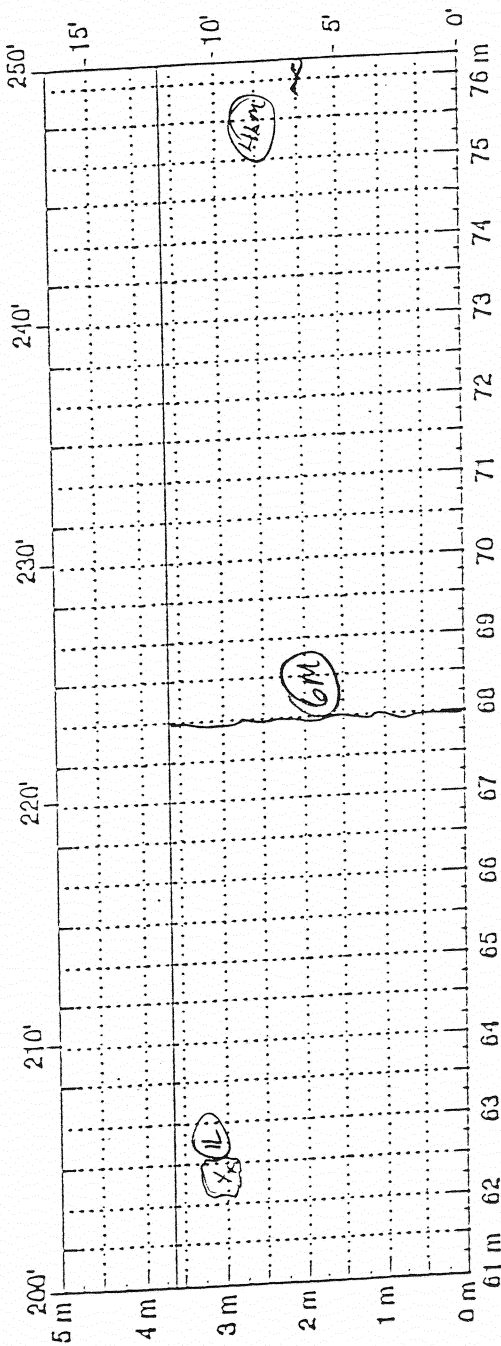


Comments: _____

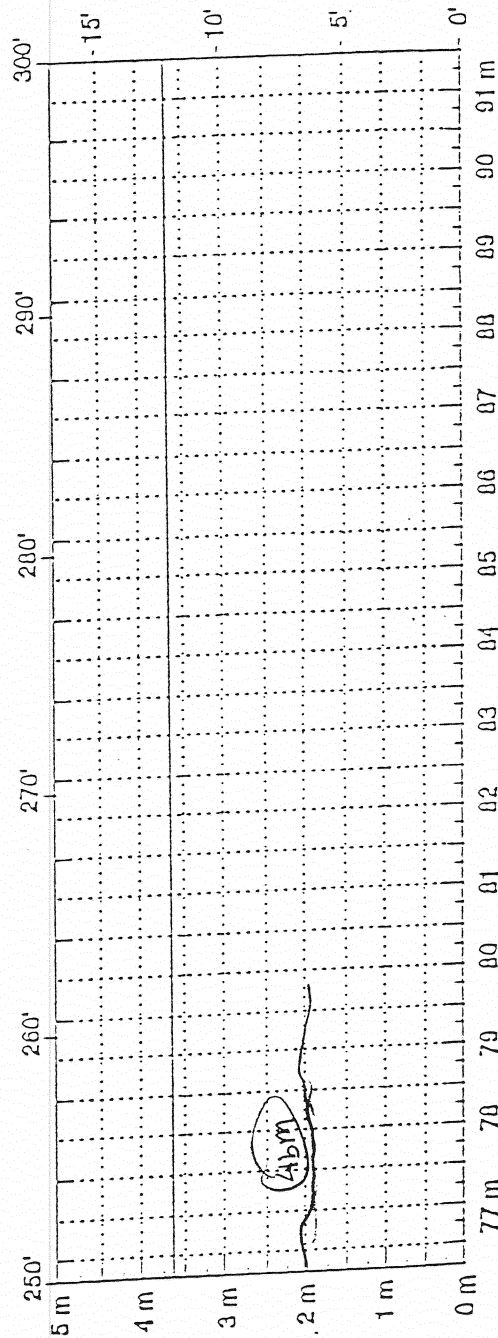


Comments: _____

State Assigned ID 40
 State Code
 SHRP Section ID 0505

42L - 0.7m
 42L - 3.7m
 6L - 3, 8.7m, 13

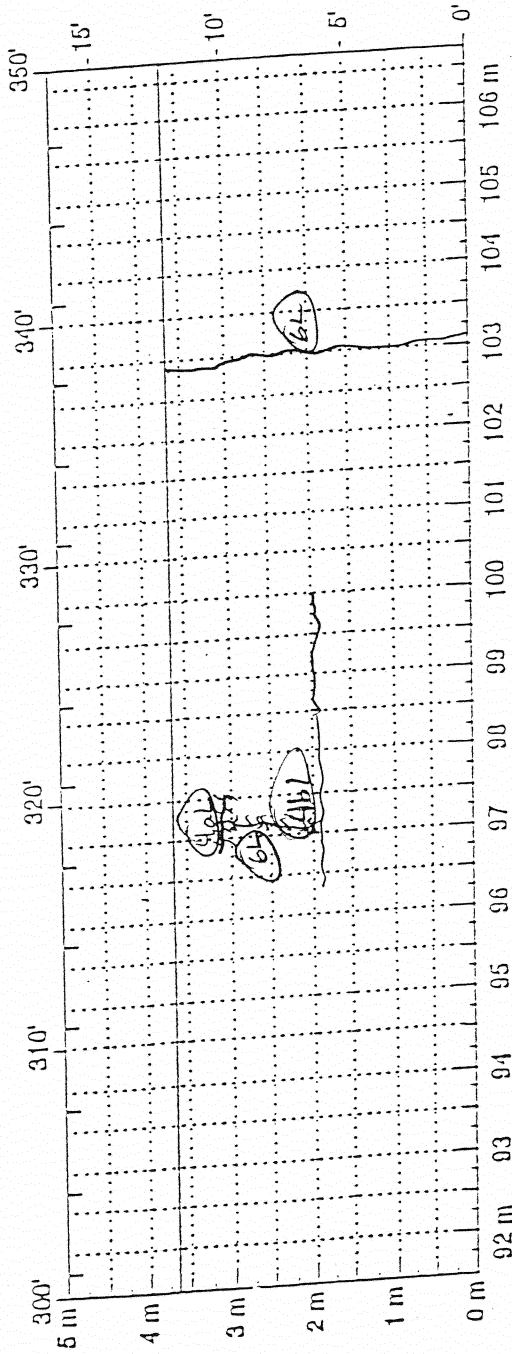

Comments:

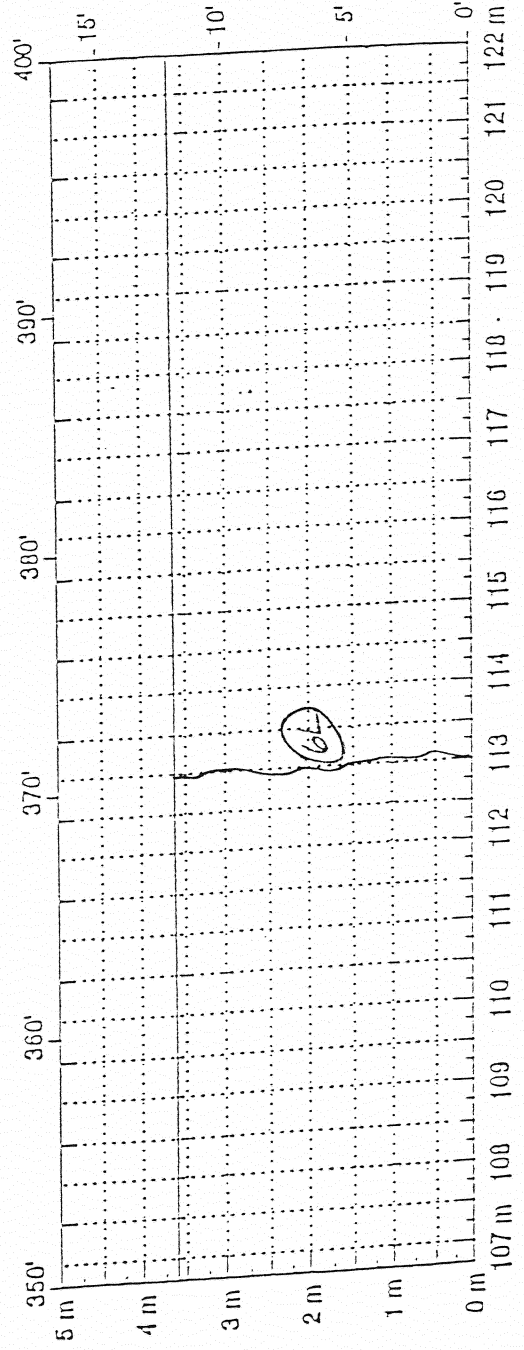


Comments:

State Assigned ID _____


40

State Code

SIIP Section ID 0505

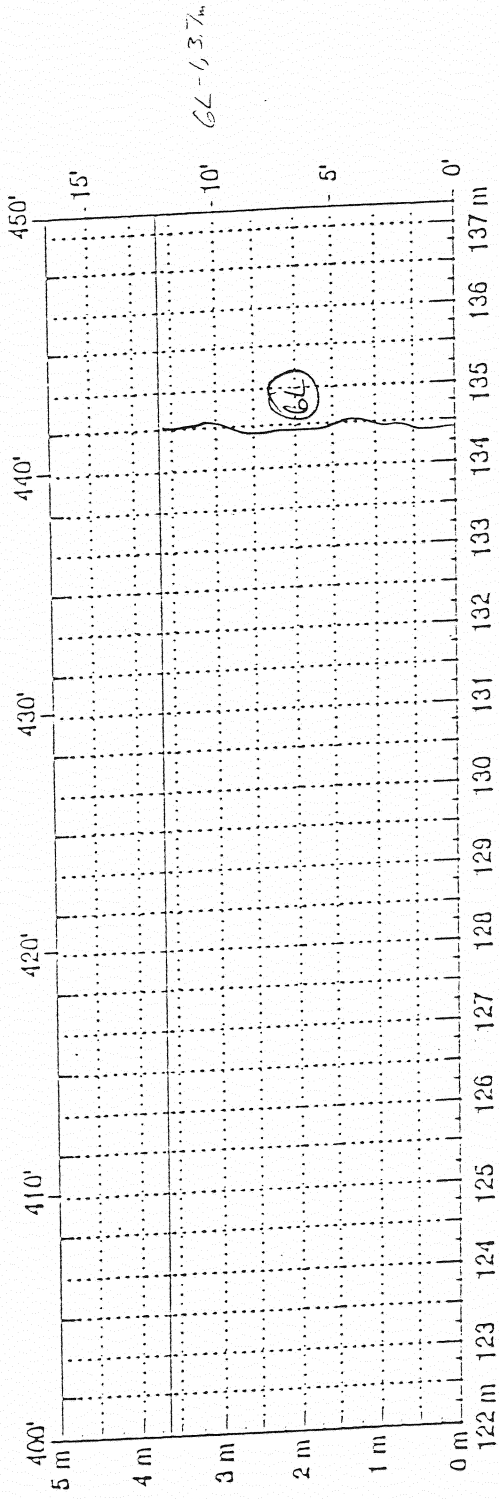

Comments: _____

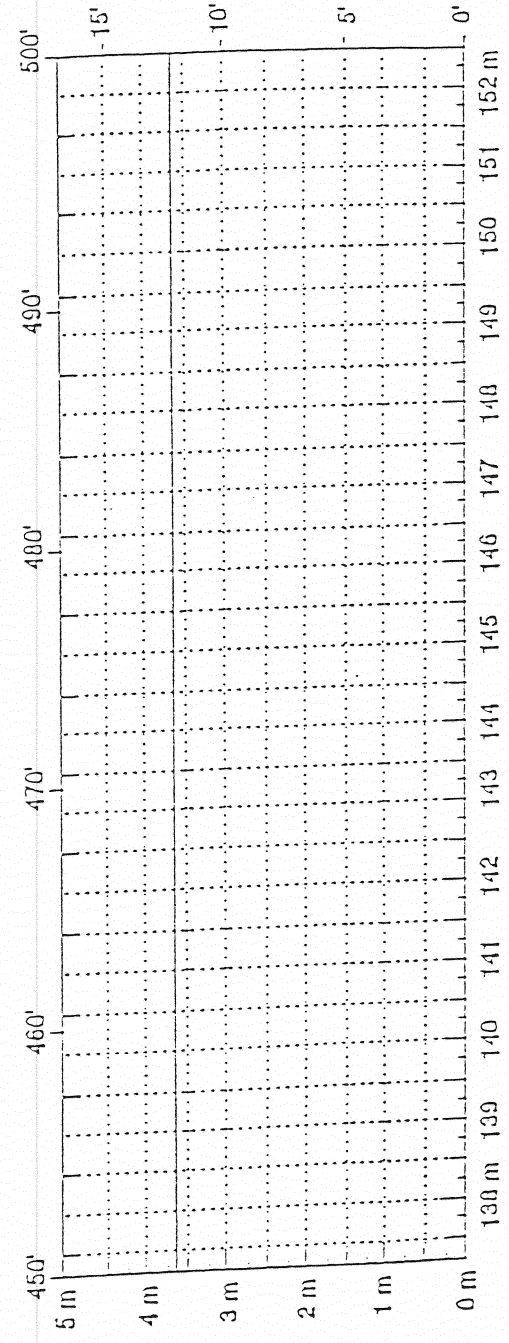

Comments: _____

LTPP Automated Dipstick Data Collection Transverse Profile Form DS-11 Zero and Calibration Checks	State Code	[4 0]
	LTPP Section ID	[0 5 0 5]
	Date (dd/mm/yy)	[0 6 / 1 7 / 9 7]

Operator: TSM/mid Employer: BRE

Dipstick Serial Number: 30023

Pre Measurement Checks

Time (military): 1 8 : 5 5

Automatic Zero Performed:

Calibration

Calibration Check	
Measurement	Reading (inches)
First Reading	.068
Second Reading on Calibration Block	.194
Second Reading - 0.125 - First Reading	.125

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Post Measurement Checks

Time (military): 1 9 : 3 0

Zero Check Acceptable: ✓

Calibration Check	
Measurement	Reading (inches)
First Reading	.067
Second Reading on Calibration Block	.192
Second Reading - 0.125 - First Reading	.125

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Comments

DATE: 6/17/97

OPERATOR: JWH

RECORDER: YAB

DIPSTICK SERIAL NUMBER: 30023

ENL V-66604 7 200907A NE

ENLIED JUL 10 1997 A II

STATE CODE: 40

SHRP SECTION I.D.: 0505

DIPSTICK READING

LOCATION	1	2	3	4	5	6	7	8	9	10	11	12	TOTAL	SUM
0100	263	025	258	352	227	133	004	122	320	426	261	245		
	-278	-017	-249	-351	-223	-121	-011	-115	-319	-422	-277	-244	-064	
0150 (15m)	261	031	273	343	212	113	012	109	341	397	220	269		
	-260	-026	-268	-342	-206	-105	-012	-111	-336	-394	-317	-267	-037	
1100 (30m)	251	034	256	373	214	114	015	095	352	401	288	250		
	-250	-029	-250	-372	-205	-107	-024	-096	-349	-349	-240	-248	-024	
1150 (45m)	090	111	204	271	136	045	-013	139	308	321	207	190		
	-082	-108	-263	-269	-134	-043	018	-131	-340	-322	-203	-192	-030	
2100 (60m)	-015	098	262	273	122	008	-028	163	280	316	234	231		
	-012	-098	-258	-271	-119	-008	029	-160	-276	-319	-235	-235	-021	
2150 (75m)	-012	060	260	297	165	-006	022	117	293	343	213	233		
	014	-061	-249	-293	-168	010	-027	-114	-210	-341	-209	-246	-017	
3100 (90m)	032	012	217	317	214	122	004	054	277	407	314	227		
	-030	-011	-216	-309	-216	-118	-002	-060	-269	-402	-310	-229	-043	
3150 (105m)	180	106	275	352	297	075	050	160	287	440	283	268		
	-175	-105	-272	-345	-289	-071	-044	-154	-286	-436	-282	-266	-048	
4100 (120m)	211	062	260	370	325	193	075	061	232	430	400	341		
	-203	-058	-252	-368	-320	-190	-066	-052	-225	-458	-364	-334	-022	
4150 (135m)	155	089	246	322	261	122	060	062	255	265	317	188		
	-162	-081	-242	-316	-256	-116	-052	-060	-248	-560	-367	-189	-058	
5100 (150m)	194	009	180	360	278	141	-008	020	220	442	326	252		
	-145	-018	-168	-348	-267	-184	016	012	-205	-437	-318	-255	-073	

COMMENTS

RECEIVED JUN 30 1997

SHEET 1

DISTRESS SURVEY

LTPP PROGRAM

STATE ASSIGNED ID

STATE CODE 40

SHRP SECTION ID 0506

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR)

06/17/97

SURVEYORS: T J M, M J D PHOTOS, VIDEO, OR BOTH WITH SURVEY (P, V, B) B
PAVEMENT SURFACE TEMP - BEFORE 19°C; AFTER 19°C

SEVERITY LEVEL

DISTRESS TYPE

LOW

MODERATE

HIGH

CRACKING

1. FATIGUE CRACKING (Square Meters)	0	0	0
2. BLOCK CRACKING (Square Meters)			
3. EDGE CRACKING (Meters)			
4. LONGITUDINAL CRACKING (Meters)			
4a. Wheel Path Length Sealed (Meters)			
4b. Non-Wheel Path Length Sealed (Meters)			
5. REFLECTION CRACKING AT JOINTS Number of Transverse Cracks			
Transverse Cracking (Meters)			
Length Sealed (Meters)			
Longitudinal Cracking (Meters)			
Length Sealed (Meters)			
6. TRANSVERSE CRACKING Number of Cracks	1	4	2
Length (Meters)	3.7	14.8	7.4
Length Sealed (Meters)	0	0	0

PATCHING AND POTHOLES

7. PATCH/PATCH DETERIORATION (Number) (Square Meters)	0	0	0
8. Potholes (Number) (Square Meters)			

FILED OCT 21 1997 J B

REVIEWED JUL 17 1997 JP

SHEET 2
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _____
STATE CODE 40
SHRP SECTION ID 0506

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/17/97

SURVEYORS: T J M, M J D

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
SURFACE DEFORMATION			
9. RUTTING - REFER TO SHEET 3 FOR SPS-3 OR Form S1 from Dipstick Manual			
10. SHOVING (Number) (Square Meters)			<u>0</u>
SURFACE DEFECTS			
11. BLEEDING (Square Meters)	<u>305.0</u>	<u>0.</u>	
12. POLISHED AGGREGATE (Square Meters)			
13. RAVELING (Square Meters)	<u>0.</u>	<u>0.</u>	
MISCELLANEOUS DISTRESSES			
14. LANE-TO-SHOULDER DROPOFF - REFER TO SHEET 3			
15. WATER BLEEDING AND PUMPING (Number) Length of Affected Pavement (Meters)			<u>↓</u>
16. OTHER (Describe)			

Revised May 29, 1992

SHEET 3
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID — — — —

STATE CODE 40

SHRP SECTION ID 0506

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/17/97

SURVEYORS: T J M, M J O

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

ENHANCED OCT 21 1997 J B

9. RUTTING (FOR SPS-3 SITE SURVEYS)

INNER WHEEL PATH			OUTER WHEEL PATH		
Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)	Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)
1	0.	— — —	1	0	— — —
2	15.25	— — —	2	15.25	— — —
3	30.5	— — —	3	30.5	— — —
4	45.75	— — —	4	45.75	— — —
5	61.	— — —	5	61.	— — —
6	76.25	— — —	6	76.25	— — —
7	91.5	— — —	7	91.5	— — —
8	106.75	— — —	8	106.75	— — —
9	122.	— — —	9	122.	— — —
10	137.25	— — —	10	137.25	— — —
11	152.5	— — —	11	152.5	— — —


SEE
DIPSTICK
DATA

14. LANE-TO-SHOULDER DROPOFF

Point No.	Point Distance ¹ Meters	Lane-to-Shoulder Dropoff (mm)
1	0.	— — 0.
2	15.25	— — 1.
3	30.5	— — 1.
4	45.75	— — 1.
5	61.	— — 1.
6	76.25	— — 1.
7	91.5	— — 1.
8	106.75	— — 1.
9	122.	— — 1.
10	137.25	— — 1.
11	152.5	— — 1.

Note 1: "Point Distance" is the distance in meters from the start of the test section to the point where the measurement was made. The values shown are SI equivalents of the 50 ft spacing used in previous surveys.


date: 6/17/97 Status Assigned ID _____
 State Code 40
 Surveyors: TJM, MSD SRRP Section ID 0506

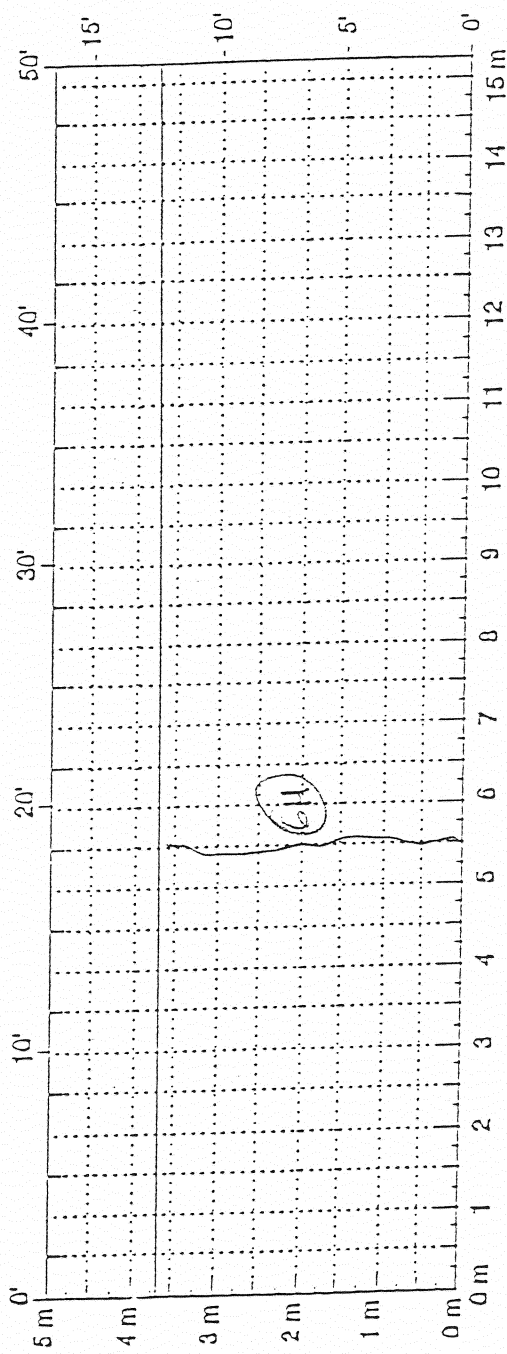

$6M = 1, 3, 7$
 $6H = 1, 3, 7$


Totals:
 6L - 1, 3, 7m
 6M - 4, 14.8 m
 6H - 2, 7.4 m
 11L - 305 m

Comments: 11L Light Severity Bleeding Throughput section in both wheel paths

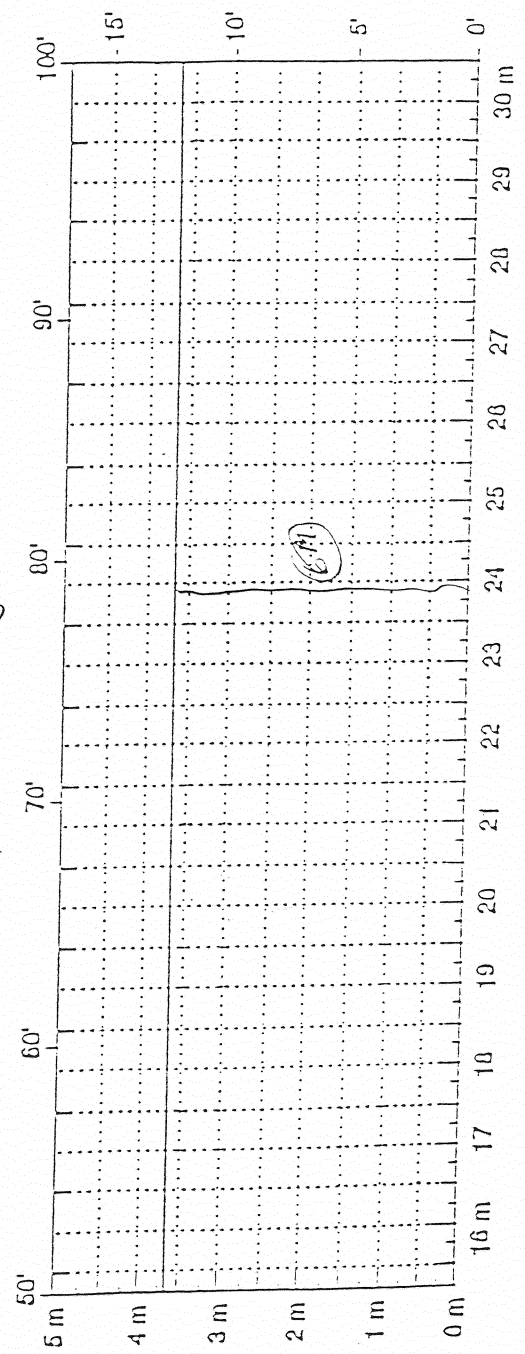


Comments: _____

State Assigned ID _____
 State Code 40
 SIIIP Section ID 0506

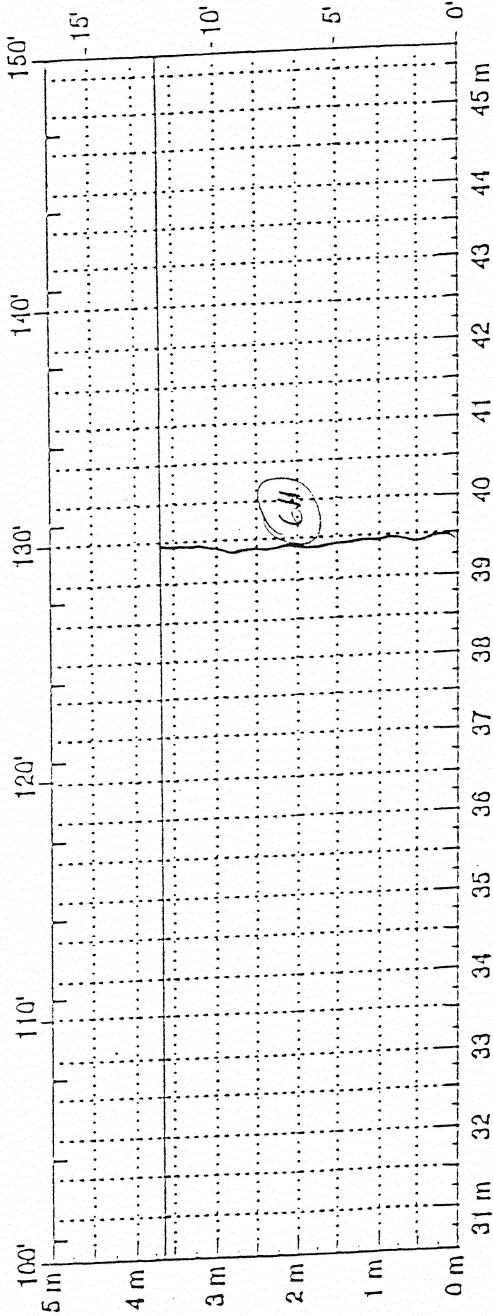


Comments:

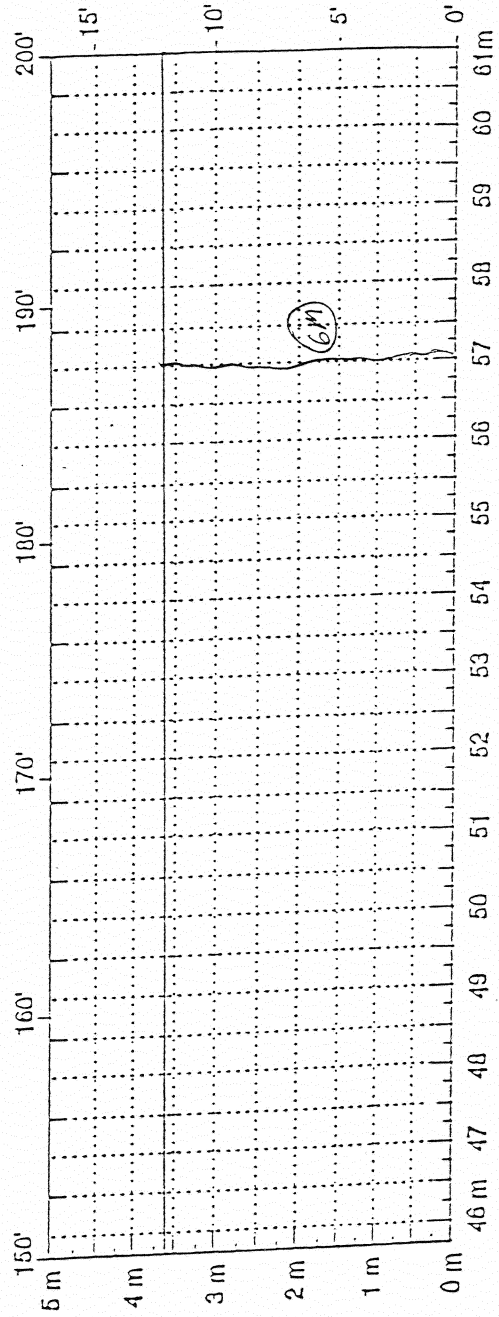


Comments:

State Assigned ID _____
 State Code 40
 SHIP Section ID 0506


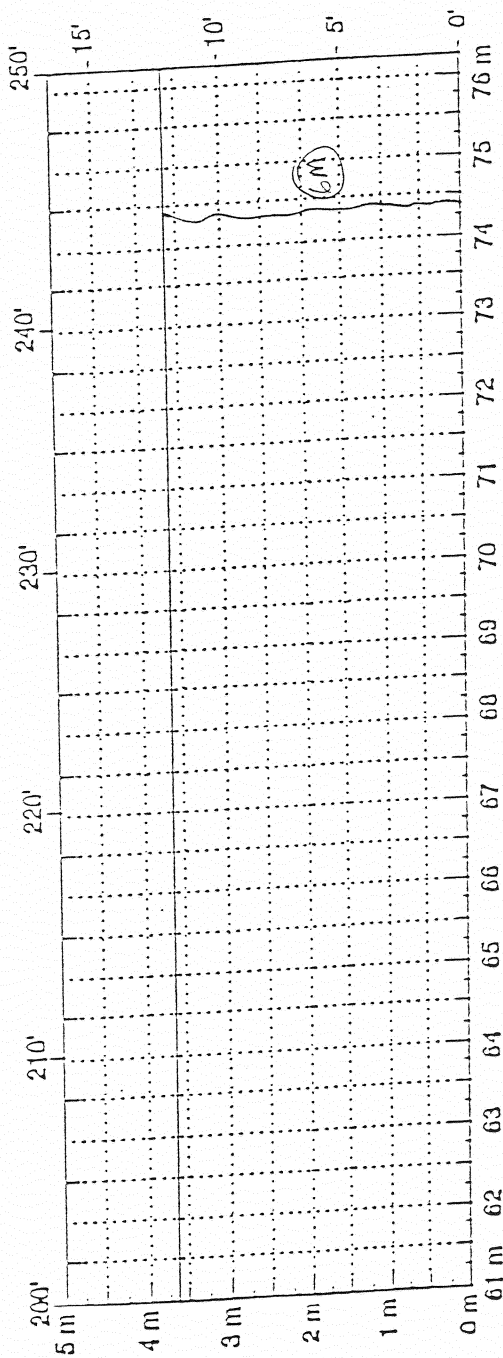


Comments: _____

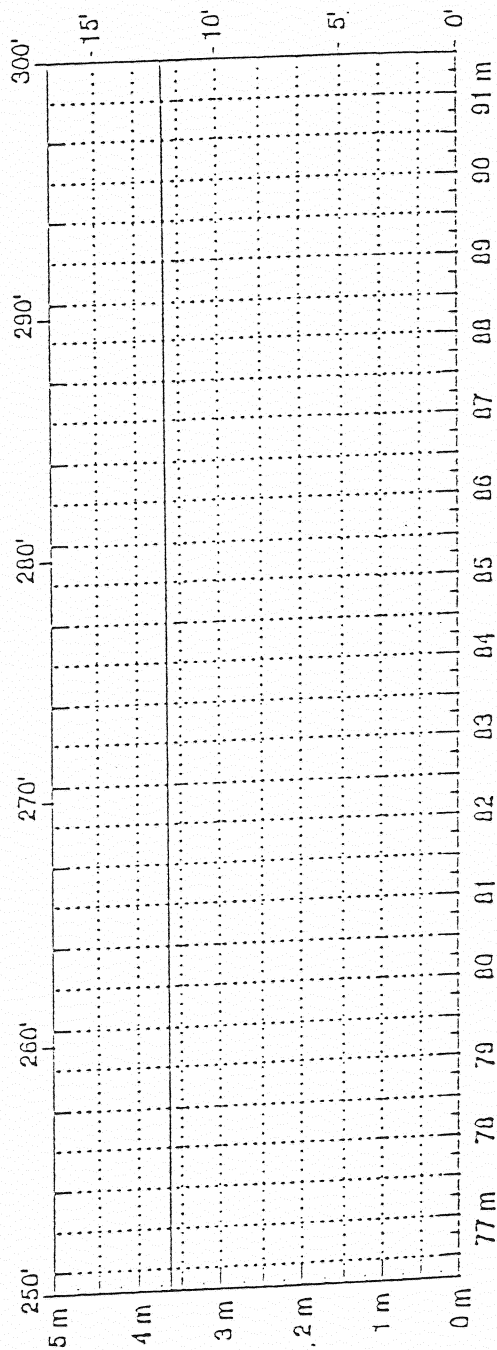

Comments: _____


State Assigned ID _____
 State Code 42
 SIIRP Section ID 0506

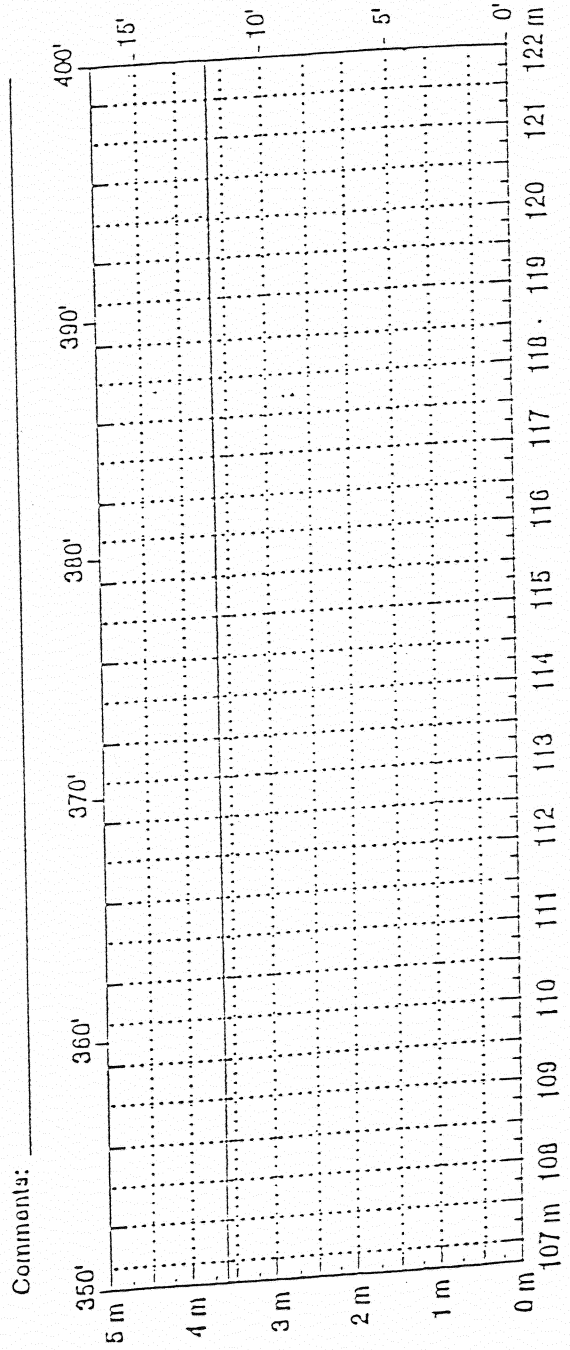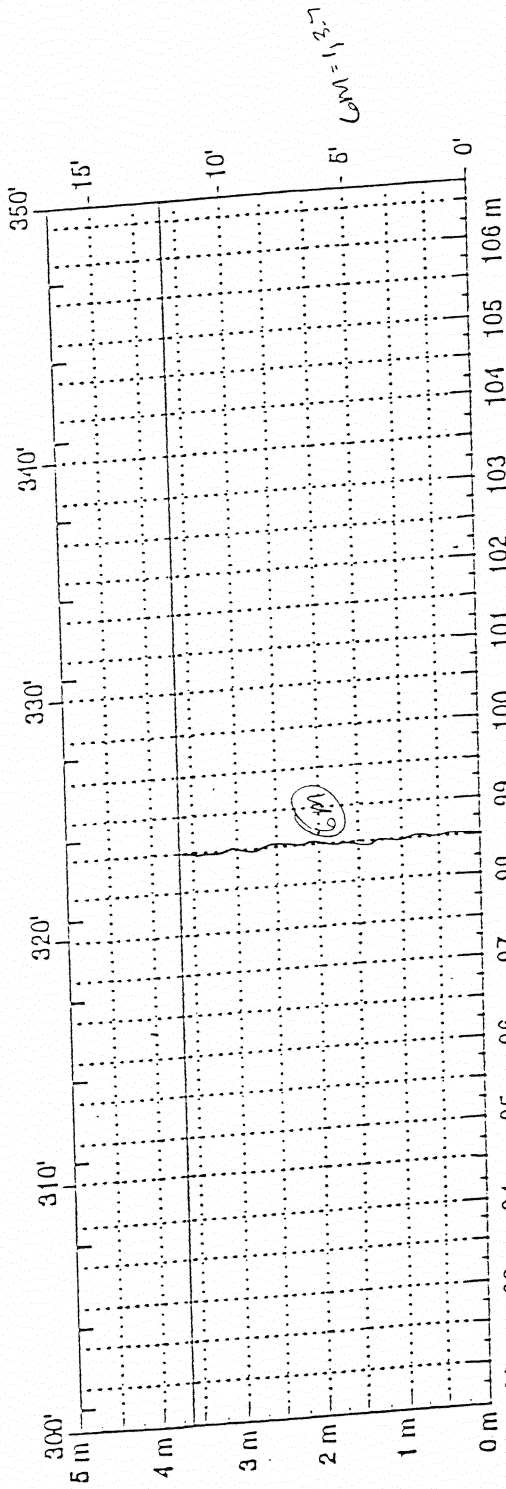


Comments: _____

Comments: _____

State Assigned ID 40
 State Code
 SIIRP Section ID 0507

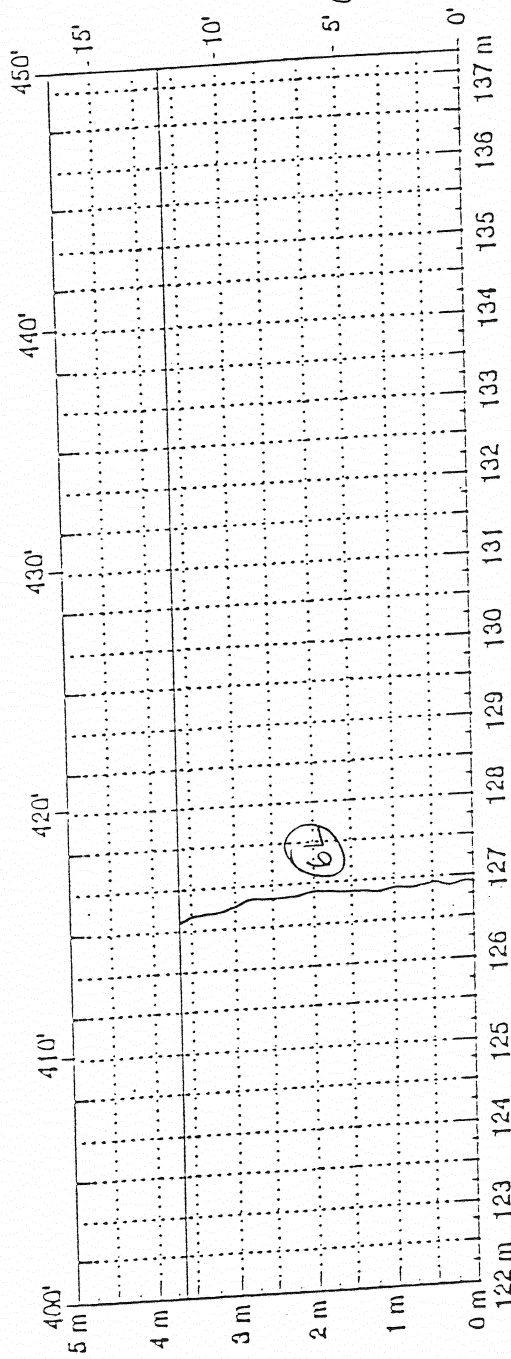

Comments:

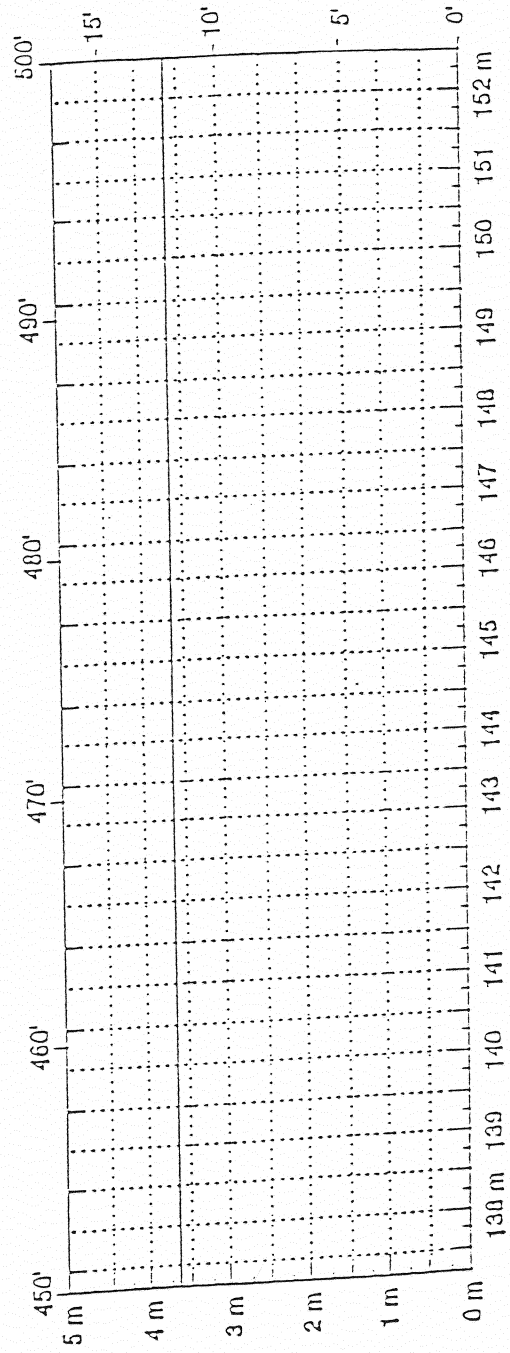

Comments:

LTPP Automated Dipstick Data Collection Transverse Profile Form DS-11 Zero and Calibration Checks	State Code [40] LTPP Section ID [0506] Date (dd/mm/yy) [06/17/97]
---	---

Operator: Tim Martin

Employer: BRE

Dipstick Serial Number: 30023

Pre Measurement Checks

Time (military): 14:40

Automatic Zero Performed: ☒

Calibration

Calibration Check	
Measurement	Reading (inches)
First Reading	.039
Second Reading on Calibration Block	.085
Second Reading - 0.125 - First Reading	.124

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Post Measurement Checks

Time (military): 15:25

Zero Check Acceptable: ☒

Calibration Check	
Measurement	Reading (inches)
First Reading	.040
Second Reading on Calibration Block	.084
Second Reading - 0.125 - First Reading	.124

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Comments

DATE: 6/11/96
 OPERATOR: TM
 RECORDER: MDS
 DIPSTICK SERIAL NUMBER: 30023

LAH VJ 4661 0712 1997 (A) H 17
 ENILED JUL 10 1997 A H

STATE CODE: 40

SHRP SECTION ID: 0506

DIPSTICK READING													TOTAL	SUM
LOCATION	1	2	3	4	5	6	7	8	9	10	11	12		
0+00	-011	-065	060	.233	144	000	-123	037	107	307	240	221		163
	015	071	-052	-233	-142	006	127	043	-102	-302	-237	-221		
0+50	-027	-032	110	230	138	012	084	-009	126	355	244	627		.011
(15m)	028	040	-100	-228	-134	-008	086	017	-121	-350	-286	-030		
1+00	-069	-039	052	178	176	-044	-072	-014	140	265	246	016		153
(30m)	068	046	-048	-173	-172	047	079	019	-134	-265	-246	-015		
1+50	053	-015	066	301	243	136	013	-051	083	257	291	106		081
(45m)	-050	018	-058	-293	-242	-131	-005	059	-077	-285	-288	-108		
(2+00)	064	075	117	266	307	174	066	003	100	261	323	126		059
(60m)	-061	-072	-110	-261	-303	-169	-060	-001	-089	-259	-313	-127		
2+50	151	000	062	262	313	176	014	-047	085	273	320	160		268
(75m)	-152	007	-053	-261	-314	-175	-039	049	-080	-278	-315	-161		
3+00	-085	-015	088	244	274	170	-034	-055	110	243	321	181		181
(90m)	082	060	-085	-243	-273	-165	037	057	-103	-241	-320	-181		
3+50	-008	-014	069	220	273	223	043	-035	116	293	415	371		057
(105m)	007	019	-065	-212	-266	-216	-078	038	-103	-281	-408	-370		
4+00	158	-044	147	255	331	257	122	026	126	310	385	440		664
(120m)	144	034	-136	-247	-327	-251	-115	-016	-116	-538	-378	-434		
4+50	164	073	053	245	348	246	116	-006	105	305	363	462		029
(135m)	114	-068	-045	-241	-347	-244	-112	014	-099	-249	-361	-403		
5+00	135	044	151	271	328	129	026	057	197	295	365	269		047
(150m)	-130	-046	-141	-272	-322	-124	-024	-054	-143	-287	-362	-265		

COMMENTS

RECEIVED JUN 3 0 1997

SHEET 1

DISTRESS SURVEY

LTPP PROGRAM

STATE ASSIGNED ID

STATE CODE 40

SHRP SECTION ID 0507

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR)

06/17/97

SURVEYORS: T J M, M J D PHOTOS, VIDEO, OR BOTH WITH SURVEY (P, V, B) B
PAVEMENT SURFACE TEMP - BEFORE 19°C; AFTER 20°C

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
CRACKING			
1. FATIGUE CRACKING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
2. BLOCK CRACKING (Square Meters)	<u>1</u>	<u>1</u>	<u>1</u>
3. EDGE CRACKING (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
4. LONGITUDINAL CRACKING (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
4a. Wheel Path Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
4b. Non-Wheel Path Length Sealed (Meters)	<u>1</u>	<u>26.3</u>	<u>1</u>
5. REFLECTION CRACKING AT JOINTS Number of Transverse Cracks	<u>0</u>	<u>0</u>	<u>0</u>
Transverse Cracking (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
Longitudinal Cracking (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
6. TRANSVERSE CRACKING Number of Cracks	<u>6</u>	<u>4</u>	<u>1</u>
Length (Meters)	<u>9.6</u>	<u>14.8</u>	<u>1</u>
Length Sealed (Meters)	<u>0</u>	<u>0</u>	<u>1</u>

PATCHING AND POTHOLES

7. PATCH/PATCH DETERIORATION (Number)	<u>0</u>	<u>0</u>	<u>0</u>
(Square Meters)	<u>1</u>	<u>1</u>	<u>1</u>
8. Potholes (Number)	<u>1</u>	<u>1</u>	<u>1</u>
(Square Meters)	<u>1</u>	<u>1</u>	<u>1</u>

ENTERED OCT 21 1997 J

REVIEWED JUL 21 1997 J D
REVIEWED JUL 17 1997 JP

Revised December 1, 1992

SHEET 2
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _____

STATE CODE 40

SHRP SECTION ID 0507

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/17/97

SURVEYORS: I J M. M J D

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
SURFACE DEFORMATION			
9. RUTTING - REFER TO SHEET 3 FOR SPS-3 OR Form S1 from Dipstick Manual			
10. SHOVING (Number) (Square Meters)			<u>0</u>
SURFACE DEFECTS			
11. BLEEDING (Square Meters)	<u>305.0</u>	<u>0</u>	
12. POLISHED AGGREGATE (Square Meters)			
13. RAVELING (Square Meters)	<u>0</u>	<u>0</u>	
MISCELLANEOUS DISTRESSES			
14. LANE-TO-SHOULDER DROPOFF - REFER TO SHEET 3			
15. WATER BLEEDING AND PUMPING (Number) Length of Affected Pavement (Meters)			
16. OTHER (Describe) _____			

SHEET 3
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _____
STATE CODE 40
SHRP SECTION ID 0507

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/17/97

SURVEYORS: I J M, M J D

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

9. RUTTING (FOR SPS-3 SITE SURVEYS)

INNER WHEEL PATH			OUTER WHEEL PATH		
Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)	Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)
1	0.	— — —	1	0.	— — —
2	15.25	— — —	2	15.25	— — —
3	30.5	— — —	3	30.5	— — —
4	45.75	— — —	4	45.75	— — —
5	61.	— — —	5	61.	— — —
6	76.25	— — —	6	76.25	— — —
7	91.5	— — —	7	91.5	— — —
8	106.75	— — —	8	106.75	— — —
9	122.	— — —	9	122.	— — —
10	137.25	— — —	10	137.25	— — —
11	152.5	— — —	11	152.5	— — —


SEE
DIPSTICK
DATA

14. LANE-TO-SHOULDER DROPOFF

Point No.	Point Distance ¹ Meters	Lane-to-Shoulder Dropoff (mm)
1	0.	— — —
2	15.25	— — —
3	30.5	— — —
4	45.75	— — —
5	61.	— — —
6	76.25	— — —
7	91.5	— — —
8	106.75	— — —
9	122.	— — —
10	137.25	— — —
11	152.5	— — —


Note 1: "Point Distance" is the distance in meters from the start of the test section to the point where the measurement was made. The values shown are SI equivalents of the 50 ft spacing used in previous surveys.

State Assigned ID _____
 date: 6/17/97 State Code 40
 Surveyors: TJM + MJD SRRP Section ID 0507

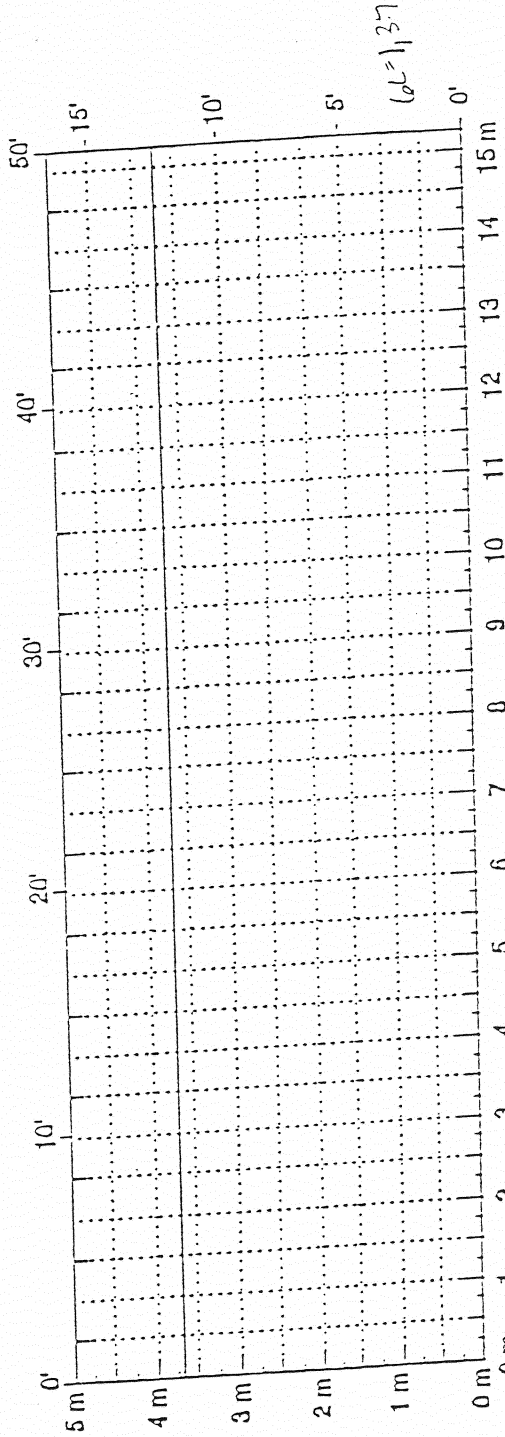

Totals:
 46m - 26.3m
 6L - 6, 9.6m
 6M - 4, 14.8m
 11L - 305 m²

Comments: Bleeding in both wheel-pulls throughout section. (11L)

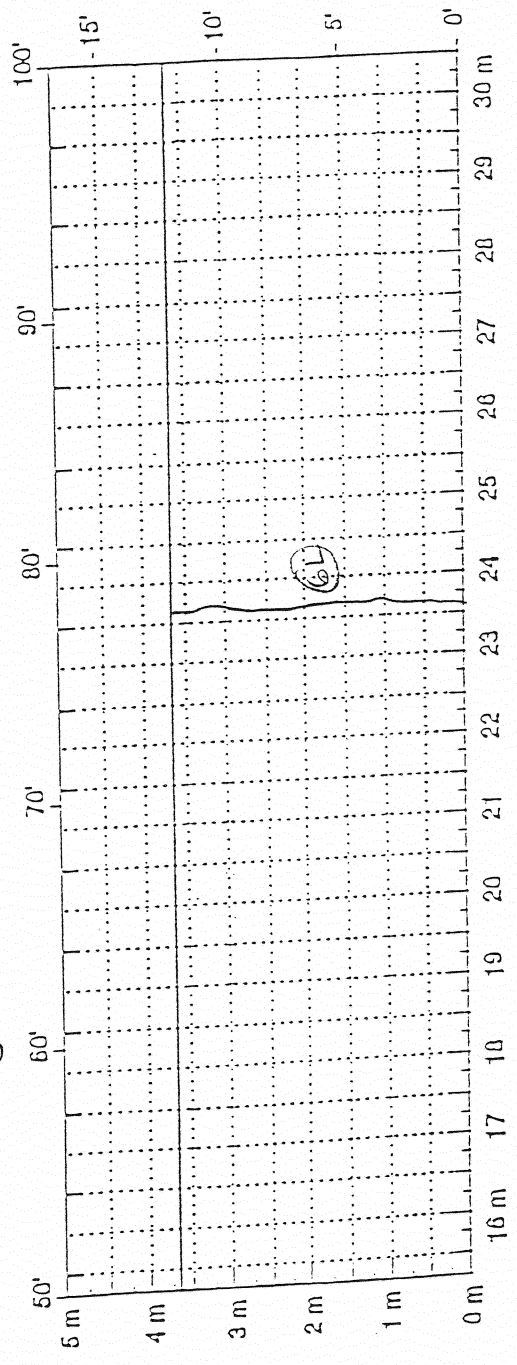


Comments: _____


State Assigned ID _____

State Code 40

SIIRP Section ID 0507

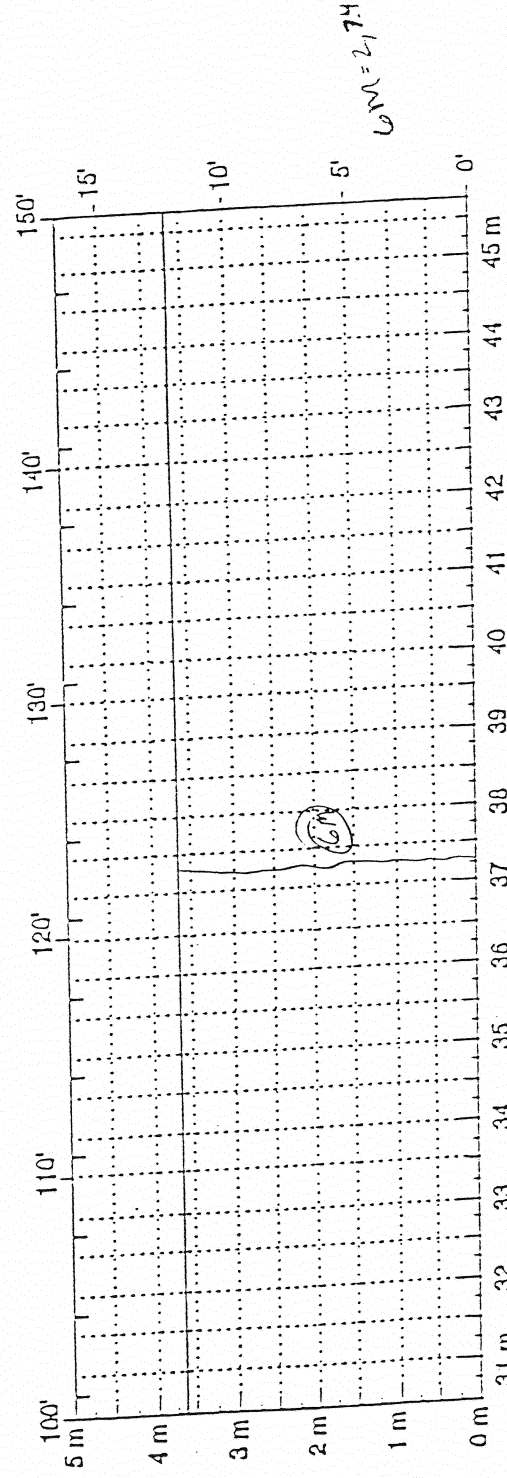

Comments: _____

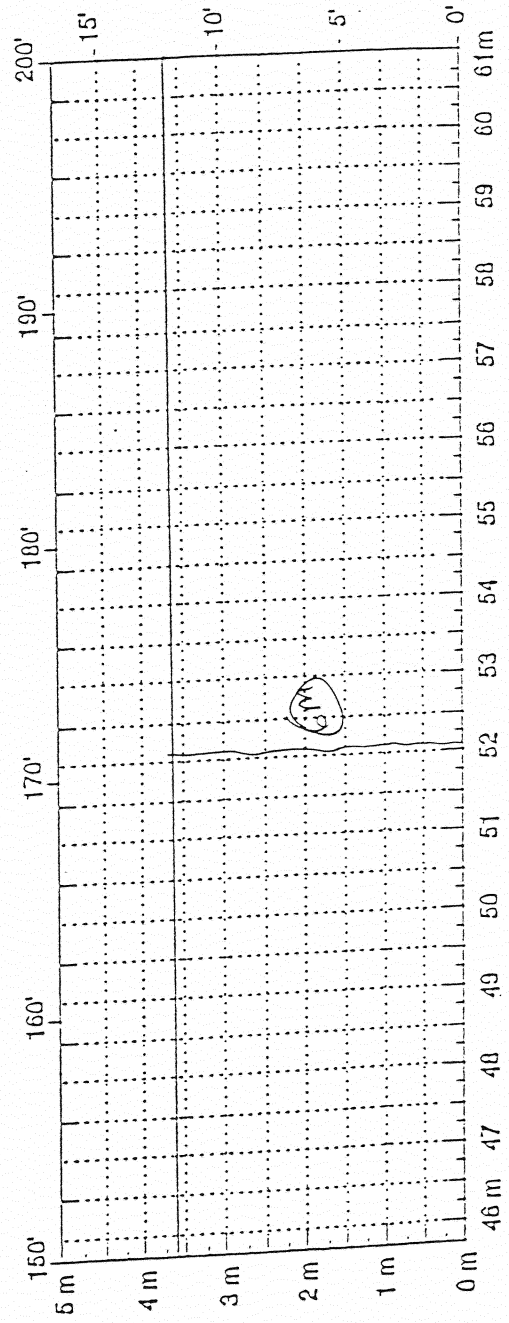


Comments: _____

State Assigned ID _____


State Code 40

SINP Section ID 0507

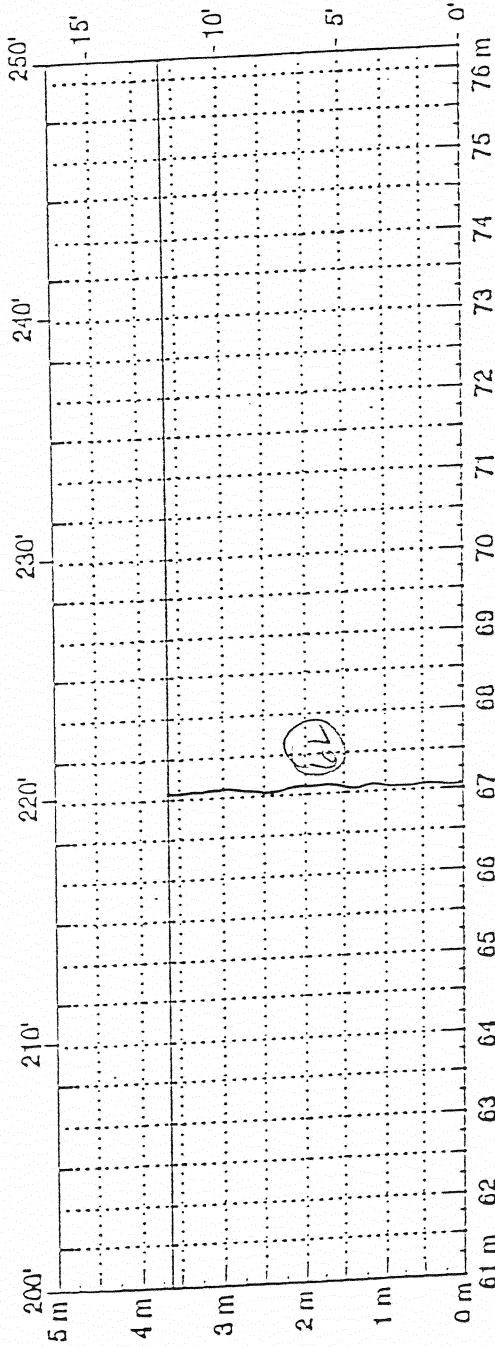



$62 = 214.7$
 $62 = 113.7$

Comments: _____

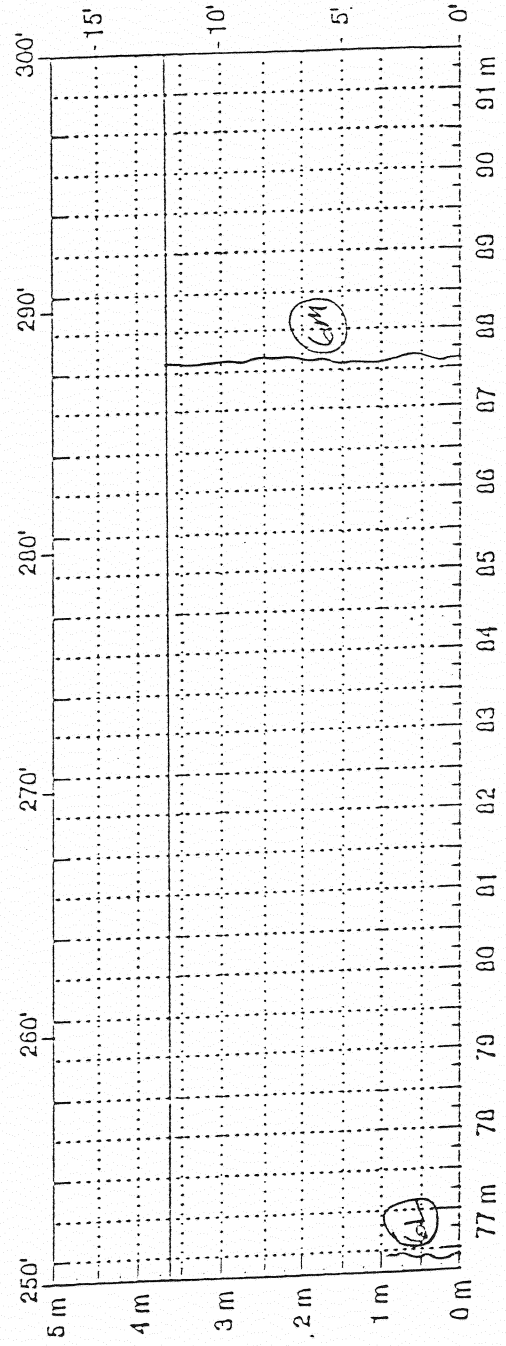

Comments: _____

State Assigned ID _____
 State Code 40
 SHRP Section ID 0507

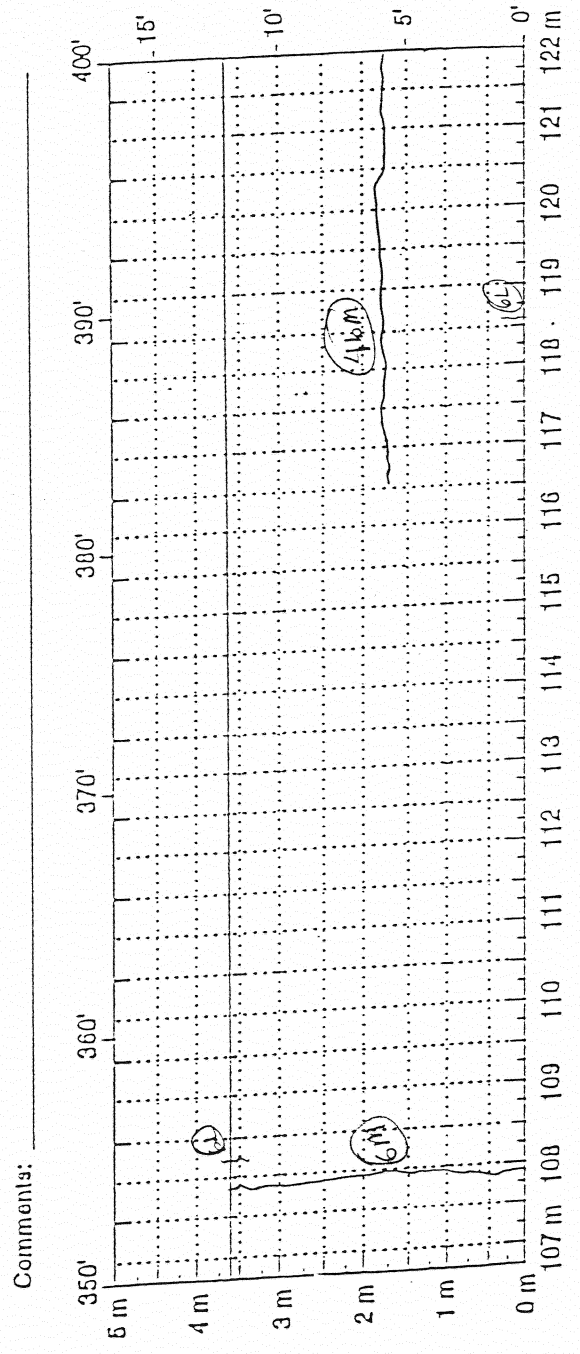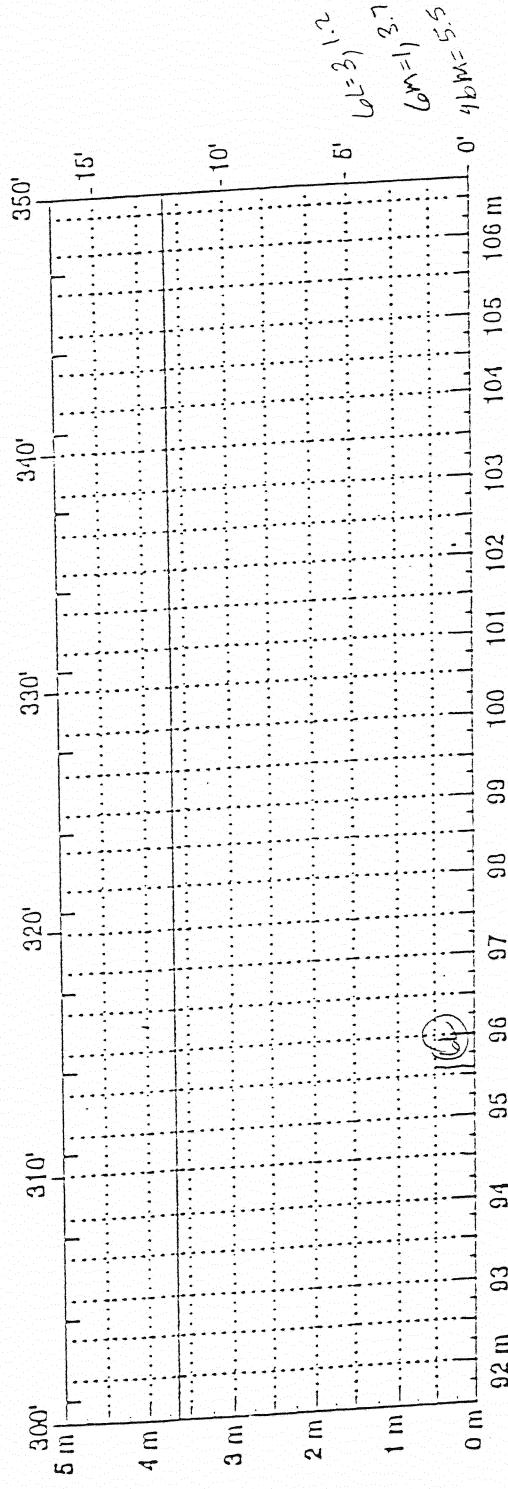


State Assigned ID

40


State Code

0507

SLIP Section ID

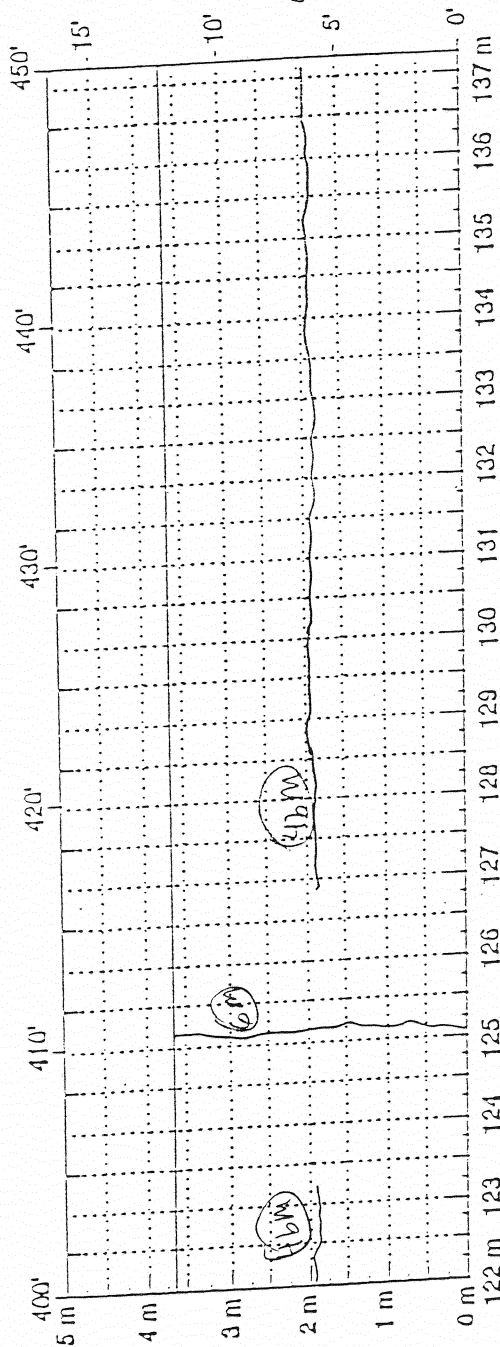

Comments:

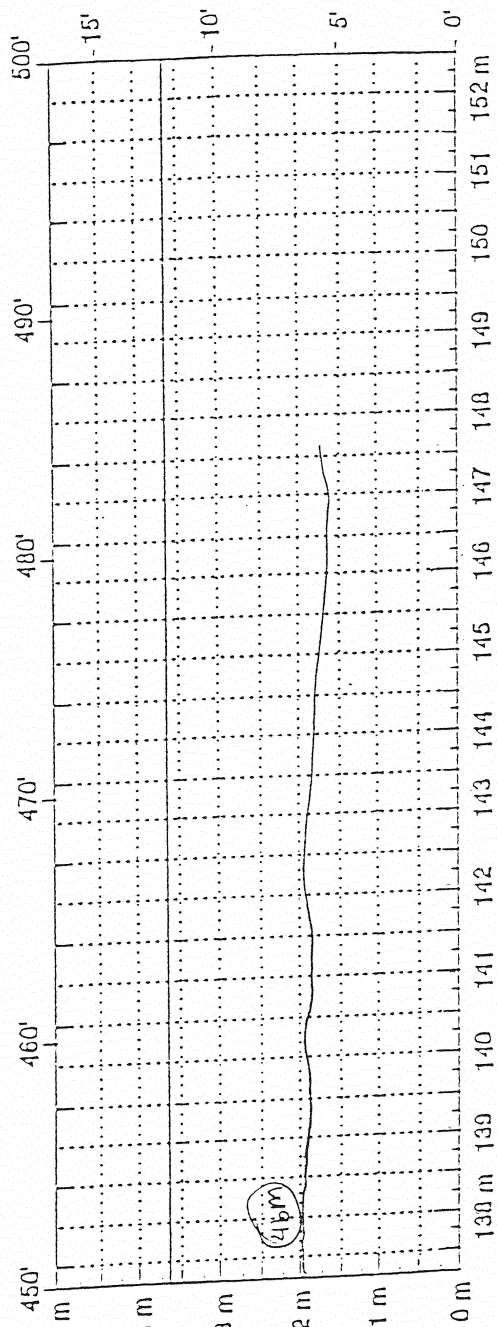

Comments:

LTPP Automated Dipstick Data Collection Transverse Profile Form DS-11 Zero and Calibration Checks	State Code [40] LTPP Section ID [0507] Date (dd/mm/yy) [6/17/97]
---	--

Operator: TSM / M.D.

Employer: BRE

Dipstick Serial Number: 30023

Pre Measurement Checks

Time (military): 17:05

Automatic Zero Performed:

Calibration

Calibration Check	
Measurement	Reading (inches)
First Reading	.035
Second Reading on Calibration Block	.167
Second Reading - 0.125 - First Reading	.126

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Post Measurement Checks

Time (military): 17:45

Zero Check Acceptable: ✓

Calibration Check	
Measurement	Reading (inches)
First Reading	.034
Second Reading on Calibration Block	.160
Second Reading - 0.125 - First Reading	.126

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Comments

EH V 666047 109907A "NE

EXPIRED JUL 10 1997 A II

STATE CODE: 40

SHRP SECTION ID: 0507

DATE: 6/17/97

OPERATOR: JWA

RECORDED: WJS

DIPSTICK SERIAL NUMBER: 26022

DIPSTICK READING													
LOCATION	1	2	3	4	5	6	7	8	9	10	11	12	TOTAL
0+00	183	061	095	210	291	186	058	+004	070	257	334	302	
	-176 ¹⁰	-051 ²⁹	-040 ²⁷	-204 ²⁹	-285 ¹³	-183 ¹²	-053 ⁹	-013 ⁴	-062 ¹³	-255 ⁵	-331 ³	-302 ²	.046
0+50	118	050	026	206	348	230	020	-042	075	300	370	348	
(15m)	-117 ⁴⁰	-047 ³⁷	-019 ³⁶	-205 ²⁷	-344 ²⁸	-227 ²¹	-040 ²¹	097 ¹¹	-072 ⁶	-294 ³	-371 ⁻³	-350 ⁻²	.040
1+00	032 ²⁸	013	086	239	242	133	064	-029	090	363	296	324 ²⁰	
(30m)	-034 ²⁴	-009 ³²	-083 ²⁴	-237 ²³	-241 ²¹	-130 ²⁰	-053 ¹⁷	+034 ¹¹	-088 ¹⁴	-260 ⁴	-293 ¹	-326 ²	.028
1+50	142	030	025	226	287	187	083	-048	088	278	327	280	
(45m)	-138 ⁵¹	-026 ⁴⁷	-021 ⁴⁵	-222 ³⁹	-283 ³⁵	-181 ³¹	-075 ²⁵	055 ¹⁷	-085 ¹⁰	-275 ⁷	-324 ⁵	-278 ²	.051
(2100)	179	037	074	316	323	253	094	-036	106	340	355	276	
(60m)	-184 ⁶³	-029 ⁶²	-028 ⁶⁰	-314 ⁵⁴	-316 ⁵²	-250 ⁴⁵	-082 ⁴²	045 ³⁰	-097 ²¹	-384 ¹²	-349 ¹⁰	-276 ⁰	.063
2+50	134	060	080	253	306	205	116	001	117	343	312	343	
(75m)	-133 ⁵⁵	-054 ⁵¹	-075 ⁴⁸	-248 ⁴³	-302 ³⁸	-201 ³¹	-114 ²⁰	-006 ³	-112 ¹³	-343 ²	-387 ⁸	-340 ³	.035
3+00	132	000	103	244	246	168	045	-060	078	413	384	316	
(90m)	-130 ⁵¹	-003 ⁵¹	-099 ⁵²	-288 ⁴⁸	-285 ⁴²	-167 ³¹	-040 ²⁰	063 ¹⁵	-075 ¹²	-406 ⁹	-381 ²	-317 ⁻¹	.031
3+50	158	016	058	324	240	078	-049	142	-008	140	102	317	
(105m)	-147 ⁴³	-012 ⁵⁴	-055 ⁵⁰	-319 ⁴⁷	-239 ⁴²	-075 ³¹	051 ¹⁸	-134 ¹⁶	012 ³	-135 ⁴	-104 ⁻¹	-316 ⁻¹	.045
4+00	242	174	307	288	478	127	000	020	136	468	262	218	
(120m)	-234 ³⁸	-175 ⁴¹	-302 ³⁵	-286 ³⁰	-480 ²²	-125 ¹⁰	-004 ⁻²	-020 ¹	-135 ²	-468 ¹	-260 ⁻¹	-219 ⁻¹	.012
4+50	071	176	259	241	365	225	093	016	098	029	146	206	
(135m)	-071 ²²	-175 ²²	-257 ¹⁶	-237 ¹¹	-363 ¹⁵	-225 ¹³	-041 ¹³	-015 ¹¹	-092 ¹⁰	-330 ⁴	-141 ⁵	-206 ⁻	.022
5+00	145	028	195	310	194	193	174	264	176	155	159	145	
(150m)	-145	-027 ²³	-189 ²¹	-309 ¹⁶	-194 ¹³	-185 ¹²	-170 ¹²	-262 ⁵	-177 ⁶	-750 ⁷	-160 ²	-142 ³	.023

COMMENTS

RECEIVED JUN 30 1997

SHEET 1

DISTRESS SURVEY

LTPP PROGRAM

STATE ASSIGNED ID

STATE CODE 40

SHRP SECTION ID 0508

ENTERED OCT 21 1997 J B

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR)

06/16/97

SURVEYORS: TJM, MJD PHOTOS, VIDEO, OR BOTH WITH SURVEY (P, V, B)
PAVEMENT SURFACE TEMP - BEFORE 49 °C; AFTER 48 °C

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
CRACKING			
1. FATIGUE CRACKING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
2. BLOCK CRACKING (Square Meters)	<u>1</u>	<u>1</u>	<u>1</u>
3. EDGE CRACKING (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
4. LONGITUDINAL CRACKING (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
4a. Wheel Path Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
4b. Non-Wheel Path Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
5. REFLECTION CRACKING AT JOINTS Number of Transverse Cracks	<u>1</u>	<u>1</u>	<u>1</u>
Transverse Cracking (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
Longitudinal Cracking (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
6. TRANSVERSE CRACKING Number of Cracks	<u>2</u>	<u>1</u>	<u>3</u>
Length (Meters)	<u>4.2</u>	<u>1</u>	<u>11.1</u>
Length Sealed (Meters)	<u>0</u>	<u>1</u>	<u>0</u>
PATCHING AND POTHOLES			
7. PATCH/PATCH DETERIORATION (Number)	<u>0</u>	<u>1</u>	<u>0</u>
(Square Meters)	<u>1</u>	<u>1</u>	<u>1</u>
8. Potholes (Number)	<u>1</u>	<u>1</u>	<u>1</u>
(Square Meters)	<u>1</u>	<u>1</u>	<u>1</u>

REVIEWED JUL 21 1997 J D
REVIEWED JUL 17 1997 JP

SHEET 2
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _ _ _ _

STATE CODE 40SHRP SECTION ID 0508DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/16/97SURVEYORS: T J M, M J O

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
SURFACE DEFORMATION			
9. RUTTING - REFER TO SHEET 3 FOR SPS-3 OR Form S1 from Dipstick Manual			
10. SHOVING (Number) (Square Meters)			<u>0</u> <u>0</u>
SURFACE DEFECTS			
11. BLEEDING (Square Meters)	<u>305.0</u>	<u>0</u>	<u>0</u>
12. POLISHED AGGREGATE (Square Meters)			<u>0</u>
13. RAVELING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
MISCELLANEOUS DISTRESSES			
14. LANE-TO-SHOULDER DROPOFF - REFER TO SHEET 3			
15. WATER BLEEDING AND PUMPING (Number) Length of Affected Pavement (Meters)			<u>0</u>
16. OTHER (Describe) _____			

Revised May 29, 1992

SHEET 3
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID — — — —

STATE CODE 40SHRP SECTION ID 0508DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/16/97SURVEYORS: TJM, MJD

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

9. RUTTING (FOR SPS-3 SITE SURVEYS)

INNER WHEEL PATH			OUTER WHEEL PATH		
Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)	Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)
1	0.	— — —	1	0.	— — —
2	15.25	— — —	2	15.25	— — —
3	30.5	— — —	3	30.5	— — —
4	45.75	— — —	4	45.75	— — —
5	61.	— — —	5	61.	— — —
6	76.25	— — —	6	76.25	— — —
7	91.5	— — —	7	91.5	— — —
8	106.75	— — —	8	106.75	— — —
9	122.	— — —	9	122.	— — —
10	137.25	— — —	10	137.25	— — —
11	152.5	— — —	11	152.5	— — —


14. LANE-TO-SHOULDER DROPOFF

Point No.	Point Distance ¹ Meters	Lane-to-Shoulder Dropoff (mm)
1	0.	— — 0.
2	15.25	— — 5.
3	30.5	— — 5.
4	45.75	— — 5.
5	61.	— — 5.
6	76.25	— — 5.
7	91.5	— — 5.
8	106.75	— — 5.
9	122.	— — 5.
10	137.25	— — 5.
11	152.5	— — 5.


Note 1: "Point Distance" is the distance in meters from the start of the test section to the point where the measurement was made. The values shown are SI equivalents of the 50 ft spacing used in previous surveys.

ENTERED OCT 21 1997 J. R

State Assigned ID _____
 date: 6/16/97
 State Code 40
 surveyors: TJM, MJD
 SIIIP Section ID 0508

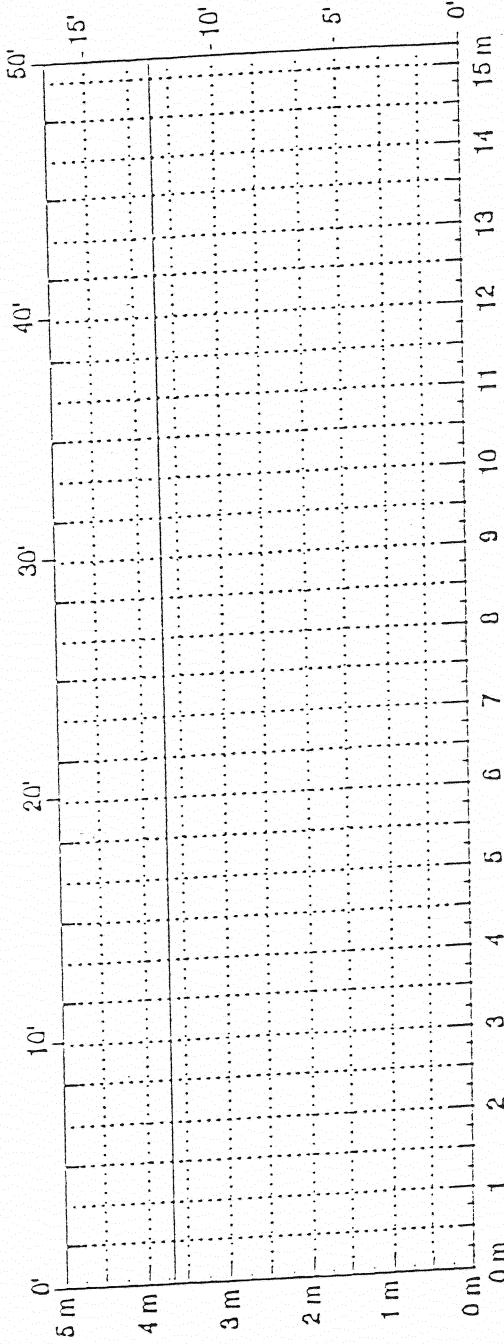


Comments: (112) Bleeding throughout section in both intercalaries.

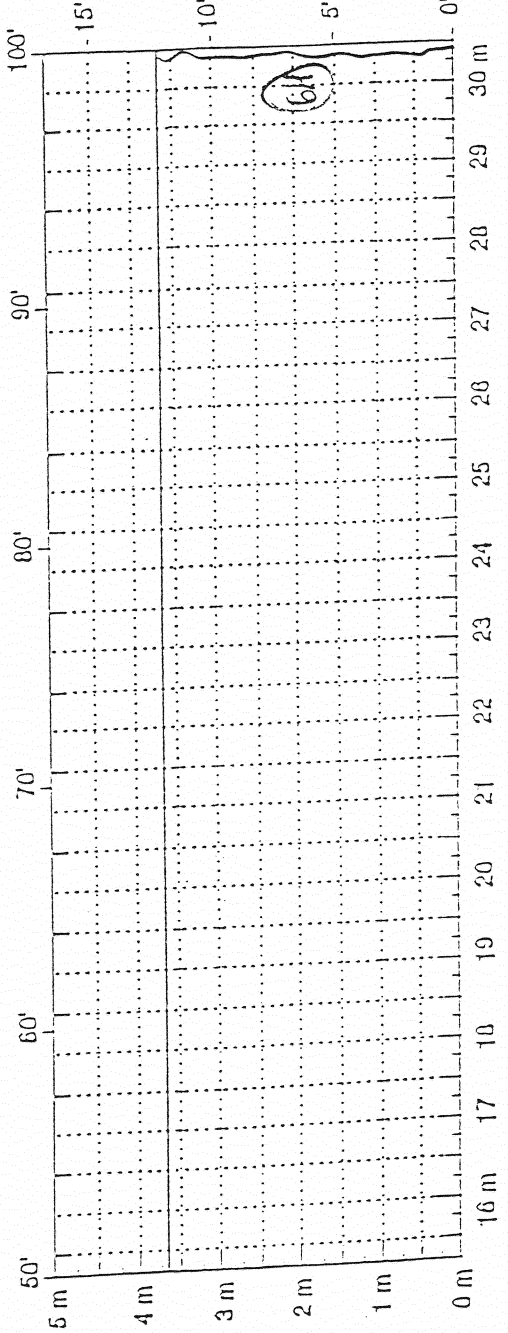


Comments: _____

Totals:
 64 - 2, 41.2 m
 64 - 3, 11.1
 112 - 305 m²

State Assigned ID _____
 State Code 40
 SHRP Section ID 0508


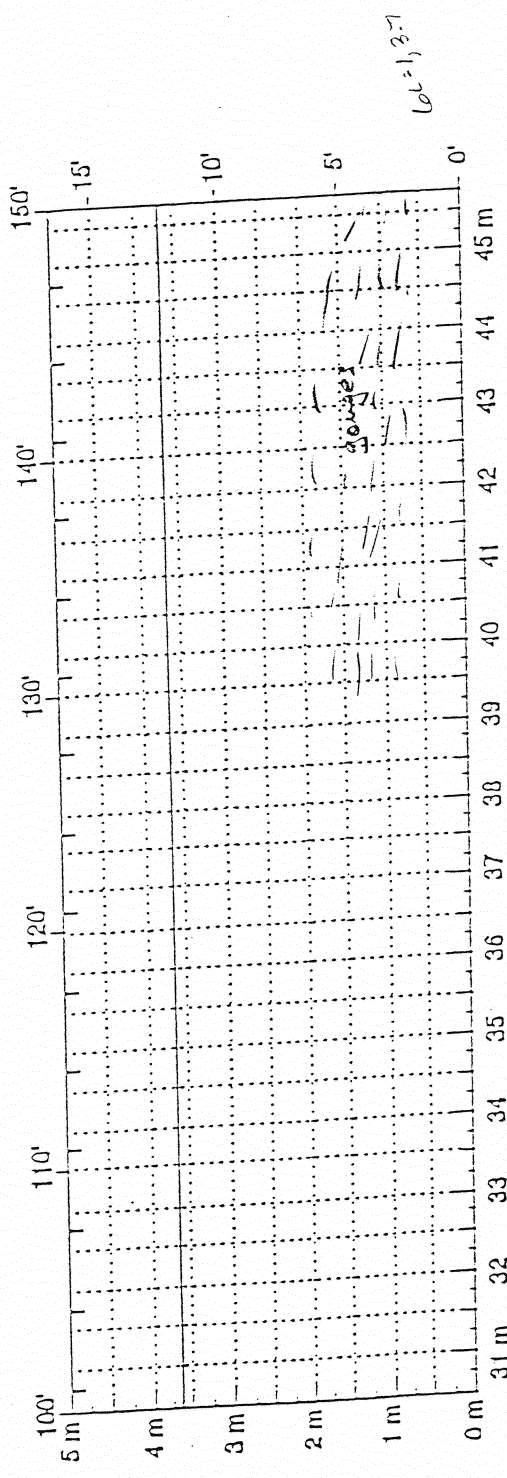


Comments:

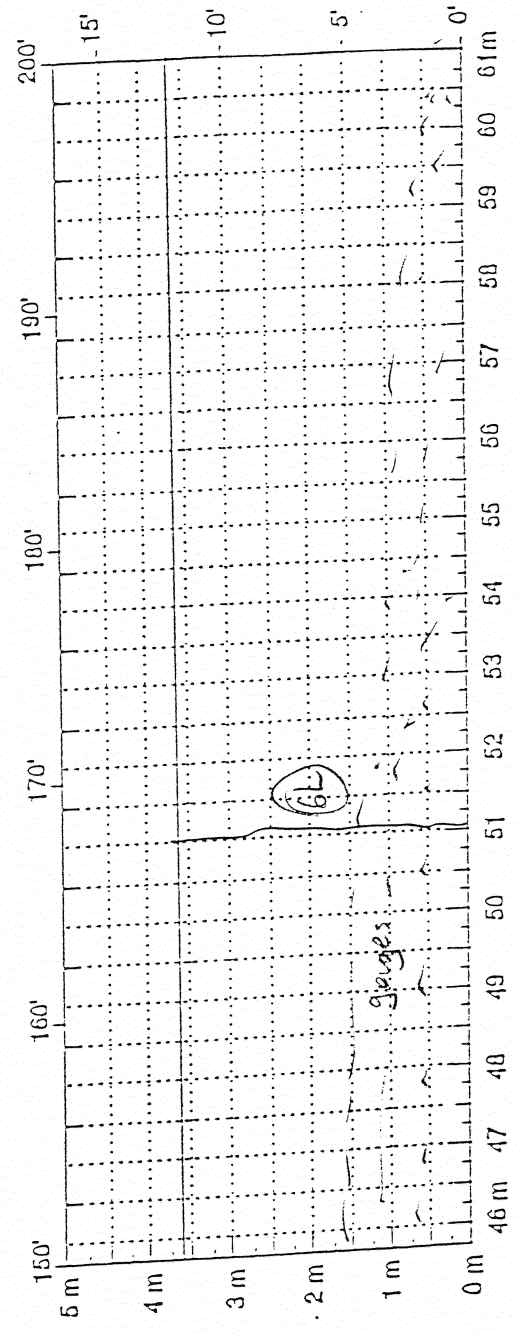

Comments:

State Assigned ID _____
 State Code 40
 SIPP Section ID 0508

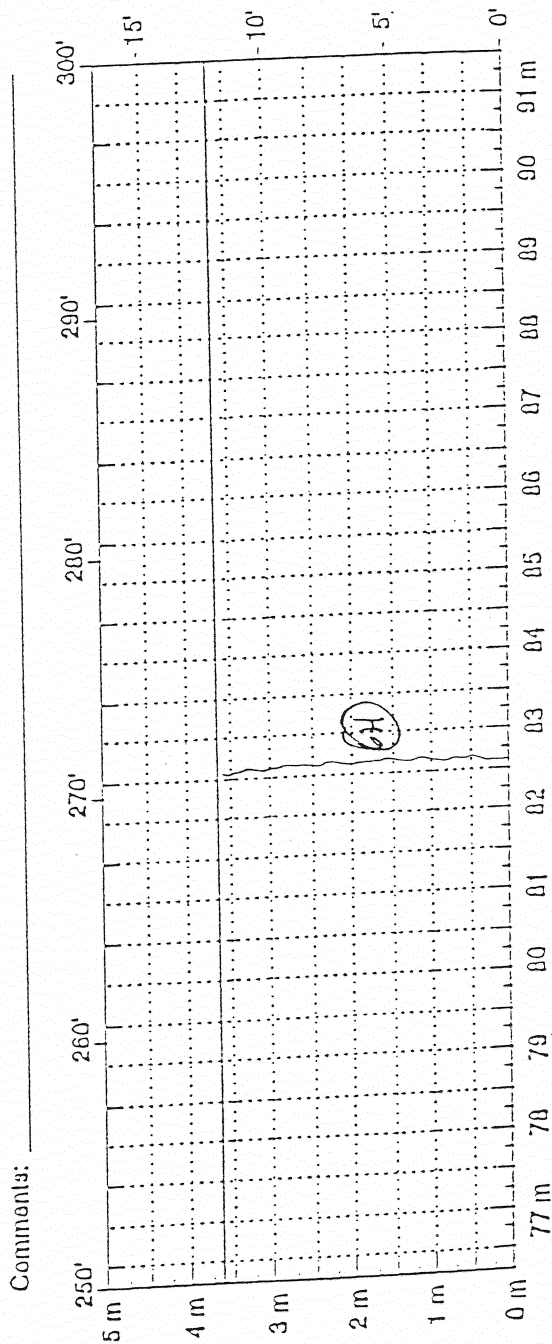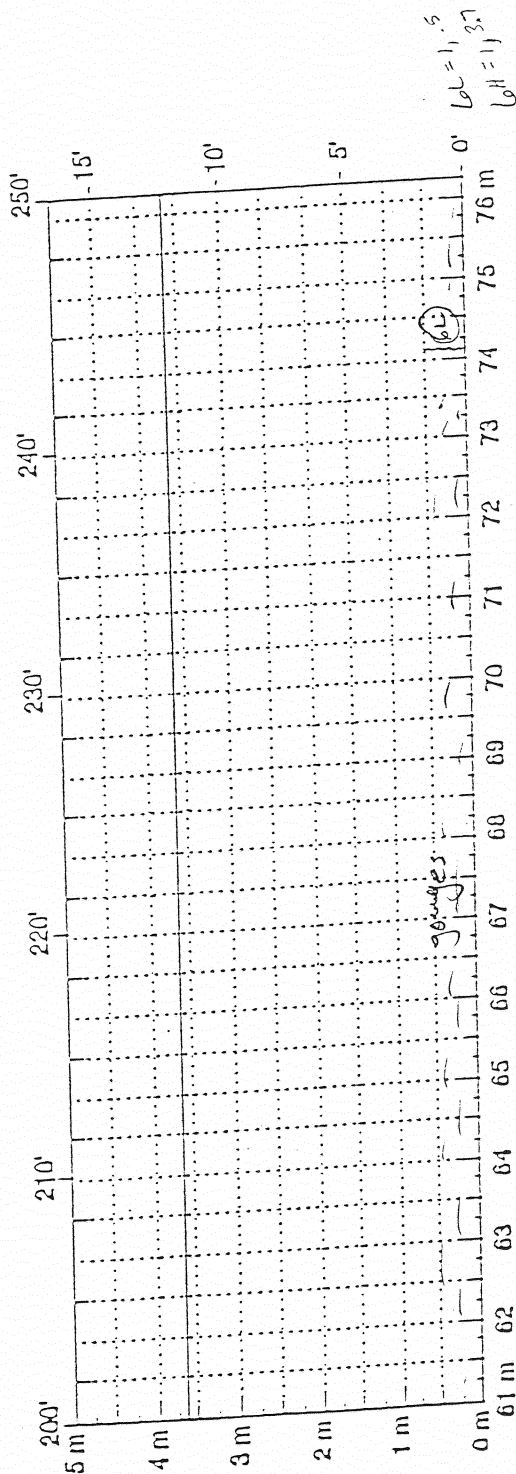

Comments:


Comments:

Stato Assigned ID


40

Stato Code

SIIRP Section ID 0508

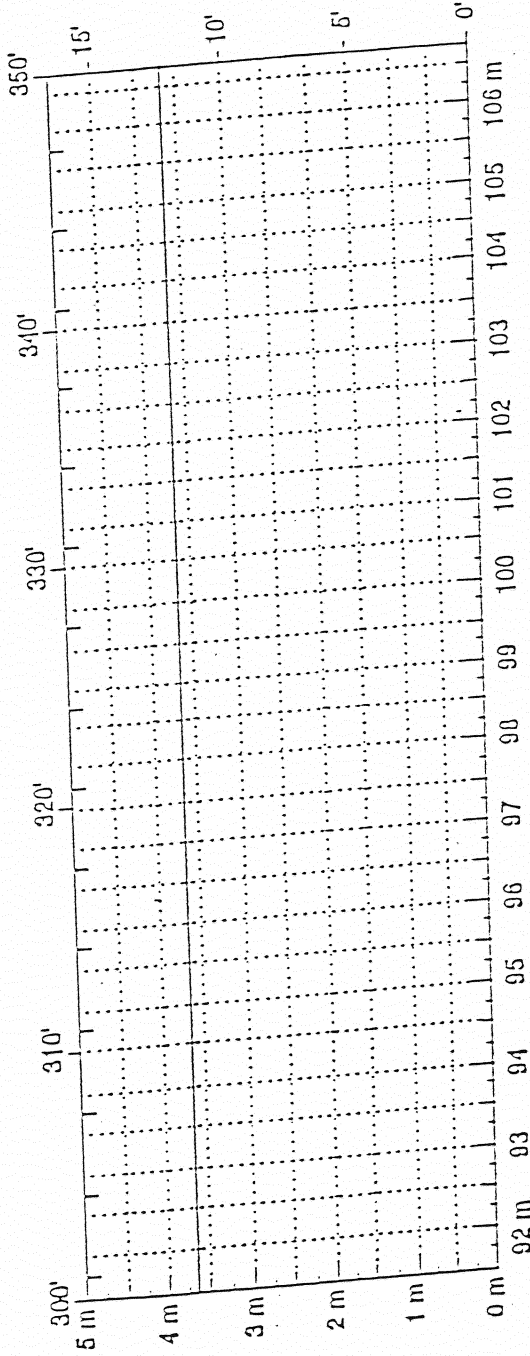


Comments:

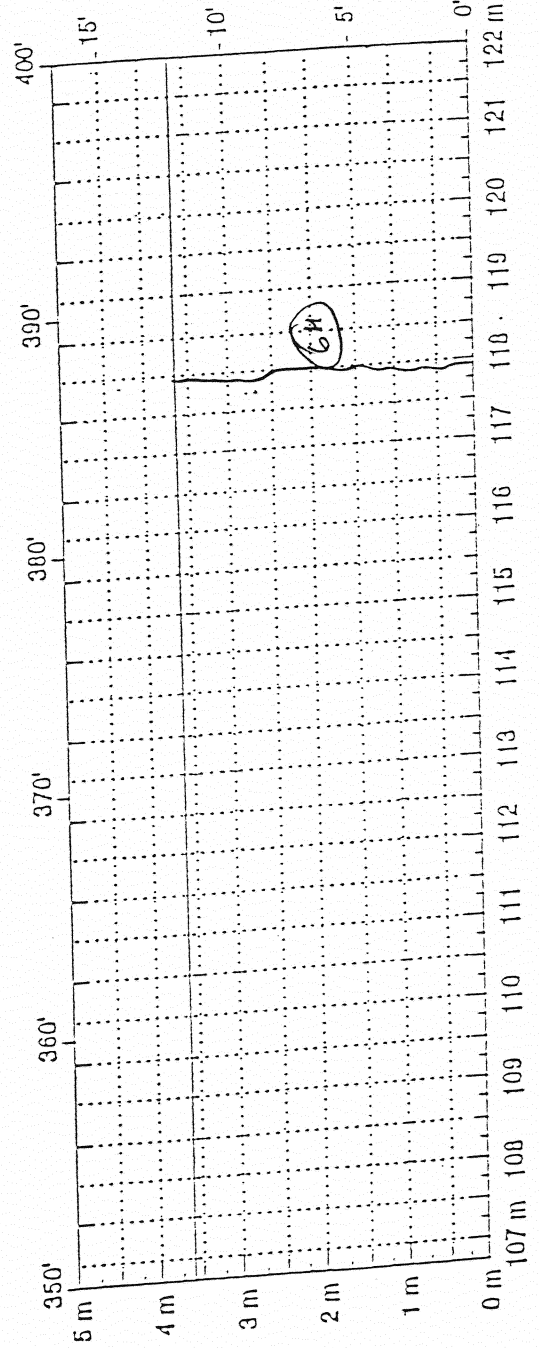


Comments:

State Assigned ID 40
 State Code
 SIPP Section ID 0508

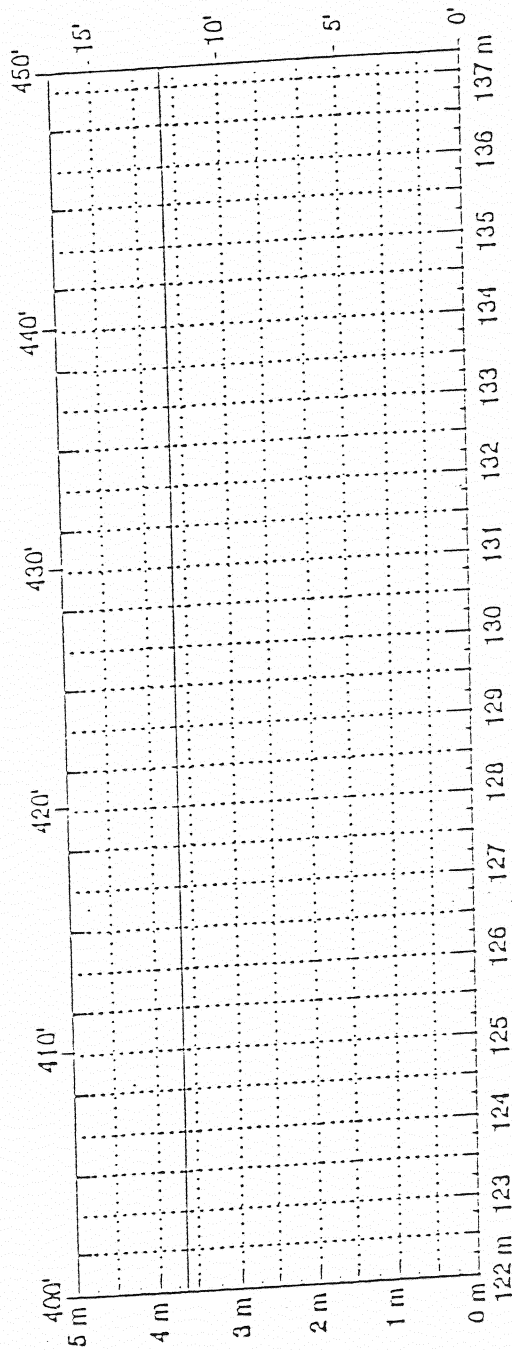

Comments:

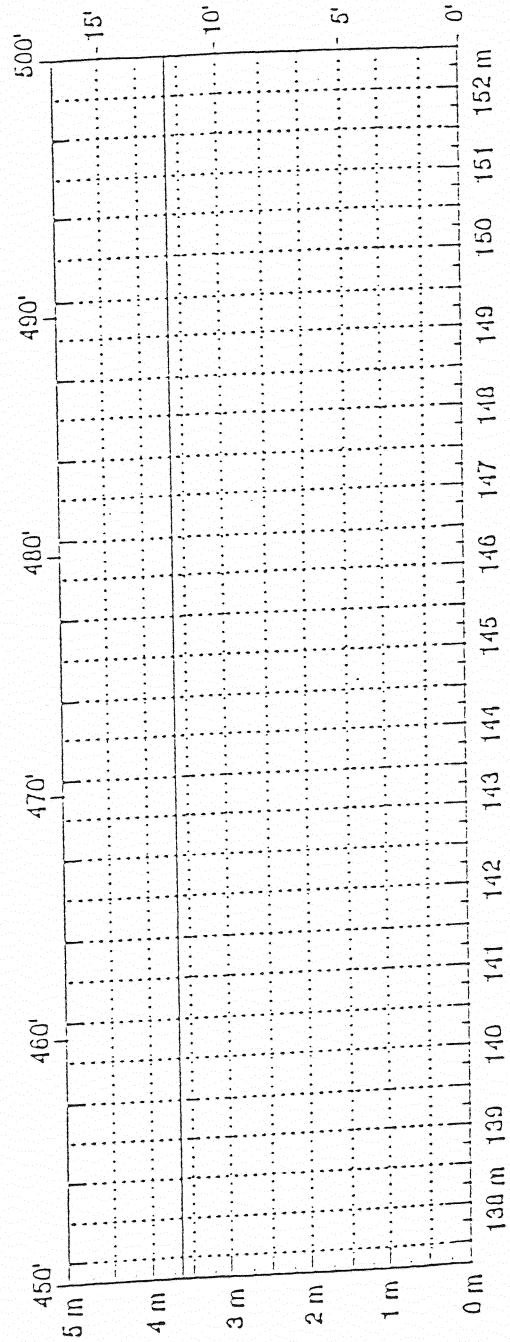

Comments:

LTPP Automated Dipstick Data Collection	State Code	[4 0]
Transverse Profile Form DS-11	LTPP Section ID	[0 5 0 8]
Zero and Calibration Checks	Date (dd/mm/yy)	[6 / 1 7 / 9 7]

Operator: Tim Martin Employer: BRE

Dipstick Serial Number: 30023

Pre Measurement Checks

Time (military): 1 1 : 0 0

Automatic Zero Performed:

Calibration

Calibration Check	
Measurement	Reading (inches)
First Reading	.404
Second Reading on Calibration Block	.529
Second Reading - 0.125 - First Reading	.125

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Post Measurement Checks

Time (military): 1 1 : 4 0

Zero Check Acceptable: ✓

Calibration Check	
Measurement	Reading (inches)
First Reading	.403
Second Reading on Calibration Block	.528
Second Reading - 0.125 - First Reading	.125

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Comments

DATE: 6/17/97

OPERATOR: T. M. M. M.

RECORDER: T. M. M. M.

DIPSTICK SERIAL NUMBER: 30212

FBI WADSWORTH 209977A - 11

STATE CODE: 40

SHIP SECTION I.D.: 0508

DIPSTICK READING

LOCATION	1	2	3	4	5	6	7	8	9	10	11	12	TOTAL	SUM
0100	139	035	101	232	095	-001	-106	-019	101	239	240	158		
	-140 ³¹	-034 ³²	-097 ³¹	-226 ²⁷	-095 ²¹	003 ²¹	112 ¹³	019 ¹³	-093 ¹³	-235 ⁵	-211 ¹	-156 ²	,034	
0150	090	041	131	254	208	091	-084	-049	063	234	295	326		
(15m)	-091 ⁷	-042 ³	-130 ⁹	-255 ⁸	-210 ¹	-089 ¹¹	090 ¹	050 ³	-067 ²	-227 ⁶	-249 ¹¹	-323 ³	,007	
1100	-242	798	036	410	373	164	127	103	082	395	453	534		
(30m)	242 ²¹	201 ²⁵	-029 ²⁰	-409 ¹⁹	-374 ¹³	-154 ¹⁰	-126 ⁹	-104 ⁸	-076 ⁴	-393 ³	-454 ¹	-532 ²	,029	
1150	170	082	131	264	285	148	-016	-067	098	217	312	315		
(45m)	-170 ²¹	-074 ³¹	-134 ²²	-256 ²⁵	-283 ¹⁷	-148 ¹⁵	023 ¹⁵	067 ³	-099 ³	-209 ¹	-309 ¹	-317 ¹¹	,030	
2100	212	024	101	314	299	242	024	047	114	309	265	341		
(60m)	-212 ²⁴	-020 ²³	-095 ²⁵	-310 ¹⁴	-298 ¹⁵	-239 ¹¹	-022 ¹¹	-047 ¹	-107 ¹	-307 ²	-266 ⁰	-343 ¹	,029	
2150	267	126	182	354	326	213	033	-024	118	271	323	301		
(75m)	-267 ²¹	-127 ²¹	-180 ²⁵	-350 ²³	-323 ¹¹	-212 ¹⁰	-031 ¹⁵	028 ¹⁵	-117 ⁹	-268 ⁸	-322 ⁵	-297 ⁴	,027	
3100	238	016	104	364	377	258	077	-011	152	410	346	420		
(90m)	-242 ²⁶	-012 ³²	-103 ³²	-362 ²⁹	-375 ³³	-257 ²⁷	-072 ²⁰	-015 ⁵¹	-154 ¹¹	-396 ¹³	-397 ¹¹	-420 ⁶	,028	
3150	128	004	121	267	272	255	054	014	162	316	284	259		
(105m)	-126 ¹¹	-003 ³¹	-120 ³	-268 ¹	-270 ³	-254 ⁶	-052 ⁵	-022 ³	-160 ¹¹	-311 ⁹	-295 ⁴	-246 ¹³	,011	
4100	116	022	116	233	188	103	091	014	123	300	263	234		
(120m)	-115 ²¹	-018 ³⁵	-115 ³¹	-234 ³⁰	-184 ³¹	-098 ³²	095 ²⁷	-005 ²³	-123 ¹⁴	-240 ¹⁴	-262 ¹¹	-231 ³	,036	
4150	060	047	130	213	172	090	-073	040	135	285	265	198		
(135m)	-055 ³²	-044 ²⁷	-125 ²⁴	-212 ¹³	-172 ¹³	-089 ¹³	078 ¹¹	-036 ¹²	-137 ³	-276 ¹²	-264 ¹	-198 ²	,032	
5100	126	072	157	293	214	057	-114	058	181	311	250	085		
(150m)	-125 ¹¹	-065 ¹¹	-179 ¹¹	-292 ³³	-210 ²¹	-052 ²¹	118 ²³	-052 ¹¹	-175 ¹²	-306 ⁷	-252 ²	-081 ¹¹	,049	

COMMENTS

RECEIVED JUN 30 1997

SHEET 1

DISTRESS SURVEY

LTPP PROGRAM

STATE ASSIGNED ID

STATE CODE 40

SHRP SECTION ID 0509

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/17/97

SURVEYORS: T J M, M J D PHOTOS, VIDEO, OR BOTH WITH SURVEY (P, V, B) B
PAVEMENT SURFACE TEMP - BEFORE 18°C; AFTER 19°C

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
CRACKING			
1. FATIGUE CRACKING (Square Meters)	0	0	0
2. BLOCK CRACKING (Square Meters)			
3. EDGE CRACKING (Meters)			
4. LONGITUDINAL CRACKING (Meters)			
4a. Wheel Path Length Sealed (Meters)			
4b. Non-Wheel Path Length Sealed (Meters)			
5. REFLECTION CRACKING AT JOINTS Number of Transverse Cracks			
Transverse Cracking (Meters)			
Length Sealed (Meters)			
Longitudinal Cracking (Meters)			
Length Sealed (Meters)			
6. TRANSVERSE CRACKING Number of Cracks	5	3	
Length (Meters)	15.8	11.1	
Length Sealed (Meters)	0	0	
PATCHING AND POTHOLES			
7. PATCH/PATCH DETERIORATION (Number)	0	0	
(Square Meters)			
8. Potholes (Number)			
(Square Meters)			

REVIEWED JUL 21 1997 J D
REVIEWED JUL 17 1997 JP

ENLINED OCT 21 1997 J B

Revised December 1, 1992

SHEET 2
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _____

STATE CODE

40

SHRP SECTION ID

0509

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/17/97

SURVEYORS: T J M, M J D

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
SURFACE DEFORMATION			
9. RUTTING - REFER TO SHEET 3 FOR SPS-3 OR Form S1 from Dipstick Manual			
10. SHOVING (Number) (Square Meters)			<u>0</u>
SURFACE DEFECTS			
11. BLEEDING (Square Meters)	<u>305.0</u>	<u>0</u>	<u>0</u>
12. POLISHED AGGREGATE (Square Meters)			<u>0</u>
13. RAVELING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
MISCELLANEOUS DISTRESSES			
14. LANE-TO-SHOULDER DROPOFF - REFER TO SHEET 3			
15. WATER BLEEDING AND PUMPING (Number) Length of Affected Pavement (Meters)			<u>0</u>
16. OTHER (Describe) _____			

Revised May 29, 1992

SHEET 3
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _____

STATE CODE 40

SHRP SECTION ID 0509

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/17/97

SURVEYORS: TJM, MJD

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

9. RUTTING (FOR SPS-3 SITE SURVEYS)

INNER WHEEL PATH			OUTER WHEEL PATH		
Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)	Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)
1	0.	— — —	1	0.	— — —
2	15.25	— — —	2	15.25	— — —
3	30.5	— — —	3	30.5	— — —
4	45.75	— — —	4	45.75	— — —
5	61.	— — —	5	61.	— — —
6	76.25	— — —	6	76.25	— — —
7	91.5	— — —	7	91.5	— — —
8	106.75	— — —	8	106.75	— — —
9	122.	— — —	9	122.	— — —
10	137.25	— — —	10	137.25	— — —
11	152.5	— — —	11	152.5	— — —

SEE
DIPSTICK
DATA


14. LANE-TO-SHOULDER DROPOFF

Point No.	Point Distance ¹ Meters	Lane-to-Shoulder Dropoff (mm)
1	0.	— — 0.
2	15.25	— — 1.
3	30.5	— — 1.
4	45.75	— — 1.
5	61.	— — 1.
6	76.25	— — 1.
7	91.5	— — 1.
8	106.75	— — 1.
9	122.	— — 1.
10	137.25	— — 1.
11	152.5	— — 1.


Note 1: "Point Distance" is the distance in meters from the start of the test section to the point where the measurement was made. The values shown are SI equivalents of the 50 ft spacing used in previous surveys.

ENL 21 OCT 21 1997 J. B

Station Assigned ID _____
 Station Code 40
 date: 6/17/97
 Surveyors: TJM, MJD
 SIIIP Section ID 0509

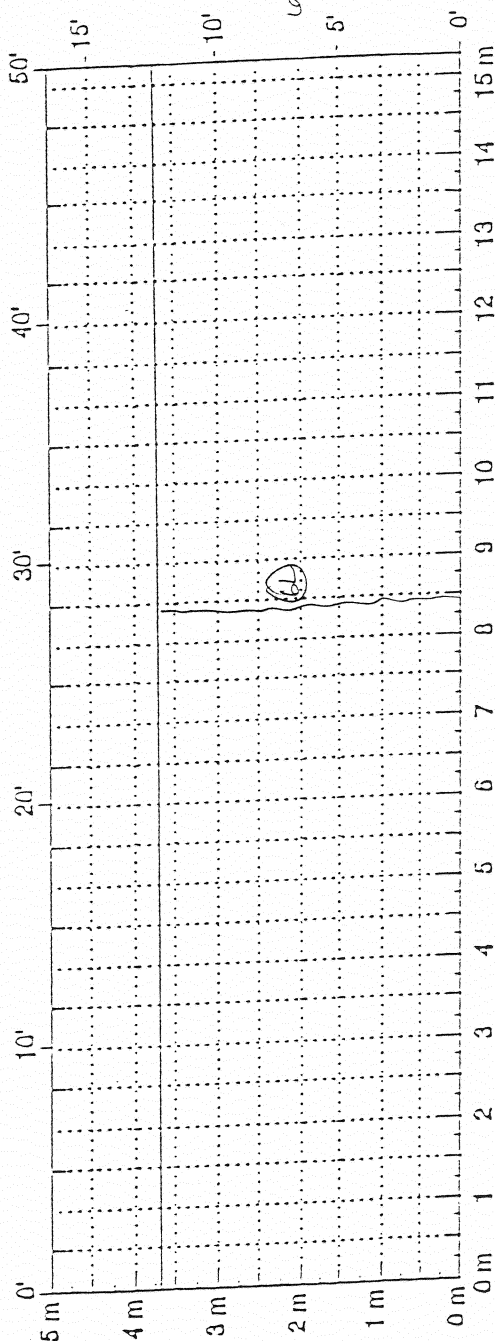

Totals:
 6L - 5, 15.8 m
 6M - 3, 11.1 m
 11L - 30.5 m

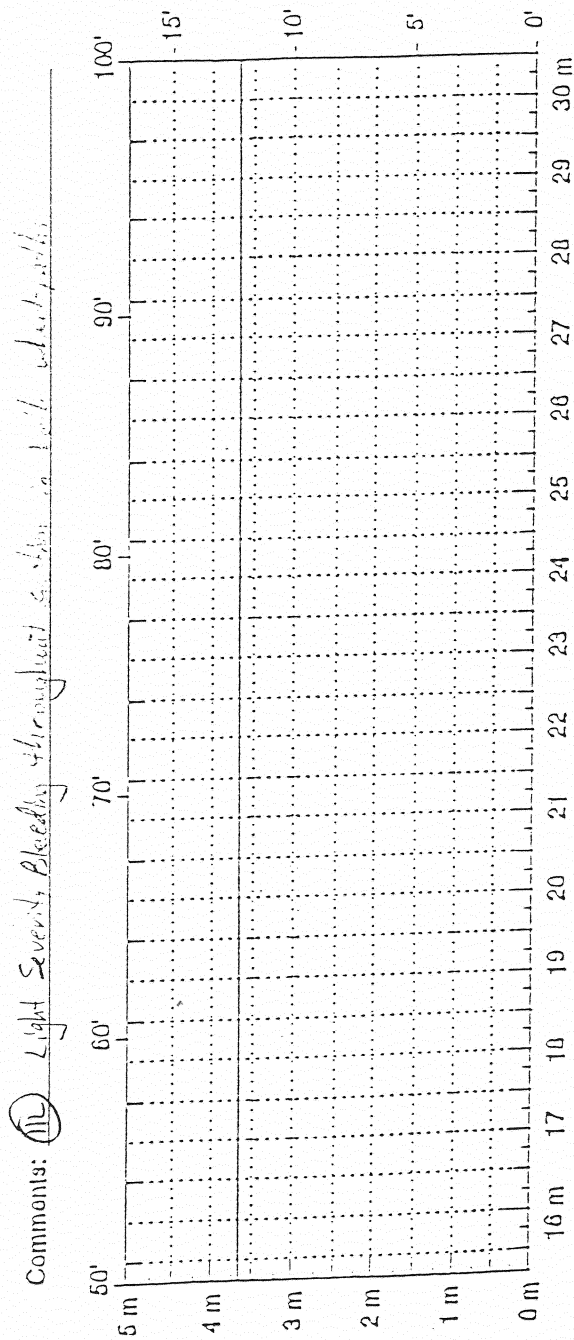


Comments: _____


State Assigned ID _____

State Code 40

SIIRP Section ID 0509

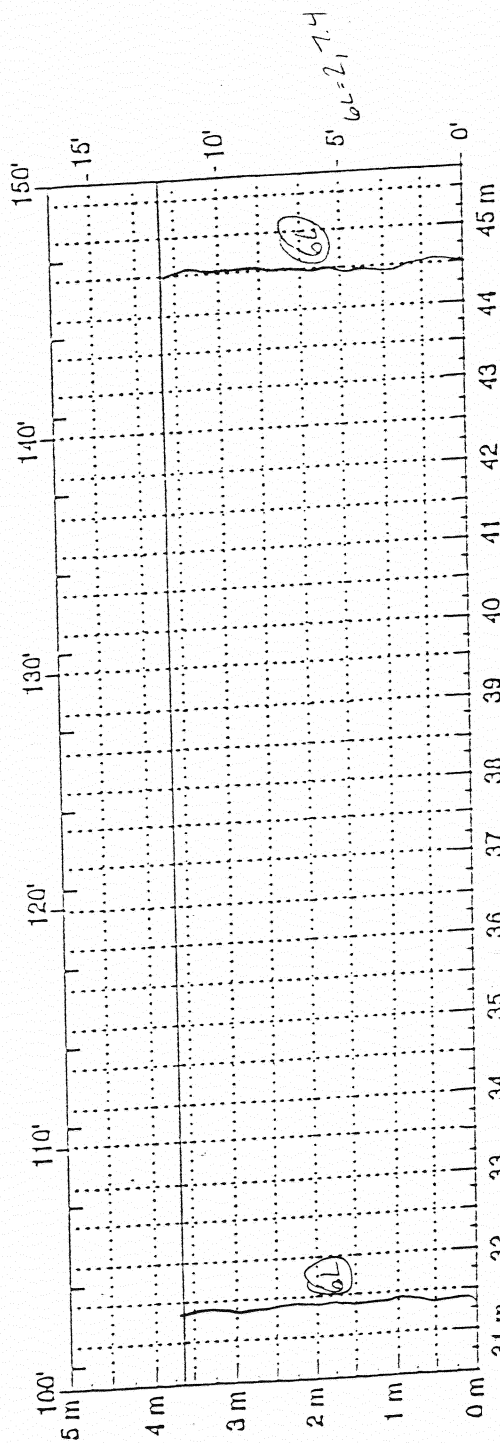


Comments: _____

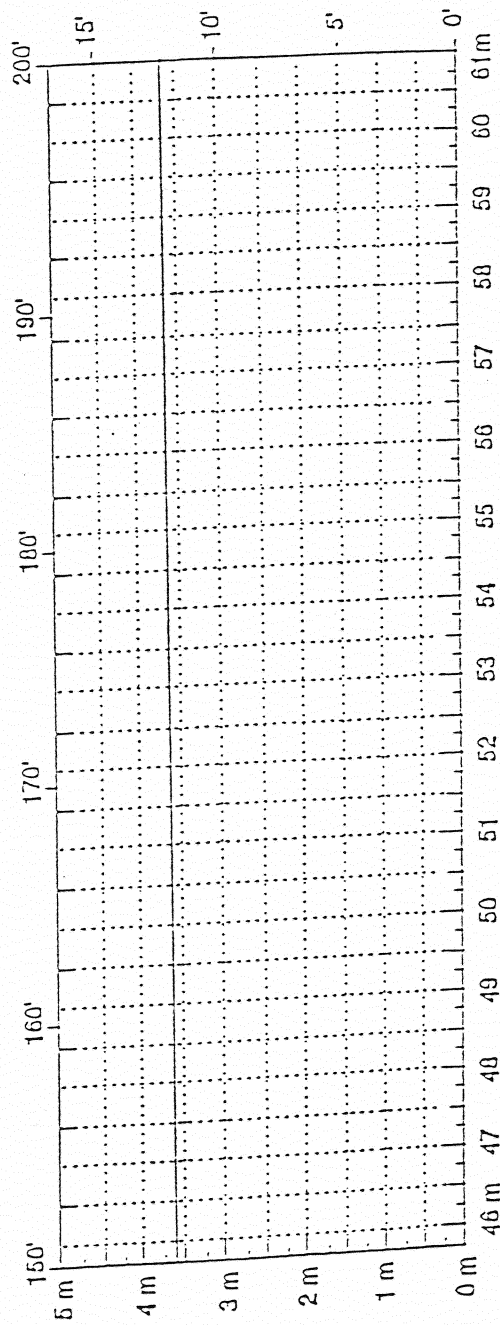


Comments: _____

Stato Assigned ID _____
 Stato Coda 40
 SINP Section ID 0509

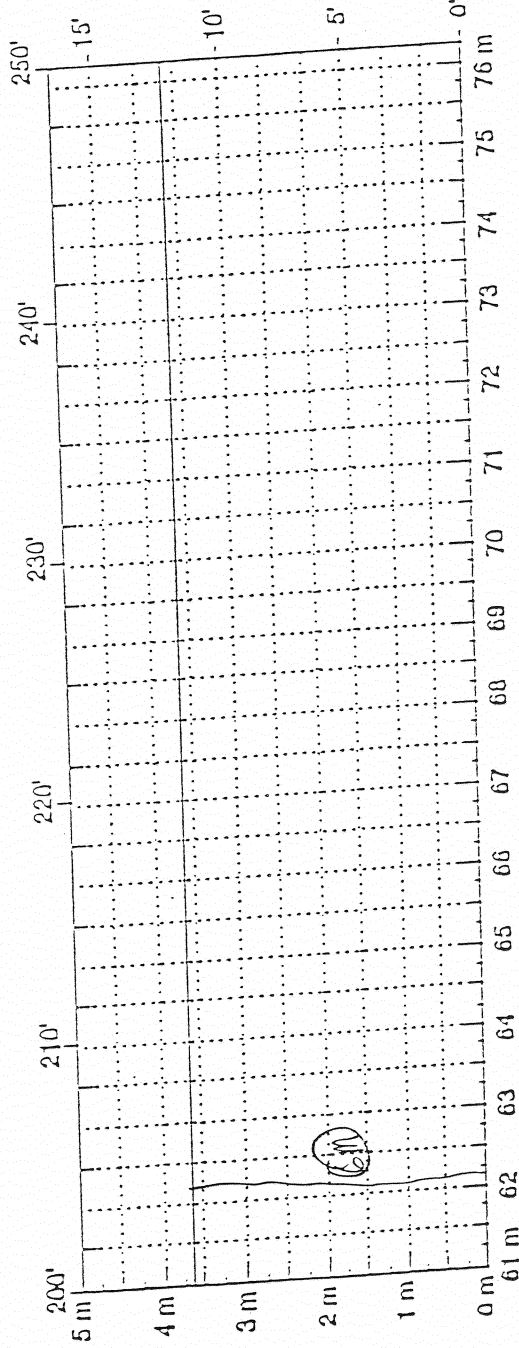


Comments: _____

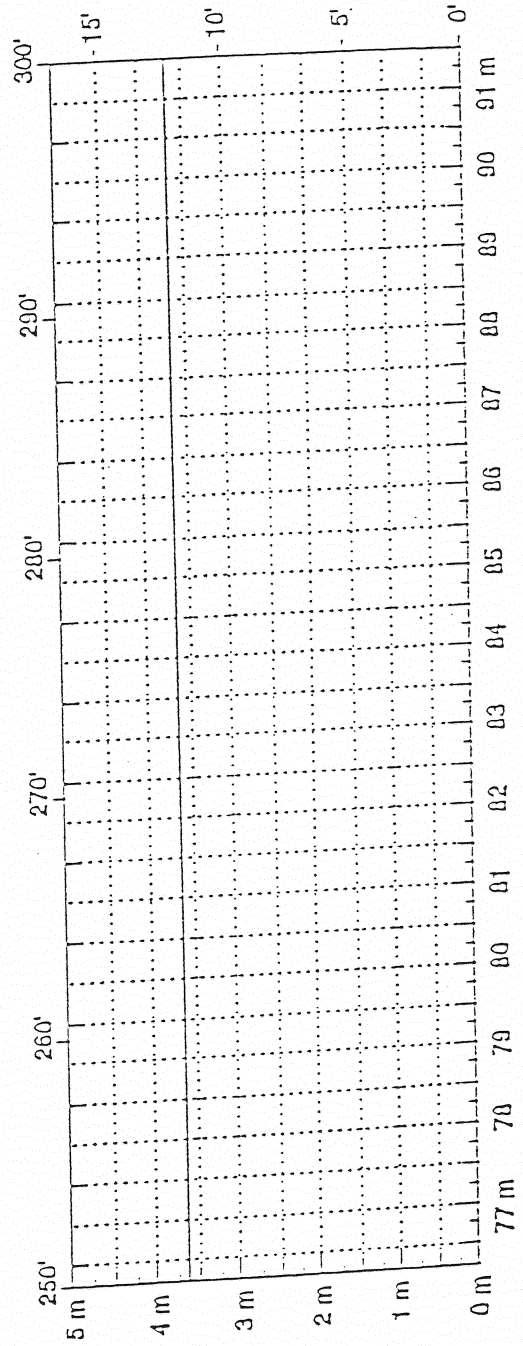


Comments: _____

State Assigned ID 40
 State Code 40
 SIIRP Section ID 0509

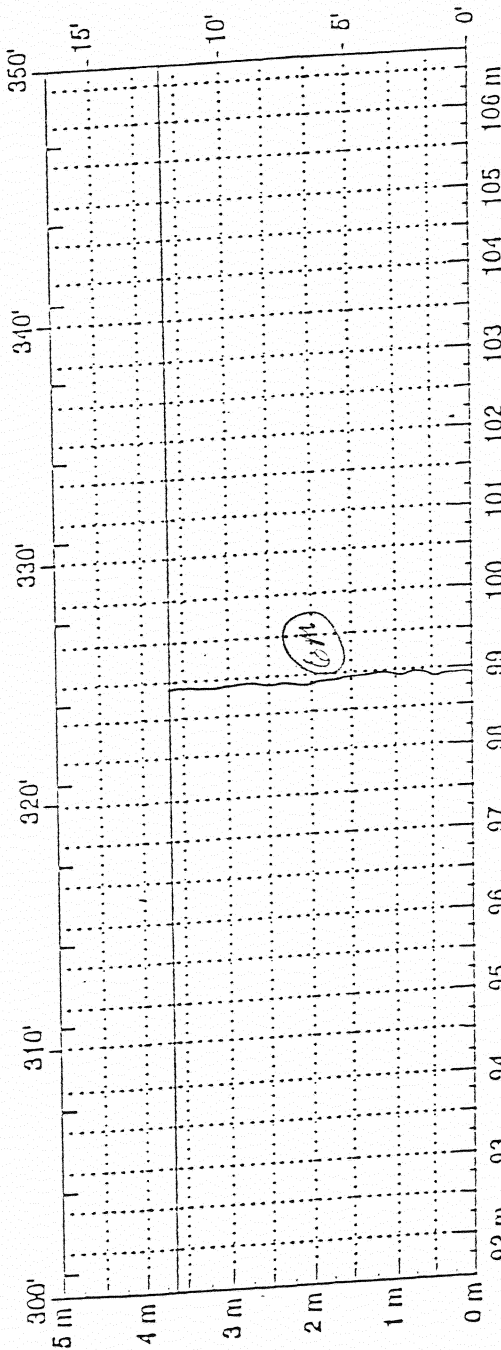


Comments: _____

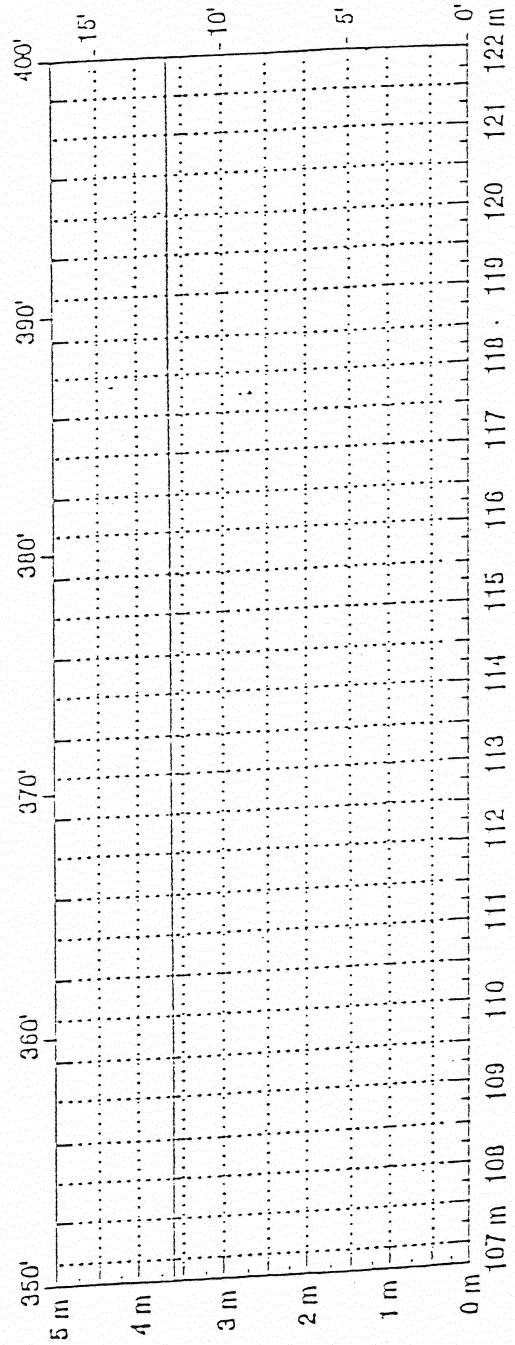


Comments: _____

State Assigned ID 40
 State Code
 SIPP Section ID 0509

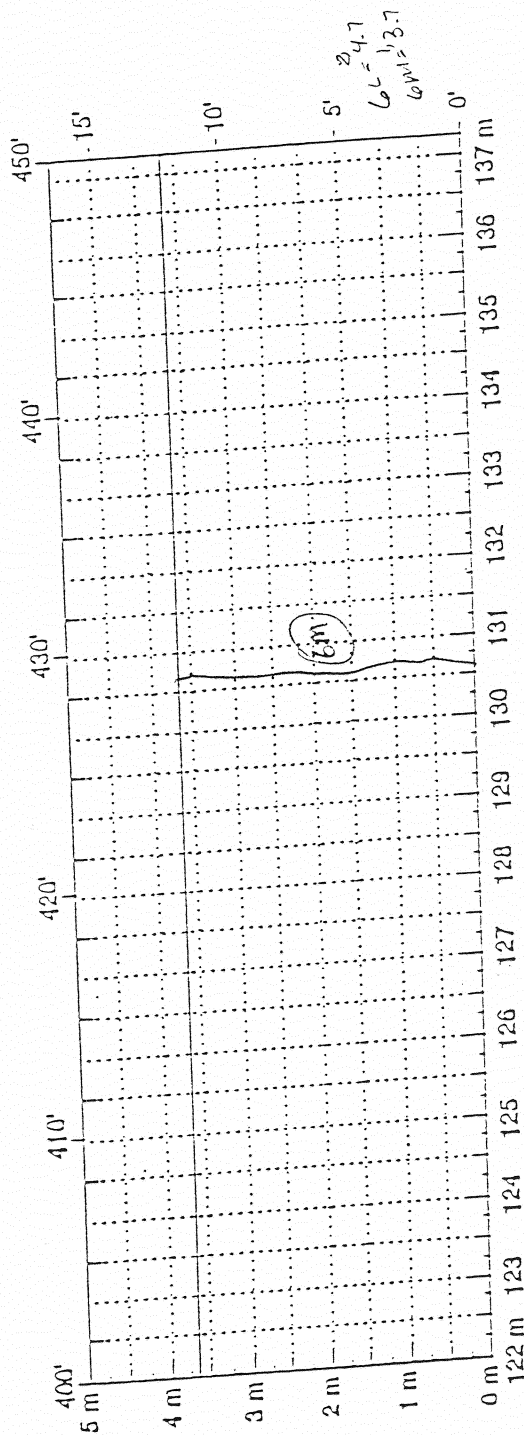

Comments:

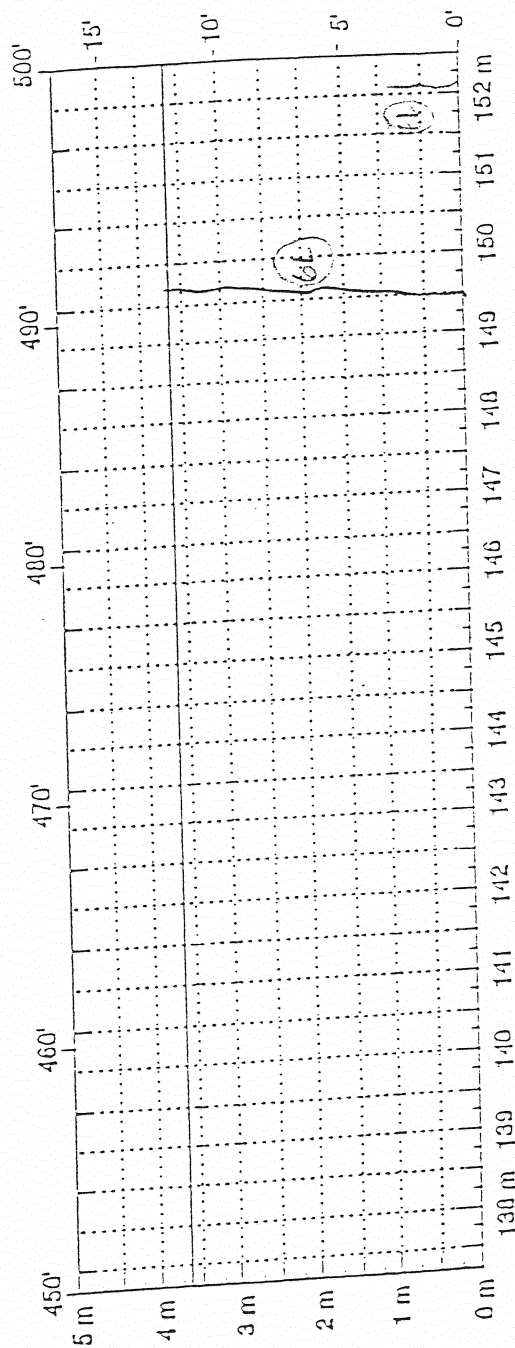

Comments:

LTPP Automated Dipstick Data Collection Transverse Profile Form DS-11 Zero and Calibration Checks	State Code [40] LTPP Section ID [0509] Date (dd/mm/yy) [06/17/97]
---	---

Operator: Tim Martin Employer: BRE

Dipstick Serial Number: 30023

Pre Measurement Checks

Time (military): 13:10

Automatic Zero Performed:

Calibration

Calibration Check	
Measurement	Reading (inches)
First Reading	.037
Second Reading on Calibration Block	.164
Second Reading - 0.125 - First Reading	.127

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Post Measurement Checks

Time (military): 13:50

Zero Check Acceptable: ✓

Calibration Check	
Measurement	Reading (inches)
First Reading	.039
Second Reading on Calibration Block	.165
Second Reading - 0.125 - First Reading	.126

Note: Reading 2 - Reading 1 must equal 0.125 with a tolerance of 0.003. If not, notify the RCOC office and contact Face Technologies for repair.

Comments

DATE: 6/17/97
 OPERATOR: T. J. Martin
 RECORDER: M. J. H. H.
 DIPSTICK SERIAL NUMBER: 50023

STATE CODE: 40
 SHRP SECTION I.D.: 0509

LOCATION	DIPSTICK READING												TOTAL	SUM
	1	2	3	4	5	6	7	8	9	10	11	12		
0+00	-065	-030	095	199	140	-014	-117	-026	+125	219	242	186	600	
	063	035	-092	-199	-139	014	116	026	-125	-216	-242	-189		
0+50	-043	008	115	212	120	061	-089	-004	124	255	211	186	010	
(15m)	044	014	-115	-210	-120	-057	092	001	-122	-248	-213	-182		
1+00	-076	026	172	242	153	026	-122	044	216	298	279	112	041	
(30m)	075	-026	-168	-239	-139	-033	126	-035	-212	-295	-276	-112	041	
1+50	062	014	163	243	140	032	159	036	224	314	274	090	014	
(45m)	061	-017	-160	-238	-138	036	157	031	-219	-313	-282	-085		
(2+00)	-010	041	168	230	156	-018	-122	031	203	316	285	111	019	
(60m)	009	-037	-166	-228	-152	020	125	-027	-199	-309	-287	-115		
2+50	001	034	185	276	158	007	103	034	194	285	243	131	010	
(75m)	003	-024	-186	-273	-157	-006	107	-035	-192	-277	-241	-137		
3+00	-002	021	153	255	196	040	-085	037	281	308	260	232	020	
(90m)	003	-018	-153	-248	-194	-038	088	-037	-176	-301	-252	-132		
3+50	012	023	174	270	193	045	044	055	169	306	275	260	030	
(105m)	009	-015	-169	-264	-191	-089	-055	-052	-167	-290	-274	-160		
4+00	018	007	141	242	198	048	090	030	175	273	208	220	800	
(120m)	-023	-005	-140	-241	-196	-045	-096	-029	-169	-276	-206	-120		
4+50	003	049	122	280	170	126	-136	001	180	341	239	110	010	
(135m)	-000	-060	-114	-279	-169	-118	141	+003	-174	-338	-243	-102		
5+00	-064	021	094	192	122	078	-075	-026	060	261	223	090	010	
(150m)	060	-022	-091	-190	-122	-070	070	020	-060	-152	-122	-059	010	

COMMENTS

FILED JUL 10 1997 A II
 L. H. W. 266107121997 A II

RECEIVED JUN 30 1997

Revised December 1, 1992

SHEET 1

DISTRESS SURVEY

LTPP PROGRAM

STATE ASSIGNED ID _____

STATE CODE 40

SHRP SECTION ID 0560

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR)

06/17/97

SURVEYORS: TJM, MJD PHOTOS, VIDEO, OR BOTH WITH SURVEY (P, V, B)
PAVEMENT SURFACE TEMP - BEFORE 36°C; AFTER 35°C

ENTERED OCT 21 1997 J H
REVIEWED JUL 21 1997 J D
JUL 17 1997 JP

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
CRACKING			
1. FATIGUE CRACKING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
2. BLOCK CRACKING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
3. EDGE CRACKING (Meters)	<u>0</u>	<u>0</u>	<u>0</u>
4. LONGITUDINAL CRACKING (Meters)			
4a. Wheel Path Length Sealed (Meters)	<u>0</u>	<u>0</u>	<u>0</u>
4b. Non-Wheel Path Length Sealed (Meters)	<u>3.5</u>	<u>0</u>	<u>0</u>
5. REFLECTION CRACKING AT JOINTS Number of Transverse Cracks	<u>0</u>	<u>0</u>	<u>0</u>
Transverse Cracking (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
Longitudinal Cracking (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
Length Sealed (Meters)	<u>1</u>	<u>1</u>	<u>1</u>
6. TRANSVERSE CRACKING Number of Cracks	<u>4</u>	<u>6</u>	<u>0</u>
Length (Meters)	<u>5.4</u>	<u>22.2</u>	<u>1</u>
Length Sealed (Meters)	<u>0</u>	<u>0</u>	<u>1</u>
PATCHING AND POTHOLES			
7. PATCH/PATCH DETERIORATION (Number)	<u>0</u>	<u>0</u>	<u>1</u>
(Square Meters)	<u>1</u>	<u>1</u>	<u>1</u>
8. Potholes (Number)	<u>1</u>	<u>1</u>	<u>1</u>
(Square Meters)	<u>1</u>	<u>1</u>	<u>1</u>

Revised December 1, 1992

SHEET 2
DISTRESS SURVEY
LTPP PROGRAM

STATE ASSIGNED ID _ _ _ _

STATE CODE 40

SHRP SECTION ID 0560

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/17/97

SURVEYORS: TJM, MJD

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

DISTRESS TYPE	SEVERITY LEVEL		
	LOW	MODERATE	HIGH
SURFACE DEFORMATION			
9. RUTTING - REFER TO SHEET 3 FOR SPS-3 OR Form S1 from Dipstick Manual			
10. SHOVING (Number) (Square Meters)			<u>0</u> <u>0</u>
SURFACE DEFECTS			
11. BLEEDING (Square Meters)	<u>305.0</u>	<u>0</u>	<u>0</u>
12. POLISHED AGGREGATE (Square Meters)			<u>0</u>
13. RAVELING (Square Meters)	<u>0</u>	<u>0</u>	<u>0</u>
MISCELLANEOUS DISTRESSES			
14. LANE-TO-SHOULDER DROPOFF - REFER TO SHEET 3			
15. WATER BLEEDING AND PUMPING (Number) Length of Affected Pavement (Meters)			<u>0</u> <u>0</u>
16. OTHER (Describe)			

Revised May 29, 1992

SHEET 3

DISTRESS SURVEY

LTPP PROGRAM

STATE ASSIGNED ID _____

STATE CODE 40

SHRP SECTION ID 0560

DATE OF DISTRESS SURVEY (MONTH/DAY/YEAR) 06/17/97

SURVEYORS: T J M, M J D

DISTRESS SURVEY FOR PAVEMENTS WITH ASPHALT CONCRETE SURFACES
(CONTINUED)

ENTERED OCT 21 1997 J. R

9. RUTTING (FOR SPS-3 SITE SURVEYS)

INNER WHEEL PATH			OUTER WHEEL PATH		
Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)	Point No.	Point Distance ¹ (Meters)	Rut Depth (mm)
1	0.	— — —	1	0	— — —
2	15.25	— — —	2	15.25	— — —
3	30.5	— — —	3	30.5	— — —
4	45.75	— — —	4	45.75	— — —
5	61.	— — —	5	61.	— — —
6	76.25	— — —	6	76.25	— — —
7	91.5	— — —	7	91.5	— — —
8	106.75	— — —	8	106.75	— — —
9	122.	— — —	9	122.	— — —
10	137.25	— — —	10	137.25	— — —
11	152.5	— — —	11	152.5	— — —

SEE
DIPSTICK
DATA


14. LANE-TO-SHOULDER DROPOFF

Point No.	Point Distance ¹ Meters	Lane-to-Shoulder Dropoff (mm)
1	0.	— — 0.
2	15.25	— — 0.
3	30.5	— — 0.
4	45.75	— — 0.
5	61.	— — 0.
6	76.25	— — 0.
7	91.5	— — 0.
8	106.75	— — 0.
9	122.	— — 0.
10	137.25	— — 0.
11	152.5	— — 0.


Note 1: "Point Distance" is the distance in meters from the start of the test section to the point where the measurement was made. The values shown are SI equivalents of the 50 ft spacing used in previous surveys.

State Assigned ID _____
 State Code 40
 SIIRP Section ID 0560

Date 6/17/97
 Surveyor TJM, MJD

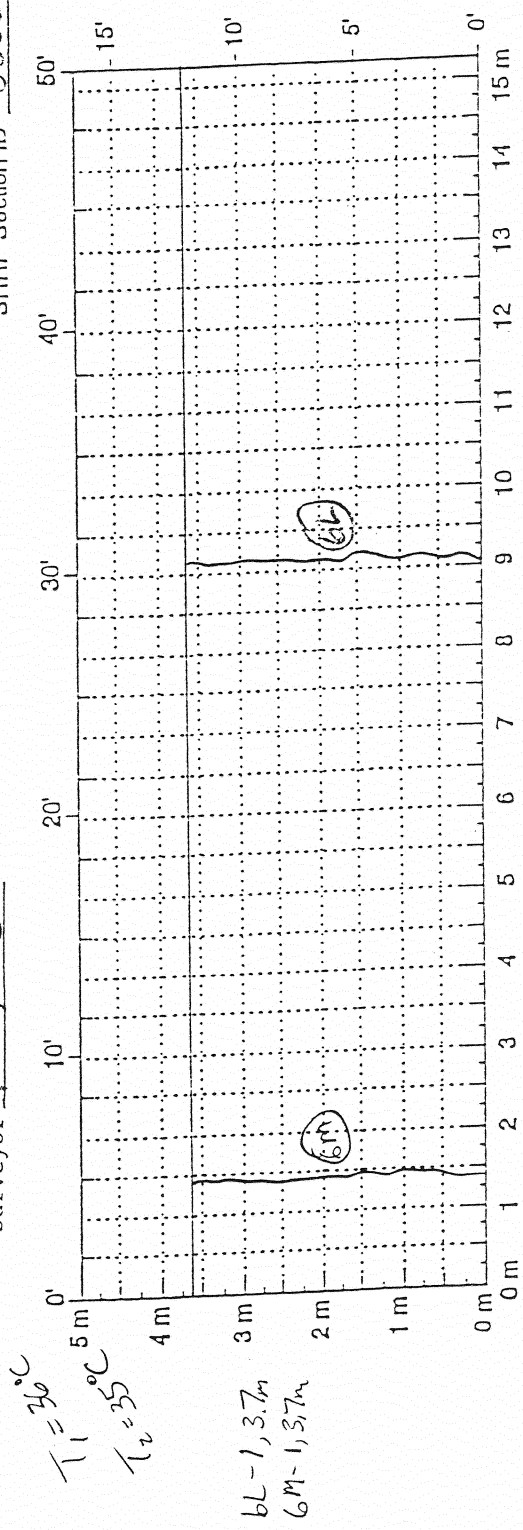


Comments: Bleeding in the wheel-paths throughout section.

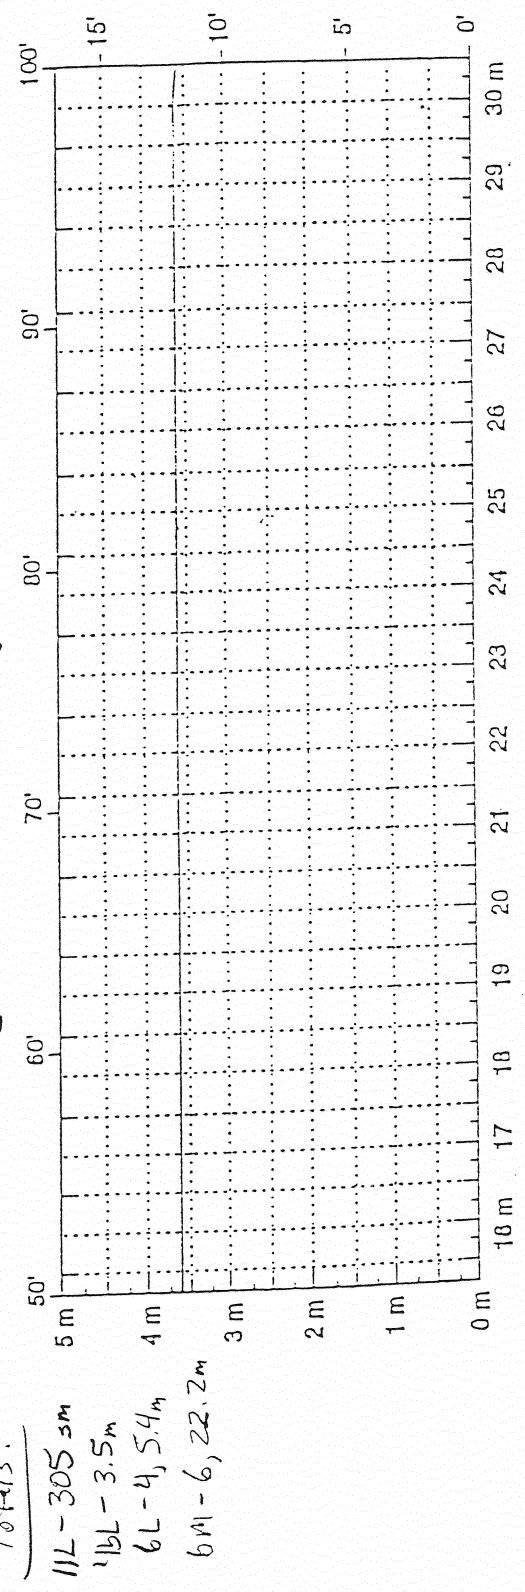


Comments: _____

State Assigned ID _____
 State Code 40
 SIIRP Section ID 0560

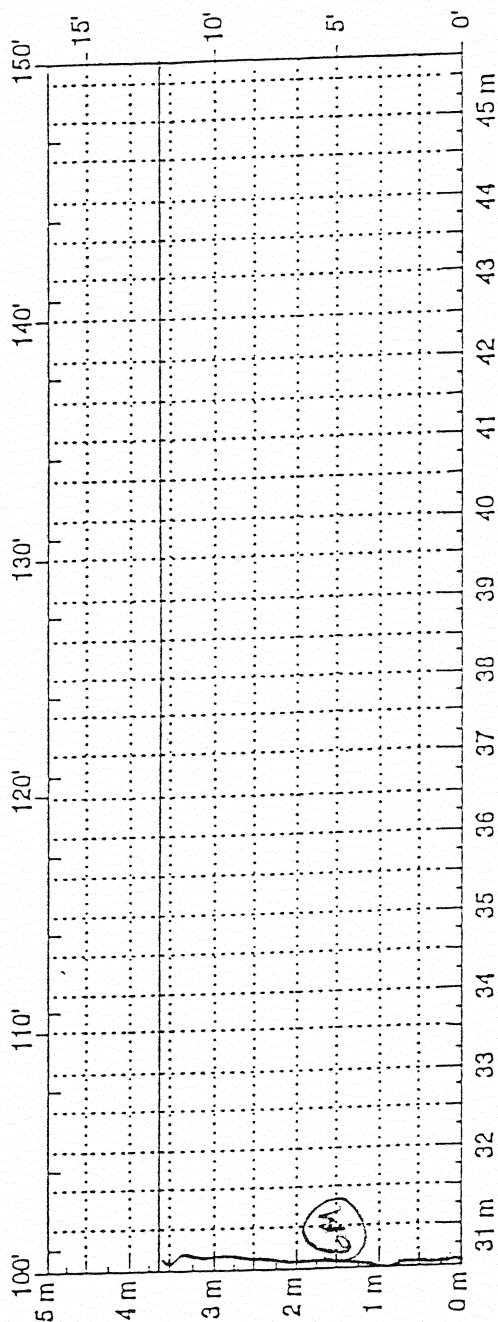


6M - 1,37m

Comments: _____

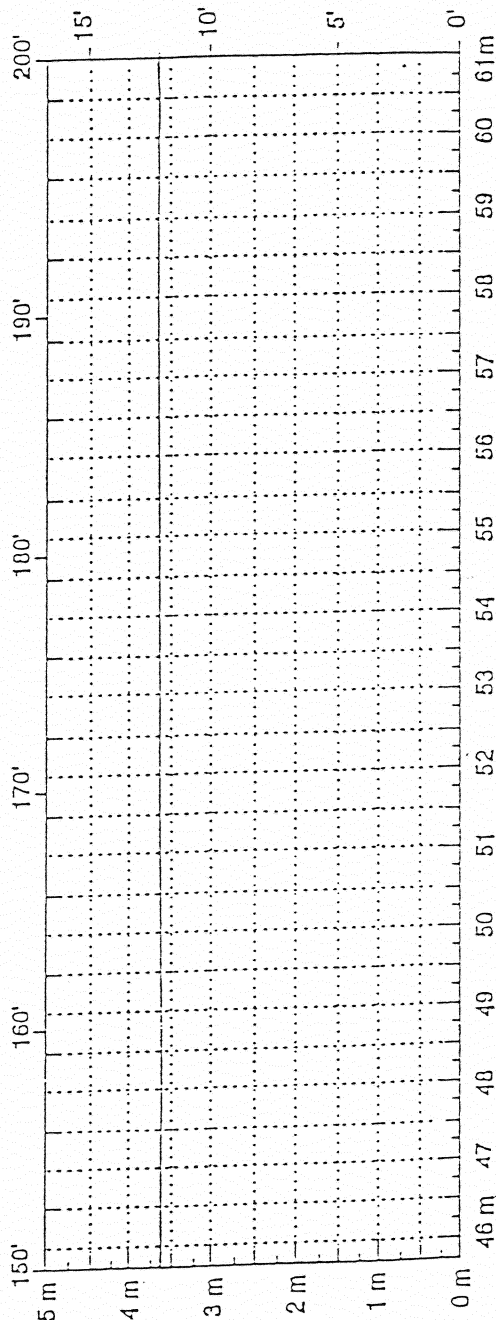


Comments: _____

State Assigned ID _____
 State Code 40
 SIIRP Section ID 0560

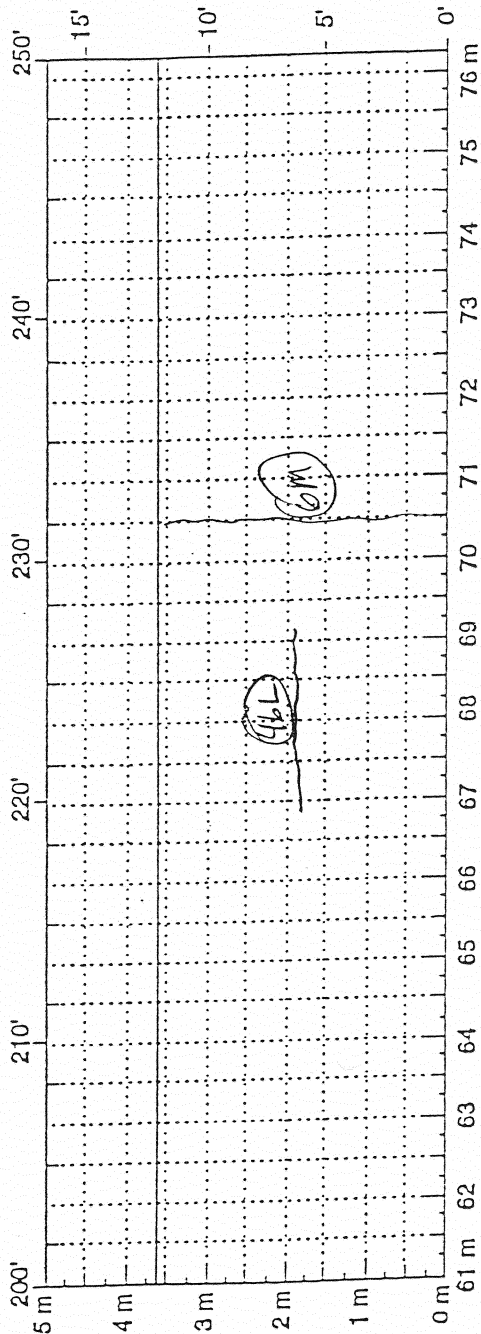


46L-3.5m
 6M-1,3.7m

Comments: _____

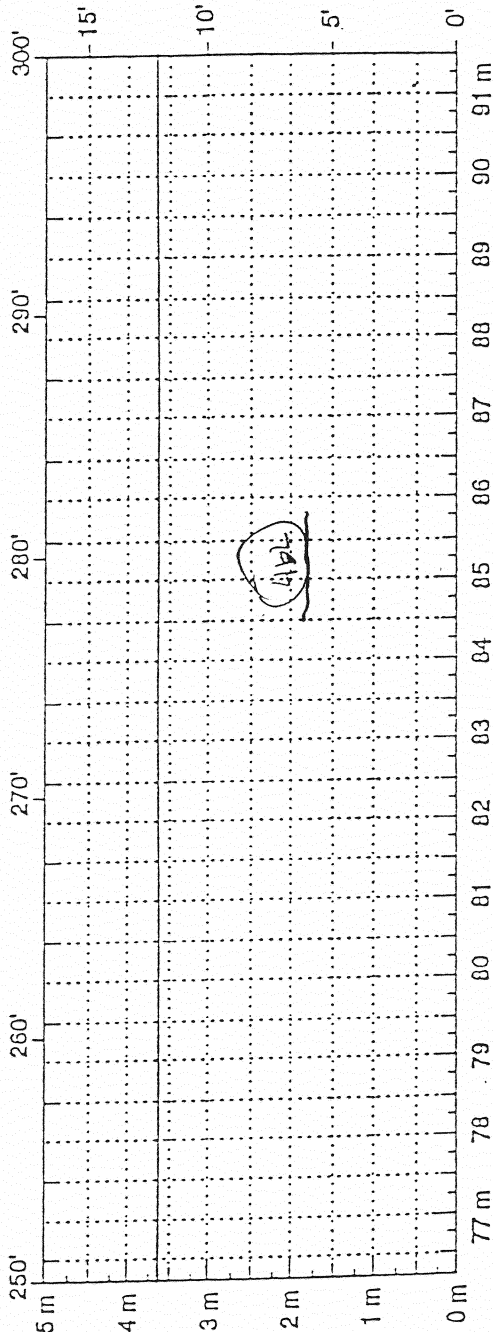


Comments: _____

State Assigned ID _____
 State Code 40
 SHRP Section ID 0560

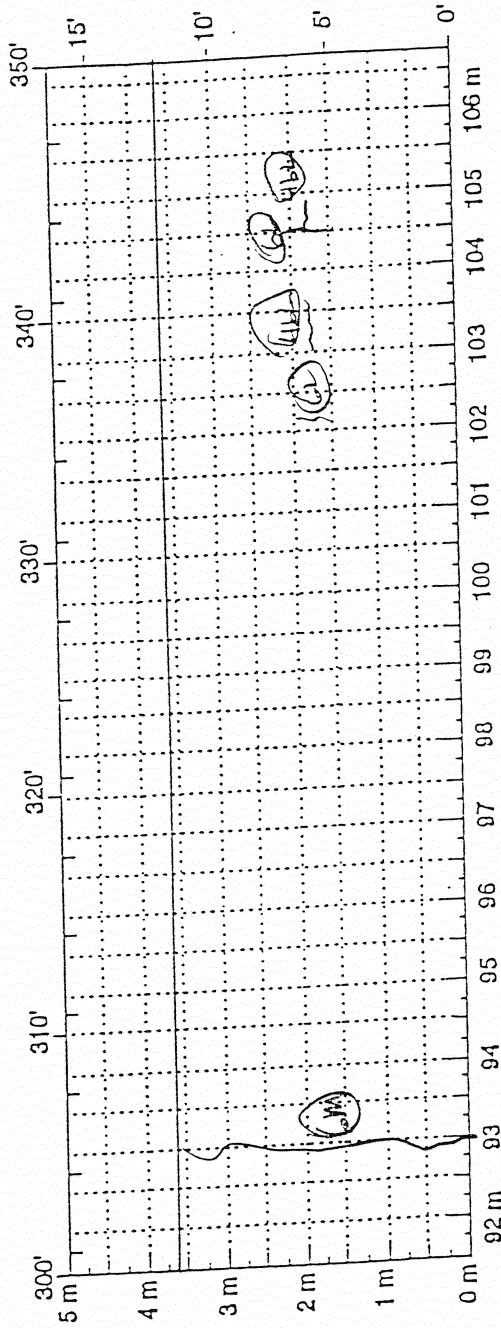

6L-1.3 m
 6M-2.74 m

Comments: _____

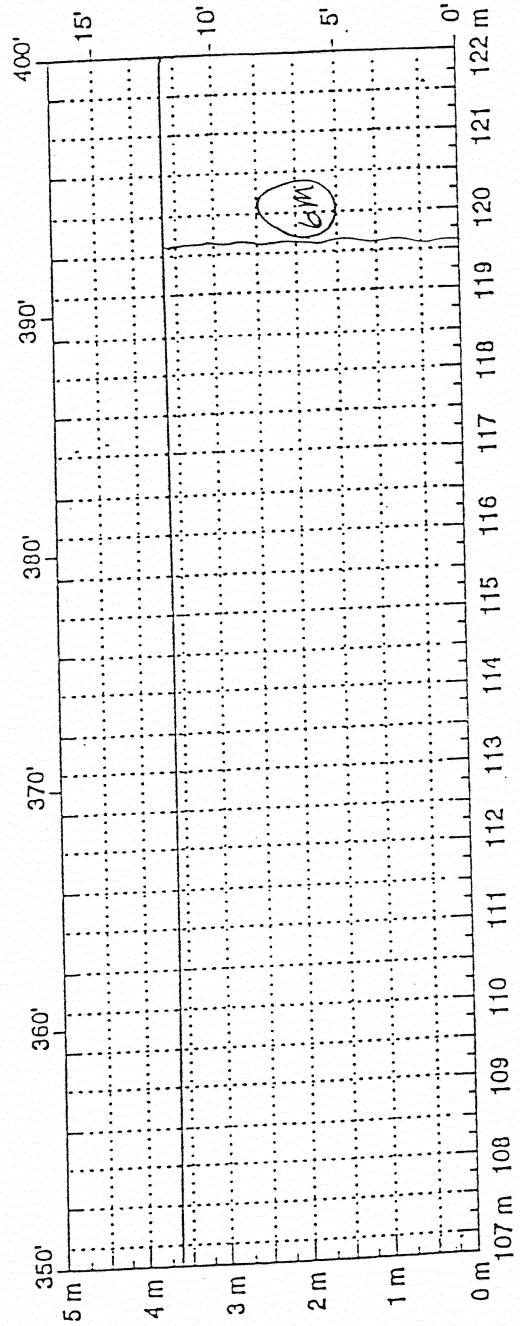


Comments: _____

State Assigned ID _____


State Code 40

SHRP Section ID D 560

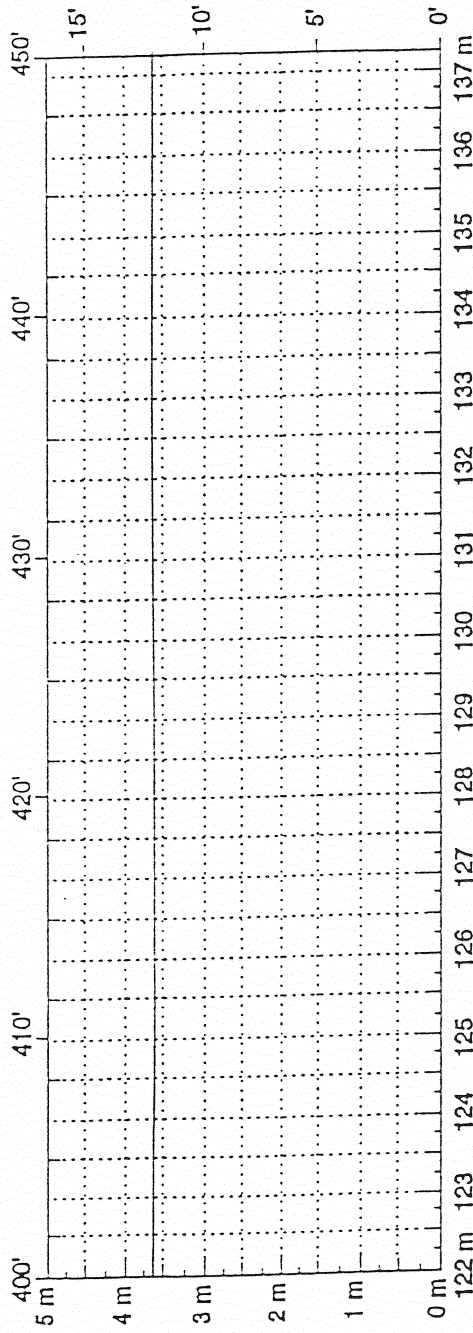

GL - 1, 1.4 m
BM - 1, 3.7 m

Comments: _____

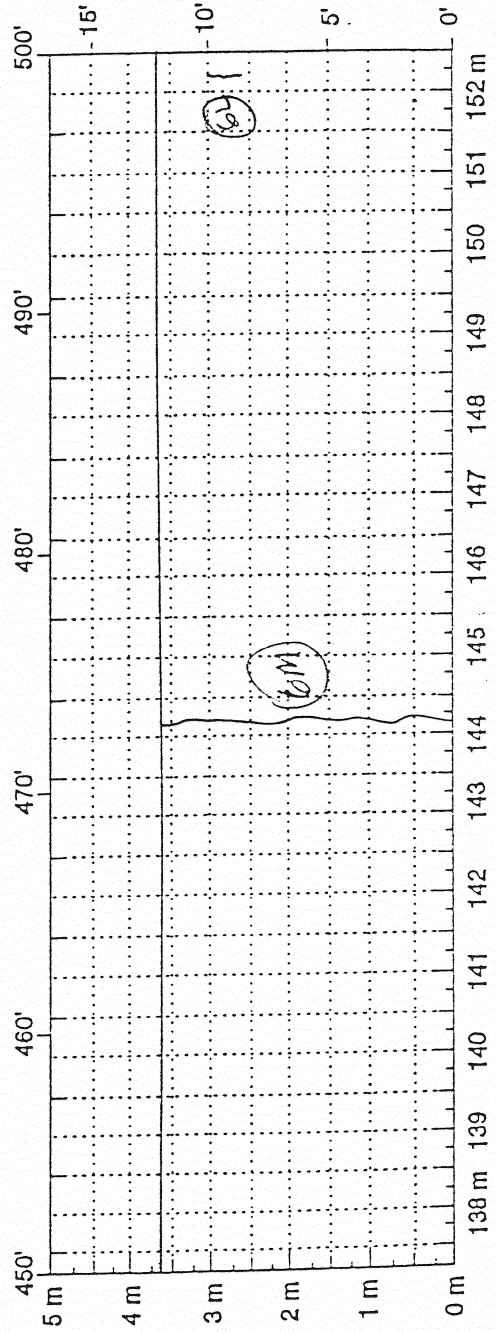

Comments: _____

LTPP Automated Dipstick Data Collection Transverse Profile Form DS-11 Zero and Calibration Checks	State Code [4 0] LTPP Section ID [0 5 6 0] Date (dd/mm/yy) [0 6 / 1 7 / 9 7]
---	--

Operator: Tim Martin Employer: BRE

Dipstick Serial Number: 30023

Pre Measurement Checks

Time (military): 20:00

Automatic Zero Performed:

Calibration

Calibration Check	
Measurement	Reading (ⁱⁿ)
First Reading	,070
Second Reading on Calibration Block	,195
Second Reading - 3.2 - First Reading	,125

Note: Reading 2 - Reading 1 must equal 3.2 with a tolerance of 0.1. If not, notify the RCOC office and contact Face Technologies for repair.

Post Measurement Checks

Time (military): 20:35

Zero Check Acceptable: ✓

Calibration Check	
Measurement	Reading (ⁱⁿ)
First Reading	,068
Second Reading on Calibration Block	,193
Second Reading - 3.2 - First Reading	,125

Note: Reading 2 - Reading 1 must equal 3.2 with a tolerance of 0.1. If not, notify the RCOC office and contact Face Technologies for repair.

Comments

DATE: 6/17/97 STATE CODE: 40
 OPERATOR: Tim Martin SHRP SECTION I.D.: 056
 RECORDER: Matt Duke
 DIPSTICK SERIAL NUMBER: 30023

LOCATION	DIPSTICK READING															TOTAL	SUM
	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15		
0+00	085 ⁰⁹	005 ⁰⁹	164	369	259	176	047	-033	214	398	282	191					
	085 ⁰⁹	016 ⁰⁹	-157 ⁵⁹	-365 ⁵¹	-255 ⁴⁷	-170 ⁴³	-035 ³⁷	043 ²⁵	-206 ¹⁵	-394 ⁷	-279 ³	-191 ⁰				069	
0+50 (15 m)	102	028	226	290	206	050	001	046	283	346	308	144					
	-101 ²⁴	028 ¹⁵	-221 ²⁵	-286 ²⁰	-206 ¹⁶	-040 ¹⁶	-005 ⁶	-037 ¹⁰	-272 ¹	-348 ⁰	-308 ²	-142 ²				026	
1+00 (30 m)	-102	010	173	334	333	027	-048	010	216	438	364	197					
	113 ⁰⁷	006 ²⁶	-157 ⁰⁰	-336 ¹⁴	-318 ¹⁶	-030 ²¹	056 ³⁴	020 ²⁶	-214 ¹⁶	-436 ¹⁴	-359 ¹²	-190 ⁷				067	
1+50 (45 m)	065	098	198	336	296	098	085	030	220	387	384	245					
	-056 ⁵⁷	-094 ⁴³	-190 ⁴⁴	-337 ³⁶	-295 ³⁷	-101 ²⁶	-071 ¹³	-043 ²⁵	-212 ¹³	-382 ¹⁰	-381 ⁵	-243 ²				057	
2+00 (60 m)	044	068	204	338	348	108	051	042	254	367	305	285					
	-041 ³⁹	065 ³⁶	-200 ³³	-335 ²⁴	-342 ²⁶	-116 ²⁰	-038 ²⁸	-034 ¹⁵	-299 ⁷	-365 ²	-364 ⁰	-286 ¹				039	
2+50 (75 m)	058	061	179	296	245	125	054	051	246	330	370	194					
	-061 ²⁴	-057 ²²	-167 ²³	-297 ¹⁶	-243 ¹⁷	-120 ¹⁵	-150 ¹⁰	-048 ⁷	-244 ⁴	-333 ²	-375 ⁵	-181 ⁹				620	
3+00 (90 m)	014	053	191	285	251	037	055	040	274	373	314	191					
	016 ²¹	-045 ¹⁹	163 ²¹	-286 ¹³	-243 ¹³	-055 ⁶	058 ⁴	-037 ⁷	274 ⁴	-371 ⁴	-313 ²	-190 ¹				027	
3+50 (105 m)	066	082	106	354	293	133	103	003	205	383	373	280					
	-060 ¹	-075 ²¹	-104 ²⁴	-348 ²	-292 ¹⁶	-135 ¹⁵	-098 ¹⁷	-002 ¹²	-196 ¹¹	-382 ³	-378 ¹	-274 ⁶				036	
4+00 (120 m)	063	092	188	330	316	136	098	054	225	314	395	267					
	-051 ³⁴	-092 ²²	194 ²²	-327 ²³	-314 ²³	-134 ²³	-093 ²¹	-047 ¹⁰	-220 ⁹	-313 ⁴	-392 ³	-267 ⁰				034	
4+50 (135 m)	111	000	162	341	260	132	076	038	252	324	353	158					
	-111 ²⁶	-003 ²⁶	-157 ²⁹	-340 ²⁴	-256 ²³	-131 ¹⁹	-065 ¹⁸	-000 ¹⁸	-255 ⁵	-332 ⁸	-348 ⁶	-157 ¹				026	
5+00 (150 m)	032	010	197	293	266	077	026	069	221	315	334	150					
	-023 ⁴⁴	-010 ³¹	-161 ²⁷	-282 ²⁴	-212 ²³	-070 ²³	-220 ²²	-170 ¹⁹	-210 ²⁰	-315 ⁹	-323 ⁸	-151 ³				040	

FORM 511/December 1997
 ENCLINUED JUL 10 1997 A H


ENCLINUED JUL 27 1997 CA H17

APPENDIX C

DEFLECTION PLOTS -


PRECONSTRUCTION AND POSTCONSTRUCTION

Deflection Data for Section: 400501A

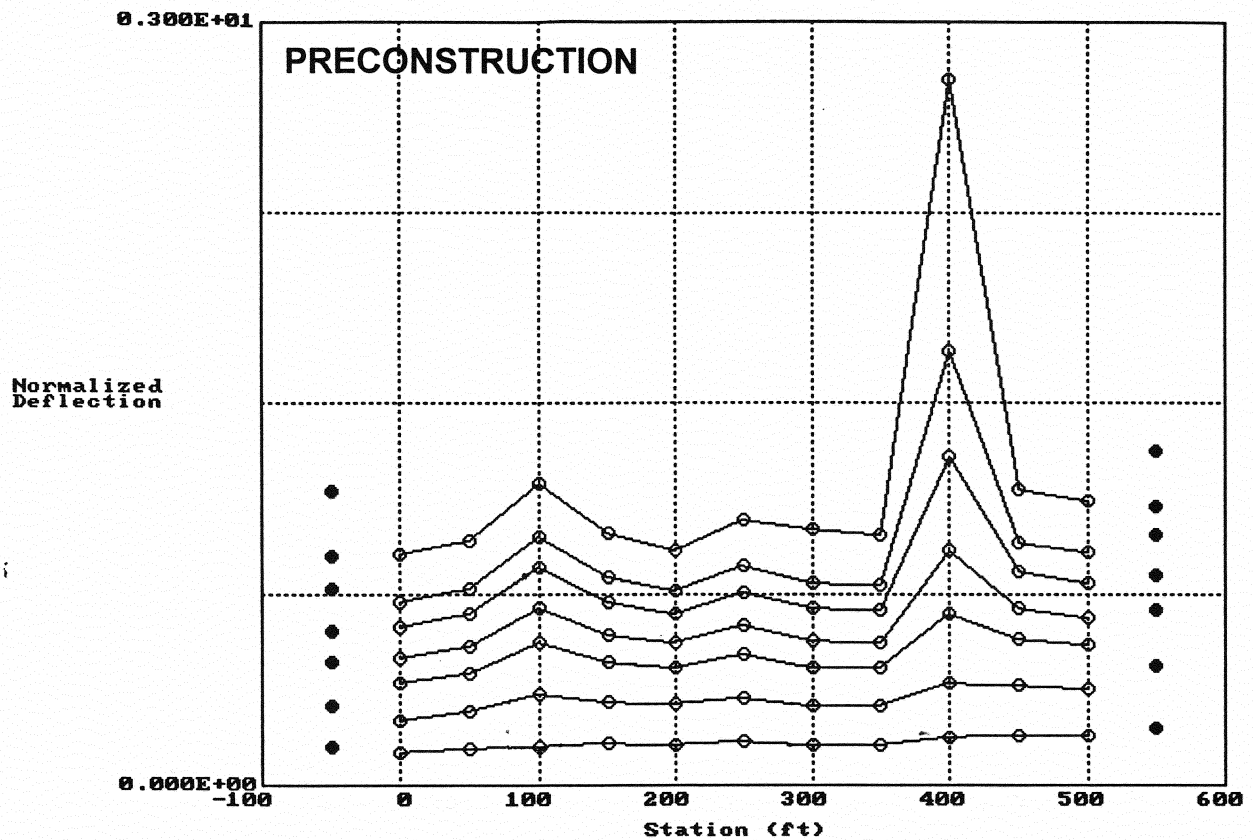


Location 1 Drop Height 2 Sensors 1, 2, 3, 4, 5, 6, 7
 F2:ScrnDump F10:Exit ⚡:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400501C

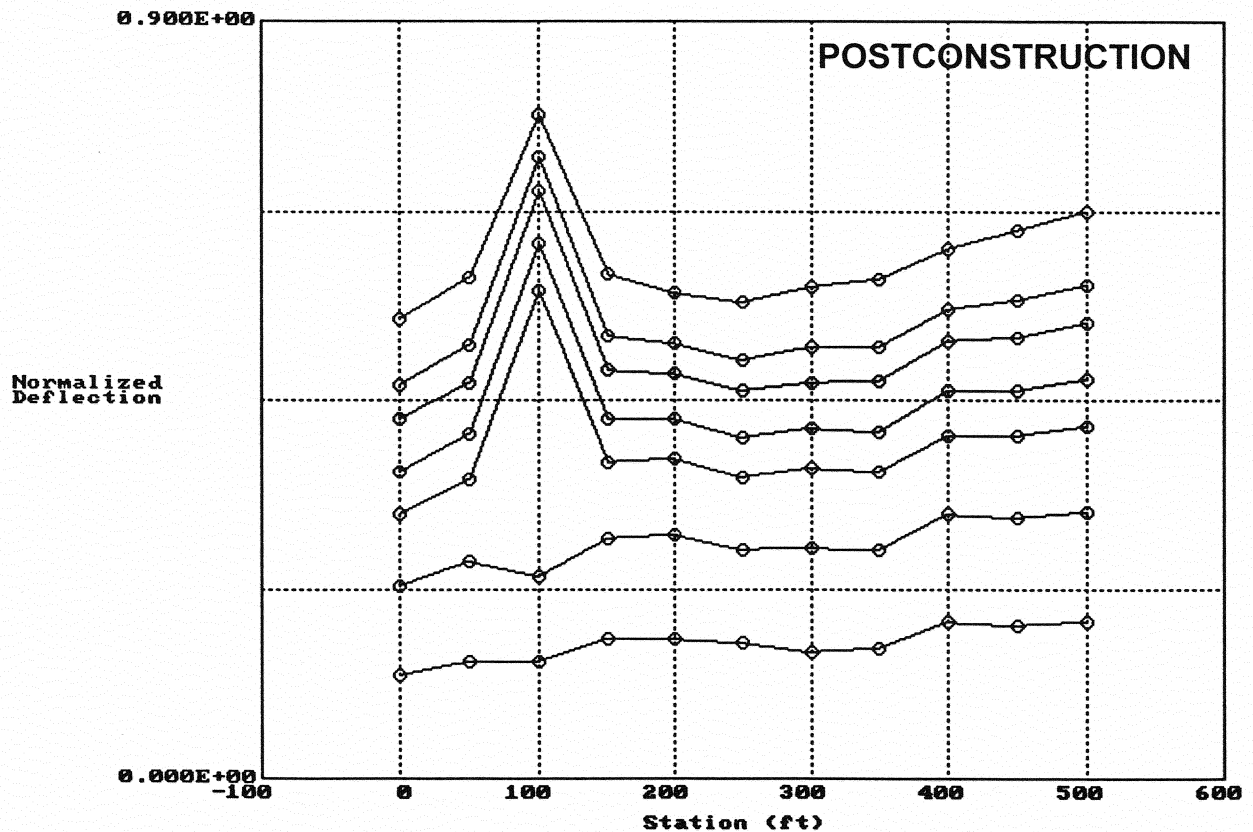


Location 1 Drop Height 2 Sensors 1, 2, 3, 4, 5, 6, 7
 F2:ScrnDump F10:Exit ⚡:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400502A

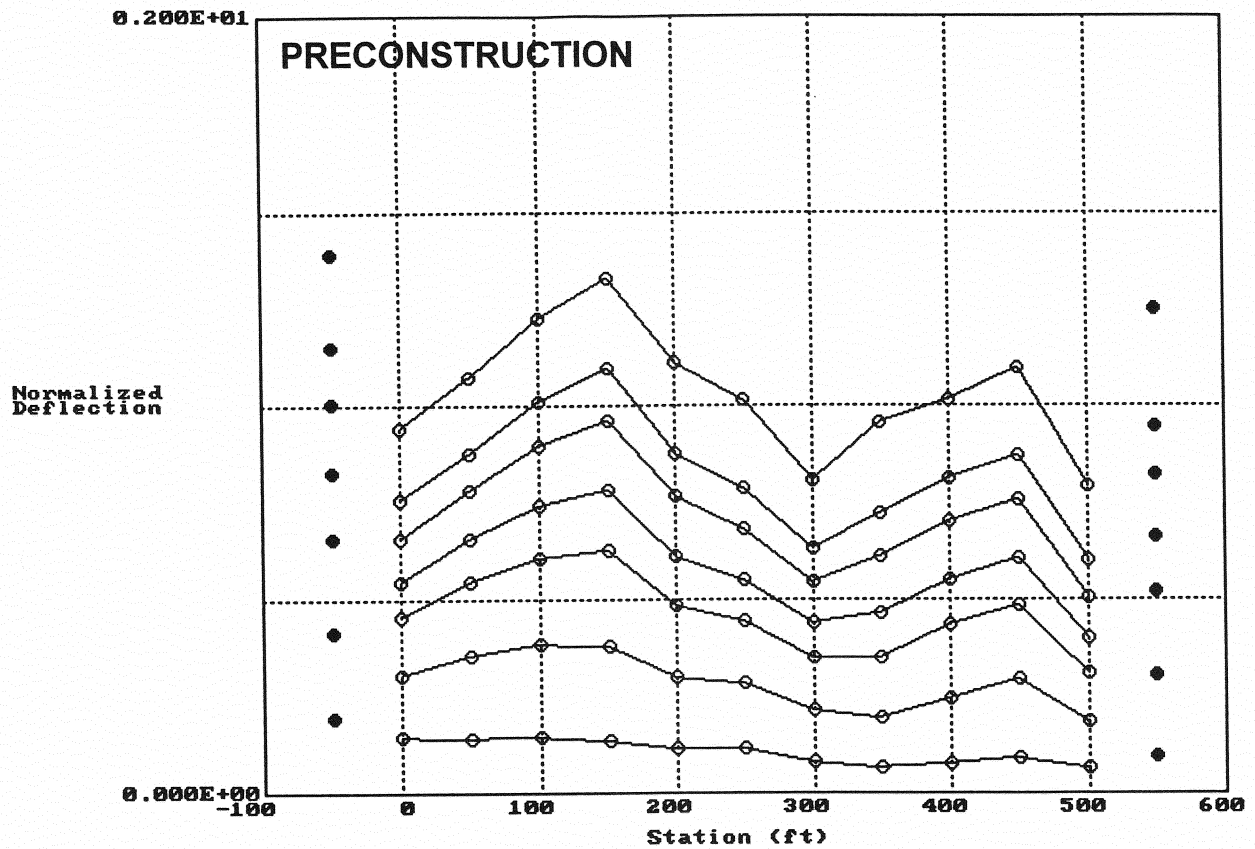


F2:ScrnDump F10:Exit ↑f:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400502C

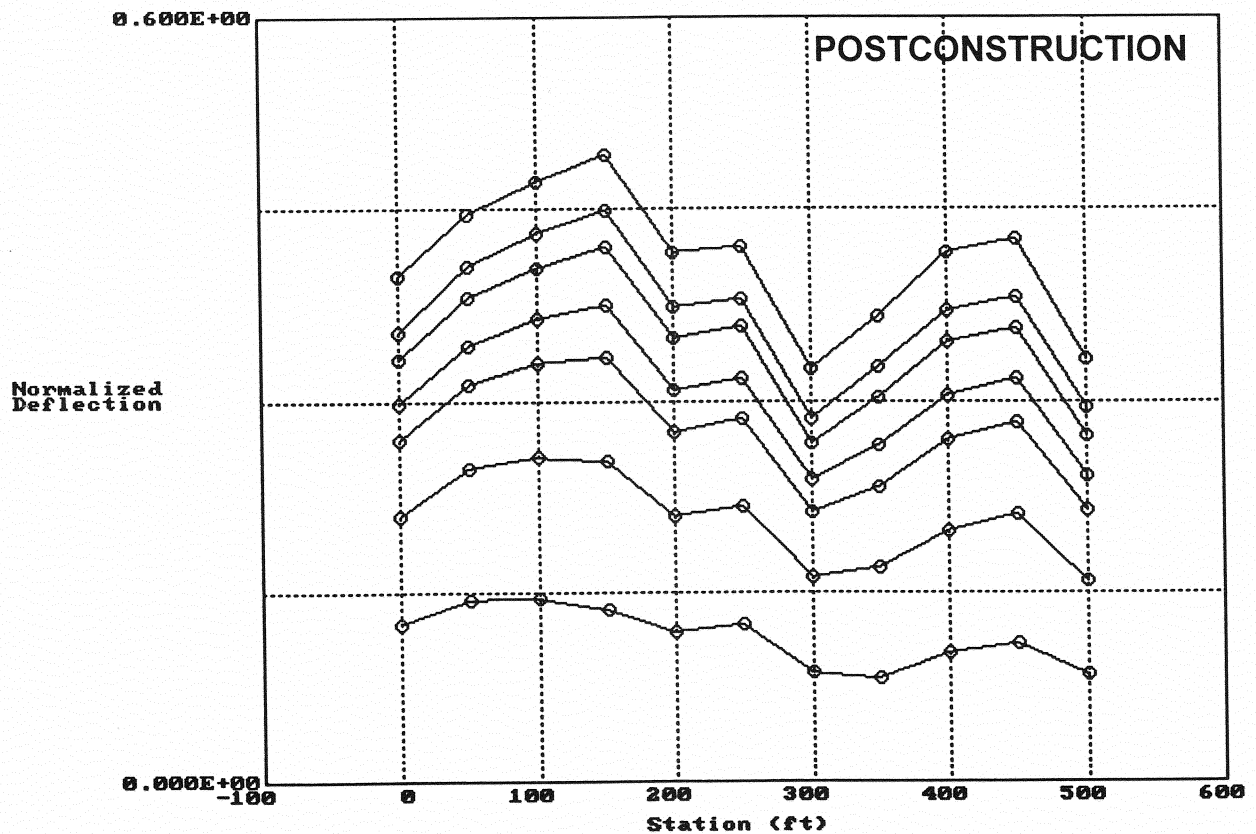


F2:ScrnDump F10:Exit ↑f:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400503A

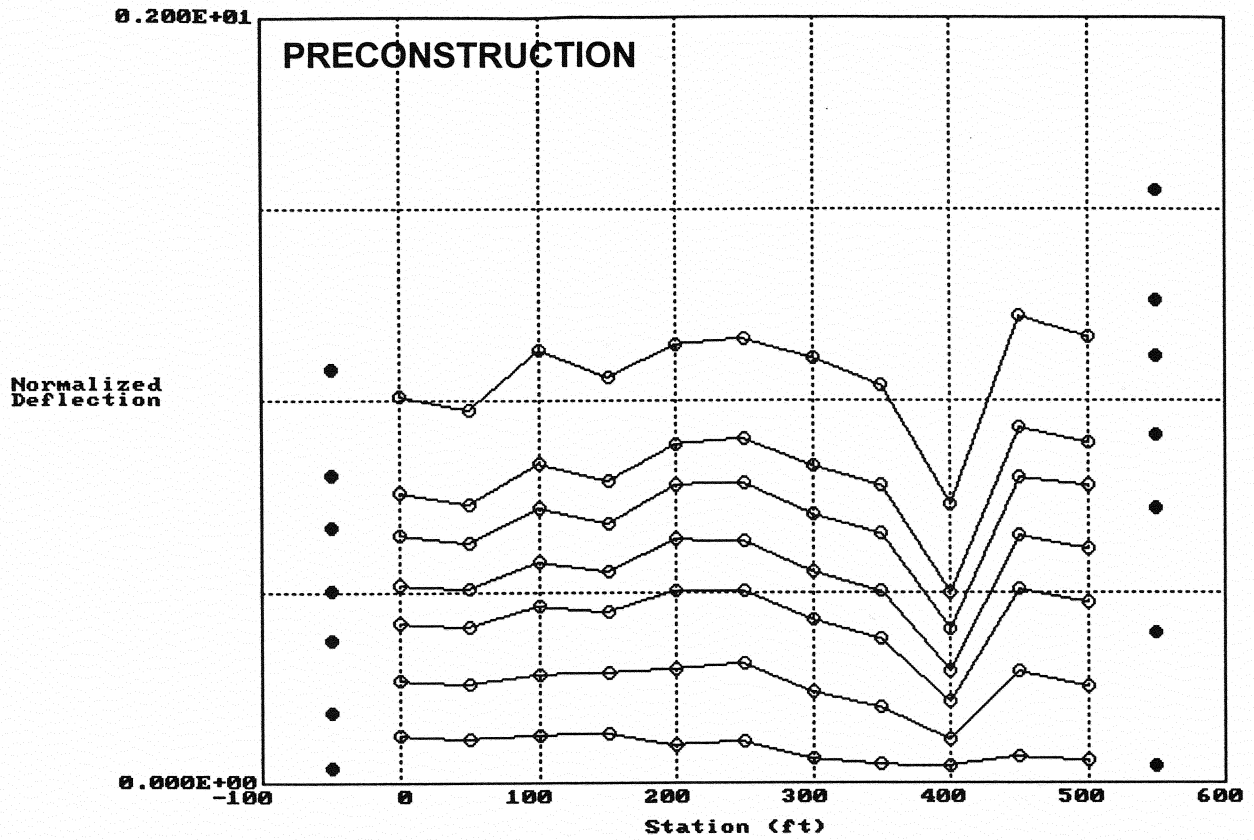



F2:ScrnDump F10:Exit ↑:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400503C

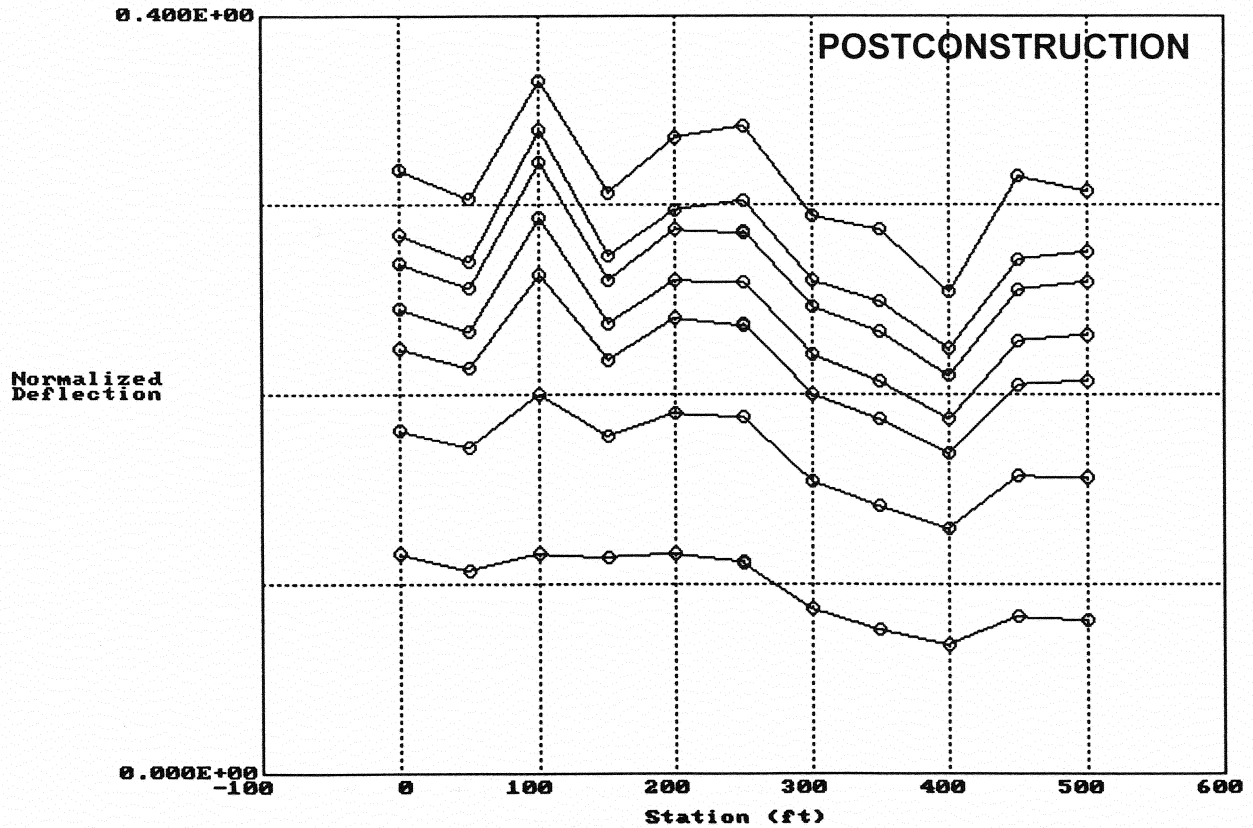


F2:ScrnDump F10:Exit ↑:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400504A

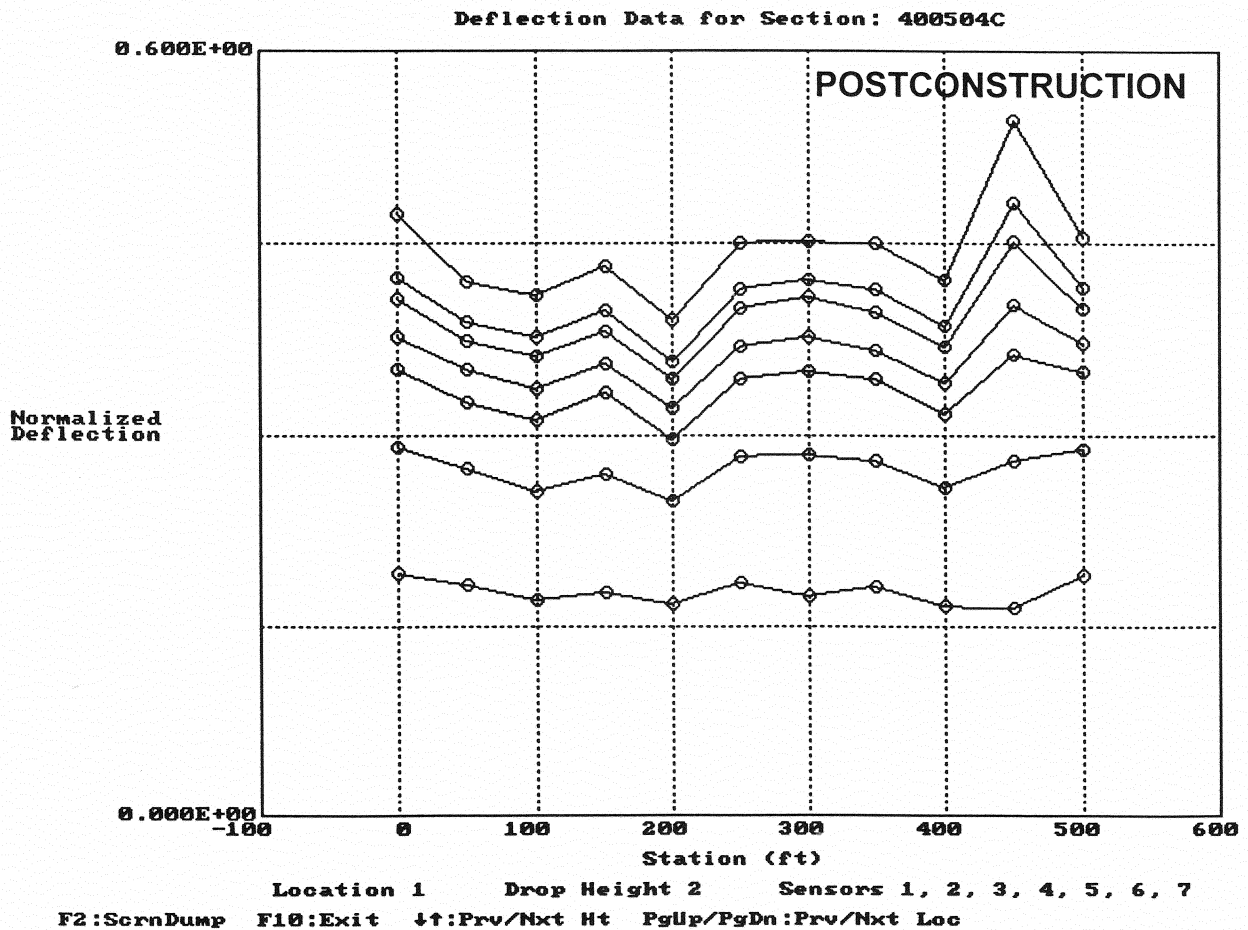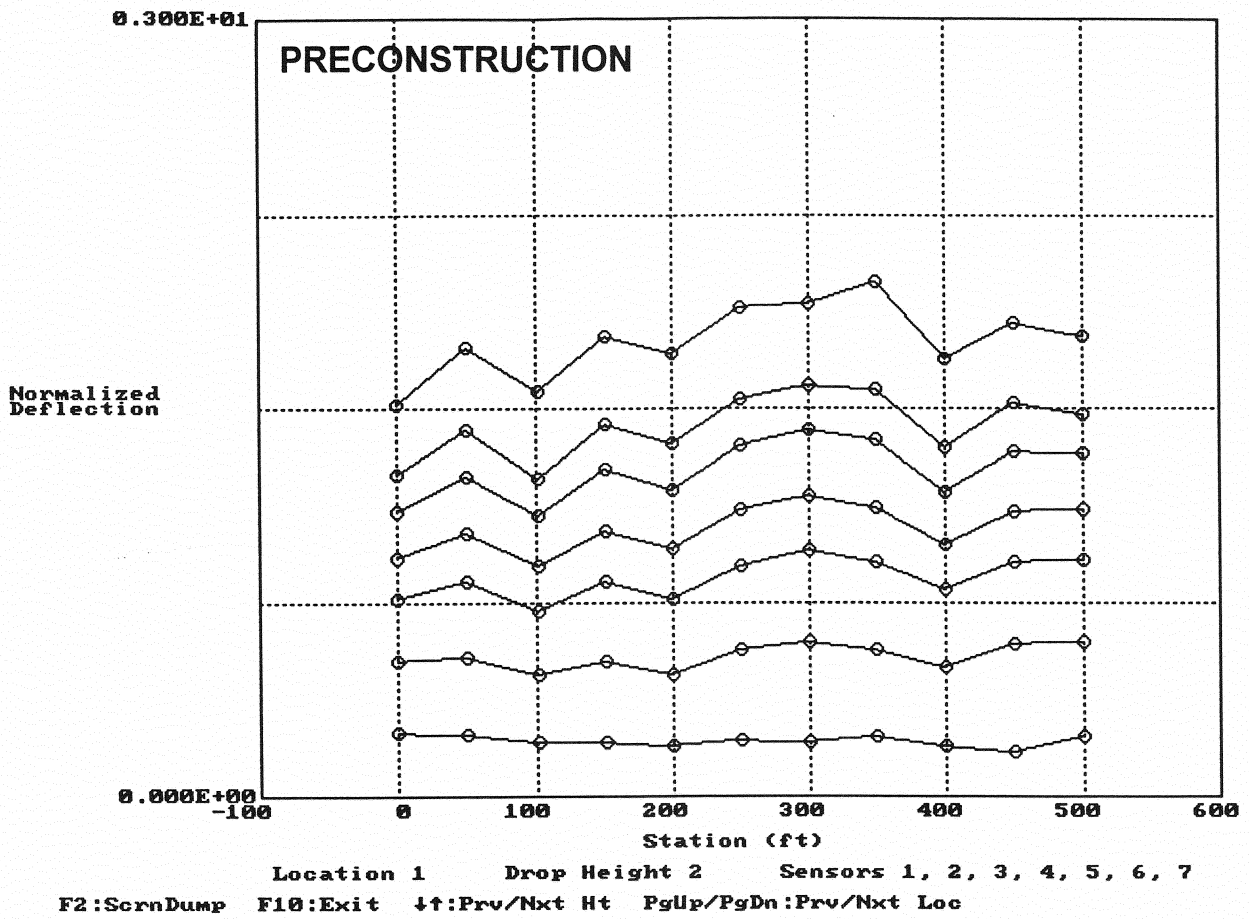


Deflection Data for Section: 400505A

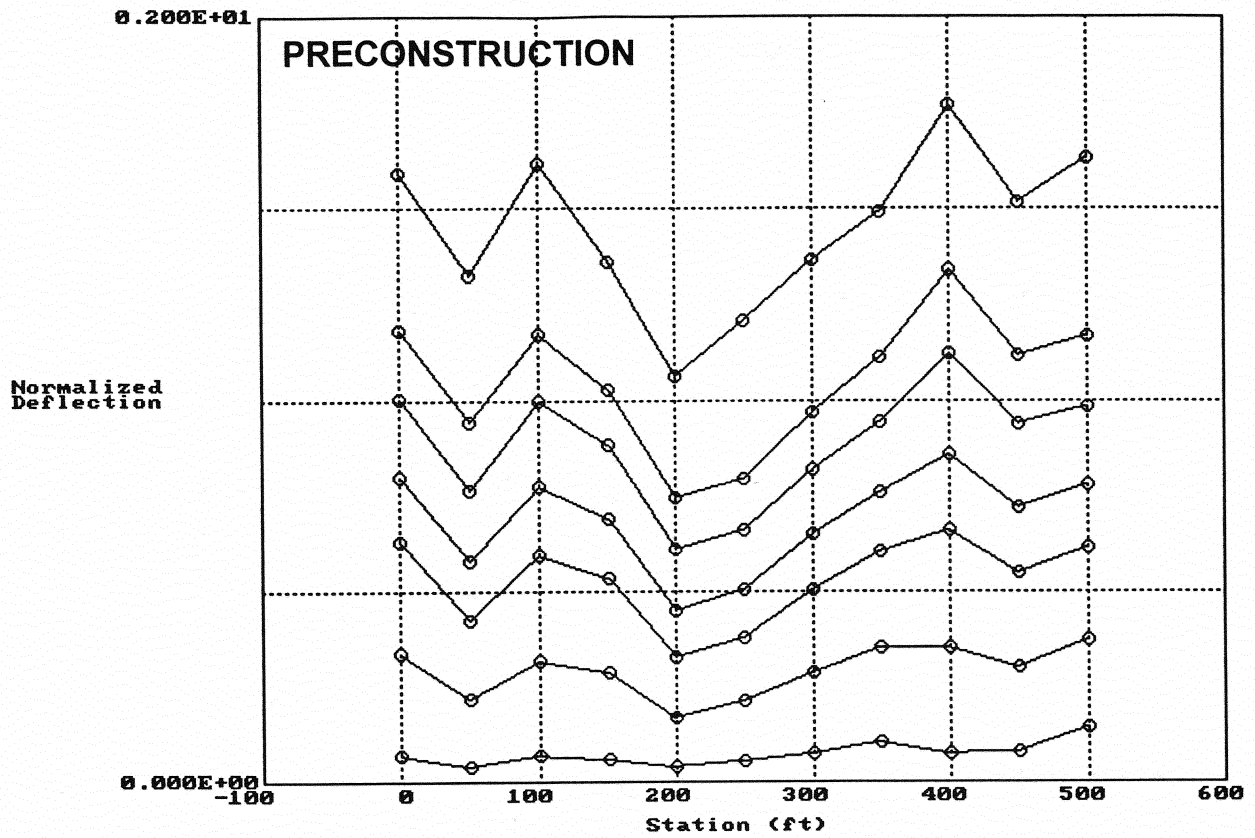


F2:ScrnDump F10:Exit ↑f:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400505C

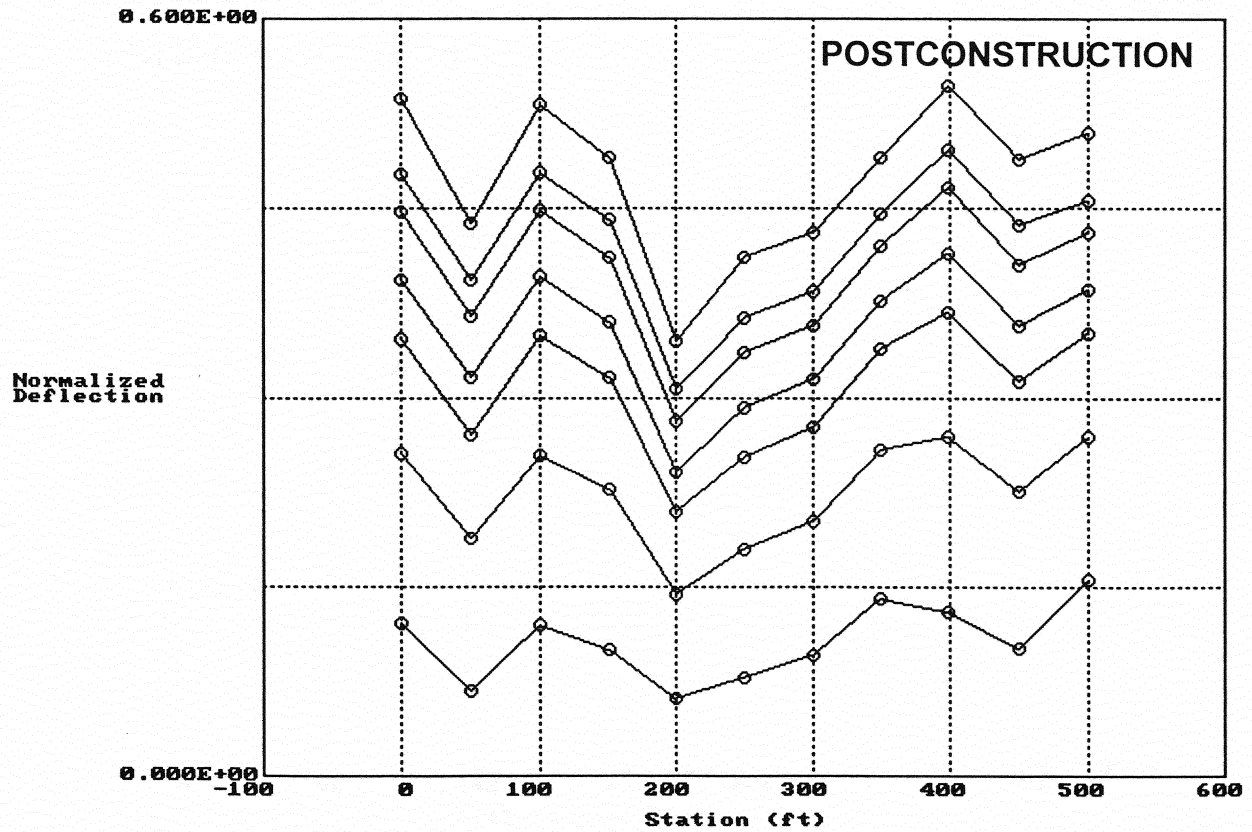


F2:ScrnDump F10:Exit ↑f:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400506A

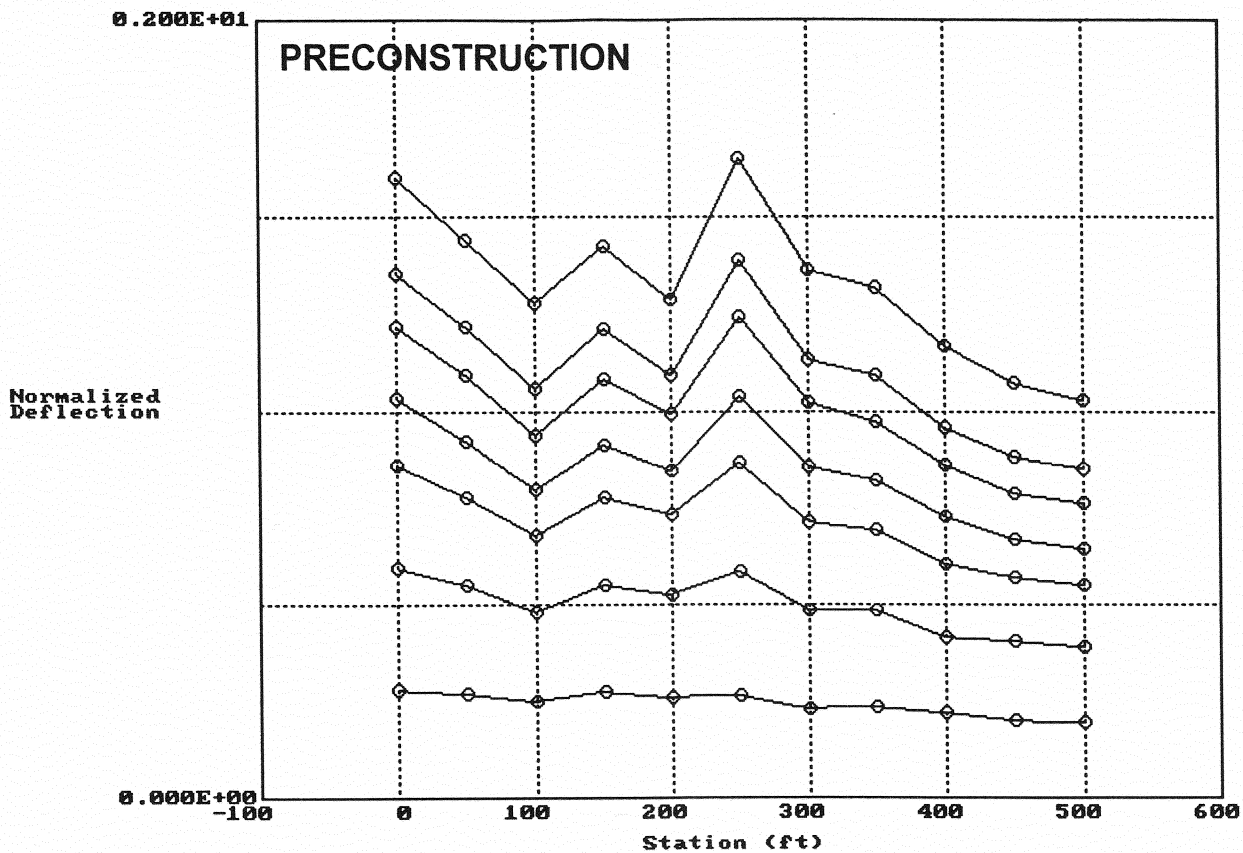


F2:ScrnDump F10:Exit ↑↑:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400506C

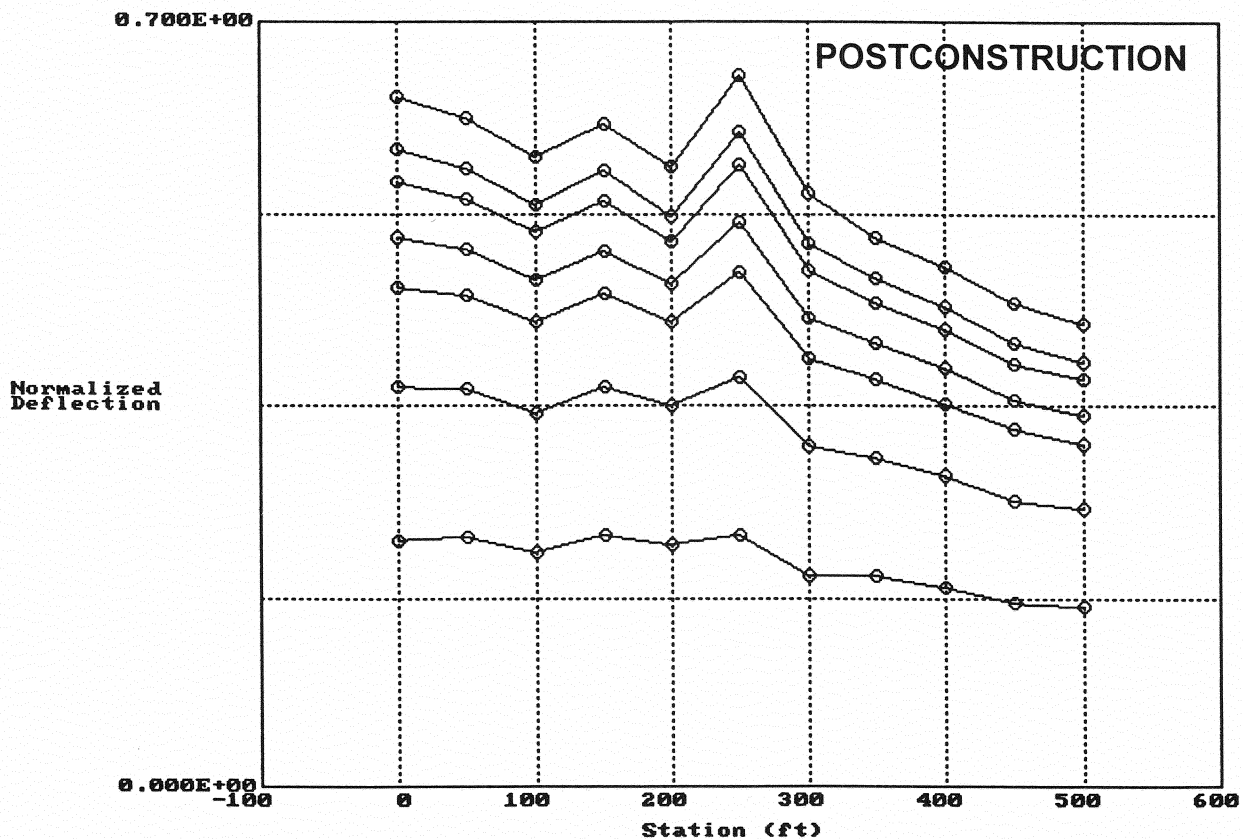


F2:ScrnDump F10:Exit ↑↑:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc


Deflection Data for Section: 400507A

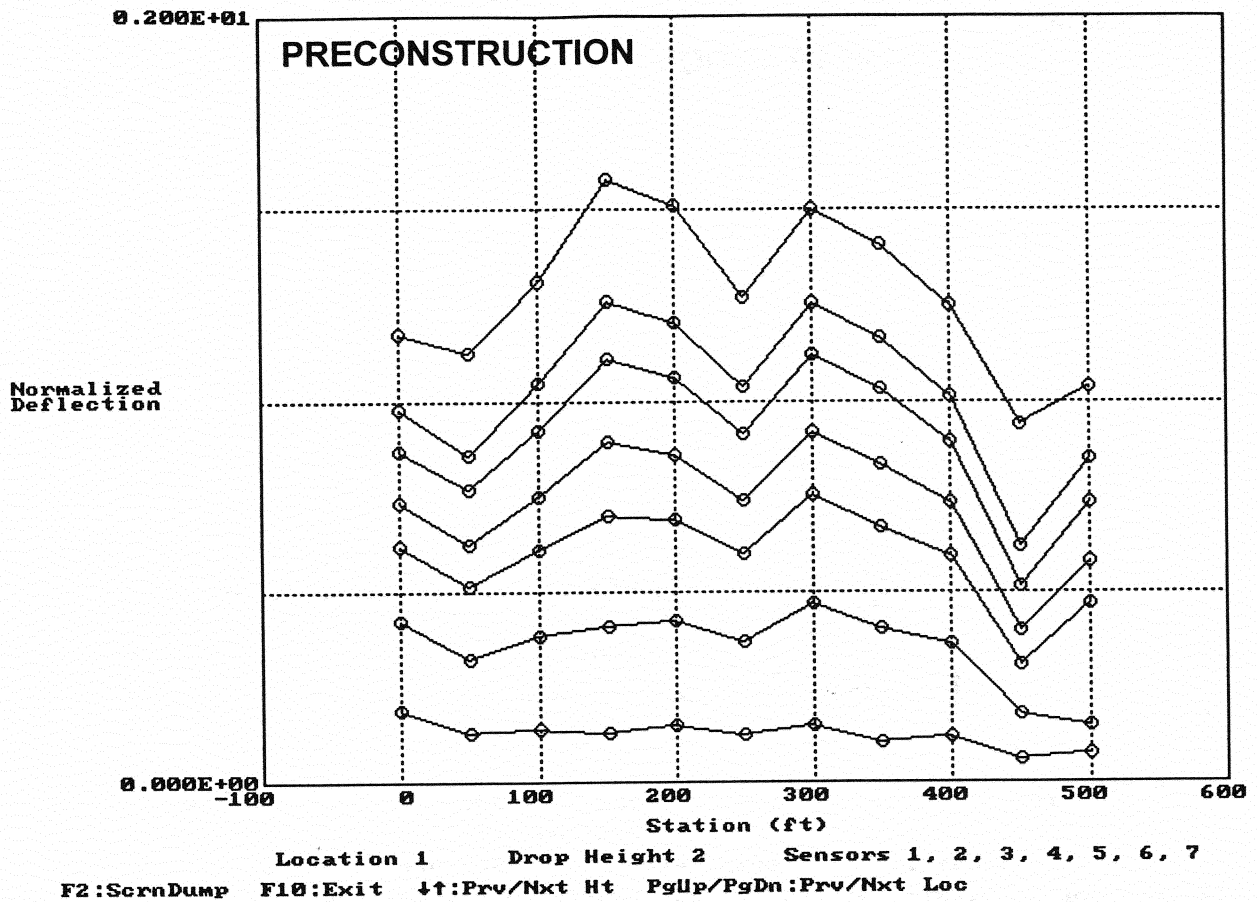

Deflection Data for Section: 400507C

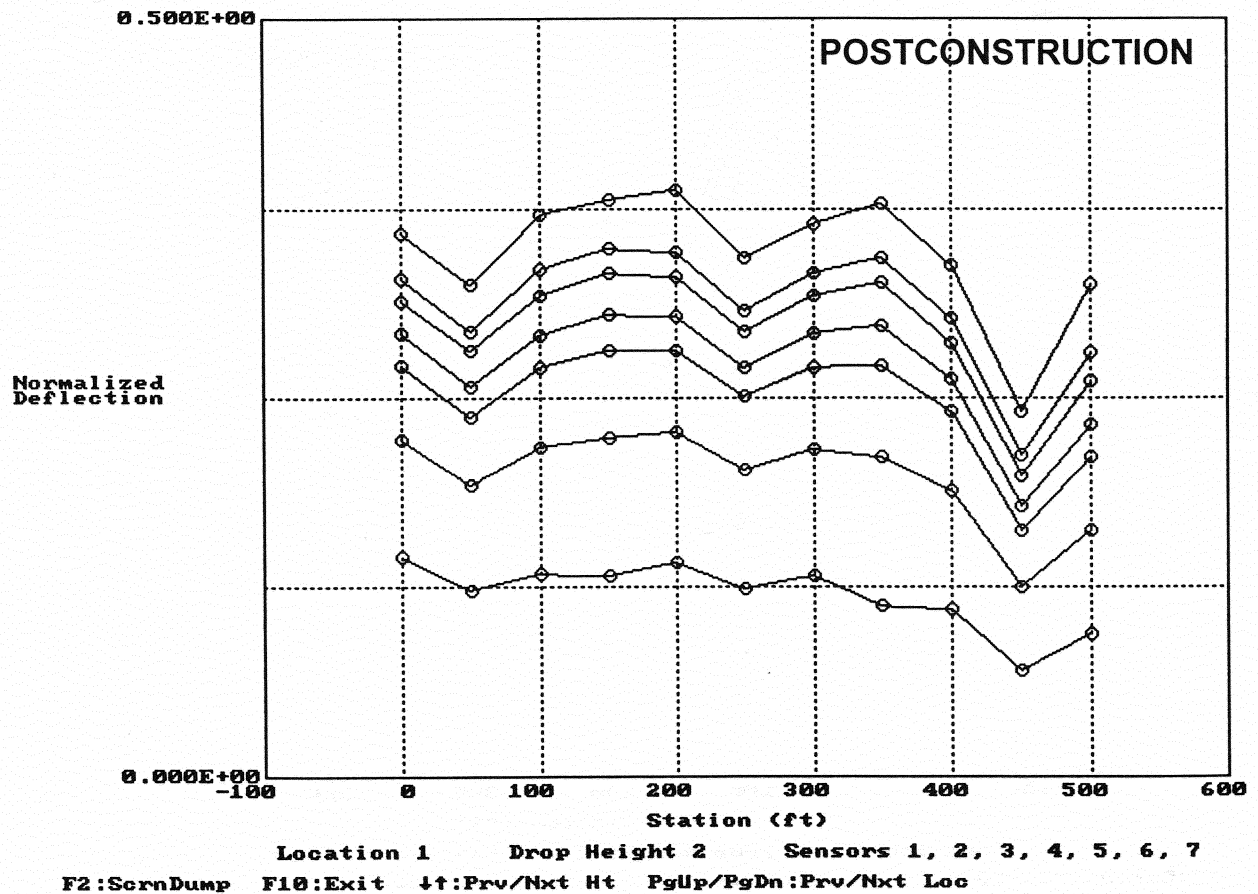


Deflection Data for Section: 400508A

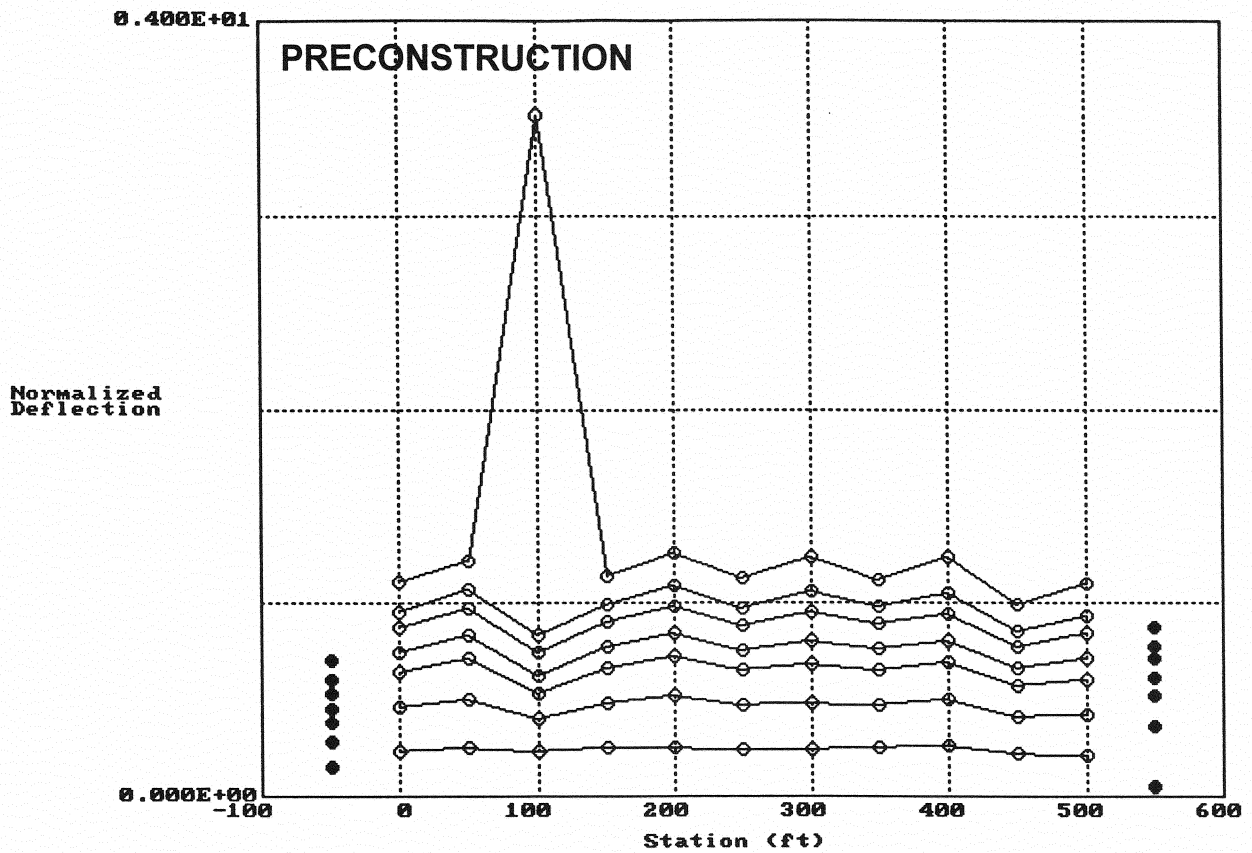


Location 1 Drop Height 2 Sensors 1, 2, 3, 4, 5, 6, 7
 F2:ScrnDump F10:Exit ↑f:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400508C

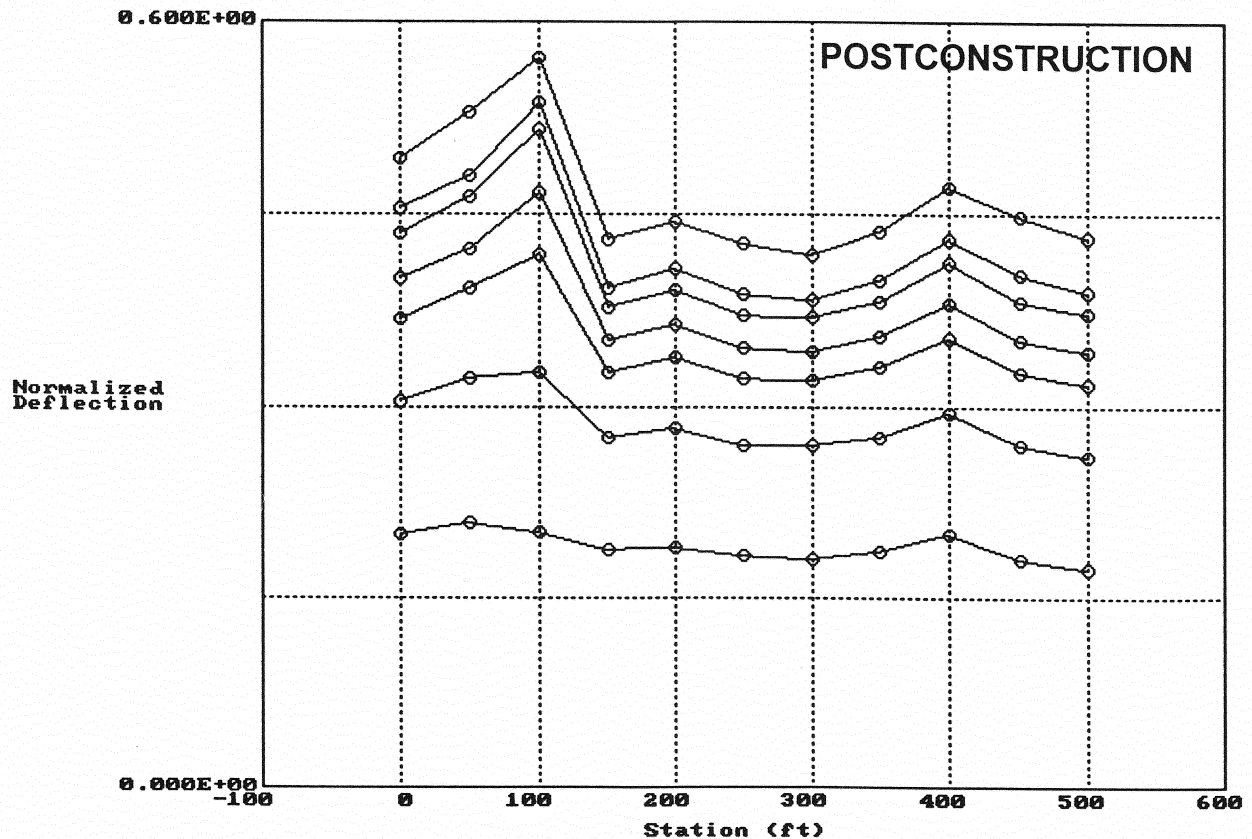


Location 1 Drop Height 2 Sensors 1, 2, 3, 4, 5, 6, 7
 F2:ScrnDump F10:Exit ↑f:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400509A

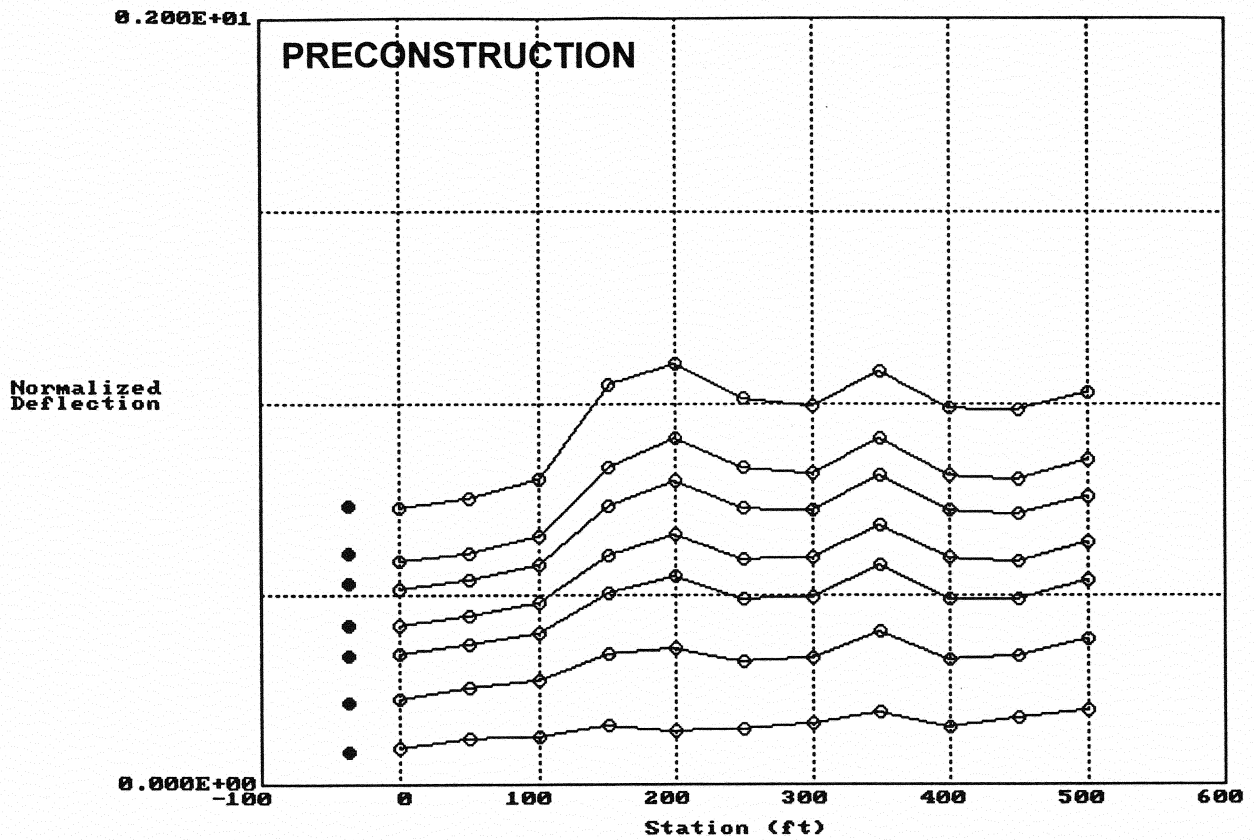


F2:ScrnDump F10:Exit ↑f:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400509C

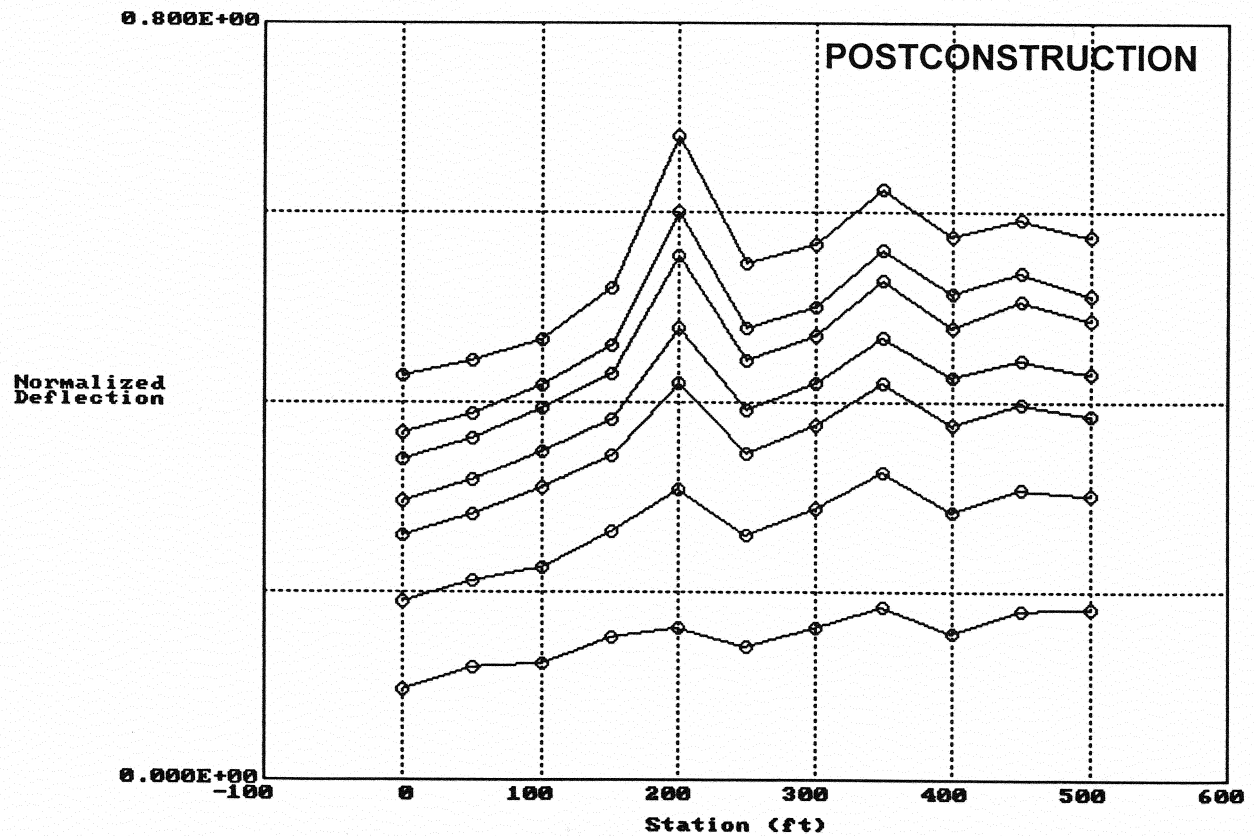


F2:ScrnDump F10:Exit ↑f:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400560A

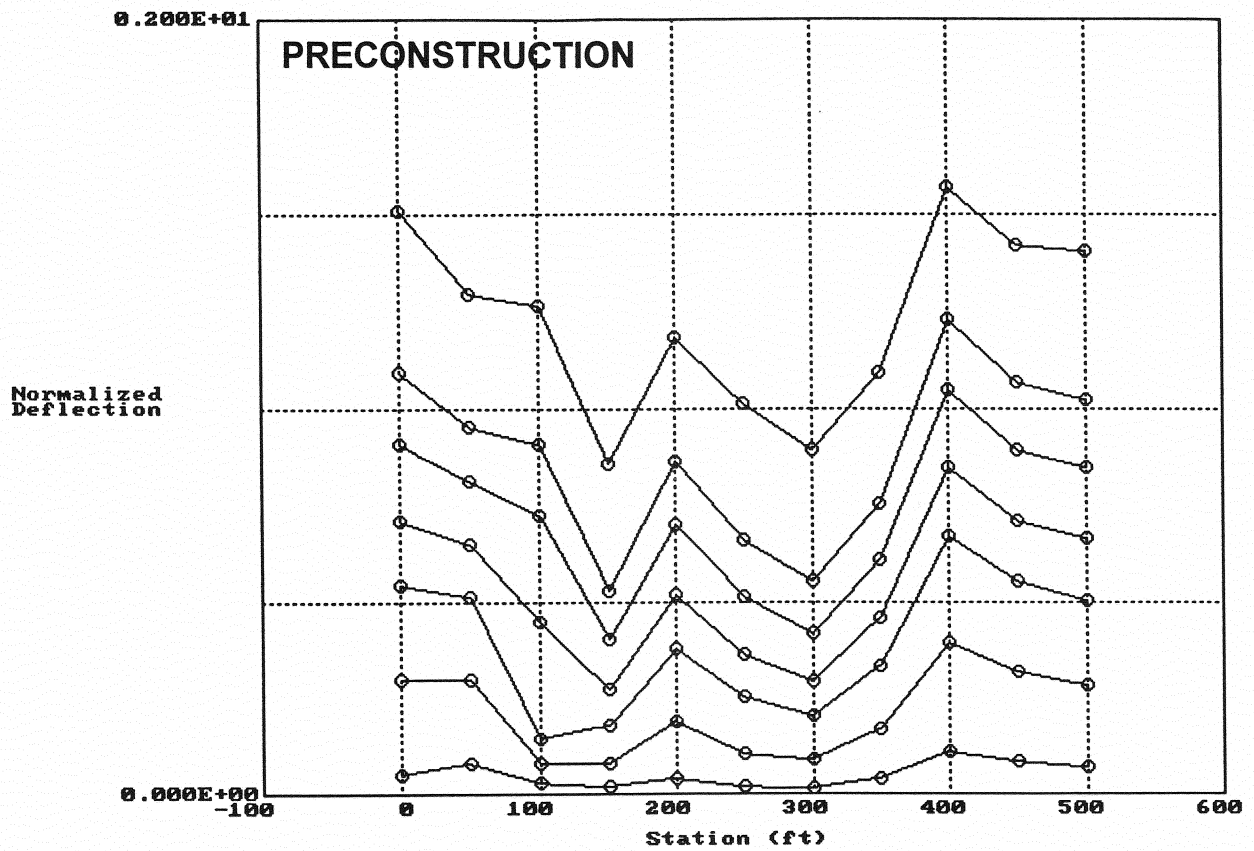

Location 1 Drop Height 2 Sensors 1, 2, 3, 4, 5, 6, 7
 F2:ScrnDump F10:Exit ↑f:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

Deflection Data for Section: 400560C

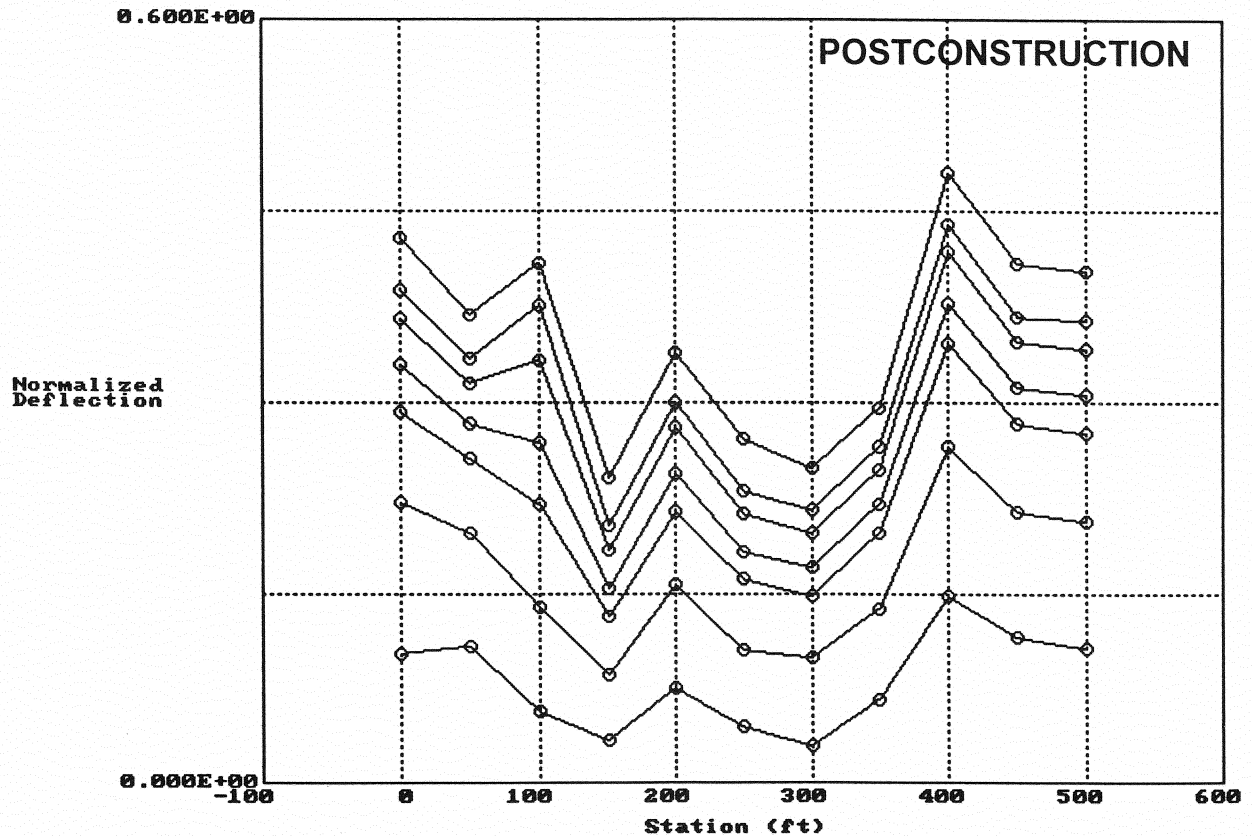

Location 1 Drop Height 2 Sensors 1, 2, 3, 4, 5, 6, 7
 F2:ScrnDump F10:Exit ↑f:Prv/Nxt Ht PgUp/PgDn:Prv/Nxt Loc

APPENDIX D

MATERIALS SAMPLING AND TESTING PLAN

Brent Rauhut Engineering Inc.



2 August 1996

Mr. Glenn Adams
Project Manager
Law Engineering & Environmental Services, Inc.
396 Plasters Avenue, N.E.
Atlanta, Georgia 30324

Subject: Materials Sampling and Testing Plan for SPS-1 and SPS-5 Projects (4001 and 4005) in Oklahoma

Dear Glenn,

Enclosed are the Materials Sampling and Testing Plans for the SPS-1 and SPS-5 projects in Cache, Oklahoma. We plan to begin collection of samples in the very near future. We will coordinate with Ginger McGovern, the Oklahoma DOT Coordinator, to minimize the number of shipments made, so that we can hopefully improve the accountability of the samples collected. We will also send Ginger another copy of the schematics for the assembly of shipping crates (by copy of this letter). I believe Ginger's office was responsible for the preparation of these crates for shipment of the samples from the maintenance effectiveness test sections and should therefore be familiar with these requirements.

Please feel free to contact me should you have any questions regarding these plans, or the projects in general. Thank you for your assistance.

Sincerely,

Jerry F. Daleiden, P.E.
Project Engineer, SRCO

JFD:dmj

Enclosures: As stated.

c.w/Enc: Ginger McGovern, OKDOT

John Miller, PCS/LAW

c.w/o Enc: Aramis Lopez, FHWA/LTPP-PPD
Rod Soule, MRL/Nichols Cons.
Amy Simpson, SRCO

Morris Reinhardt, RE/SRCO
Mark Gardner, SRCO

FROM THE DESK OF

Jerry Daleiden

6/22/96

GINGER

HERE IS THE REVISED MATERIALS
SAMPLING & TESTING PLAN FOR
THE SPS-5 PROJECT. EDITS HAVE
BEEN MADE TO REFLECT THE
REVISED LAYOUT OF 6/20/96.
PLEASE CALL IF I CAN BE OF
FURTHER ASSISTANCE.

THANK YOU

Jerry

Brent Rauhut Engineering Inc.



12 July 1996

Ms. Ginger McGovern
Oklahoma Department of Transportation
200 N.E. 21st Street, Room 2A2
Oklahoma City, Oklahoma 73105-3204

Subject: Revised Materials Sampling and Testing Plans

Dear Ginger,

Enclosed are the revised Materials Sampling and Testing Plans incorporating the revisions and standard Oklahoma DOT sections per our discussions earlier this week.

Please let me know if we can be of any further assistance.

Sincerely,

A handwritten signature in black ink, appearing to read 'Jerry'.

Jerry F. Daleiden, P.E.
Project Engineer, SRCO

JFD:dmj

Enclosures: As stated.

c.w/Enc: Rosemarie Case, OKDOT
Tim Martin, SRCO

MATERIAL SAMPLING AND TESTING PLAN

**OKLAHOMA SPS-5 PROJECT 400500
COMANCHE COUNTY, OKLAHOMA
US-62 WESTBOUND**

PREPARED BY:

**BRENT RAUHUT ENGINEERING INC.
FHWA/LTPP SOUTHERN REGION COORDINATION OFFICE
8240 MOPAC, SUITE 220
AUSTIN, TEXAS 78759**

REVISED JULY 1996

**MATERIAL SAMPLING AND TESTING PLAN
OKLAHOMA SPS-5 PROJECT (400500), US-62 WBL
COMANCHE COUNTY, OKLAHOMA**

INTRODUCTION

As part of their participation in the FHWA/LTPP studies, the State of Oklahoma has elected to construct an SPS-5 project to study the rehabilitation of flexible pavements. This project will consist of multiple test sections with similar details and materials along US-62, in the westbound lane, in Comanche County, Oklahoma. It is the intent of this document to provide a complete plan for the material sampling, testing, and laboratory material testing that will occur as a part of this project.

This document has been prepared in accordance with guidelines provided by the Strategic Highway Research Program in Operational Memorandum N^o.SHRP-LTPP-OM-014, entitled "Specific Pavement Studies Material Sampling and Testing Requirements for Experiment SPS-5, Rehabilitation of Asphalt Concrete Pavements, October 1990". Recognizing the apparent variability in the construction of roadway projects, the goal of this effort is to develop a sampling and testing plan for the project materials that will be consistent with other projects in this experiment, and therefore make the information obtained suitable for analysis.

The objective of the SPS-5 study is to evaluate rehabilitation methods that can be used to restore the condition and extend the service life of flexible (asphalt concrete) pavements. The pavement type and condition, environment, traffic, intended pavement preparation, and type of asphalt concrete overlay are primary considerations in selecting an appropriate rehabilitation method. The standard SPS-5 experiment layout includes nine test sections. The in-service tests proposed in this experiment will help quantify the influence of these parameters on pavement performance and life expectancy, and improve current design procedures. Consequently, the experiment will help highway agencies select methods and strategies for rehabilitation of existing flexible pavements.

This sampling and testing plan has been developed by Brent Rauhut Engineering, Inc. the Southern Region Coordination Office under contract to the Federal Highway Administration. If, during the construction activities, any questions arise regarding the sampling and/or testing to be conducted, one should first coordinate these questions with the Oklahoma Department of Transportation, who may refer them to the Southern Region Coordination Office.

This document has been prepared in three distinct parts, each covering a particular area of this rather formidable exercise. The three sections are:

- A. General Layout Information
- B. Materials Sampling and Testing
- C. Laboratory Material Testing

The General Layout section provides tables and figures of the layout showing the nine test sections along the roadway and the layer structure of each test section.

The Material Sampling and Testing section defines in detail all of the material samples to be obtained, testing to be performed in the field, and provides an itemized list showing where each sample is to be shipped for laboratory testing.

Finally, the Laboratory Material Testing section outlines the laboratory material test program to be conducted and provides tracking charts showing the testing to be performed on each sample of each material in each laboratory.

SECTION A

GENERAL LAYOUT INFORMATION

SECTION A

GENERAL LAYOUT INFORMATION

This section of the plan provides a description of the SPS-5 project in terms of the location of the test sections along the roadway. Table A-1 lists the test sections in order of increasing station, providing an indication of the cross-section of each test section. Table A-2 tracks the test sections from the beginning of the first section at Station 832 to the end of the last section at Station 948. This table indicates transition areas between sections and the variation of pavement layer materials within these transitions.

Finally, Figure A-1 depicts the layout of the test sections along the roadway and shows the variation of material type and layer thickness.

The referenced project stationing was provided by the Oklahoma DOT in the form of preliminary project plans. If there are significant changes in alignment or stationing, this plan should be reviewed closely to determine if revisions are warranted.

TABLE A-1. TEST SECTION LAYOUT

Section (Cell ID)	Cross Section	Begin Station	End Station
400501	Control Section Routine Maintenance	832	839
400502	Minimum Surface Prep.	841	848
	2" Recycled AC Overlay		
400503	Minimum Surface Prep.	851	858
	5" Recycled AC Overlay		
400508	Intensive Surface Prep.	864	871
	5" Recycled AC Overlay		
400509	Intensive Surface Prep.	875	882
	2" Recycled AC Overlay		
400506	Intensive Surface Prep.	897	904
	2" Virgin AC Overlay		
400507	Intensive Surface Prep.	916	923
	5" Virgin AC Overlay		
400504	Minimum Surface Prep.	925	932
	5" Virgin AC Overlay		
400505	Minimum Surface Prep.	941	948
	2" Virgin AC Overlay		
400560	Minimum Maximum Surface Prep.	968	975
	3½" Virgin AC Overlay		

TABLE A-2. ORDERING OF SECTIONS ALONG CENTER LINE STATIONING

Begin Sta.	End Sta.	Section ID	Thickness (In.)		
			AC Overlay*	Material Type	Milled Depth
832	839	400501	0	N/A	0
839	841	Transition	0-2	Recycled	0
841	848	400502	2	Recycled	0
848	851	Transition	5	Recycled	0
851	858	400503	5	Recycled	0
858	864	Transition	5	Recycled	0-2 1/2
864	871	400508	5	Recycled	2 1/2
871	875	Transition	2	Recycled	2 1/2
875	882	400509	2	Recycled	2 1/2
882	897	Transition	2	Virgin-Recycled	2 1/2
897	904	400506	2	Virgin	2 1/2
904	916	Transition	2-5	Virgin	2 1/2
916	923	400507	5	Virgin	2 1/2
923	925	Transition	5	Virgin	1/2 2-0
925	932	400504	5	Virgin	0
932	941	Transition	5-2	Virgin	0
941	948	400505	2	Virgin	0
948	968	Transition	2-3 1/2	Virgin	0-1 1/2
968	975	400560	3 1/2	Virgin	0 1/2

* Combined Binder and Wearing Course Thickness

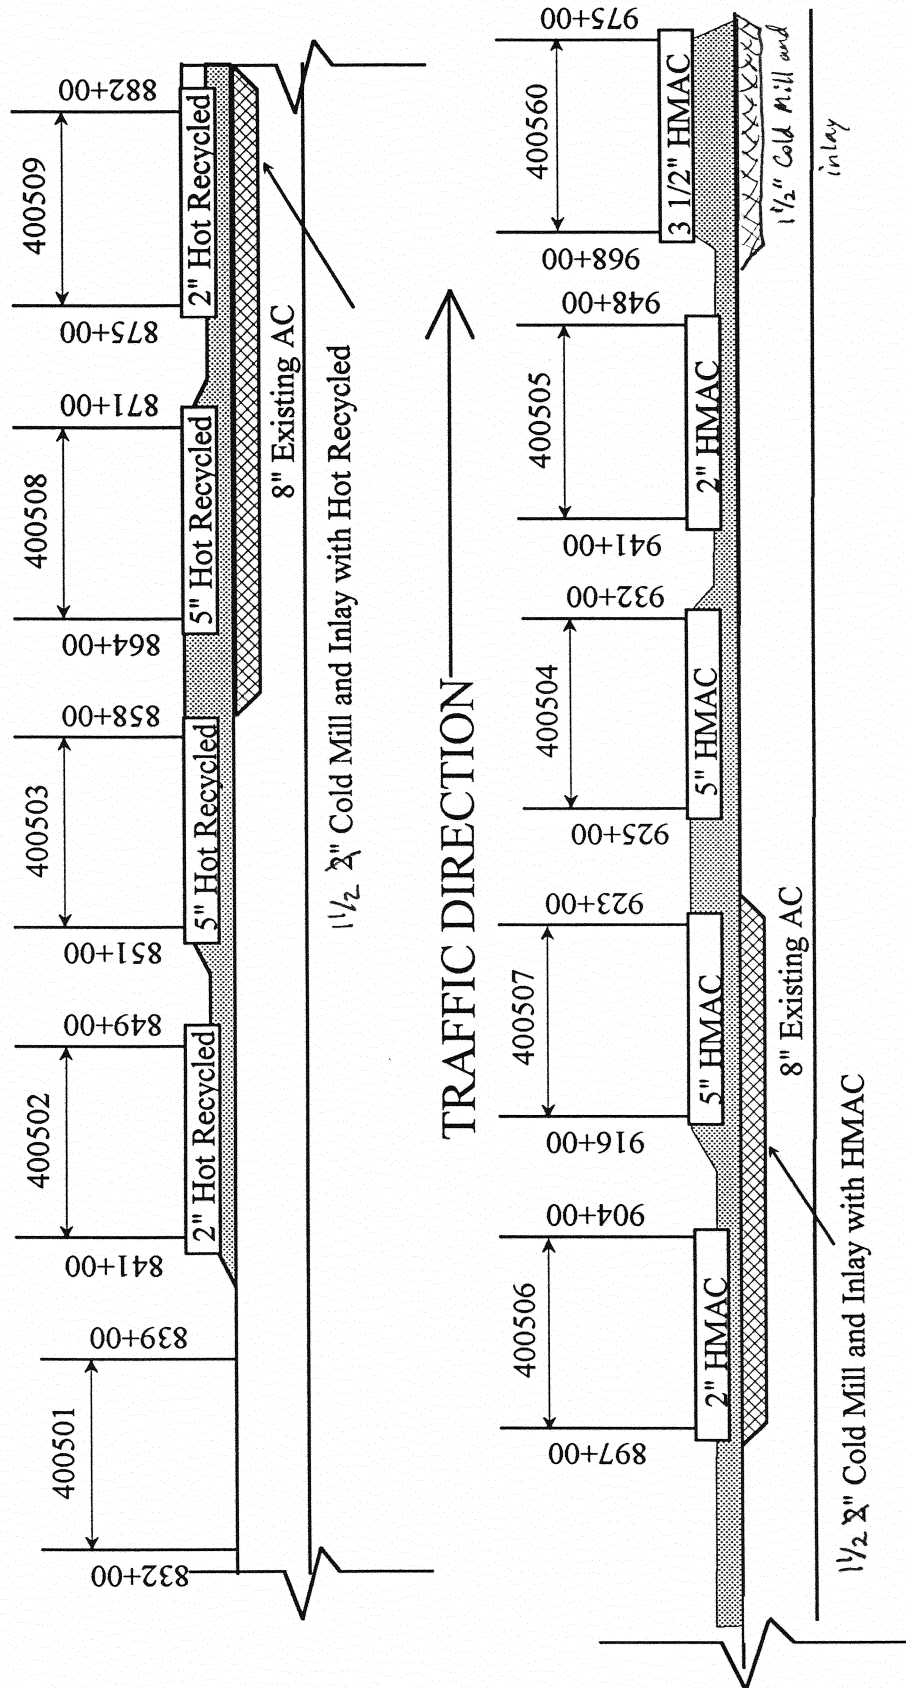


FIGURE A-1. LAYOUT OF TEST SECTIONS
OKLAHOMA SPS-5 (400500)

SECTION B

MATERIAL SAMPLING AND TESTING

SECTION B

MATERIAL SAMPLING AND TESTING

This section of the plan provides for the material sampling and testing activities that occur in the field. Table B-1 provides the project layer numbering schema, while Table B-2 provides the scope of the material sampling and testing activities. It is very important that the project layer numbering be consistent, to ensure that the resulting data is not misunderstood. Table B-3 describes special sampling needs for the Materials Reference Library and provides contact information to coordinate sample shipping arrangements.

Figures B-1 through B-12 show the locations and numbering scheme for the many samples and tests scheduled. Figures B-2 and B-3 show the sampling and testing to occur for each stage of the paving, while Figures B-4 through B-12 show all sampling and testing scheduled for each test section.

Finally, Tables B-4 and B-5 list samples to be shipped to the state laboratory (or their designee), and those samples to be shipped to the FHWA/LTPP testing contractor, respectively. Shipment of samples to the FHWA/LTPP testing contractor, LAW Engineering in Atlanta, Georgia, should be coordinated through the Southern Region Coordination Office.

TABLE B-1. PROJECT LAYER NUMBERING

Layer Nº.	LTPP Description	Oklahoma Description
1	Subgrade	Silty Clay
2	Asphalt Treated Base	Plant Mix Bituminous Base
3	Hot Mix Asphalt Concrete Binder (Existing)	Asphaltic Concrete, Type A
4	Hot Mix Asphalt Concrete Surface (Existing)	Asphaltic Concrete, Type C
5	Hot Mix Asphalt Concrete Overlay Virgin Binder	Asphaltic Concrete, Type AH
6	Hot Mix Asphalt Concrete Overlay Virgin Surface	Asphaltic Concrete, Type BH
7	Hot Mix Asphalt Concrete Overlay Recycled Binder	Asphaltic Concrete, Type AH
8	Hot Mix Asphalt Concrete Overlay Recycled Surface	Asphaltic Concrete, Type BH

TABLE B-2. SCOPE OF MATERIALS SAMPLING AND FIELD TESTING

MATERIAL & SAMPLING DESCRIPTION	Nº. OF MATERIAL SAMPLES	SAMPLE TYPE DESIGNATION
<u>PRE-CONSTRUCTION SAMPLING</u>		
1. Asphalt Concrete (Original Layer)		
Coring - 4" diam. cores	28	C1-C28
Coring - 6" diam. cores	3	A1-A3
Coring - 12" diam. cores	6	BA1-BA6
2. Unbound Base/Subbase Layers (Per Layer)		
Augering 6" diam. holes	3	A1-A3
Bulk Sampling in 12" diam. holes	6	BA1-BA6
Bulk Sampling in Test Pits	1	TP1
In Situ Density & Moisture Content (Nuclear Gauge)	1	TP1
Moisture Content Samples	7	TP1, BA1-BA6
3. Subgrade		
Thin-walled Tube Sampling *(Two tube samples per hole. If undisturbed tube sampling is not possible, splitspoon sampling will be conducted.)	6*	A1-A3
Bulk Sampling in 12" diam. holes	6	BA1-BA6
Bulk Sampling in Test Pits	1	TP1
In Situ Density & Moisture Content (Nuclear Gauge)	1	TP1
Moisture Content Samples	7	BA1-BA6, TP1
4. Shoulder Auger Probes	3	S1-S3
<u>DURING CONSTRUCTION SAMPLING</u>		
1. Virgin Asphalt Concrete - 100 lb/mix (Uncompacted Mix)	3 3	BV1-BV3 (BINDER) AH BV4-BV6 (SURFACE) BH
2. Recycled Asphalt Concrete - 100 lb/mix (Uncompacted Mix)	3 3	BR1-BR3 (BINDER) AH BR4-BR6 (SURFACE) BH
<u>POST-CONSTRUCTION SAMPLING</u>		
1. Asphaltic Concrete (Overlay)		
Coring - 4" diam. cores	44	C29-C72

**TABLE B-3. MATERIAL SAMPLING FOR
THE MATERIALS REFERENCE LIBRARY (MRL)**

Material And Sample Description	Nº. Of Samples	Sample Location
Asphalt Cement (5 Gallon Containers Each Type Used)	3	From Plant
Aggregate (55 Gallon Drum Each Blend)	1	From Plant
Finished Asphaltic Concrete Mix (5 Gallon Containers Each Mix)	3	From Paver

Note: Containers for this sampling will be provided by the LTPP Materials Reference Library (MRL). Scheduling information including (1) date containers needed, (2) state agency contact name, and (3) shipping address and telephone number should be provided to the MRL Contractor as soon as it is feasible to do so. The contact name, address and telephone number for the MRL Contractor are as follows:

Mr. Rod Soule
Nichols Consulting Engineers, Chtd.
1625 Crane Way
Reno, Nevada 89431
(702) 358-7574

These samples should be labeled according to applicable guidelines provided elsewhere and shipped to the MRL Contractor upon completion of sampling activities.

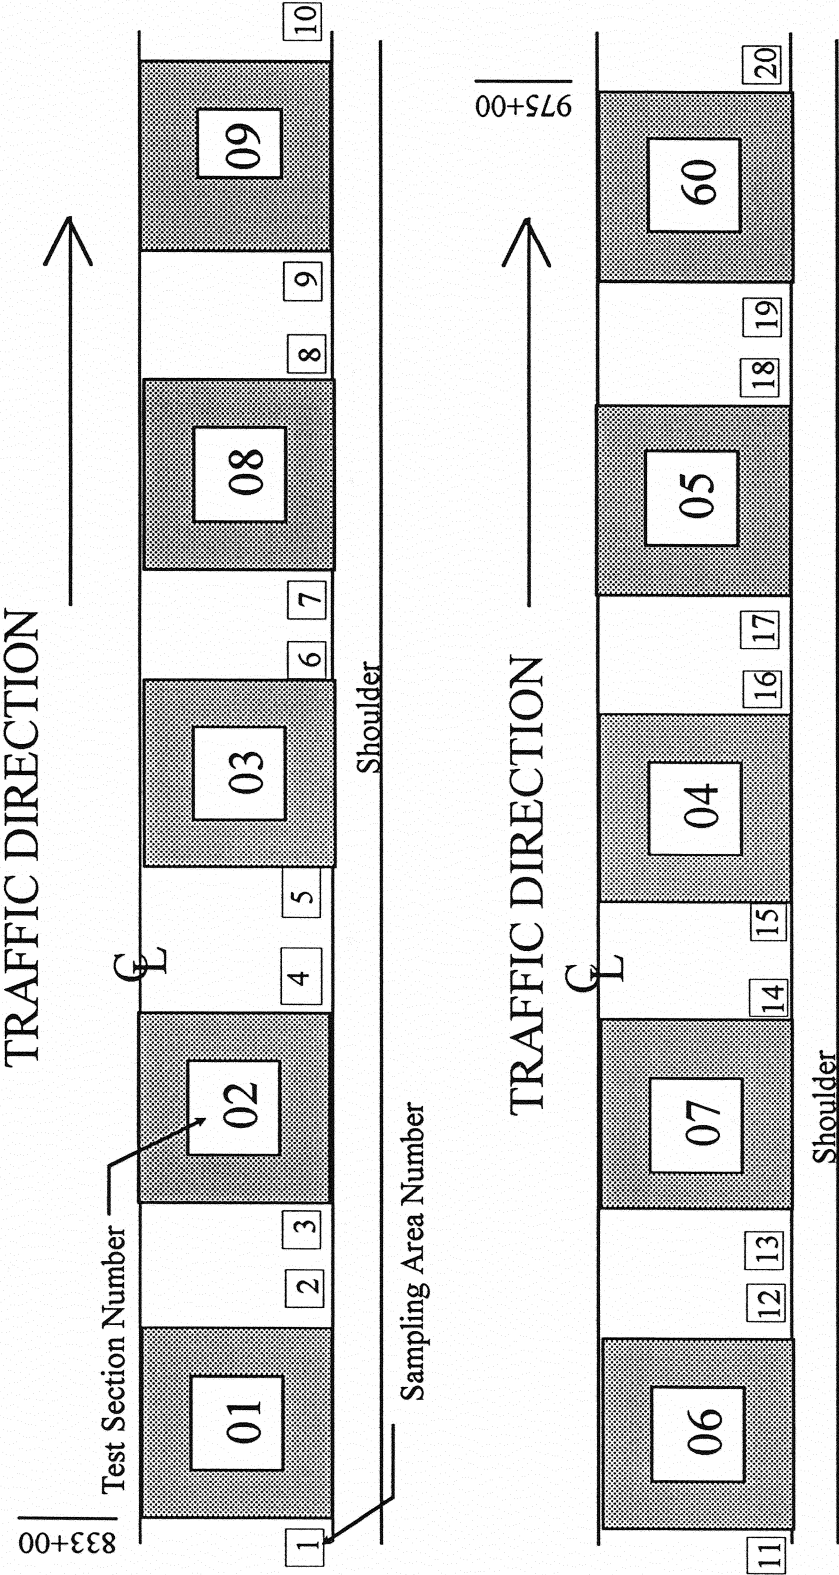


FIGURE B-1. SITE LAYOUT WITH SAMPLING AREAS
OKLAHOMA SPS-5 (400500)

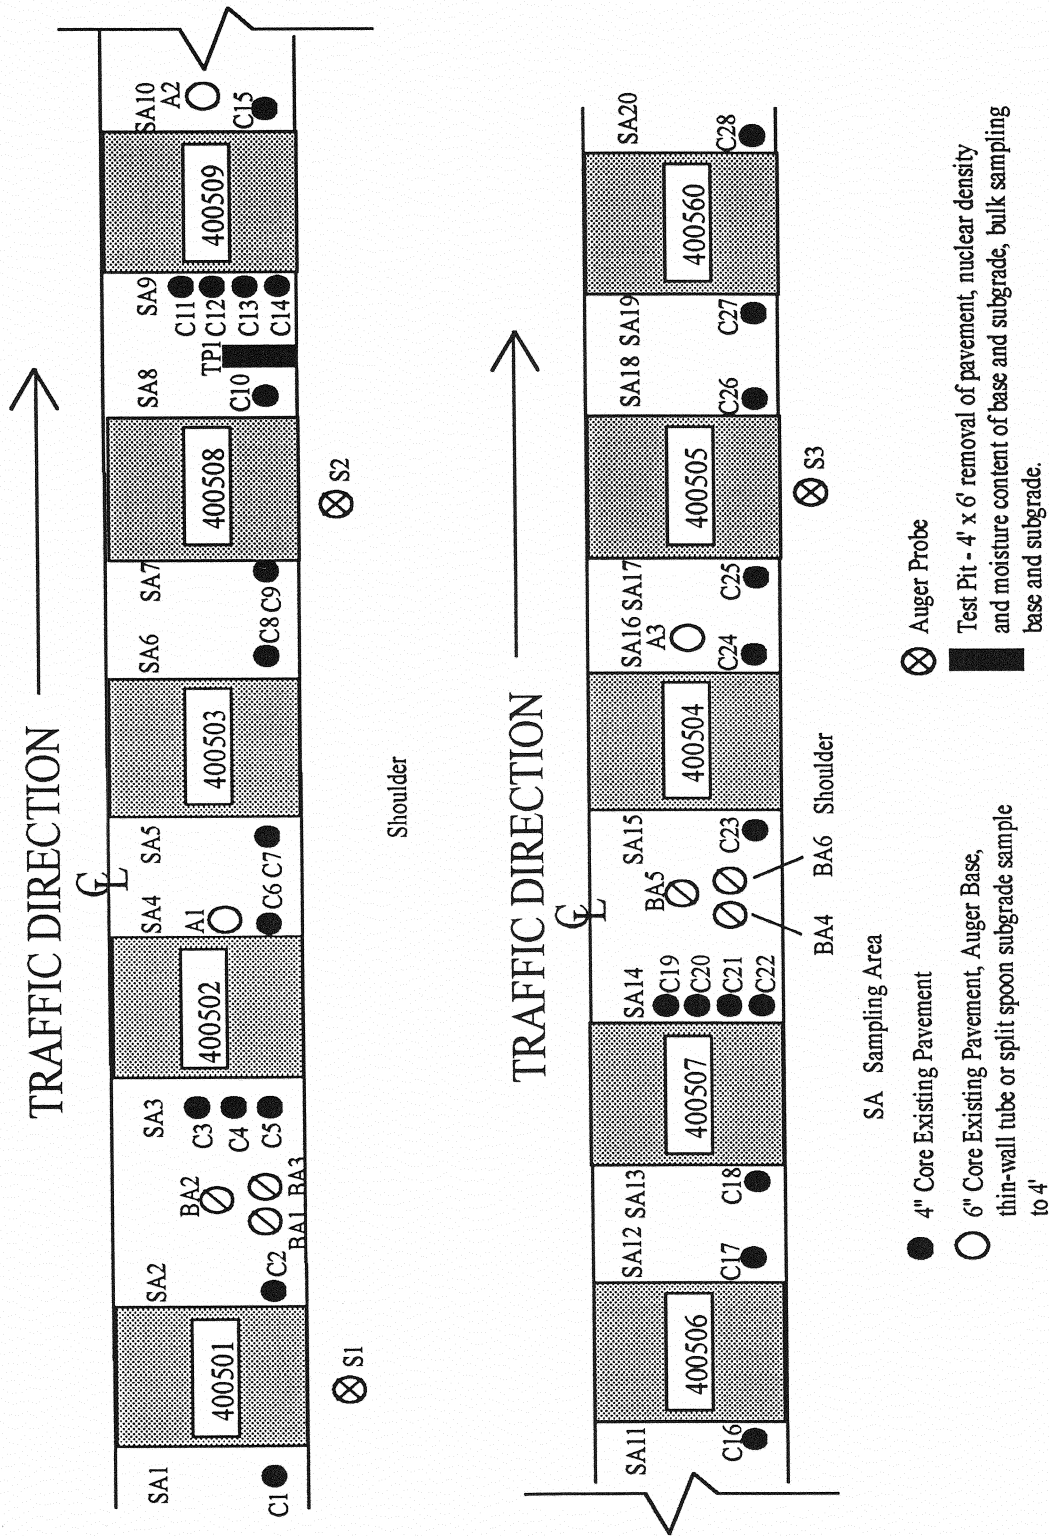


FIGURE B-2. PRECONSTRUCTION SAMPLING AND TESTING LOCATIONS
 OKLAHOMA SPS-5 (400500)



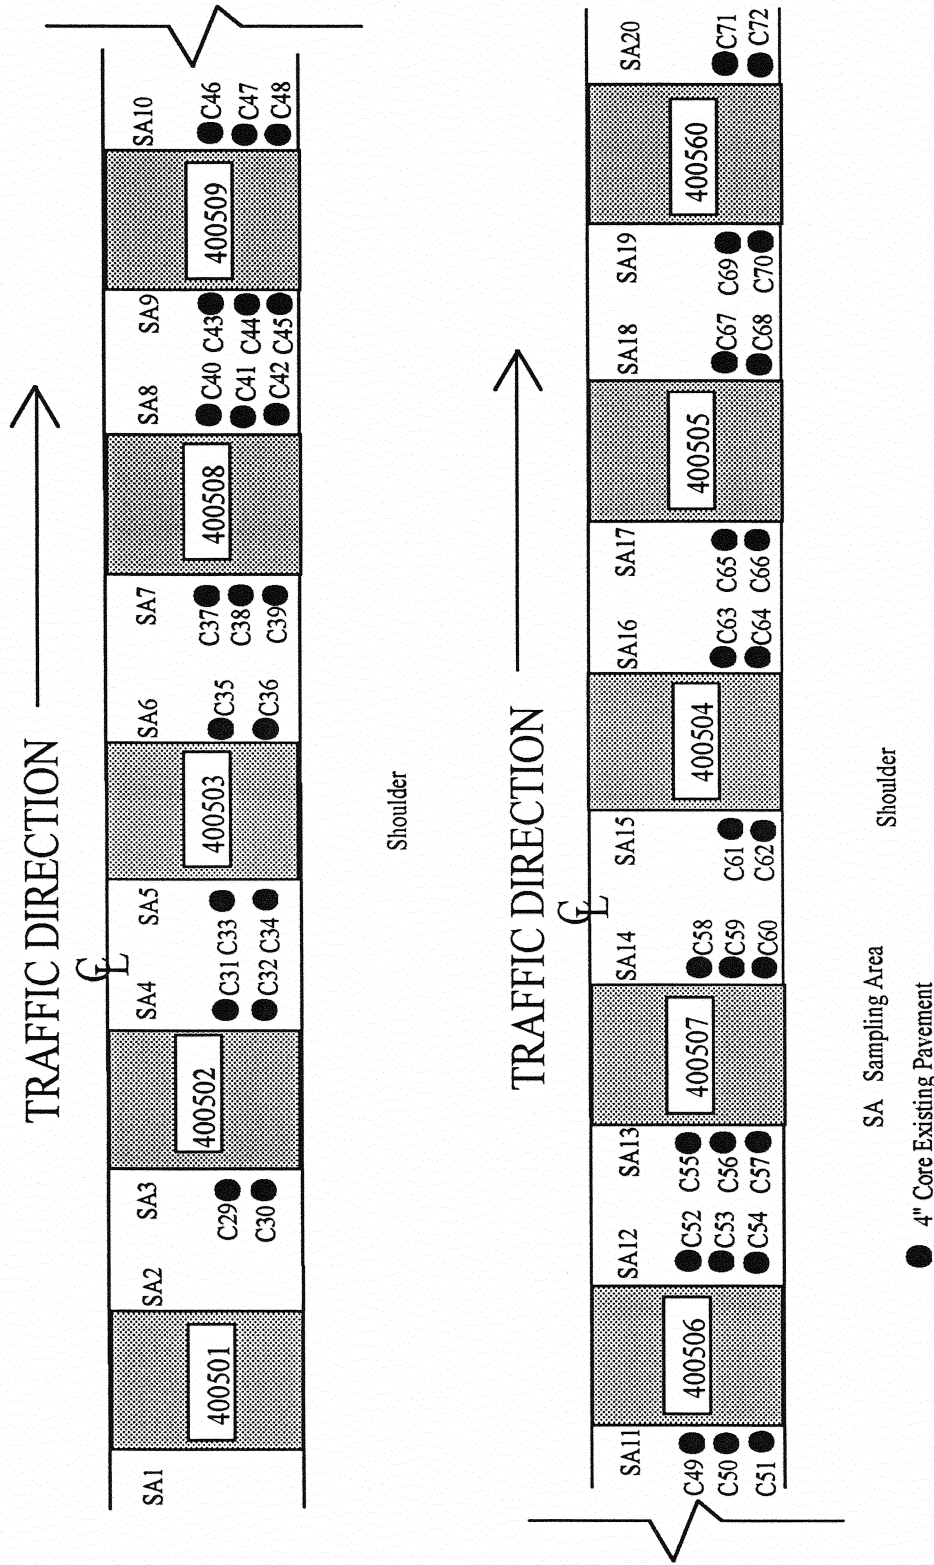



FIGURE B-3. POSTCONSTRUCTION SAMPLING AND TESTING LOCATIONS
OKLAHOMA SPS-5 (400500)

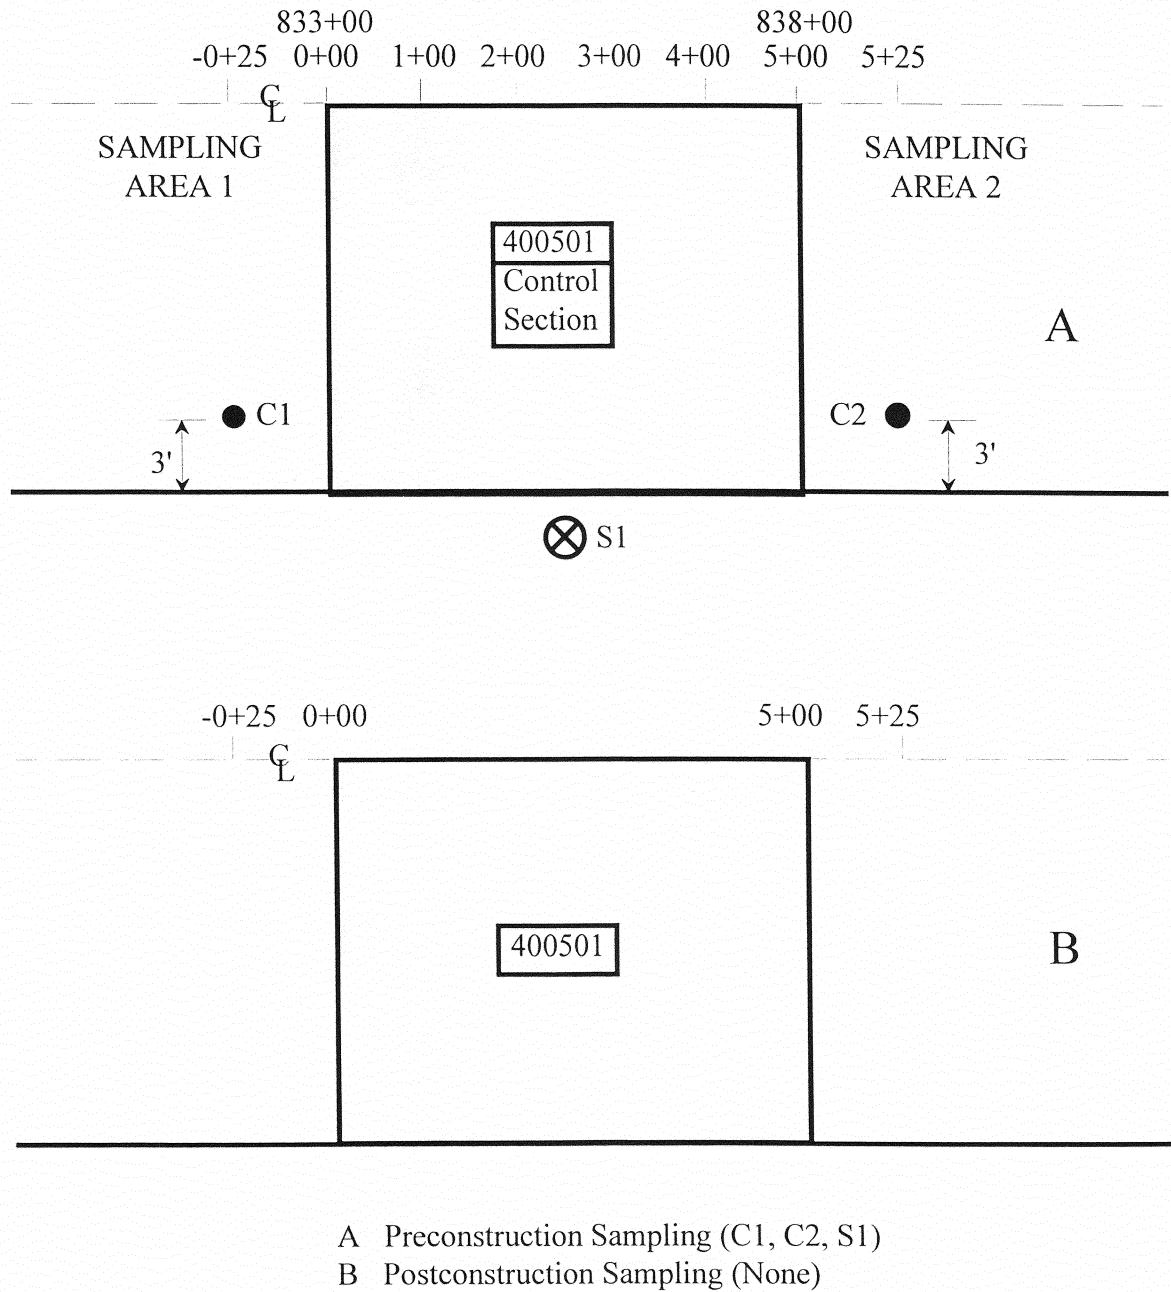


**FIGURE B-4. SAMPLING AND TESTING PLAN FOR TEST SECTION 400501
OKLAHOMA SPS-5 (400500)**

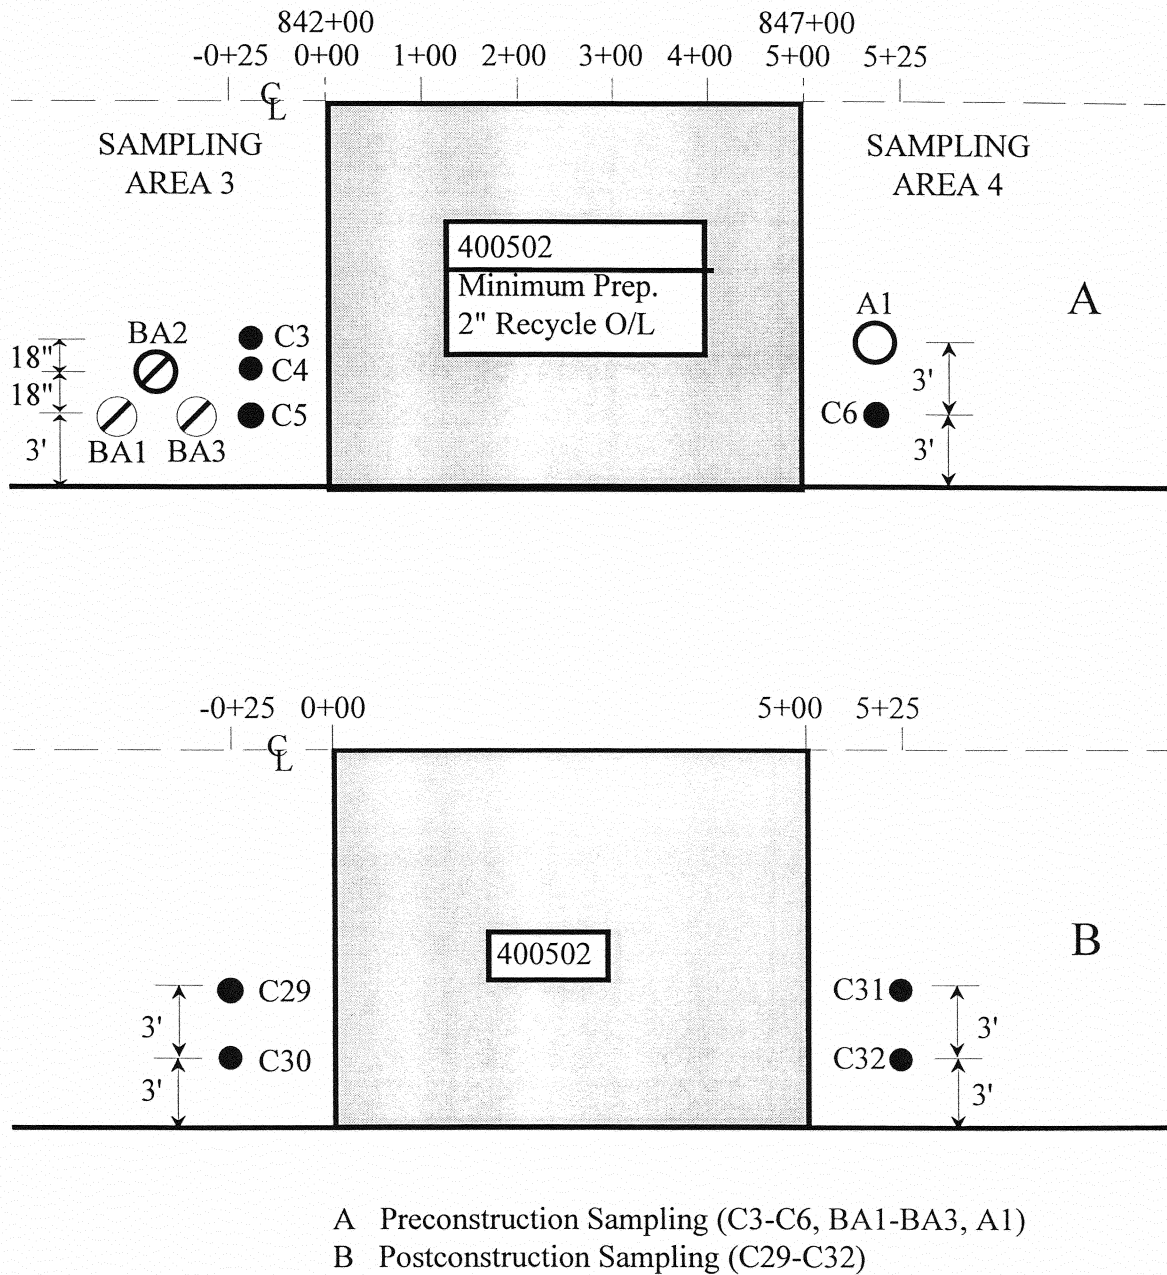


**FIGURE B-5. SAMPLING AND TESTING PLAN FOR TEST SECTION 400502
OKLAHOMA SPS-5 (400500)**

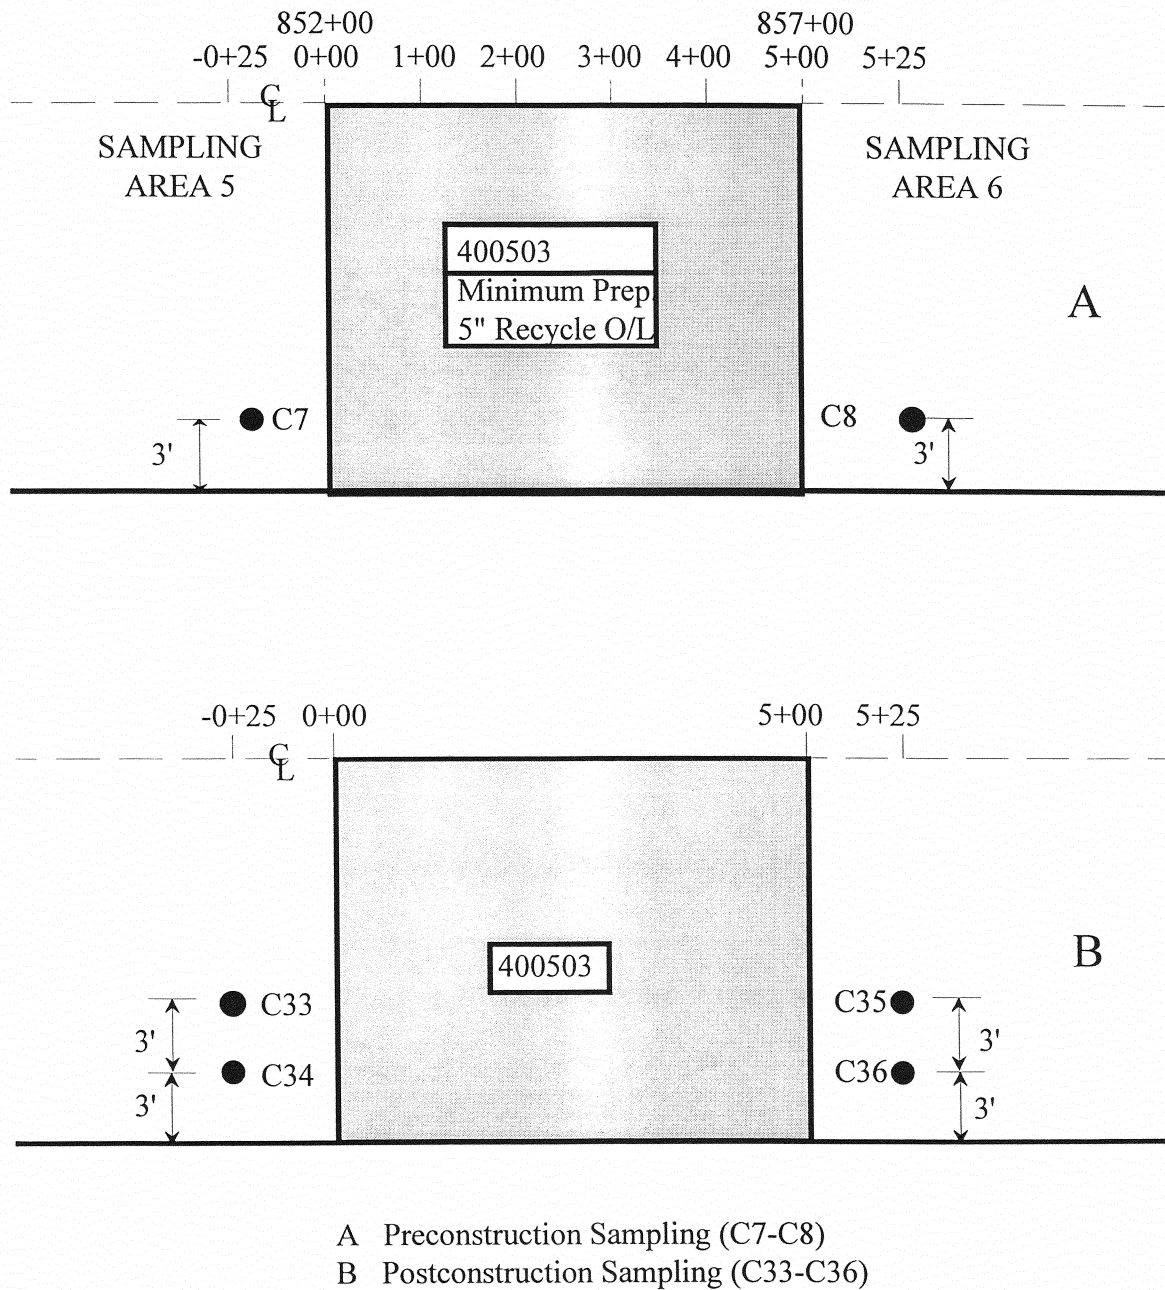


**FIGURE B-6. SAMPLING AND TESTING PLAN FOR TEST SECTION 400503
OKLAHOMA SPS-5 (400500)**

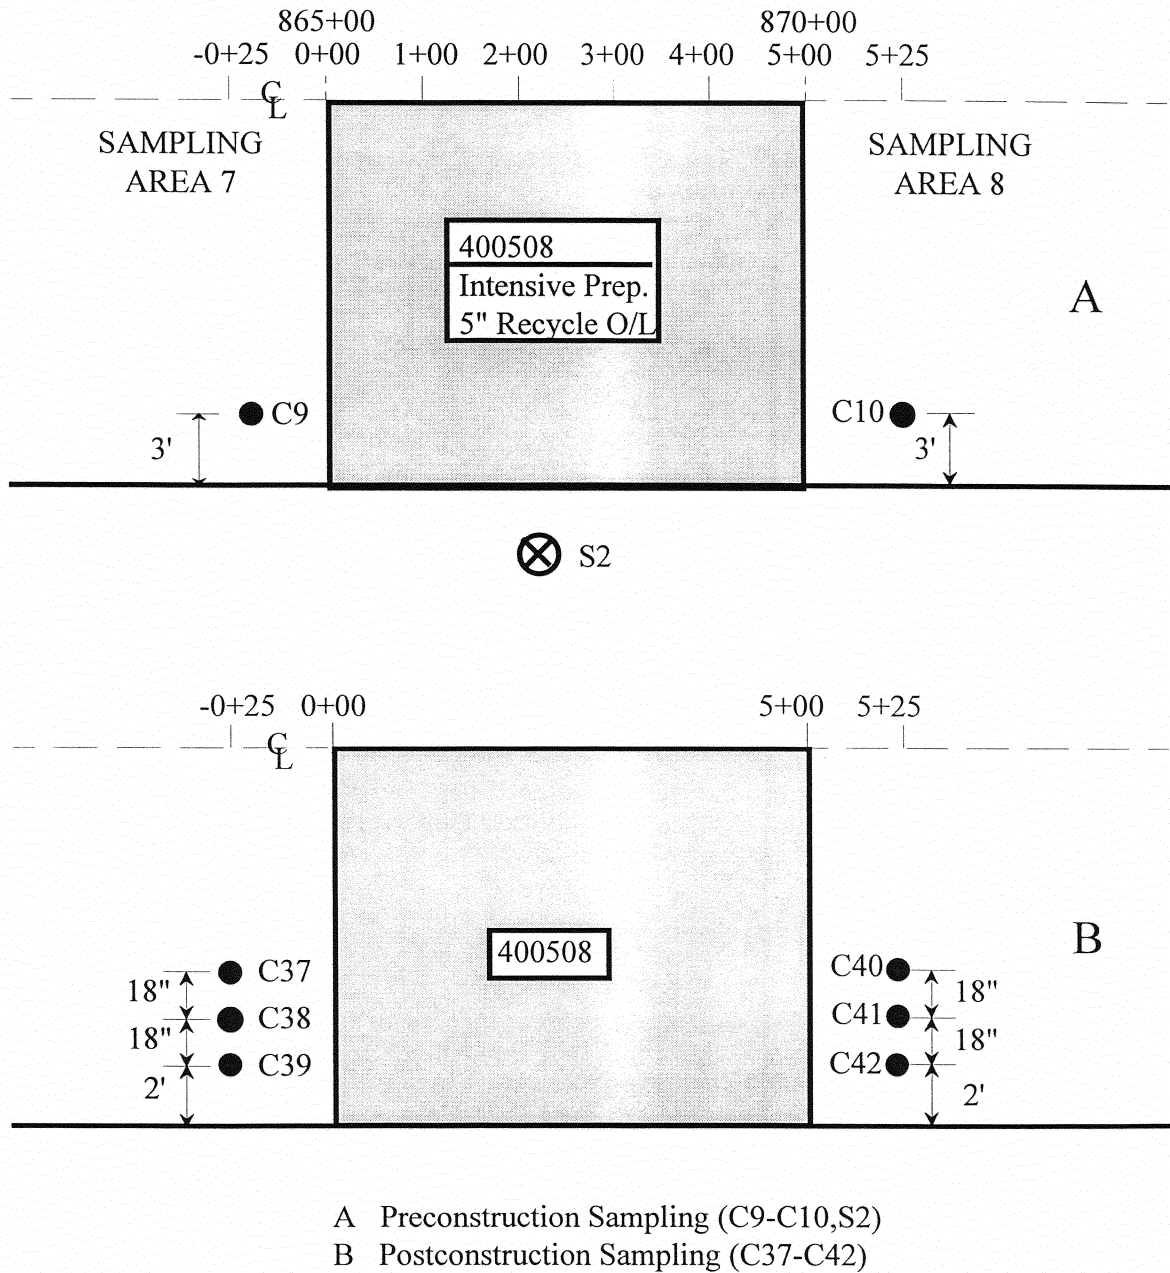


**FIGURE B-7. SAMPLING AND TESTING PLAN FOR TEST SECTION 400508
 OKLAHOMA SPS-5 (400500)**

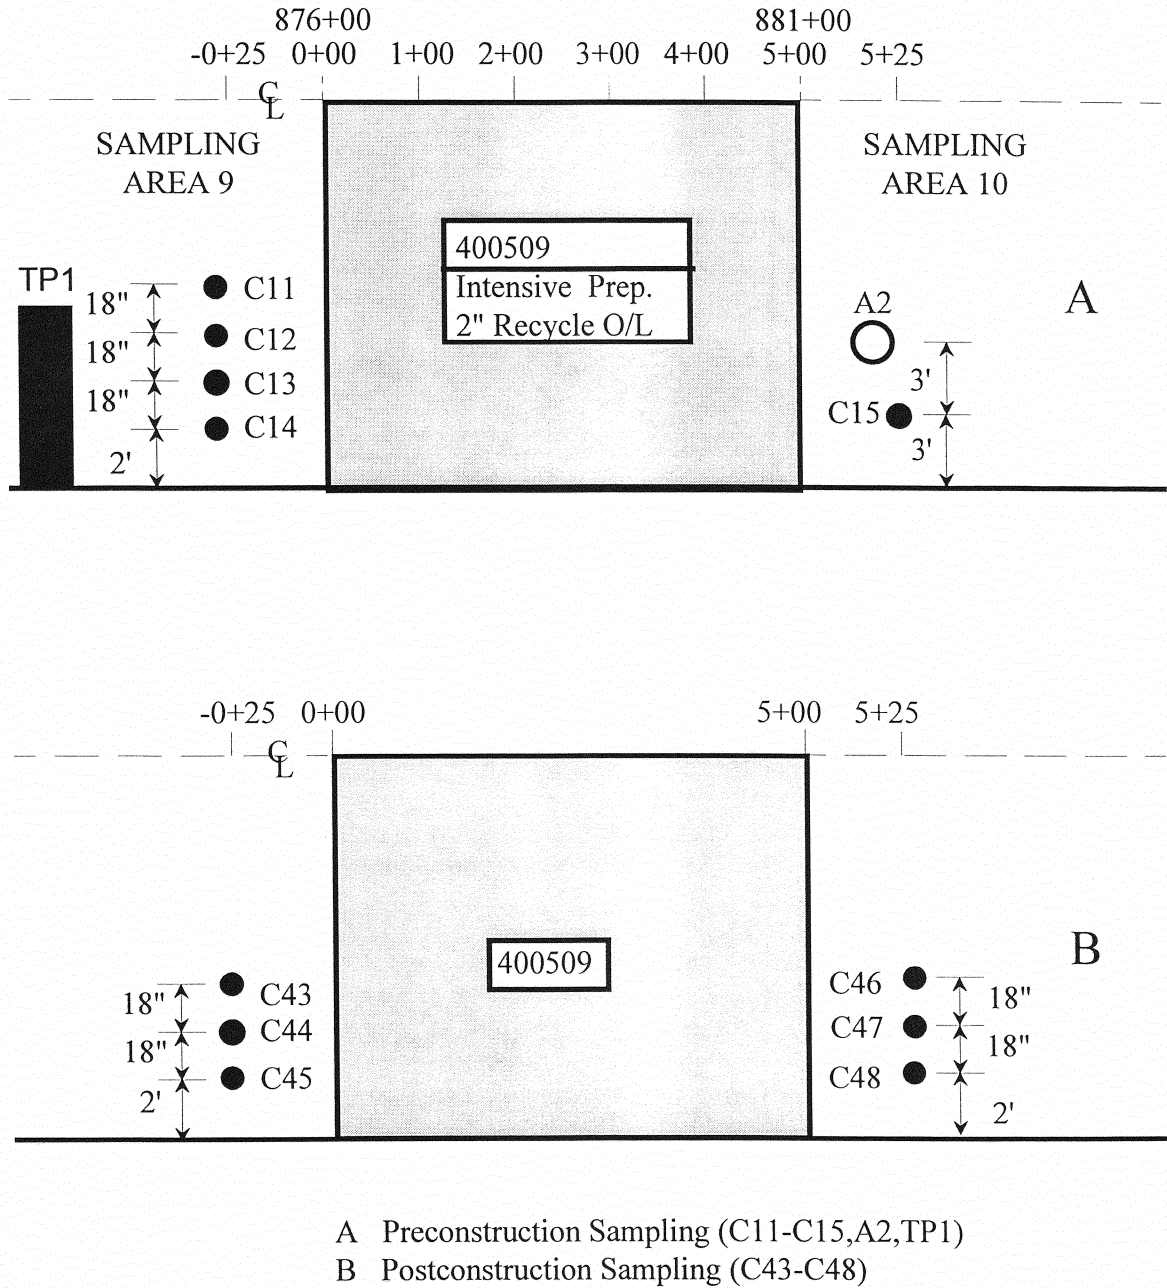


**FIGURE B-8. SAMPLING AND TESTING PLAN FOR TEST SECTION 400509
OKLAHOMA SPS-5 (400500)**

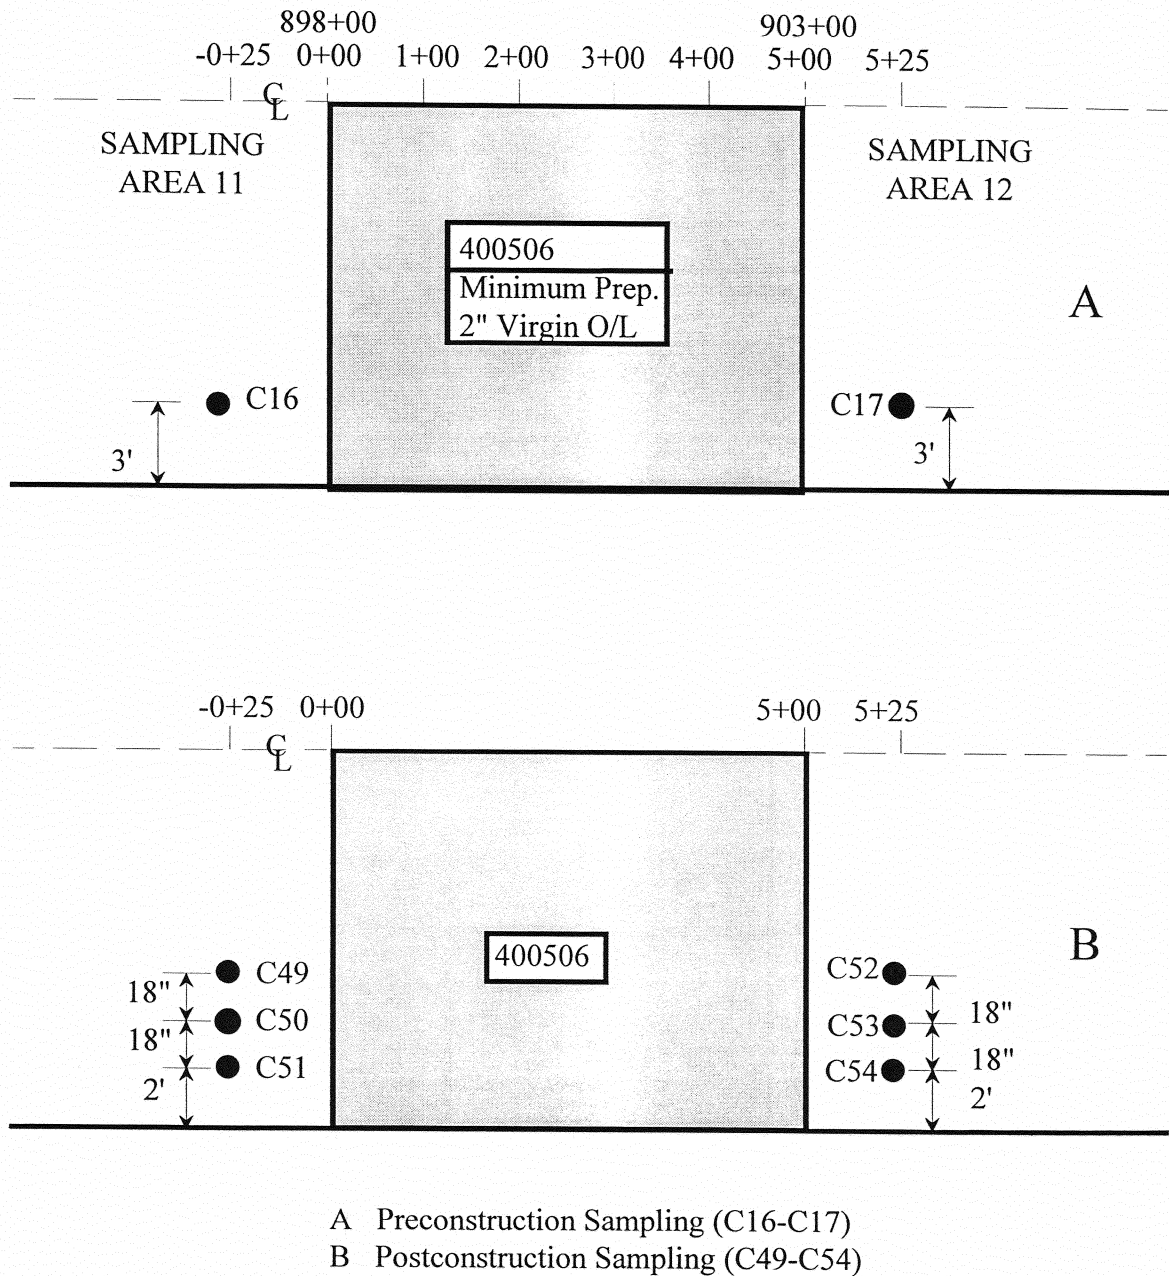


**FIGURE B-9. SAMPLING AND TESTING PLAN FOR TEST SECTION 400506
 OKLAHOMA SPS-5 (400500)**

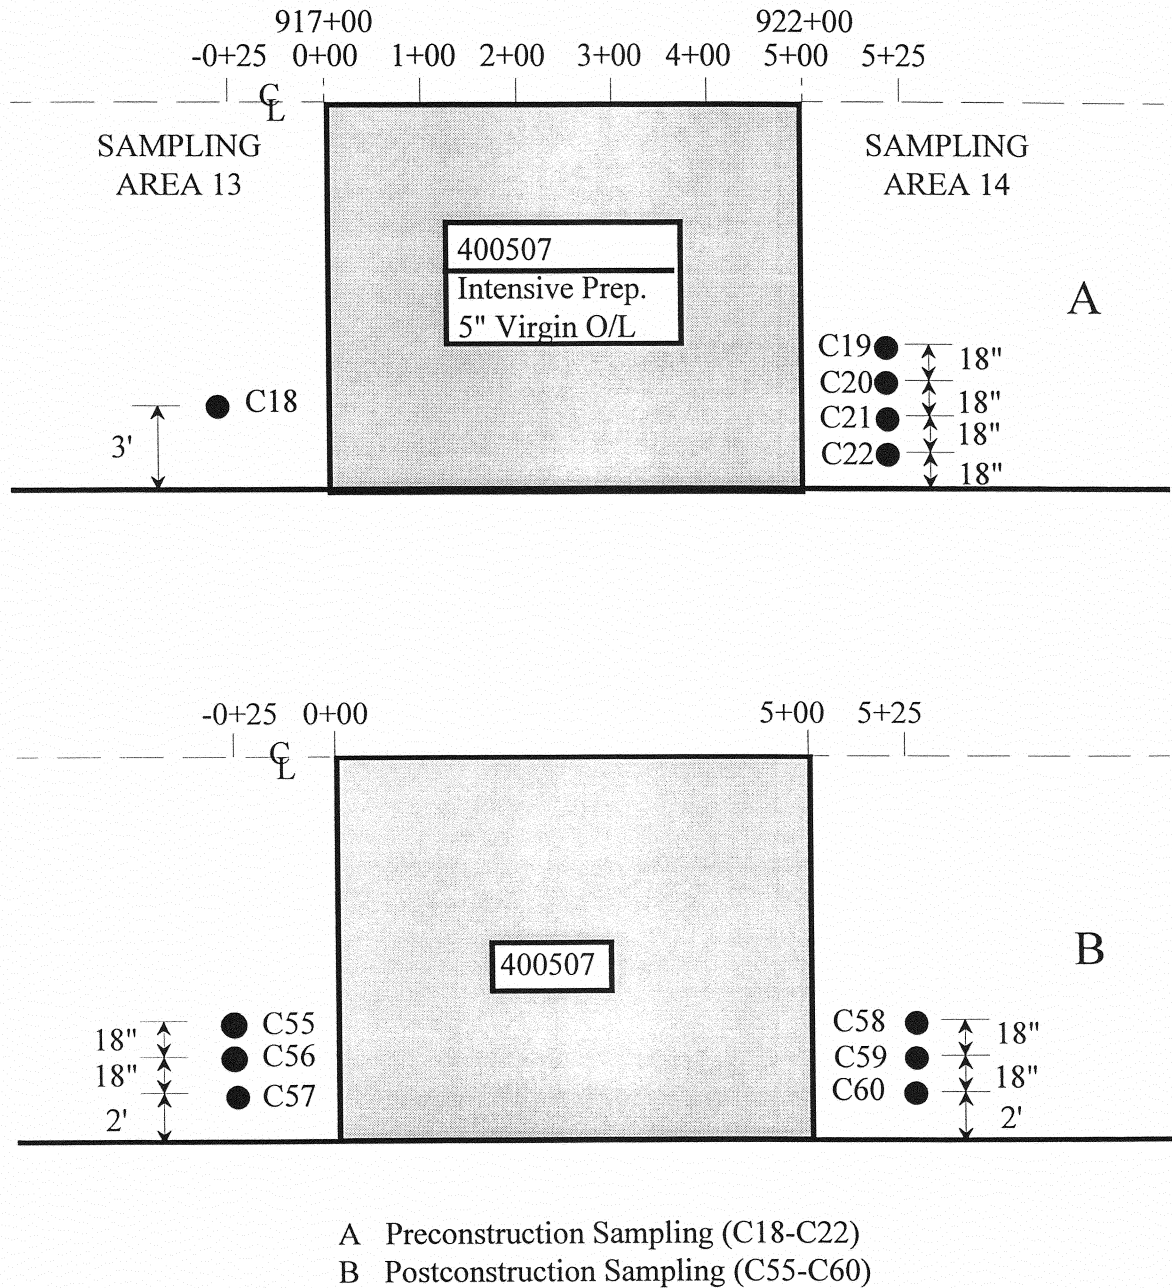

**FIGURE B-10. SAMPLING AND TESTING PLAN FOR TEST SECTION 400507
OKLAHOMA SPS-5 (400500)**

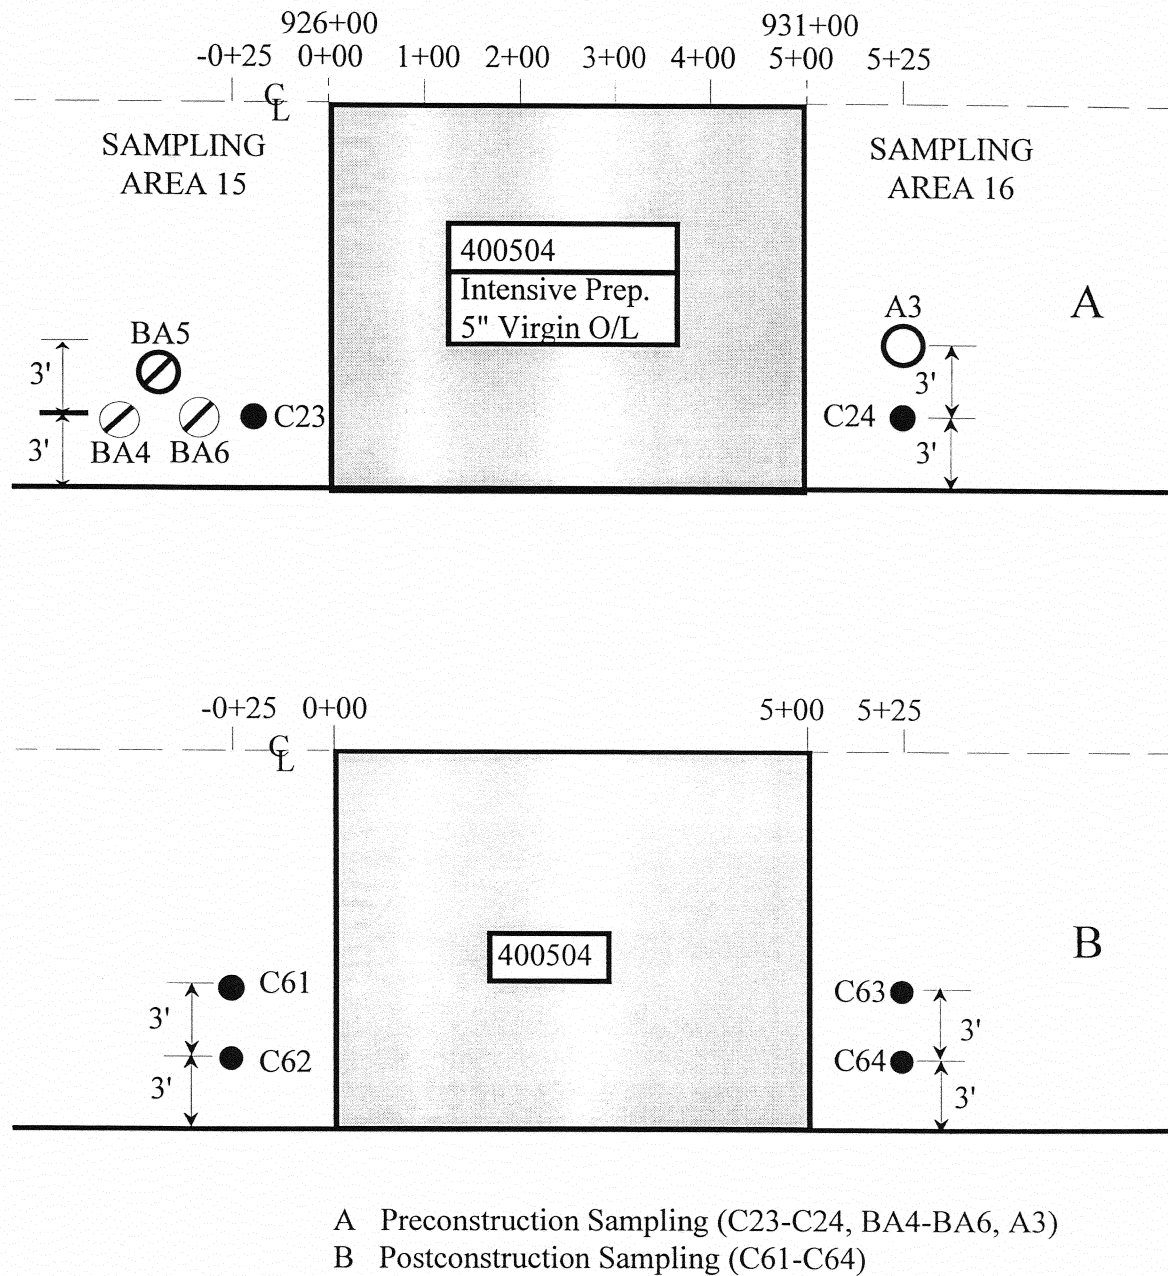

**FIGURE B-11. SAMPLING AND TESTING PLAN FOR TEST SECTION 400504
OKLAHOMA SPS-5 (400500)**

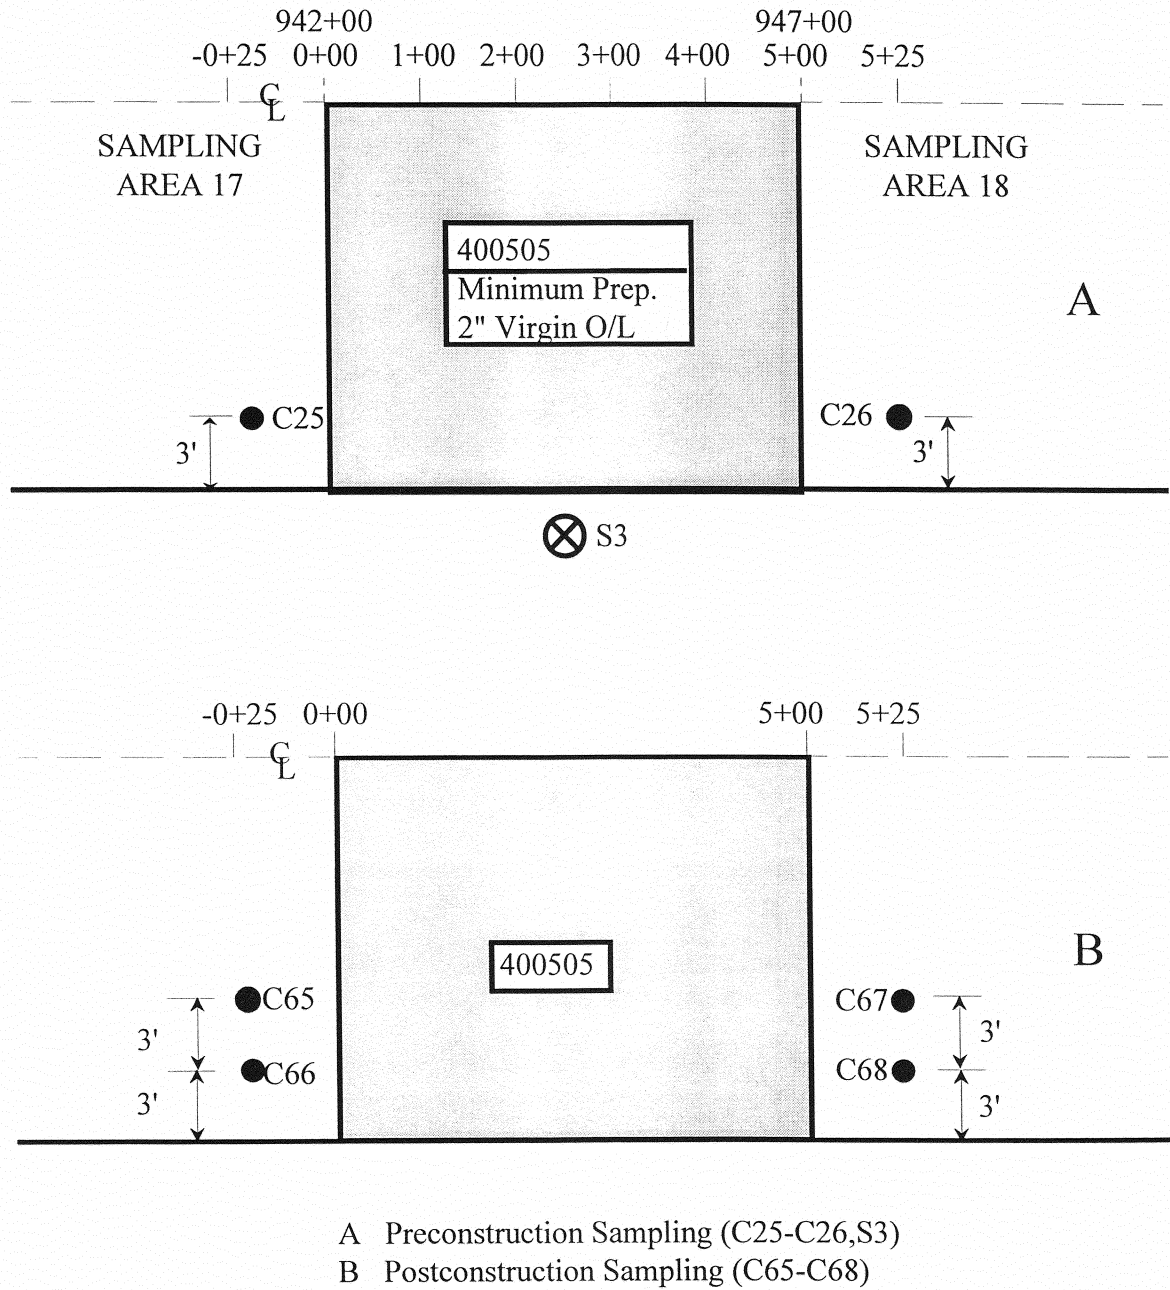

**FIGURE B-12. SAMPLING AND TESTING PLAN FOR TEST SECTION 400505
OKLAHOMA SPS-5 (400500)**

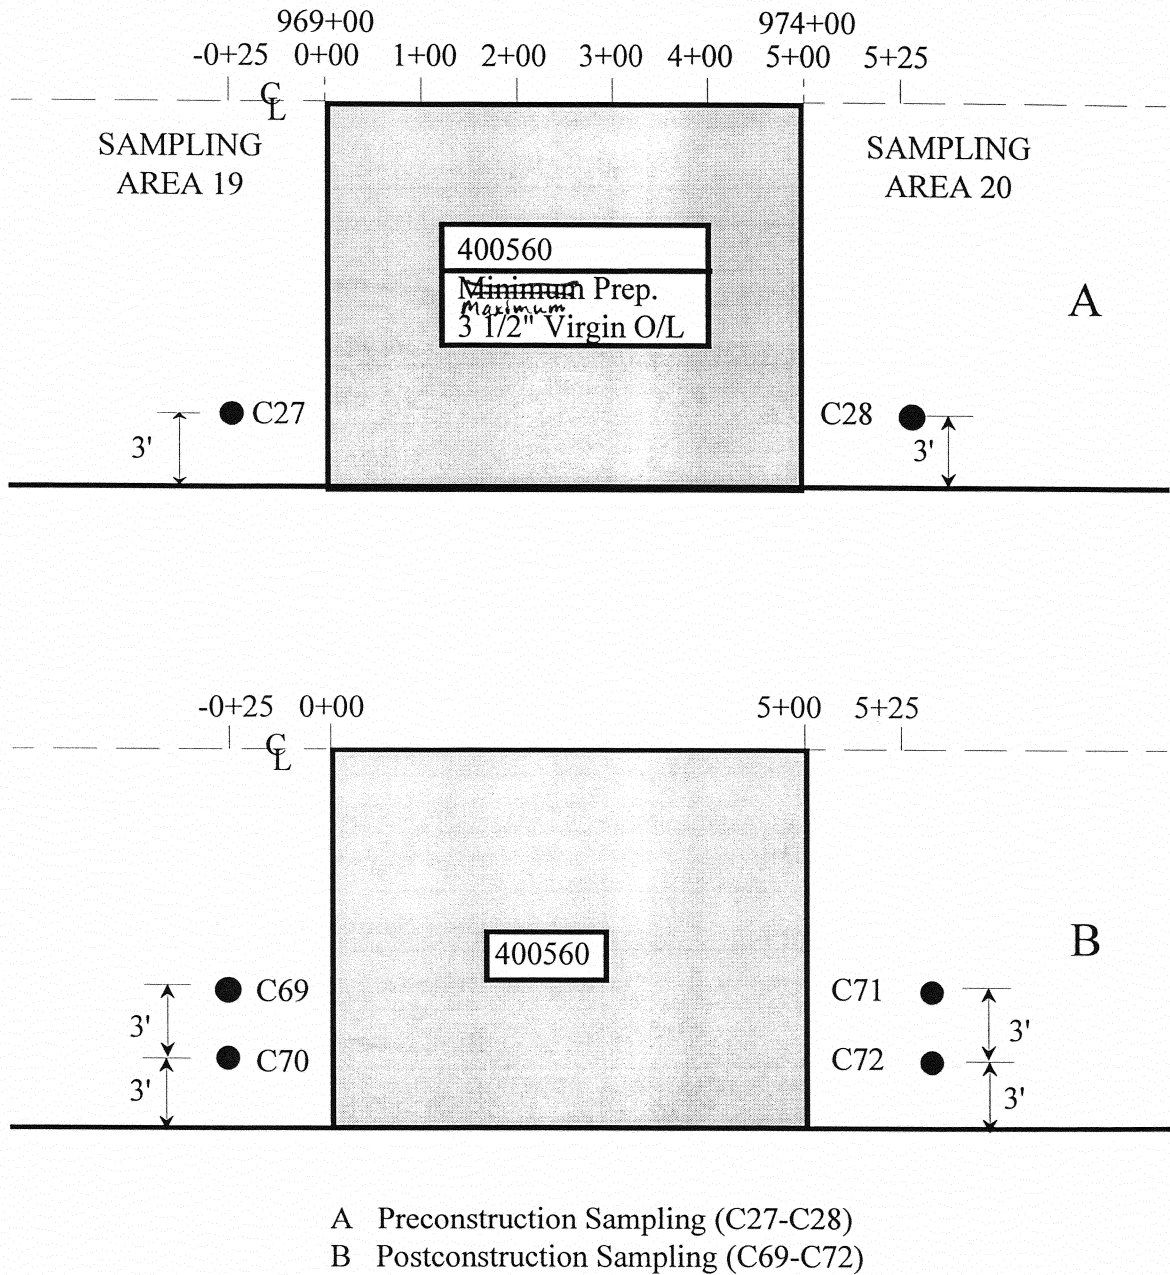


FIGURE B-13. SAMPLING AND TESTING PLAN FOR TEST SECTION 400560
 OKLAHOMA SPS-5 (400500)

TABLE B-4. SAMPLES TO BE SHIPPED TO THE STATE LABORATORY (OR THEIR DESIGNEE)

Sample Location	Sample Nº.	Lab Test Nº.	Type of Sample
Asphalt Concrete			
BA1	BA01	1	305 mm (12 in.) Core
BA2	BA02	1	305 mm (12 in.) Core
BA3	BA03	1	305 mm (12 in.) Core
BA4	BA04	1	305 mm (12 in.) Core
BA5	BA05	1	305 mm (12 in.) Core
BA6	BA06	1	305 mm (12 in.) Core
TP1	BA07	1	305 mm × 305 mm (12 in. × 12 in.) Block
A1	A1	2	152 mm (6 in.) Core
A2	A2	2	152 mm (6 in.) Core
A3	A3	2	152 mm (6 in.) Core
BV1	BV1	3	Virgin Bulk Sample Uncompacted Mix (Binder)
BV2	BV2	3	" Bulk Sample Uncompacted Mix "
BV3	BV3	3	" Bulk Sample Uncompacted Mix "
BR1	BR1	3	Recycled Bulk Sample Uncompacted Mix "
BR2	BR2	3	" Bulk Sample Uncompacted Mix "
BR3	BR3	3	" Bulk Sample Uncompacted Mix "
Line-Treated Subgrade Subbase			
All Samples Shipped to FHWA Laboratory			
Subgrade			
BA1	MS01	1	Moisture Content Jar Sample
BA2	MS02	1	Moisture Content Jar Sample
BA3	MS03	1	Moisture Content Jar Sample
BV4	BV4	3	Virgin Bulk Sample Uncompacted Mix (Surface)
BV5	BV5	"	"
BV6	BV6	"	"
BR4	BR4	"	Recycled
BR5	BR5	"	"
BR6	BR6	"	"

**TABLE B-4. SAMPLES TO BE SHIPPED TO THE
STATE LABORATORY (OR THEIR DESIGNEE)
(Continued)**

Sample Location	Sample Nº.	Lab Test Nº.	Type of Sample
BA1	BS01	1	45 kg (100 lb) Bulk Sample
BA2	BS02	1	45 kg (100 lb) Bulk Sample
BA3	BS03	1	45 kg (100 lb) Bulk Sample
A1	TS01	3	Thin-wall Tube
A2	TS03	3	Thin-wall Tube
A3	TS05	3	Thin-wall Tube

**TABLE B-5. SAMPLES TO BE SHIPPED TO THE
FHWA-LTPP TESTING CONTRACTOR LABORATORY**

Sample Location	Sample Nº.	Lab Test Nº.	Type of Sample
Asphalt Concrete			
C1	CA01	1	102 mm (4 in.) Core
C2	CA02	2	102 mm (4 in.) Core
C3	CA03	1	102 mm (4 in.) Core
C4	CA04	1	102 mm (4 in.) Core
C5	CA05	1	102 mm (4 in.) Core
C6	CA06	2	102 mm (4 in.) Core
C7	CA07	1	102 mm (4 in.) Core
C8	CA08	2	102 mm (4 in.) Core
C9	CA09	1	102 mm (4 in.) Core
C10	CA10	1	102 mm (4 in.) Core
C11	CA11	1	102 mm (4 in.) Core
C12	CA12	1	102 mm (4 in.) Core
C13	CA13	1	102 mm (4 in.) Core
C14	CA14	1	102 mm (4 in.) Core
C15	CA15	2	102 mm (4 in.) Core
C16	CA16	1	102 mm (4 in.) Core
C17	CA17	2	102 mm (4 in.) Core
C18	CA18	2	102 mm (4 in.) Core
C19	CA19	2	102 mm (4 in.) Core
C20	CA20	2	102 mm (4 in.) Core
C21	CA21	2	102 mm (4 in.) Core
C22	CA22	2	102 mm (4 in.) Core
C23	CA23	1	102 mm (4 in.) Core
C24	CA24	2	102 mm (4 in.) Core

**TABLE B-5. SAMPLES TO BE SHIPPED TO THE
FHWA-LTPP TESTING CONTRACTOR LABORATORY
(Continued)**

Sample Location	Sample Nº.	Lab Test Nº.	Type of Sample
C25	CA25	1	102 mm (4 in.) Core
C26	CA26	2	102 mm (4 in.) Core
C27	CA27	1	102 mm (4 in.) Core
C28	CA28	2	102 mm (4 in.) Core
C29	CA29	1	102 mm (4 in.) Core
C30	CA30	1	102 mm (4 in.) Core
C31	CA31	2	102 mm (4 in.) Core
C32	CA32	2	102 mm (4 in.) Core
C33	CA33	1	102 mm (4 in.) Core
C34	CA34	1	102 mm (4 in.) Core
C35	CA35	2	102 mm (4 in.) Core
C36	CA36	2	102 mm (4 in.) Core
C37	CA37	1	102 mm (4 in.) Core
C38	CA38	1	102 mm (4 in.) Core
C39	CA39	1	102 mm (4 in.) Core
C40	CA40	2	102 mm (4 in.) Core
C41	CA41	2	102 mm (4 in.) Core
C42	CA42	2	102 mm (4 in.) Core
C43	CA43	1	102 mm (4 in.) Core
C44	CA44	1	102 mm (4 in.) Core
C45	CA45	1	102 mm (4 in.) Core
C46	CA46	2	102 mm (4 in.) Core
C47	CA47	2	102 mm (4 in.) Core
C48	CA48	2	102 mm (4 in.) Core
C49	CA49	1	102 mm (4 in.) Core

**TABLE B-5. SAMPLES TO BE SHIPPED TO THE
FHWA-LTPP TESTING CONTRACTOR LABORATORY
(Continued)**

Sample Location	Sample Nº.	Lab Test Nº.	Type of Sample
C50	CA50	1	102 mm (4 in.) Core
C51	CA51	1	102 mm (4 in.) Core
C52	CA52	2	102 mm (4 in.) Core
C53	CA53	2	102 mm (4 in.) Core
C54	CA54	2	102 mm (4 in.) Core
C55	CA55	1	102 mm (4 in.) Core
C56	CA56	1	102 mm (4 in.) Core
C57	CA57	1	102 mm (4 in.) Core
C58	CA58	2	102 mm (4 in.) Core
C59	CA59	2	102 mm (4 in.) Core
C60	CA60	2	102 mm (4 in.) Core
C61	CA61	1	102 mm (4 in.) Core
C62	CA62	1	102 mm (4 in.) Core
C63	CA63	2	102 mm (4 in.) Core
C64	CA64	2	102 mm (4 in.) Core
C65	CA65	1	102 mm (4 in.) Core
C66	CA66	1	102 mm (4 in.) Core
C67	CA67	2	102 mm (4 in.) Core
C68	CA68	2	102 mm (4 in.) Core
C69	CA69	1	102 mm (4 in.) Core
C70	CA70	1	102 mm (4 in.) Core
C71	CA71	2	102 mm (4 in.) Core
C72	CA72	2	102 mm (4 in.) Core

**TABLE B-5. SAMPLES TO BE SHIPPED TO THE
FHWA-LTPP TESTING CONTRACTOR LABORATORY
(Continued)**

Sample Location	Sample Nº.	Lab Test Nº.	Type of Sample
Lime-Treated Subgrade Subbase			
BA1	BG01	1	136 kg (300 lb) Bulk Sample
BA2	BG02	1	136 kg (300 lb) Bulk Sample
BA3	BG03	1	136 kg (300 lb) Bulk Sample
BA4	BG04	2	136 kg (300 lb) Bulk Sample
BA5	BG05	2	136 kg (300 lb) Bulk Sample
BA6	BG06	2	136 kg (300 lb) Bulk Sample
TP1	BG07	1	136 kg (300 lb) Bulk Sample
BA1	MG01	1	Moisture Content Jar Sample
BA2	MG02	1	Moisture Content Jar Sample
BA3	MG03	1	Moisture Content Jar Sample
BA4	MG04	1	Moisture Content Jar Sample
BA5	MG05	1	Moisture Content Jar Sample
BA6	MG06	1	Moisture Content Jar Sample
TP1	MG07	1	Moisture Content Jar Sample
Subgrade			
BA1	BS01	1	136 kg (300 lb) Bulk Sample
BA2	BS02	1	136 kg (300 lb) Bulk Sample
BA3	BS03	1	136 kg (300 lb) Bulk Sample
BA4	BS04	1	136 kg (300 lb) Bulk Sample
BA5	BS05	1	136 kg (300 lb) Bulk Sample
BA6	BS06	1	136 kg (300 lb) Bulk Sample
TP1	BS07	1	136 kg (300 lb) Bulk Sample
A1	TS02	3	Thin-wall Tube Sample
A2	TS04	3	Thin-wall Tube Sample
A3	TS06	3	Thin-wall Tube Sample

SECTION C

LABORATORY MATERIAL TESTING

SECTION C

LABORATORY MATERIAL TESTING

It is the intent of this section of the sampling and testing plan to provide an outline for the laboratory testing that is planned for the Oklahoma SPS-5 project. The previous section ended with lists of samples to be shipped to each of two laboratories; the state designated laboratory and the FHWA/LTPP contracted laboratory. In this section, the tests to be performed on each sample are listed.

The reference project layer numbering scheme was provided in Table B-1. It is important that the two laboratories reference the same layer by number to ensure meaningful results.

Tables C-1 and C-2 provide listings of the preconstruction and postconstruction laboratory tests to be performed for each material type and pavement layer, and the associated laboratory testing protocol. It is imperative that the protocols listed be strictly followed during testing.

Tables C-3 through C-7 provide tracking tables for the testing to be conducted for each material type. These tables itemize the testing to occur on each sample and provide an indication of whether the sample is to be disposed of.

TABLE C-1. SPS-5 LABORATORY TESTING PLANS - PRECONSTRUCTION

MATERIAL TYPE AND PROPERTIES	LTPP DESIGNATION	LTPP PROTOCOL	Nº OF TESTS PER LAYER	SAMPLING LOCATION	TEST CONDUCTED BY:	
					STATE	FHWA
A. ASPHALTIC CONCRETE: Core Examination/Thickness Bulk Specific Gravity Maximum Specific Gravity Asphalt Content (Extraction) Creep Compliance Resilient Modulus Tensile Strength Field Moisture Damage	AC01	P01	28	C1-C28		X
	AC02	P02	12	C3-C6, C11-14, C19-C22		X
	AC03	P03	3	BA1-BA3, TP1, BA4-BA6	X	
	AC04	P04	3	BA1-BA3, TP1, BA4-BA6	X	
	AC06	P06	3	C2, C16, C24		X
	AC07	P07	9	C3-C5, C12-C14, C20-C22		X
	AC07	P07	12	C3-C6, C11-C14, C19-C22		X
	AC08	P08	3	A1, A2, A3	X	
B. EXTRACTED AGGREGATE: Type and Classification: Coarse Aggregate Fine Aggregate Gradation of Aggregate NAA Test for Fine Aggregate Particle Shape	AG03	P13	3	BA1-BA3, TP1, BA4-BA6	X	
	AG03	P13	3	BA1-BA3, TP1, BA4-BA6	X	
	AG04	P14	3	BA1-BA3, TP1, BA4-BA6	X	
	AG05	P14A	3	BA1-BA3, TP1, BA4-BA6	X	
C. ASPHALT CEMENT: Absorb Recovery Penetration at 77F & 115F Specific Gravity (60F) Viscosity at 77F Viscosity at 140F & 275F	AE01	P21	3	BA1-BA3, TP1, BA4-BA6	X	
	AE02	P22	3	BA1-BA3, TP1, BA4-BA6	X	
	AE03	P23	3	BA1-BA3, TP1, BA4-BA6	X	
	AE04	P24	3	BA1-BA3, TP1, BA4-BA6	X	
	AE05	P25	3	BA1-BA3, TP1, BA4-BA6	X	
D. LIME-TREATED SUBGRADE SUBBASE Particle Size Analysis Sieve Analysis (Washed) Atterberg Limits Moisture-Density Relations Resilient Modulus Classification Permeability Natural Moisture Content	UG01	P41	3	BA1-BA3, TP1, BA4-BA6		X
	UG02	P41	3	BA1-BA3, TP1, BA4-BA6		X
	UG04	P43	3	BA1-BA3, TP1, BA4-BA6		X
	UG05	P44	3	BA1-BA3, TP1, BA4-BA6		X
	UG07	P46	3	BA1-BA3, TP1, BA4-BA6		X
	UG08	P47	3	BA1-BA3, TP1, BA4-BA6		X
	UG09	P48	3	BA1-BA3, TP1, BA4-BA6		X
	UG10	P49	3	BA1-BA3, TP1, BA4-BA6		X
E. SUBGRADE Sieve Analysis Hydrometer to 0.001 mm. Atterberg Limits Classification Moisture-Density Relations Resilient Modulus Unit Weight Natural Moisture Content Depth to Rigid Layer	SS01	P51	3	BA1-BA3, TP1, BA4-BA6		X
	SS02	P42	3	BA1-BA3, TP1, BA4-BA6		X
	SS03	P43	3	BA1-BA3, TP1, BA4-BA6		X
	SS04	P52	3	BA1-BA3, TP1, BA4-BA6		X
	SS05	P55	3	BA1-BA3, TP1, BA4-BA6		X
	SS07	P46	3	A1, A2, A3		X
	SS08	P56	3	A1, A2, A3	X	
	SS09	P49	3	BA1-BA3	X	
				S1, S2, S3	X	

TABLE C-2. SPS-5 LABORATORY TESTING PLANS - POSTCONSTRUCTION

MATERIAL TYPE AND PROPERTIES	LTPP DESIGNATION	LTPP PROTOCOL	Nº. OF TESTS PER LAYER	SAMPLING LOCATION	TEST CONDUCTED BY:	
					STATE	FHWA
A. ASPHALTIC CONCRETE:						
Core Examination/Thickness	AC01	P01	44	C29-C72		X
Bulk Specific Gravity	AC02	P02	44	C29-C72		X
Maximum Specific Gravity	AC03	P03	6	BV1-BV3, BR1-BR3	X	
Asphalt Content (Extraction)	AC04	P04	6	BV1-BV3, BR1-BR3	X	
Moisture Susceptibility	AC05	P05	6	BV1-BV3, BR1-BR3	X	
Creep Compliance	AC06	P06	4	C31, C36, C61, C67		X
Resilient Modulus	AC07	P07	12	C37-C39, C43-C45, C49-C51, C55-C57		X
Tensile Strength	AC07	P07	16	C37-C40, C43-C46, C49-C52, C55-C58		X
B. EXTRACTED AGGREGATE:						
Bulk Specific Gravity:						
Coarse Aggregate	AG01	P11	6	BV1-BV3, BR1-BR3	X	
Fine Aggregate	AG02	P12	6	BV1-BV3, BR1-BR3	X	
Type and Classification:						
Coarse Aggregate	AG03	P13	6	BV1-BV3, BR1-BR3	X	
Fine Aggregate	AG03	P13	6	BV1-BV3, BR1-BR3	X	
Gradation of Aggregate	AG04	P14	6	BV1-BV3, BR1-BR3	X	
NAA Test for Fine Aggregate	AG05	P14A	6	BV1-BV3, BR1-BR3	X	
Particle Shape						
C. ASPHALT CEMENT:						
Abson Recovery	AE01	P21	6	BV1-BV3, BR1-BR3	X	
Penetration at 77F & 115F	AE02	P22	6	BV1-BV3, BR1-BR3	X	
Specific Gravity (60F)	AE03	P23	6	BV1-BV3, BR1-BR3	X	
Viscosity at 77F	AE04	P24	6	BV1-BV3, BR1-BR3	X	
Viscosity at 140F & 275F	AE05	P25	6	BV1-BV3, BR1-BR3	X	

**TABLE C-3. TRACKING TABLE OF ASPHALTIC CONCRETE TESTING
IN THE STATE LABORATORY(OR THEIR DESIGNEE)**

Sample Location	Sample Nº.	Lab Test Nº.	Steps Involved in Laboratory Handling and Testing Sequence							
			Required Laboratory Tests Per Layer					Extra Sample	Sample Storage ¹	Sample Disposed? ²
			First	Second	Third	Fourth	Fifth			
Asphalt Concrete Mix										
BA1	BA01	1	AC03/P03	AC04/P04				Yes	(a)	No
BA2	BA02	1	AC03/P03	AC04/P04				Yes	(a)	No
BA3	BA03	1	AC03/P03	AC04/P04				Yes	(a)	No
BA4	BA04	1	AC03/P03	AC04/P04				Yes	(a)	No
BA5	BA05	1	AC03/P03	AC04/P04				Yes	(a)	No
BA6	BA06	1	AC03/P03	AC04/P04				Yes	(a)	No
TP1	BA07	1	AC03/P03	AC04/P04				Yes	(a)	No
A1	A1	2	AC08/P08					Yes	(a)	No
A2	A2	2	AC08/P08					Yes	(a)	No
A3	A3	2	AC08/P08					Yes	(a)	No
BV1	BV1	3	See Figure C-1					No	(a)	Yes
BV2	BV2	3	See Figure C-1					No	(a)	Yes
BV3	BV3	3	See Figure C-1					No	(a)	Yes
BR1	BR1	3	See Figure C-1					No	(a)	Yes
BR2	BR2	3	See Figure C-1					No	(a)	Yes
BR3	BR3	3	See Figure C-1					No	(a)	Yes
Extracted Aggregate										
BA1-3	BA01-03	1	AG03/P13	AG04/P14				No	(a)	Yes
BA4-6	BA04-06	1	AG03/P13	AG04/P14				No	(a)	Yes
TP1	BA07	1	AG03/P13	AG04/P14				No	(a)	Yes
Extracted Asphalt										
BA1-3	BA01-03	1	AE01/P21	AE02/P22	AE03/P23	AE04/P24	AE05/P25	No	(a)	Yes
BA4-6	BA04-06	1						No	(a)	Yes
TP1	BA07	1						No	(a)	Yes

**TABLE C-3. TRACKING TABLE OF ASPHALTIC CONCRETE TESTING
IN THE STATE LABORATORY(OR THEIR DESIGNEE)
(Continued)**

- ¹ Sample Storage
 - a. Environmentally protected and controlled storeroom at 5-21°C (40-70°F).
 - b. Environmentally protected and controlled storeroom at 5-38°C (40-100°F).
 - c. Thin-walled tube samples of the subgrade that should be stored in a fully supported condition and at temperatures between 5°C (40°F) and 21°C (70°F) in an environmentally protected storeroom. They shall be stored on their ends and shall always be stored in a vertical position with respect to the longitudinal axis of the tube in the same orientation as that retrieved from the field.
- ² Sample Disposal? - Indicates whether or not a sample can be disposed of after testing. Generally all samples, or portions of samples, that are not tested are saved until further notice.

Note: All of the core specimens noted herein shall be stored for possible future use. In the future, these specimens may be used to evaluate test procedures for the SUPERPAVE program.

**TABLE C-4. TRACKING TABLE OF ASPHALTIC CONCRETE TESTING
IN THE FHWA-LTPP TESTING CONTRACTOR LABORATORY**

Sample Location	Sample Nº.	Lab Test Nº.	Steps Involved in Laboratory Handling and Testing Sequence						
			Required Laboratory Tests Per Layer				Extra Sample	Sample Storage	Sample Disposed?
			First	Second	Third	Fourth			
C1	CA01	1	AC01/P01				No	(a)	Yes
C2	CA02	2	AC01/P01	AC06/P06			No	(a)	Yes
C3	CA03	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C4	CA04	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C5	CA05	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C6	CA06	2	AC01/P01	AC02/P02	AC07/P07 (ITS)		No	(a)	Yes
C7	CA07	1	AC01/P01				No	(a)	Yes
C8	CA08	2	AC01/P01				No	(a)	Yes
C9	CA09	1	AC01/P01				No	(a)	Yes
C10	CA10	2	AC01/P01				No	(a)	Yes
C11	CA11	1	AC01/P01	AC02/P02	AC07/P07 (ITS)		No	(a)	Yes
C12	CA12	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C13	CA13	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C14	CA14	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C15	CA15	2	AC01/P01				No	(a)	Yes
C16	CA16	1	AC01/P01	AC06/P06			No	(a)	Yes
C17	CA17	2	AC01/P01				No	(a)	Yes
C18	CA18	1	AC01/P01				No	(a)	Yes
C19	CA19	2	AC01/P01	AC02/P02	AC07/P07 (ITS)		No	(a)	Yes
C20	CA20	2	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C21	CA21	2	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C22	CA22	2	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C23	CA23	1	AC01/P01				No	(a)	Yes
C24	CA24	2	AC01/P01	AC06/P06			No	(a)	Yes
C25	CA25	1	AC01/P01				No	(a)	Yes
C26	CA26	2	AC01/P01				No	(a)	Yes

**TABLE C-4. TRACKING TABLE OF ASPHALTIC CONCRETE TESTING
IN THE FHWA-LTPP TESTING CONTRACTOR LABORATORY
(Continued)**

Sample Location	Sample Nº.	Lab Test Nº.	Steps Involved in Laboratory Handling and Testing Sequence						
			Required Laboratory Tests Per Layer				Extra Sample	Sample Storage	Sample Disposed?
			First	Second	Third	Fourth			
C27	CA27	1	AC01/P01	AC02/P02			No	(a)	Yes
C28	CA28	2	AC01/P01	AC02/P02			No	(a)	Yes
C29	CA29	1	AC01/P01	AC02/P02			No	(a)	Yes
C30	CA30	1	AC01/P01	AC02/P02			No	(a)	Yes
C31	CA31	2	AC01/P01	AC02/P02	AC06/P06		No	(a)	Yes
C32	CA32	2	AC01/P01	AC02/P02			No	(a)	Yes
C33	CA33	1	AC01/P01	AC02/P02			No	(a)	Yes
C34	CA34	1	AC01/P01	AC02/P02			No	(a)	Yes
C35	CA35	2	AC01/P01	AC02/P02			No	(a)	Yes
C36	CA36	2	AC01/P01	AC02/P02	AC06/P06		No	(a)	Yes
C37	CA37	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C38	CA38	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C39	CA39	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C40	CA40	2	AC01/P01	AC02/P02	AC07/P07 (ITS)		No	(a)	Yes
C41	CA41	2	AC01/P01	AC02/P02			No	(a)	Yes
C42	CA42	2	AC01/P01	AC02/P02			No	(a)	Yes
C43	CA43	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C44	CA44	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C45	CA45	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C46	CA46	2	AC01/P01	AC02/P02	AC07/P07 (ITS)		No	(a)	Yes
C47	CA47	2	AC01/P01	AC02/P02			No	(a)	Yes
C48	CA48	2	AC01/P01	AC02/P02			No	(a)	Yes
C49	CA49	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C50	CA50	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C51	CA51	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes

**TABLE C-4. TRACKING TABLE OF ASPHALTIC CONCRETE TESTING
IN THE FHWA-LTPP TESTING CONTRACTOR LABORATORY
(Continued)**

Sample Location	Sample Nº.	Lab Test Nº.	Steps Involved in Laboratory Handling and Testing Sequence						
			Required Laboratory Tests Per Layer				Extra Sample	Sample Storage	Sample Disposed?
			First	Second	Third	Fourth			
C52	CA52	2	AC01/P01	AC02/P02	AC07/P07 (ITS)		No	(a)	Yes
C53	CA53	2	AC01/P01	AC02/P02			No	(a)	Yes
C54	CA54	2	AC01/P01	AC02/P02			No	(a)	Yes
C55	CA55	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C56	CA56	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C57	CA57	1	AC01/P01	AC02/P02	AC07/P07		No	(a)	Yes
C58	CA58	2	AC01/P01	AC02/P02	AC07/P07 (ITS)		No	(a)	Yes
C59	CA59	2	AC01/P01	AC02/P02			No	(a)	Yes
C60	CA60	2	AC01/P01	AC02/P02			No	(a)	Yes
C61	CA61	1	AC01/P01	AC02/P02	AC06/P06		No	(a)	Yes
C62	CA62	1	AC01/P01	AC02/P02			No	(a)	Yes
C63	CA63	2	AC01/P01	AC02/P02			No	(a)	Yes
C64	CA64	2	AC01/P01	AC02/P02			No	(a)	Yes
C65	CA65	1	AC01/P01	AC02/P02			No	(a)	Yes
C66	CA66	1	AC01/P01	AC02/P02			No	(a)	Yes
C67	CA67	2	AC01/P01	AC02/P02	AC06/P06		No	(a)	Yes
C68	CA68	2	AC01/P01	AC02/P02			No	(a)	Yes
C69	CA69	1	AC01/P01	AC02/P02			No	(a)	Yes
C70	CA70	1	AC01/P01	AC02/P02			No	(a)	Yes
C71	CA71	2	AC01/P01	AC02/P02			No	(a)	Yes
C72	CA72	2	AC01/P01	AC02/P02			No	(a)	Yes

**TABLE C-5. TRACKING TABLE OF LIME-TREATED SUBGRADE SUBBASE
IN THE FHWA-LTPP TESTING CONTRACTOR LABORATORY**

Sample Location	Sample No.	Lab Test No.	Steps Involved in Laboratory Handling and Testing Sequence										Extra Sample	Sample Storage	Sample Disposed?
			Required Laboratory Tests Per Layer							Seventh					
			First	Second	Third	Fourth	Fifth	Sixth							
BA1	BG01	2	UG01/P41	UG02/P41	UG04/P43	UG08/P47	UG05/P44	UG09/P48	UG07/P46	No	(b)	Yes			
BA2	BG02	2	UG01/P41	UG02/P41	UG04/P43	UG08/P47	UG05/P44	UG09/P48	UG07/P46	No	(b)	Yes			
BA3	BG03	2	UG01/P41	UG02/P41	UG04/P43	UG08/P47	UG05/P44	UG09/P48	UG07/P46	No	(b)	Yes			
BA4	BG04	2	UG01/P41	UG02/P41	UG04/P43	UG08/P47	UG05/P44	UG09/P48	UG07/P46	No	(b)	Yes			
BA5	BG05	2	UG01/P41	UG02/P41	UG04/P43	UG08/P47	UG05/P44	UG09/P48	UG07/P46	No	(b)	Yes			
BA6	BG06	2	UG01/P41	UG02/P41	UG04/P43	UG08/P47	UG05/P44	UG09/P48	UG07/P46	No	(b)	Yes			
TP1	BG07	2	UG01/P41	UG02/P41	UG04/P43	UG08/P47	UG05/P44	UG09/P48	UG07/P46	No	(b)	Yes			
BA1	MG01	2	UG10/P49							No	(b)	Yes			
BA2	MG02	2	UG10/P49							No	(b)	Yes			
BA3	MG03	2	UG10/P49							No	(b)	Yes			
BA4	MG04	2	UG10/P49							No	(b)	Yes			
BA5	MG05	2	UG10/P49							No	(b)	Yes			
BA6	MG06	2	UG10/P49							No	(b)	Yes			
TP1	MG07	2	UG10/P49							No	(b)	Yes			

**TABLE C-6. TRACKING TABLE OF SUBGRADE TESTING
IN THE STATE LABORATORY (OR THEIR DESIGNEE)**

Sample Location	Sample Nº.	Lab Test Nº.	Steps Involved in Laboratory Handling and Testing Sequence						
			Required Laboratory Tests Per Layer				Extra Sample	Sample Storage	Sample Disposed ?
			First	Second	Third	Fourth			
A1	TS01	3	SS08/P56				No	(c)	Yes
A2	TS03	3	SS08/P56				No	(c)	Yes
A3	TS05	3	SS08/P56				No	(c)	Yes
BA1	MS01	2	SS09/P49				No	(b)	Yes
BA2	MS02	2	SS09/P49				No	(b)	Yes
BA3	MS03	2	SS09/P49				No	(b)	Yes

**TABLE C-7. TRACKING TABLE OF SUBGRADE TESTING
IN THE FHWA-LTPP TESTING CONTRACTOR LABORATORY**

Sample Location	Sample №.	Lab Test №.	Steps Involved in Laboratory Handling and Testing Sequence										Extra Sample	Sample Storage	Sample Disposed?
			Required Laboratory Tests Per Layer						Sixth						
			First	Second	Third	Fourth	Fifth								
BA1	BS01	1	SS01/P51	SS02/P42	SS03/P43	SS04/P52	SS05/P55		No	(b)	Yes				
BA2	BS02	1	SS01/P51	SS02/P42	SS03/P43	SS04/P52	SS05/P55		No	(b)	Yes				
BA3	BS03	1	SS01/P51	SS02/P42	SS03/P43	SS04/P52	SS05/P55		No	(b)	Yes				
BA4	BS04	1	SS01/P51	SS02/P42	SS03/P43	SS04/P52	SS05/P55		No	(b)	Yes				
BA5	BS05	1	SS01/P51	SS02/P42	SS03/P43	SS04/P52	SS05/P55		No	(b)	Yes				
BA6	BS06	1	SS01/P51	SS02/P42	SS03/P43	SS04/P52	SS05/P55		No	(b)	Yes				
TP1	BS07	1	SS01/P51	SS02/P42	SS03/P43	SS04/P52	SS05/P55		No	(b)	Yes				
A1	TS02	3	SS04/P52	SS07/P46					No	(c)	Yes				
A2	TS04	3	SS04/P52	SS07/P46					No	(c)	Yes				
A3	TS06	3	SS04/P52	SS07/P46					No	(c)	Yes				
BA1	MS01	1	SS09/P49						No	(b)	Yes				
BA2	MS02	1	SS09/P49						No	(b)	Yes				
BA3	MS03	1	SS09/P49						No	(b)	Yes				
BA4	MS04	1	SS09/P49						No	(b)	Yes				
BA5	MS05	1	SS09/P49						No	(b)	Yes				
BA6	MS06	1	SS09/P49						No	(b)	Yes				
TP1	MS07	1	SS09/P49						No	(b)	Yes				

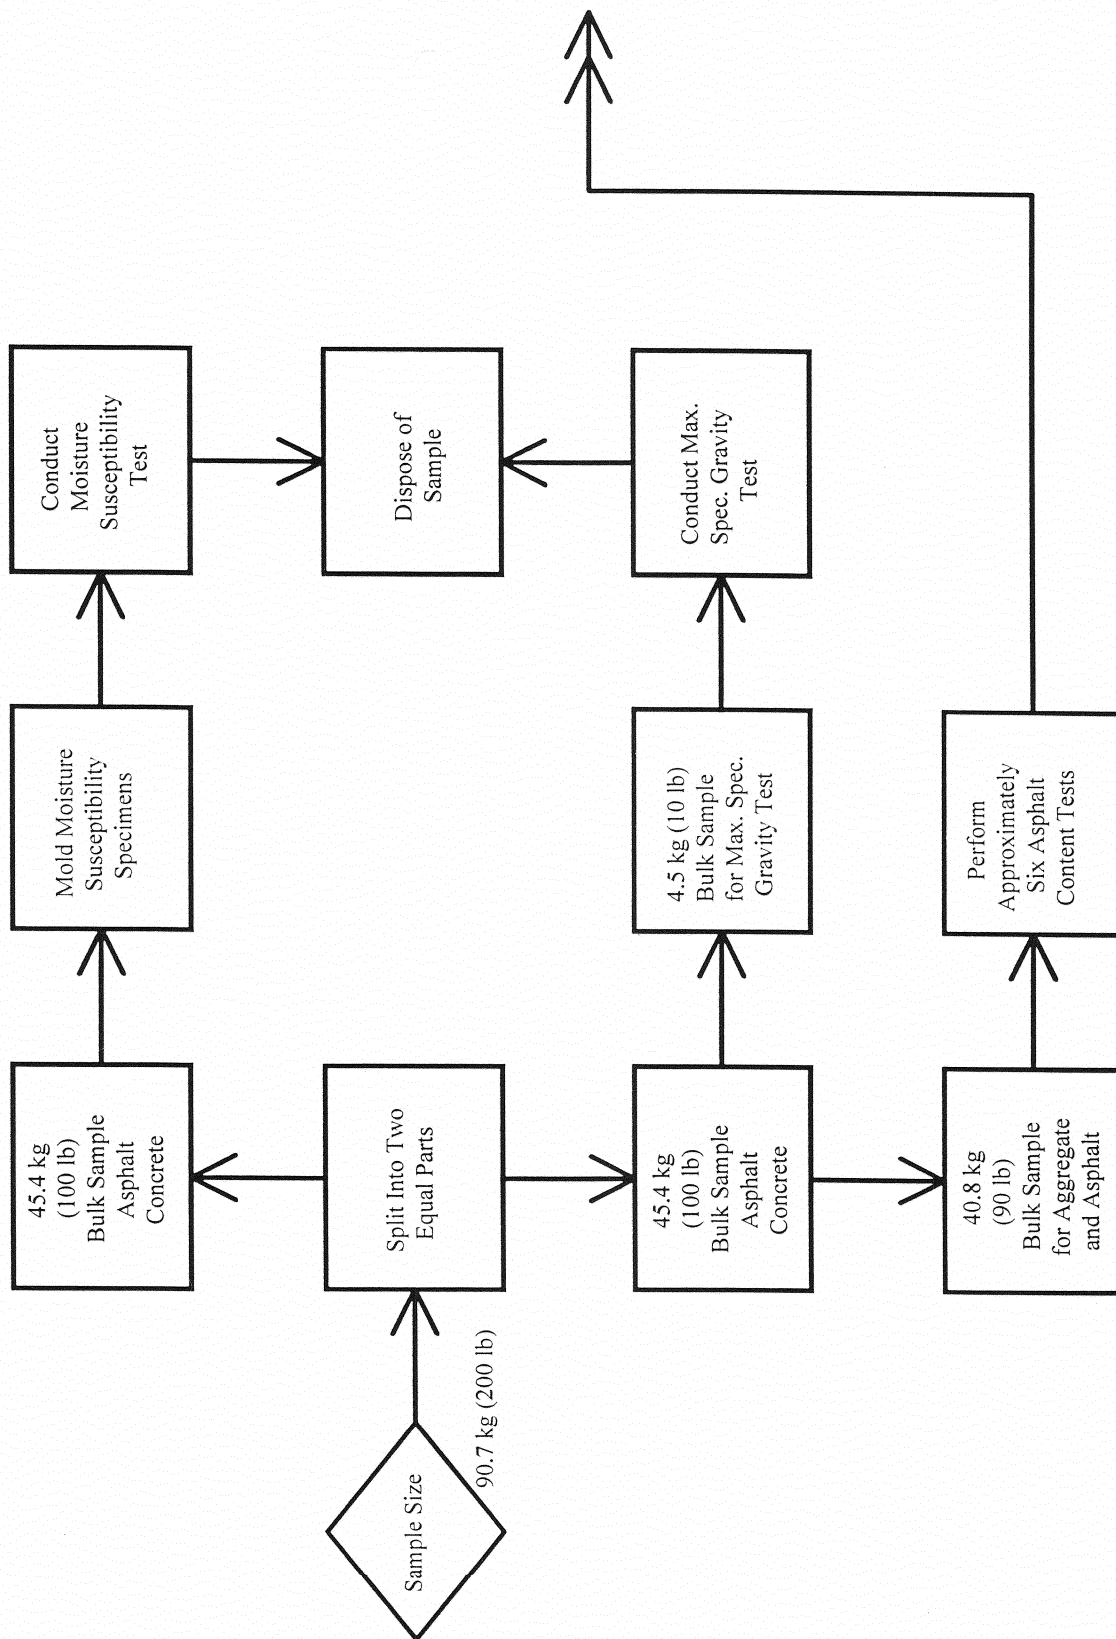


FIGURE C.1. FLOWCHART FOR ASPHALT CONCRETE BULK SAMPLES

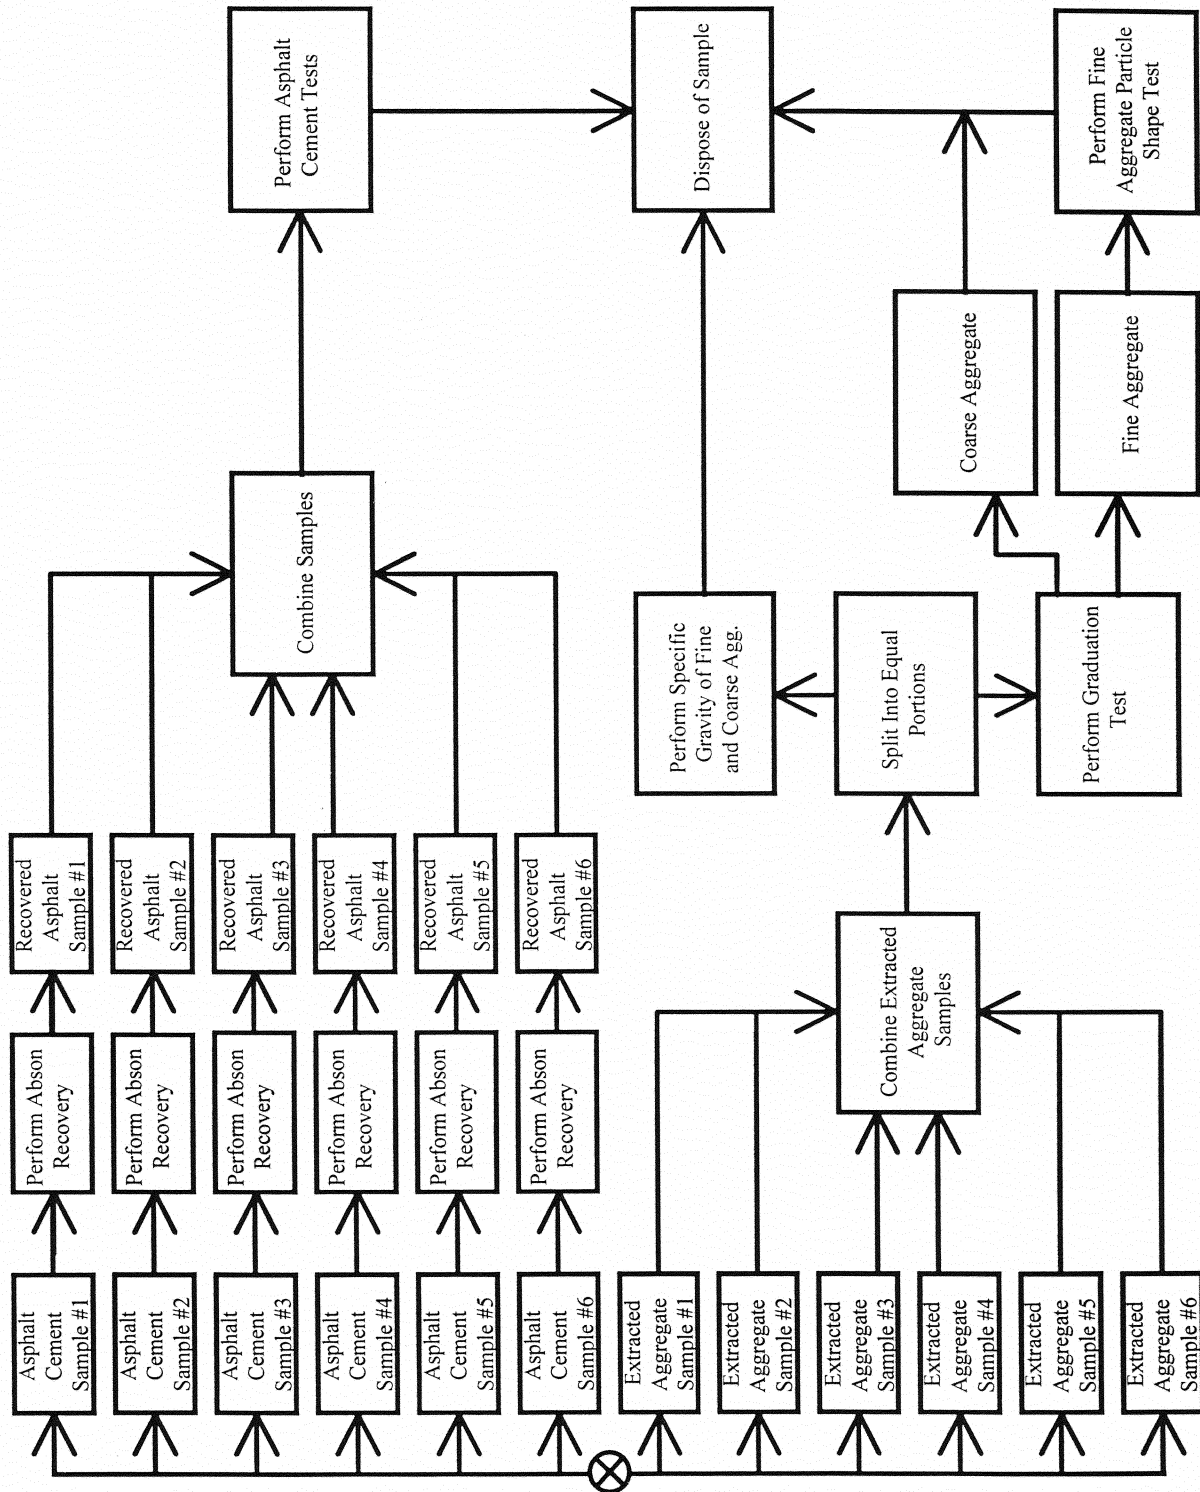


FIGURE C.1. FLOWCHART FOR ASPHALT CONCRETE BULK SAMPLES
(Continued)

APPENDIX E
CONSTRUCTION AND REHABILITATION
DATA AND PLANS

SURVEY CONTROL DATA

A. HORIZONTAL CONTROL FOR THIS SURVEY IS THE OILHOLMA STATE DEPARTMENT OF TRANSPORTATION PLANE COORDINATE SYSTEM. LAMBERT PROJECTION (SOUTH ZONE). ALL COORDINATES SHOWN ARE OILHOLMA STATE DEPARTMENT OF TRANSPORTATION PLANE COORDINATES WHICH WERE DERIVED BY MEASURING THE DISTANCE AND ANGLE FACTOR OF FLOOD CONTROL DISTRICT. OILHOLMA STATE DEPARTMENT OF TRANSPORTATION COORDINATE SYSTEM PLANE IS 2350 FEET ABOVE THE OILHOLMA USACE PLANE.

A. ACCURACY - 1ST ORDER OR BETTER

2. BEARINGS 1

THE BEARINGS SHOWN HEREIN OR HEREON ARE GRID BEARINGS DERIVED FROM THE USCLCS OKLAHOMA PLANE COORDINATE SYSTEM AND ARE NOT ASTRONOMICAL. THE ANGLE OF VARIANCE BETWEEN GRID NORTH (GN) AND THE ASTRONOMICAL TRUE NORTH (TN) IS DEPICTED DIAGRAMMATICALLY.

3. VERTICAL CONTROLS :

1. IFVEI DATUM IS MEAN SEA LEVEL (USC&GS).

A - ACCURACY - 2ND ORDER OR BETTER

DESIGN DATA	
ADT 1994	* 4,350
ADT 2014	* 7,850
DIVISIONE WAY1	518
KIDRV/ADT-1 to WAY-12X	* 53%
D	
T (% OF DRV)	* 13%
T (% ADT)	* 17%
T3 (% OF ADT)	* 13%
V	* 70 MPH

SCALES $\frac{1 \text{ inch}}{100 \text{ feet}}$

PLAN 1" = 100'

PROFILE HOR. 1" = 100'

VER. 1" = 10'

ABOUT 140' x 5,280'


Downloaded from <http://ajphaphapublications.sagepub.com/> at 09:08 04 October 2014

1941-1942	1943-1944	1945-1946	1947-1948	1949-1950	1951-1952	1953-1954	1955-1956	1957-1958	1959-1960	1961-1962	1963-1964	1965-1966	1967-1968	1969-1970	1971-1972	1973-1974	1975-1976	1977-1978	1979-1980	1981-1982	1983-1984	1985-1986	1987-1988	1989-1990	1991-1992	1993-1994	1995-1996	1997-1998	1999-2000	2001-2002	2003-2004	2005-2006	2007-2008	2009-2010	2011-2012	2013-2014	2015-2016	2017-2018	2019-2020	2021-2022	2023-2024	2025-2026	2027-2028	2029-2030	2031-2032	2033-2034	2035-2036	2037-2038	2039-2040	2041-2042	2043-2044	2045-2046	2047-2048	2049-2050	2051-2052	2053-2054	2055-2056	2057-2058	2059-2060	2061-2062	2063-2064	2065-2066	2067-2068	2069-2070	2071-2072	2073-2074	2075-2076	2077-2078	2079-2080	2081-2082	2083-2084	2085-2086	2087-2088	2089-2090	2091-2092	2093-2094	2095-2096	2097-2098	2099-2100	2101-2102	2103-2104	2105-2106	2107-2108	2109-2110	2111-2112	2113-2114	2115-2116	2117-2118	2119-2120	2121-2122	2123-2124	2125-2126	2127-2128	2129-2130	2131-2132	2133-2134	2135-2136	2137-2138	2139-2140	2141-2142	2143-2144	2145-2146	2147-2148	2149-2150	2151-2152	2153-2154	2155-2156	2157-2158	2159-2160	2161-2162	2163-2164	2165-2166	2167-2168	2169-2170	2171-2172	2173-2174	2175-2176	2177-2178	2179-2180	2181-2182	2183-2184	2185-2186	2187-2188	2189-2190	2191-2192	2193-2194	2195-2196	2197-2198	2199-2200	2201-2202	2203-2204	2205-2206	2207-2208	2209-2210	2211-2212	2213-2214	2215-2216	2217-2218	2219-2220	2221-2222	2223-2224	2225-2226	2227-2228	2229-2230	2231-2232	2233-2234	2235-2236	2237-2238	2239-2240	2241-2242	2243-2244	2245-2246	2247-2248	2249-2250	2251-2252	2253-2254	2255-2256	2257-2258	2259-2260	2261-2262	2263-2264	2265-2266	2267-2268	2269-2270	2271-2272	2273-2274	2275-2276	2277-2278	2279-2280	2281-2282	2283-2284	2285-2286	2287-2288	2289-2290	2291-2292	2293-2294	2295-2296	2297-2298	2299-2300	2301-2302	2303-2304	2305-2306	2307-2308	2309-2310	2311-2312	2313-2314	2315-2316	2317-2318	2319-2320	2321-2322	2323-2324	2325-2326	2327-2328	2329-2330	2331-2332	2333-2334	2335-2336	2337-2338	2339-2340	2341-2342	2343-2344	2345-2346	2347-2348	2349-2350	2351-2352	2353-2354	2355-2356	2357-2358	2359-2360	2361-2362	2363-2364	2365-2366	2367-2368	2369-2370	2371-2372	2373-2374	2375-2376	2377-2378	2379-2380	2381-2382	2383-2384	2385-2386	2387-2388	2389-2390	2391-2392	2393-2394	2395-2396	2397-2398	2399-2400	2401-2402	2403-2404	2405-2406	2407-2408	2409-2410	2411-2412	2413-2414	2415-2416	2417-2418	2419-2420	2421-2422	2423-2424	2425-2426	2427-2428	2429-2430	2431-2432	2433-2434	2435-2436	2437-2438	2439-2440	2441-2442	2443-2444	2445-2446	2447-2448	2449-2450	2451-2452	2453-2454	2455-2456	2457-2458	2459-2460	2461-2462	2463-2464	2465-2466	2467-2468	2469-2470	2471-2472	2473-2474	2475-2476	2477-2478	2479-2480	2481-2482	2483-2484	2485-
-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-------

MISS OKLAHOMA STANDARD SPECIFICATIONS FOR HIGHWAY CONSTRUCTION GOVERN APPROVED BY THE U.S. DEPARTMENT OF TRANSPORTATION, FEDERAL HIGHWAY ADMINISTRATION, JANUARY 3, 1959. SUPPLEMENTAL SPECIFICATIONS TO THE 1958 STANDARD SPECIFICATIONS TO GOVERN OVER THE STANDARD SPECIFICATIONS.

STATE OF OKLAHOMA
DEPARTMENT OF TRANSPORTATION

PLAN OF PROPOSED
STATE HIGHWAY
SURFACING PLANS
FEDERAL AID PROJECT NO. NH-215(60)
U.S. HIGHWAY NO. 62
COMANCHE COUNTY
STATE JOB NO. 0404006
CONTROL SECTION NO. 62-16-03

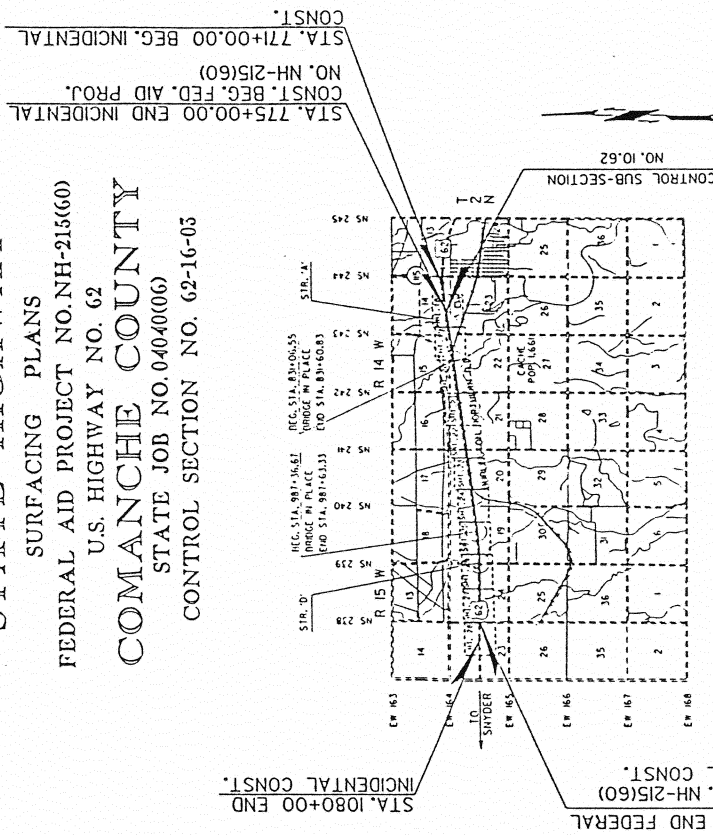


ROADWAY LENGTH-----29,064.78 FT.-----5.504 MI.
BRIDGE LENGTH-----0.00 FT.-----0.000 MI.
PROJECT LENGTH-----5.504 MI.
EQUATIONS : STA. 1016+43.53 BR. + STA. 1016+43.31 FWD.
BRIDGE EXCEPTION: STA. 782+19.17 - STA. 795+00.83 L-3B1-6E
BRIDGE EXCEPTION: STA. 795+00.83 L-3B1-6E
BRIDGE EXCEPTION: STA. 795+00.83 L-3B1-6E

THE FOLLOWING STANDARDS WILL BE
REQUIRED FOR THIS PROJECT:

SWO-1-22	ICD-10-5	RSD-1-25
SP1-2-3	ICD-15-0	RSD-3-11
PCL5-2-2	ICD-19-0	WSD-6-5
SP1-4-0	ICD-19-2	WSD-1-3
GUEL-4-0	ICD-1-22	MOO-1-3
GRU-2-7	ICD-3-17	WSD-1-17
GRAU-3-4	ICD-2-20	ICD-3-11
ICD-1-11	SSA-1A-1	WSD-5A-1
ICD-1A-1	SSP-1-1	SSS-1A-1
ICD-3-5	PN-1-16	SSS-2A-1
ICD-5-9	PN-3-10	SSS-2A-1
ICD-6-6	PN-4-12	FHTMP-3-2
ICD-7-6	PN-6-14	FHTCP-1-1

[illegible]


RELATIONAL DIMENSIONS & ELEVATIONS			
NO.	DESCRIPTION	ELEVATION	REMARKS
1	Top of Road	101.50	
2	Top of Shoulder	101.00	
3	Top of Subgrade	100.50	
4	Top of Base	100.00	
5	Top of Pavement	99.50	

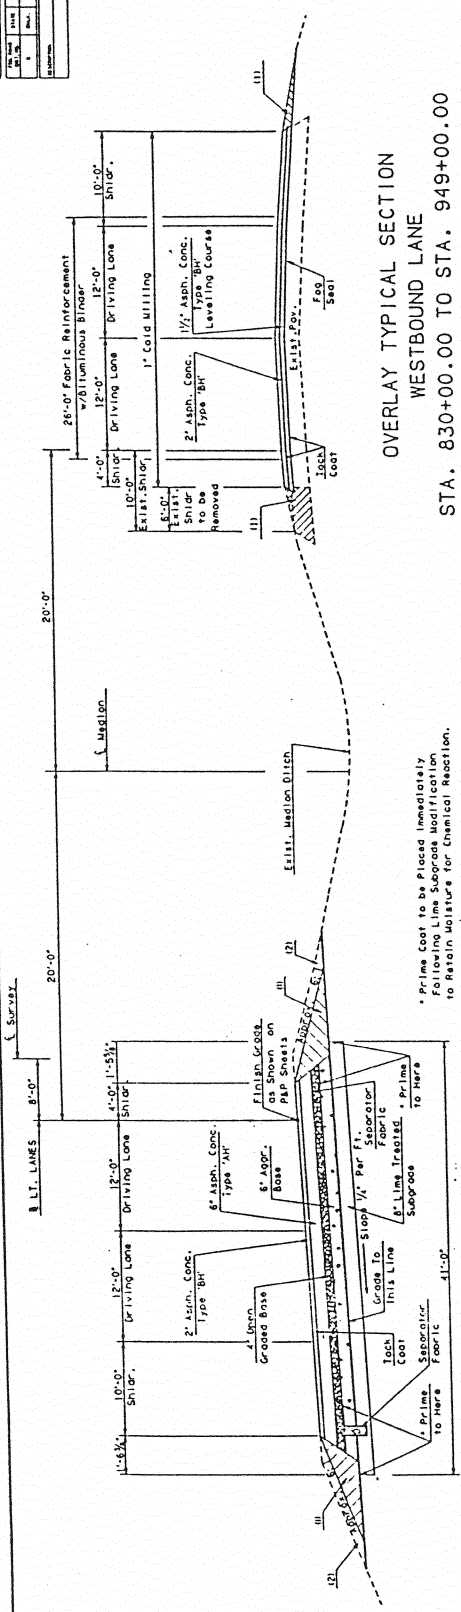

NEW CONSTRUCTION TYPICAL SECTION
EASTBOUND LANE
STA. 775+00.00 TO STA. 1072+50.00


1.61852 S.Y./L.F.
SEPARATOR FABRIC
OVERLAP
DETAIL

OVERLAY TYPICAL SECTION
WESTBOUND LANE
STA. 830+00.00 TO STA. 949+00.00



TYPICAL SECTION
COUNTY ROAD

MEDIAN OPENING TYPICAL

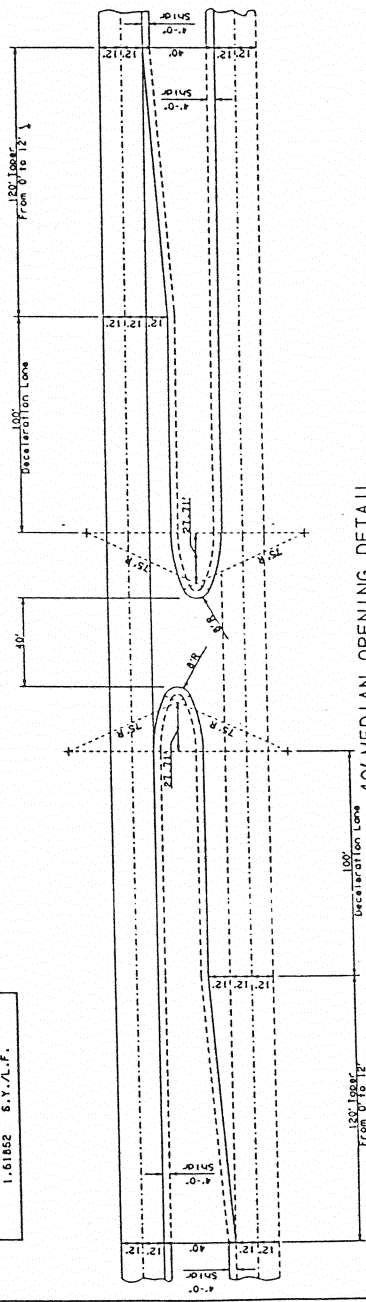


① BACKFILL NOTE:
To Be Backfilled and Composed As
Part of the Finishing Operations.

② TOPSOIL NOTE:
Topsoil Shall Be Spread Approx. 5" Thick,
First On Completed Backfill Areas And
The Remainder On Other Priority Areas
Located By The Engineer.


TYPICAL SECTION			
NO.	DESCRIPTION	ELEVATION	REMARKS
1	Top of Road	101.50	
2	Top of Shoulder	101.00	
3	Top of Subgrade	100.50	
4	Top of Base	100.00	
5	Top of Pavement	99.50	

STA. 832+00 TO STA. 839+00 CONTROL SECTION
(NO OVERLAY)

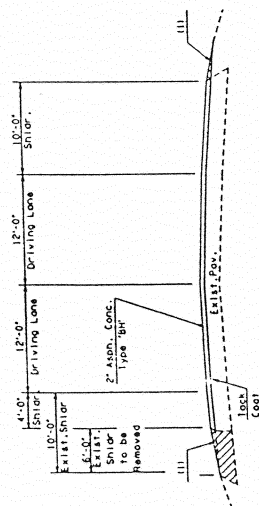


#2, #5

STA. 840+00.00 TO STA. 848+00.00 (RECYCLED AC)
STA. 941+00.00 TO STA. 948+00.00 (VIRGIN AC)

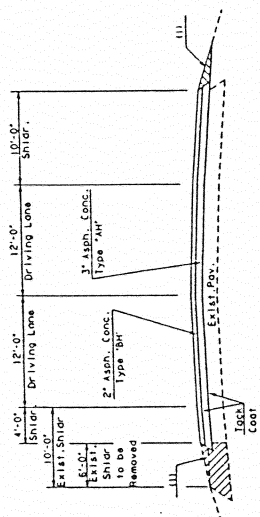


#3, #4

STA. 851+00.00 TO STA. 862+00.00 (RECYCLED AC)
STA. 924+00.00 TO STA. 939+00.00 (VIRGIN AC)

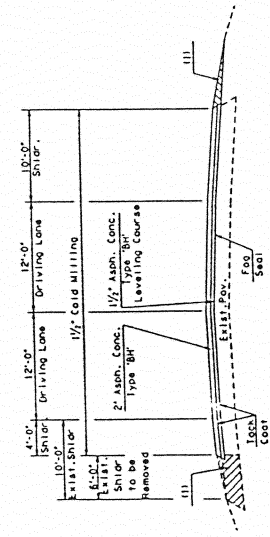

#6, #9

STA. 882+00.00 TO STA. 897+00.00 (EITHER VIRGIN
OR RECYCLED AC)
STA. 897+00.00 TO STA. 914+00.00 (VIRGIN AC)
STA. 873+00.00 TO STA. 882+00.00 (RECYCLED AC)

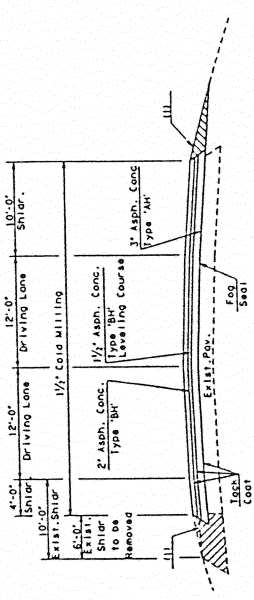

#7, #8


STA. 864+00.00 TO STA. 871+00.00 (RECYCLED AC)
STA. 916+00.00 TO STA. 923+00.00 (VIRGIN AC)


① BACKFILL NOTE:
To be Backfilled and Compacted As
Part of the Finishing Operations.



DATE	BY	CHKD	APPD
11/11/11	J. L. HARRIS	J. L. HARRIS	J. L. HARRIS
11/11/11	J. L. HARRIS	J. L. HARRIS	J. L. HARRIS
11/11/11	J. L. HARRIS	J. L. HARRIS	J. L. HARRIS


DATE	BY	CHKD	APPD
11/11/11	J. L. HARRIS	J. L. HARRIS	J. L. HARRIS
11/11/11	J. L. HARRIS	J. L. HARRIS	J. L. HARRIS
11/11/11	J. L. HARRIS	J. L. HARRIS	J. L. HARRIS

OKLAHOMA DEPARTMENT OF TRANSPORTATION
DESIGN DIVISION
TYPICAL SECTION
STATE JOB NO. 0409004 SHEET NO. 6
CONTRACT CO.

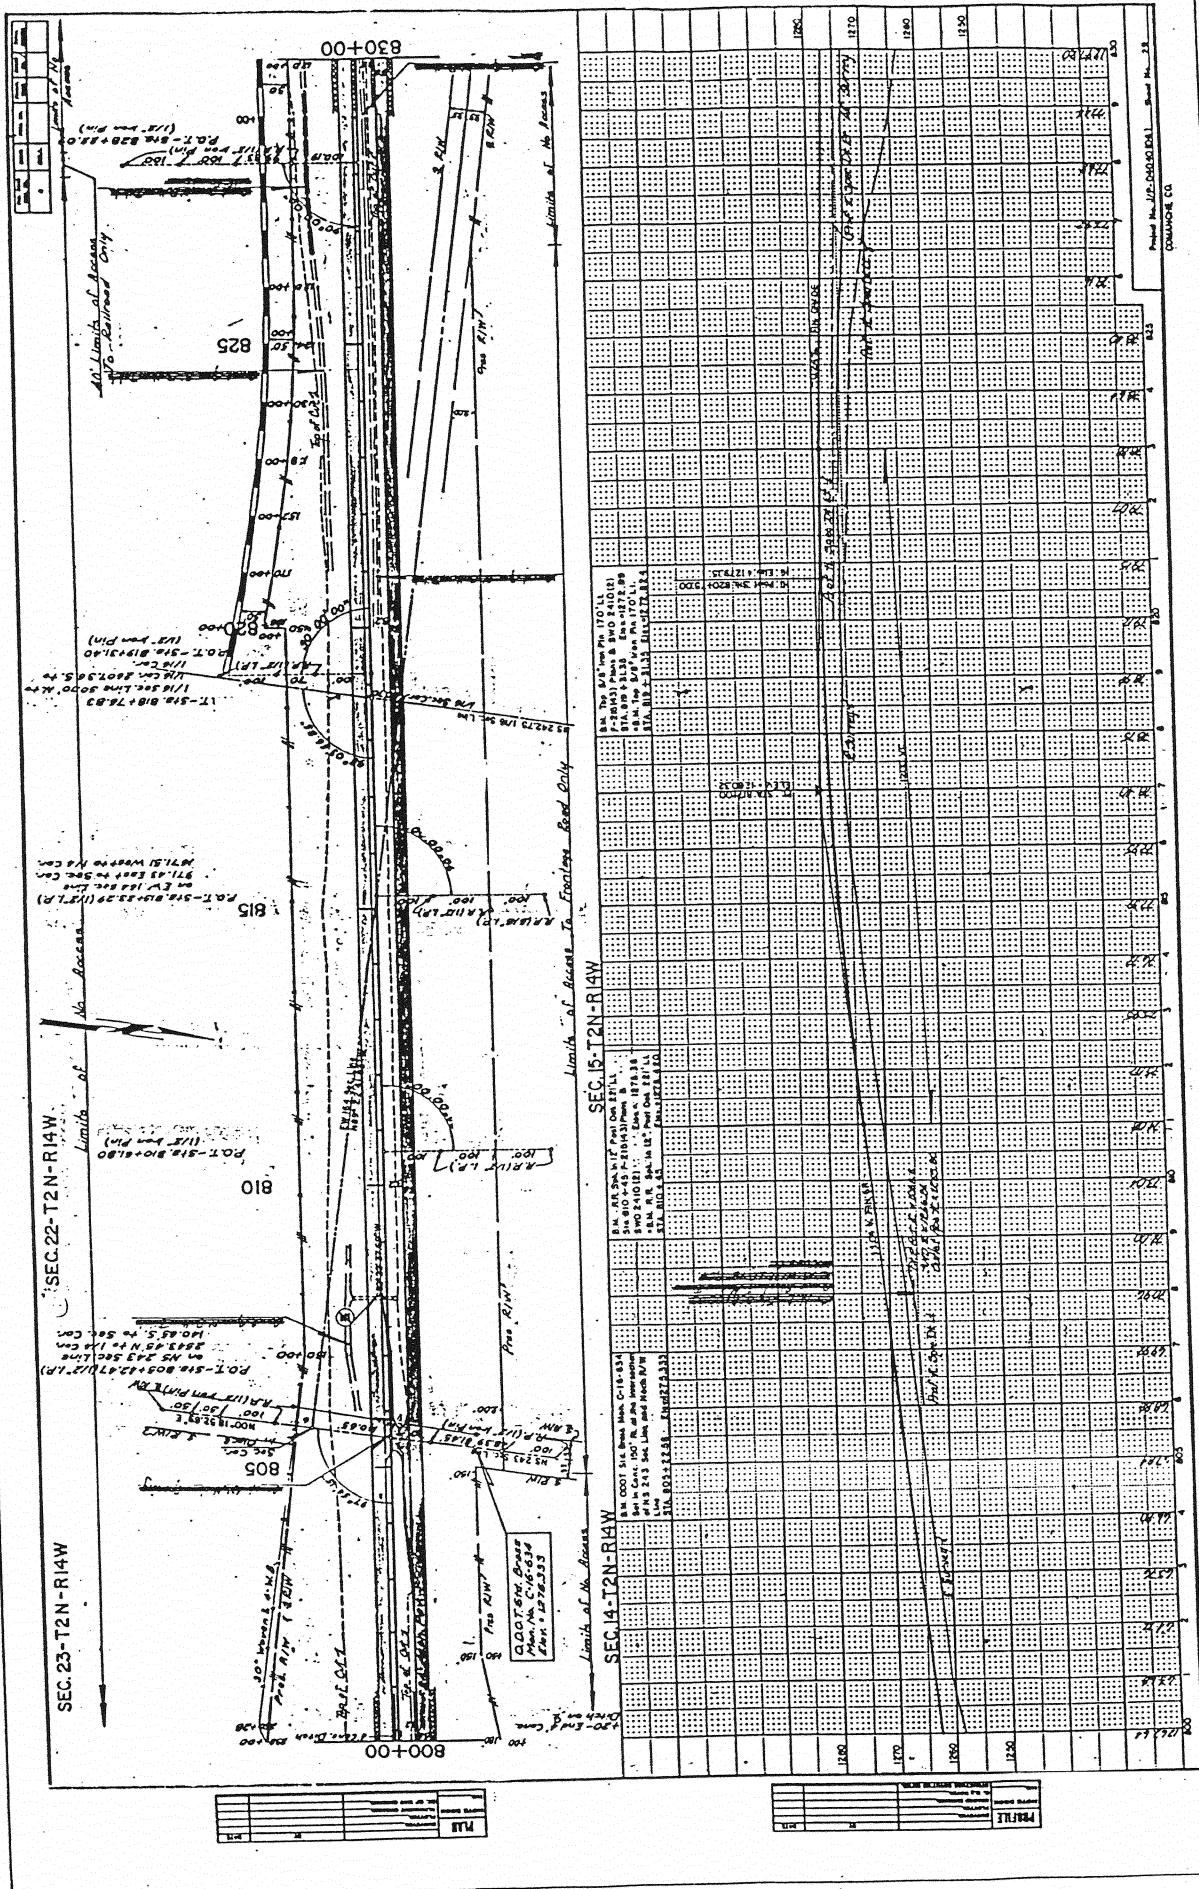

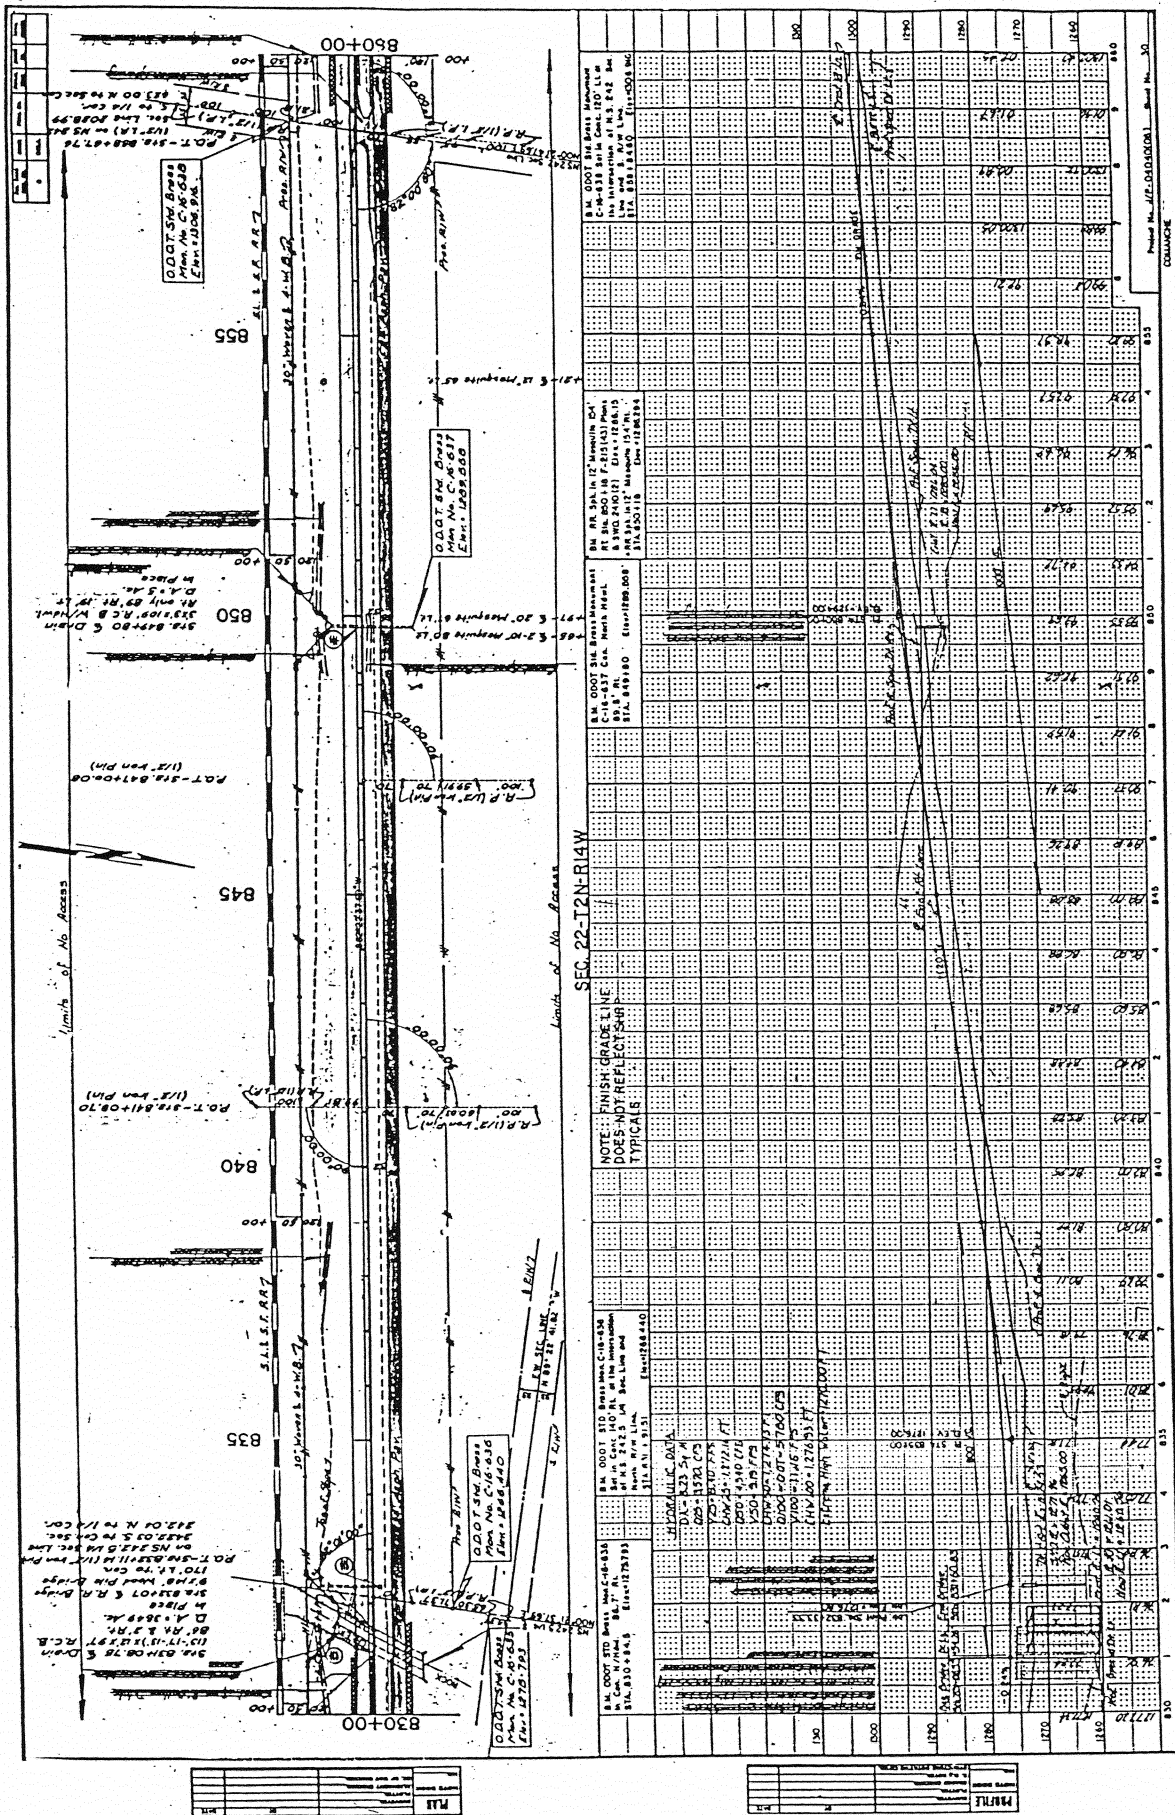

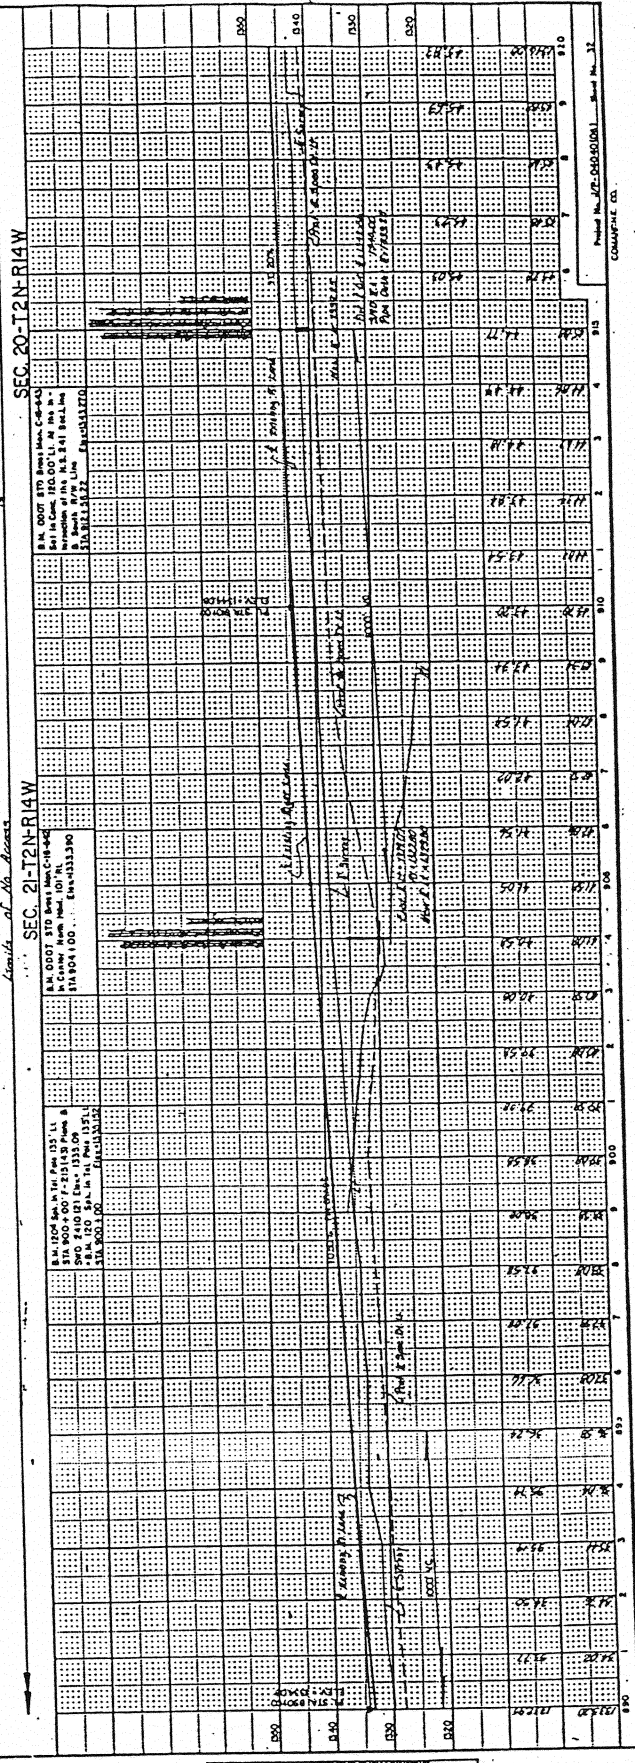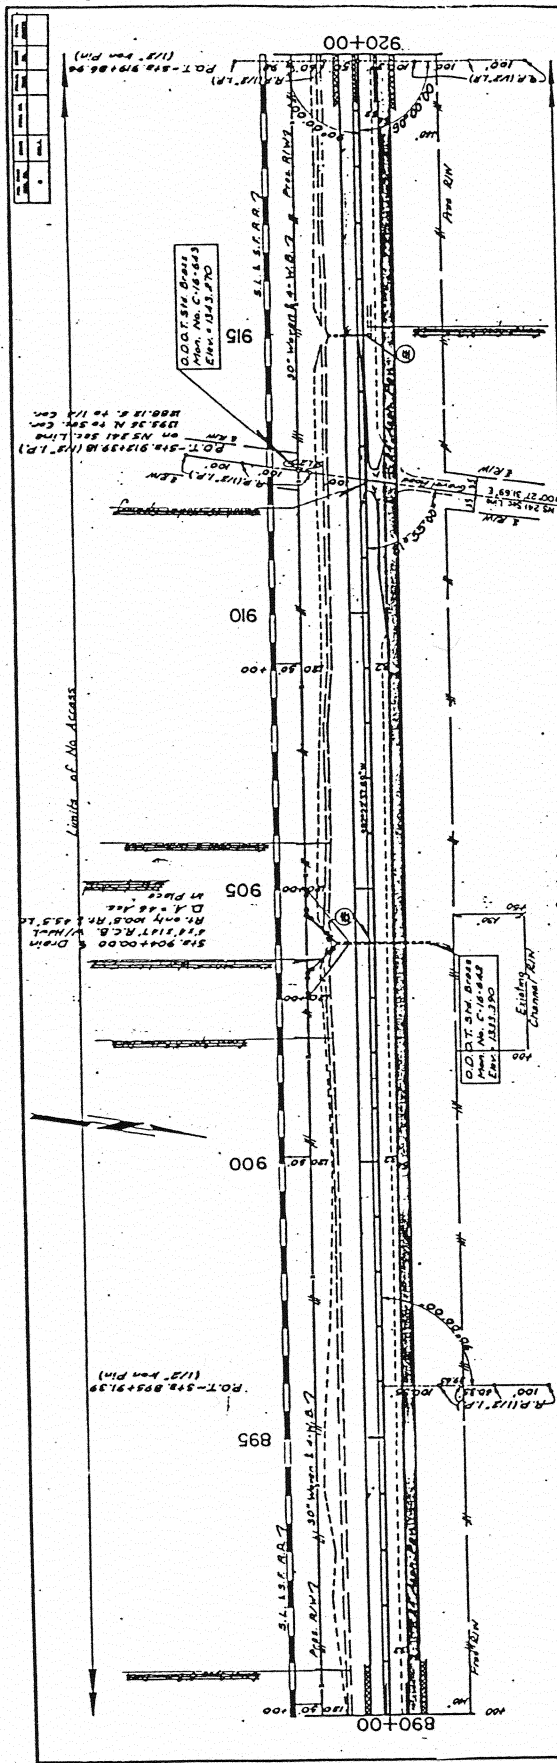

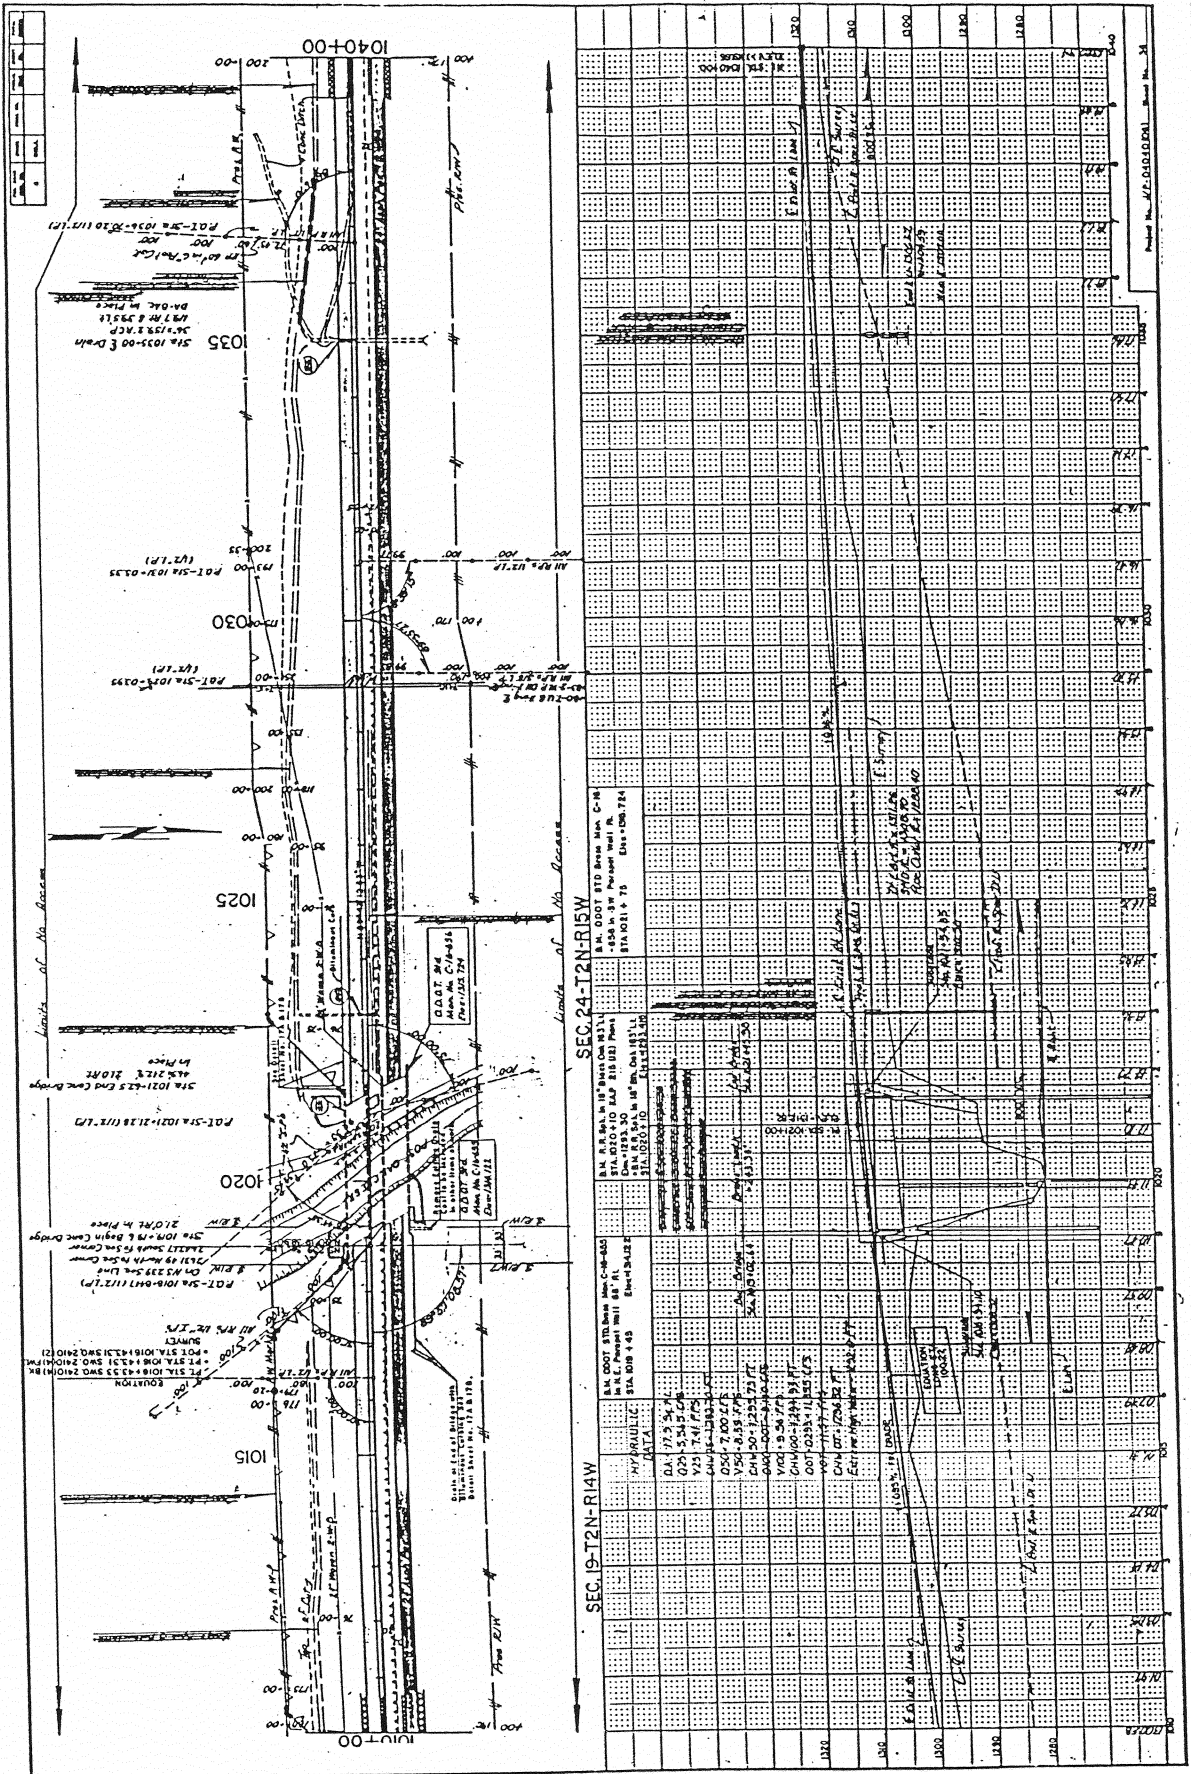

PLAN ESTIMATES															
ITEM NO.	APPROXIMATE STATION LOCATION	TYPE OF SIGN	TYPE OF POSTS	ESTIMATED POST LENGTHS & LINEAR FEET			LATERAL CLEARANCE	POST SPACE	FIG. DES. NO.	SIRL. CONC. CU. YD.	REINF. STEEL LBS.	SIGN AREA SQUARE FEET			REMARKS
				A	B	C						SHEET	PANEL	OVERLAY	
11774+25	(RT)	RS-1a	2-1/4" SQ	12,000								6,000			
21774+00	(RT)	RS-1	2-1/4" SQ	11,500								6,250			
31774+30	(MEDIAN)	RA-7	2-1/4" SQ	11,500								5,000			
41774+50	(MEDIAN)	RA-7	2-1/4" SQ	11,500								5,000			
51774+00	(LT)	RS-1	2-1/4" SQ	11,500								5,250			
61774+40	(LT)	RS-1a	2-1/4" SQ	11,000								6,000			
71774+00	(RT)	ROUTE ASSEMBLY NO. 1	2-1/4" SQ	11,500								6,000			
81774+00	(LT)	RS-1101	2-1/4" SQ	11,500								5,000			
91774+00	(LT)	ROUTE ASSEMBLY NO. 2	2-1/4" SQ	11,000								5,000			
101774+00	(RT)	RS-1101	2-1/4" SQ	11,500								5,000			
111774+00	(RT)	ON-3111 EXISTING													
121774+00	(RT)	ON-3121 EXISTING													
131774+00	(LT)	ON-3111	2-1/4" SQ	11,000								3,000			
141774+00	(LT)	ON-3121	2-1/4" SQ	11,000								3,000			
151774+00	(RT)	RS-1a	2-1/4" SQ	11,000								6,000			
161774+00	(RT)	RS-1	2-1/4" SQ	11,500								6,250			
171774+00	(MEDIAN)	RA-7	2-1/4" SQ	11,500								5,000			
181774+00	(MEDIAN)	RA-7	2-1/4" SQ	11,500								5,000			
191774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
201774+00	(LT)	RS-1a	2-1/4" SQ	11,000								6,000			
211774+00	(RT)	RS-1a	2-1/4" SQ	11,000								6,000			
221774+00	(RT)	RS-1	2-1/4" SQ	11,500								6,250			
231774+00	(MEDIAN)	RA-7	2-1/4" SQ	11,500								5,000			
241774+00	(MEDIAN)	RA-7	2-1/4" SQ	11,500								5,000			
251774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
261774+00	(LT)	RS-1a	2-1/4" SQ	11,000								6,000			
271774+00	(RT)	RS-1a	2-1/4" SQ	11,000								6,000			
281774+00	(RT)	RS-1	2-1/4" SQ	11,500								6,250			
291774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
301774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
311774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
321774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
331774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
341774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
351774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
361774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
371774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
381774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
391774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
401774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
411774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
421774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
431774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
441774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
451774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
461774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
471774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
481774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
491774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
501774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
511774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
521774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
531774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
541774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
551774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
561774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
571774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
581774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
591774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
601774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
611774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
621774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
631774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
641774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
651774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
661774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
671774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
681774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
691774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
701774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
711774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
721774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
731774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
741774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
751774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
761774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
771774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
781774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
791774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
801774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
811774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
821774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
831774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
841774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
851774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
861774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
871774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
881774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
891774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
901774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
911774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
921774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
931774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
941774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
951774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
961774+00	(LT)	RS-1	2-1/4" SQ	11,500								6,250			
971774+00	(LT)	RS-1	2-1/4" SQ	11,500											

RECEIVED NOV 20 1997

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 1 REFERENCE PROJECT STATION TABLE	* STATE CODE [4 0] * SPS PROJECT CODE [0 5] * TEST SECTION NO. [0 0]
---	--

ORDER	TEST SECTION ID NO (1)	REFERENCE PROJECT STATION NUMBER		(4) CUT-FILL ¹	
		(2) START	(3) END	TYPE	STATION
1	4 0 0 5 0 1	0 + 0 0	— — — 5 + 0 0	2	— + — —
2	4 0 0 5 0 2	— — — 9 + 0 0	— — — 1 4 + 0 0	2	— + — —
3	4 0 0 5 0 3	— — — 1 9 + 0 0	— — — 2 4 + 0 0	2	— + — —
4	4 0 0 5 0 8	— — — 3 2 + 0 0	— — — 3 7 + 0 0	2	— + — —
5	4 0 0 5 0 9	— — — 4 3 + 0 0	— — — 4 8 + 0 0	2	— + — —
6	4 0 0 5 0 6	— — — 6 5 4 + 0 0	— — — 7 8 + 0 0	2	— + — —
7	4 0 0 5 0 7	— — — 8 4 + 0 0	— — — 8 9 + 0 0	2	— + — —
8	4 0 0 5 0 4	— — — 9 3 + 0 0	— — — 9 8 + 0 0	2	— + — —
9	4 0 0 5 0 5	— — — 1 0 9 + 0 0	— — — 1 1 4 + 0 0	2	— + — —
10	4 0 0 5 6 0	— — — 1 3 6 + 0 0	— — — 1 4 1 + 0 0	2	— + — —
11	— — — — —	— — — — + — —	— — — — + — —	—	— + — —
12	— — — — —	— — — — + — —	— — — — + — —	—	— + — —
13	— — — — —	— — — — + — —	— — — — + — —	—	— + — —
14	— — — — —	— — — — + — —	— — — — + — —	—	— + — —
15	— — — — —	— — — — + — —	— — — — + — —	—	— + — —
16	— — — — —	— — — — + — —	— — — — + — —	—	— + — —
17	— — — — —	— — — — + — —	— — — — + — —	—	— + — —
18	— — — — —	— — — — + — —	— — — — + — —	—	— + — —
19	— — — — —	— — — — + — —	— — — — + — —	—	— + — —
20	— — — — —	— — — — + — —	— — — — + — —	—	— + — —

5. SPS - GPS TEST SECTION EQUALITIES

GPS section — — — — — is the same as SPS section — — — — —
GPS section — — — — — is the same as SPS section — — — — —

6. INTERSECTIONS BETWEEN TEST SECTION ON THE PROJECT RAMP | --- INTERSECTION --- |

ROUTE	PROJECT STATION NO.	EXIT	ENT	STOP	SIGNAL	UNSIG
— — — — —	— — — — —	—	—	—	—	—
— — — — —	— — — — —	—	—	—	—	—
— — — — —	— — — — —	—	—	—	—	—

Note 1. Indicate the type of subgrade section the test section is located on:
Cut..... 1 Fill..... 2 At-Grade..... 3 Cut and Fill..... 4
If cut-fill transition is located in a test section, enter test section station of the cut-fill transition location.

PREPARER MRC EMPLOYER PAE DATE 7/21/97

ENTERED JUL 22 1997 J B

G.W. ENTERED JUN 17 1998

10/24/97

RECEIVED NOV 20 1997

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 2 REVISED LAYER DESCRIPTIONS	* STATE CODE [4 0] * SPS PROJECT CODE [0 5] * TEST SECTION NO. [0 2]
--	--

EX-10 MAY 13 1998 J B

1. LAYER NUMBER	2. LAYER DESCRIPTION	3. MATERIAL TYPE CLASS	4. LAYER THICKNESSES (Inches)			
			AVERAGE	MINIMUM	MAXIMUM	STD. DEV.
1	SUBGRADE(7)	[5 6]				
2	[0 5]	[4 6]	[_ 8.0]	_ _ . _	_ _ . _	_ _ . _
3	[0 4]	[0 1]	[_ 3.0]	_ _ . _	_ _ . _	_ _ . _
4	[0 3]	[0 1]	[_ 1.5]	_ _ . _	_ _ . _	_ _ . _
5	[0 2]	[7 3]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
6	[0 1]	[1 3]	[_ 1.8]	_ 1.0	_ 2.5	_ 0.3
7	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
8	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
9	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
10	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
11	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
12	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
13	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
14	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
15	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _

NOTES:

- Layer 1 is subgrade soil, the highest numbered layer is the pavement surface.
- Layer description codes:
 Overlay.....01 Base Layer.....05 Porous Friction Course..09
 Seal/Tack Coat.....02 Subbase Layer.....06 Surface Treatment.....10
 Original Surface.....03 Subgrade.....07 Embankment (Fill).....11
 HMAC Layer (Subsurface).04 Interlayer.....08
 If milling was performed, the layers which were milled shall be assigned their previous layer number and material type. If the layer was completely removed by milling, it shall still be shown as a layer with a zero thickness.
- Enter the material type classification codes from Tables A.5, A.6, A.7 and A.8 which best describes the material in each layer. If the layer was milled, enter the material classification code corresponding to the type material which was removed.
- Enter the average thickness of each layer and the maximum, minimum, and standard deviation of the thickness measurements, if known. If a layer was partially milled, the remaining thickness of the layer shall be indicated.

PREPARED

John A. Martin

EMPLOYER

BRE

DATE

11/18/97

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 4 ASPHALT CONCRETE PATCHES	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [02]
--	---

1. DATE PATCHING OPERATIONS BEGAN (Month-Day-Year) [07-08-97]
2. DATE PATCHING OPERATIONS COMPLETED [07-08-97]
3. PRIMARY DISTRESS OCCURRENCE PATCHED (code from Table A.22) [06]
Other (Specify) Transverse Cracking of moderate to high severity
4. SECONDARY DISTRESS OCCURRENCE PATCHED (code from Table A.22) []
Other (Specify) _____
5. SUMMARY OF PATCHING
- | | NUMBER | TOTAL AREA (SQ. FT.) |
|--------------------------------------|--------|----------------------|
| Surface Only | [03] | [100] |
| Surface and partial base replacement | [00] | [] |
| Full depth | [00] | [] |
6. METHOD USED TO DETERMINE LOCATION AND SIZES OF PATCHES [3]
Deflection.... 1 Coring.... 2 Visual..... 3
Other..... 4 (specify) _____
7. METHOD USED TO FORM PATCH BOUNDARIES [1]
None 1 Saw Cut..... 2 Air Hammer..... 3 Cold Milling..... 4
Other..... 5 (Specify) _____
8. COMPACTION EQUIPMENT [2]
None 1 Pneumatic roller.... 2 Vibratory Plate Compactor. 3
Vibratory Roller.. 4 Steel Wheel Roller.. 5 Truck Tire..... 6
Hand Tools..... 7 Other..... 8 (Specify) _____
9. PATCH MATERIAL [1]
Hot Mix Asphalt Concrete... 1 Plant Mix with Cutback Asphalt, Cold Laid.... 2
Plant Mix with Emulsified Asphalt, Cold Laid. 3 Road Mix with Cutback Asphalt. 4
Road Mix with Emulsified Asphalt..... 5 Portland Cement Concrete..... 6
Other.. 7 (Specify) _____
10. MINIMUM TIME FROM MATERIAL PLACEMENT TO OPENING TO TRAFFIC (Hrs) [48]
11. MAXIMUM MATERIAL TEMPERATURE FOR TRAFFIC OPENING (if used) (°F) []
12. AIR TEMPERATURE DURING PLACEMENT OPERATIONS [85]
High Temperature (°F) [60]
Low Temperature (°F) []
13. PREDOMINATE ROAD SURFACE MOISTURE CONDITION DURING PLACEMENT OPERATIONS [1]
Dry..... 1 Moist..... 2 Wet..... 3

PREPARER

Timothy J. Smith

EMPLOYER

BRE

DATE

11/4/97

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 7 OVERLAY PLACEMENT OPERATIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [02]
--	---

1. DATE SURFACE PREPARATION BEGAN (Month-Day-Year) [07-14-97]
2. DATE SURFACE PREPARATION COMPLETED [07-14-97]
3. SURFACE PREPARATION PRIOR TO PLACEMENT OF OVERLAY [3]
None..... 1 Broomed..... 2 Broomed + Asphaltic Tack Coat.... 3
Asphaltic Tack Coat (only).... 4
4. TACK COAT
Layer Numbers [05] []
Material Type None..... 1 SS-1..... 2 SS-1H..... 3 CRS-1..... 4 [02]
CRS-2..... 5 CMS-2..... 6 CMS-2H.. 7 CSS-1..... 8 CSS-1H... 9
Other.... 10 (Specify) _____
5. TACK COAT DILUTION (Percent) [50]
Mixing Rate _____ Parts Diluent 1 TO Parts Asphalt 1
6. TACK COAT APPLICATION RATE (Gal/Sq. Yd.) [0.03]
7. ASPHALT CONCRETE PLANT AND HAUL

	Type	Name	Haul Distance (Mi)	Time (Min)	Layer Numbers
Plant 1	[2]	Aztec	[] [] [7]	[10]	[6] [] []
Plant 2	[]	_____	[] [] []	[] [] []	[] [] []
Plant 3	[]	_____	[] [] []	[] [] []	[] [] []

Plant Type: Batch..... 1 Drum Mix.... 2 Other... 3 Specify _____
8. MANUFACTURER OF ASPHALT CONCRETE PAVER Blaw-Knox
9. MODEL DESIGNATION OF ASPHALT CONCRETE PAVER PF-510
10. SINGLE PASS LAYDOWN WIDTH (Feet) [22.0]
11. AC BINDER COURSE LIFT
Layer Number [] []
Nominal First Lift Placement Thickness (Inches) [] []
Nominal Second Lift Placement Thickness (Inches) [] []
12. AC SURFACE COURSE LIFT
Layer Number [06]
Nominal First Lift Placement Thickness (Inches) [2.5]
Nominal Second Lift Placement Thickness (Inches) [] []
13. SURFACE FRICTION COURSE
Layer Number [] []
Nominal Placement Thickness (Inches) [] []
14. TEST SECTION STATION OF TRANSVERSE JOINTS (within test section)
Binder Course [] + [] []
Surface Course [] + [] []
Surface Friction Course [] + [] []
15. LOCATION OF LONGITUDINAL SURFACE JOINT
Between lanes.. 1 Within lane.. 2 (specify offset from O/S feet) [1] [22.0] 11/12/98
16. SIGNIFICANT EVENTS DURING CONSTRUCTION(disruptions, rain, equip. problems, etc.)

PREPARER Shirley J. Marks

EMPLOYER BRE

DATE 11/19/97

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA	* STATE CODE	[4 0]
SHEET 8	* SPS PROJECT CODE	[0 5]
OVERLAY COMPACTION DATA	* TEST SECTION NO.	[0 2]

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) [0 7 - 1 4 - 9 7]
2. DATE PAVING OPERATIONS COMPLETED [0 7 - 1 6 - 9 7]
3. LAYER NUMBER [1 6]
4. MIXING TEMPERATURE (°F) [3 1 5]
5. LAYDOWN TEMPERATURES (°F)
- Mean..... 3 0 5. Number of Tests — —
- Minimum..... — — —. Maximum..... — — —.
- Standard Deviation... — — —.

ROLLER DATA

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	1 2.0				
7	B	Steel-Whl Tandem	— — —				
8	C	Steel-Whl Tandem	— — —				
9	D	Steel-Whl Tandem	— — —				
10	E	Pneumatic-Tired	1 8.0	1 2 0.			
11	F	Pneumatic-Tired	— — —	— — —			
12	G	Pneumatic-Tired	— — —	— — —			
13	H	Pneumatic-Tired	— — —	— — —			
14	I	Single-Drum Vibr.	— — —		— — —	— — —	— — —
15	J	Single-Drum Vibr.	— — —		— — —	— — —	— — —
16	K	Single-Drum Vibr.	— — —		— — —	— — —	— — —
17	L	Single-Drum Vibr.	— — —		— — —	— — —	— — —
18	M	Double-Drum Vibr.	1 1.2		3 2 0 0.	0 2	— — —
19	N	Double-Drum Vibr.	— — —		— — —	— — —	— — —
20	O	Double-Drum Vibr.	— — —		— — —	— — —	— — —
21	P	Double-Drum Vibr.	— — —		— — —	— — —	— — —
22	Q	Other					

	COMPACTION DATA	First Lift	Second Lift	Third Lift	Fourth Lift
23	BREAKDOWN				
24	Roller Code (A-Q)	M	—	—	—
24	Coverages	— 1.	— —	— —	— —
25	INTERMEDIATE				
26	Roller Code (A-Q)	E	—	—	—
26	Coverages	— 2.	— —	— —	— —
27	FINAL				
28	Roller Code (A-Q)	A	—	—	—
28	Coverages	— 1.	— —	— —	— —
29	Air Temperature (°F)	— 8 5.	— — —	— — —	— — —
30	Compacted Thickness (In)	— 2.0	— —	— —	— —
31	Curing Period (Days)	— — —	— — —	— — —	— — —

PREPARER Benjamin J. M...

EMPLOYER BRE

DATE 11/19/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE <u>[4 0]</u> * SPS PROJECT CODE <u>[0 5]</u> * TEST SECTION NO. <u>[0 2]</u>
---	---

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 1 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCION LAYER
<u>0+00</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>				<u>1 1</u> <u>1 7</u> <u>1 7</u> <u>1 9</u> <u>1 7</u>	
<u>0+50</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>				<u>1 0</u> <u>1 4</u> <u>1 3</u> <u>1 6</u> <u>1 1</u>	
<u>1+00</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>				<u>1 4</u> <u>1 8</u> <u>1 6</u> <u>1 9</u> <u>1 6</u>	
<u>1+50</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>				<u>1 7</u> <u>1 7</u> <u>1 3</u> <u>1 9</u> <u>1 4</u>	
<u>2+00</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>				<u>1 6</u> <u>1 7</u> <u>1 6</u> <u>1 3</u> <u>1 6</u>	
<u>2+50</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>				<u>1 6</u> <u>1 8</u> <u>1 8</u> <u>1 9</u> <u>1 8</u>	
<u>3+00</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>				<u>2 0</u> <u>2 2</u> <u>2 2</u> <u>2 3</u> <u>2 5</u>	
LAYER NUMBER					<u>0 6</u>	

PREPARER

Anthony J. Rota

EMPLOYER

DRE

DATE

10/27/97

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	<table style="width: 100%; border-collapse: collapse;"> <tr> <td style="width: 60%;">* STATE CODE</td> <td style="width: 40%; text-align: right;">[4 0]</td> </tr> <tr> <td>* SPS PROJECT CODE</td> <td style="text-align: right;">[0 5]</td> </tr> <tr> <td>* TEST SECTION NO.</td> <td style="text-align: right;">[0 2]</td> </tr> </table>	* STATE CODE	[4 0]	* SPS PROJECT CODE	[0 5]	* TEST SECTION NO.	[0 2]
* STATE CODE	[4 0]						
* SPS PROJECT CODE	[0 5]						
* TEST SECTION NO.	[0 2]						

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 2 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCTION LAYER
<u>3+50</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>2 . 2</u> <u>2 . 0</u> <u>2 . 0</u> <u>2 . 2</u> <u>1 . 9</u>	— — . — — — . — — — . — — — . — — — . —
<u>4+00</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>1 . 6</u> <u>1 . 9</u> <u>2 . 0</u> <u>2 . 0</u> <u>1 . 9</u>	— — . — — — . — — — . — — — . — — — . —
<u>4+50</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>1 . 9</u> <u>2 . 2</u> <u>2 . 2</u> <u>2 . 4</u> <u>1 . 9</u>	— — . — — — . — — — . — — — . — — — . —
<u>5+00</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>1 . 6</u> <u>1 . 9</u> <u>2 . 2</u> <u>2 . 3</u> <u>2 . 2</u>	— — . — — — . — — — . — — — . — — — . —
<u>— + —</u>	— — — — — — — — — — — — — — —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —
<u>— + —</u>	— — — — — — — — — — — — — — —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —
<u>— + —</u>	— — — — — — — — — — — — — — —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —
LAYER NUMBER	— — —	— — —	— — —	— — —	<u>0 6</u>	— — —

PREPARER *James J. M. K.*

EMPLOYER BRE

DATE 10/27/97

ENTERED OCT 19 1997

SPS-5 CONSTRUCTION DATA SHEET 11 MISCELLANEOUS CONSTRUCTION NOTES AND COMMENTS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [02]
--	---

Provide any miscellaneous comments and notes concerning construction operations which may have an influence on the ultimate performance of the test sections or which may cause undesired performance differences to occur between test sections. Also include any quality control measurements or data for which space is not provided on other forms. Provide an indication of the basis for such measurements, such as an ASTM, AASHTO, or Agency standard test designation.

Patching was used to seal 6 large ^{depressed} transverse cracks. This was done using an HMAC level-up and rolling w/ pneumatic roller.

PREPARER

Samuel J. Clark

EMPLOYER

BRE

DATE

11/19/97

Revised December 15, 1989

SHEET 1
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]
*STATE CODE [4 0]
*SHRP SECTION ID [0 5 0 2]

IMPROVEMENT LISTING

* 1. DATE COMPLETED (MO/DAY/YR)	* 2. WORK ¹ TYPE CODE (TABLE A.17)	* 3. WORK QUANTITY (UNITS FROM (TABLE A.17))	4. THICKNESS (INCHES)	5. COST ² (THOUSANDS OF DOLLARS PER LANE-MILE)
[0 7 / 1 6 / 9 7]	[4 3]	[_ 2 2 0 0 .]	_ 2 . 0	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ . _	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ . _	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ . _	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ . _	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ . _	_ _ _ .

NOTES:

1. For each specific work type, the appropriate set of sheets should be completed (as indexed in Table 7.1). It is recognized that parts of both Chapter 6 (Maintenance Data Collection) and Chapter 7 (Rehabilitation Data Collection) may be required to adequately record a given set of improvements for a test section.
2. Cost includes only pavement structure cost. Non-pavement costs such as cut and fill work, work on bridges, culverts, lighting, and guard rails are to be excluded.

GWL ENTERED JUN 16 1998

Revised December 15, 1989

SHEET 2
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]
*STATE CODE [4 0]
*SHRP SECTION ID [0 5 0 2]

G.W. ENTERED JUN 16 1993

REVISED LAYER DESCRIPTIONS

1.	*2.	*3.	*4.			
LAYER ¹ NUMBER	LAYER ² DESCRIP- TION	MATERIAL ^{3,4} TYPE CLASSIFICATION	LAYER THICKNESS (IN)			
			<----- MEAN	MIN.	MAX.	STD. DEV.
1	SUBGRADE(7)	[5 6]				
2	[0 5]	[4 6]	[_ 8.0]	_ _ . _	_ _ . _	_ _ . _
3	[0 4]	[0 1]	[_ 3.0]	_ _ . _	_ _ . _	_ _ . _
4	[0 3]	[0 1]	[_ 1.5]	_ _ . _	_ _ . _	_ _ . _
5	[0 2]	[7 3]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
6	[0 1]	[1 3]	[_ 1.8]	_ 1.0	_ 2.5	_ 0.3
7	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
8	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
9	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _

NOTES:

- Layer 1 is subgrade soil, last layer is existing surface.
- Layer description codes:

Overlay.....01	Base Layer.....05	Porous Friction
Seal/Tack Coat.....02	Subbase Layer.....06	Course.....09
Original Surface...03	Subgrade.....07	Surface Treatment....10
HMAC Layer (Below	Interlayer.....08	Embankment (Fill)....11
Surface Layer)...04		Recycled Layer.....12
- The material type classification codes for surface, base or subbase, subgrade, and seal coat or interlayer materials appear in Tables A.5, A.6, A.7 and A.8, respectively.
- If the materials or thicknesses of a layer has not changed during the rehabilitation, enter "99" as the material type classification and leave the layer thicknesses for that layer blank. If a layer has changed, enter the appropriate codes and thicknesses.

RECEIVED NOV 20 1997

SPS-5 CONSTRUCTION DATA SHEET 2 REVISED LAYER DESCRIPTIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [03]
--	---

1. LAYER NUMBER	2. LAYER DESCRIPTION	3. MATERIAL TYPE CLASS	4. LAYER THICKNESSES (Inches)			
			AVERAGE	MINIMUM	MAXIMUM	STD. DEV.
1	SUBGRADE(7)	[56]				
2	[05]	[46]	[8.0]	---	---	---
3	[04]	[01]	[3.0]	---	---	---
4	[03]	[01]	[1.5]	---	---	---
5	[02]	[73]	[]	---	---	---
6	[04]	[13]	[2.5]	1.1	3.7	0.6
7	[01]	[13]	[1.9]	1.0	2.6	0.4
8	[]	[]	[]	---	---	---
9	[]	[]	[]	---	---	---
10	[]	[]	[]	---	---	---
11	[]	[]	[]	---	---	---
12	[]	[]	[]	---	---	---
13	[]	[]	[]	---	---	---
14	[]	[]	[]	---	---	---
15	[]	[]	[]	---	---	---

NOTES:

- Layer 1 is subgrade soil, the highest numbered layer is the pavement surface.
- Layer description codes:

Overlay.....01	Base Layer.....05	Porous Friction Course..09
Seal/Tack Coat.....02	Subbase Layer.....06	Surface Treatment.....10
Original Surface.....03	Subgrade.....07	Embankment (Fill).....11
HMAC Layer (Subsurface).04	Interlayer.....08	

If milling was performed, the layers which were milled shall be assigned their previous layer number and material type. If the layer was completely removed by milling, it shall still be shown as a layer with a zero thickness.
- Enter the material type classification codes from Tables A.5, A.6, A.7 and A.8 which best describes the material in each layer. If the layer was milled, enter the material classification code corresponding to the type material which was removed.
- Enter the average thickness of each layer and the maximum, minimum, and standard deviation of the thickness measurements, if known. If a layer was partially milled, the remaining thickness of the layer shall be indicated.

PREPARER

Anthony J. Mada

EMPLOYER

BRE

DATE 11/18/97

RECEIVED MAY 18 1998 J B

SPS-5 CONSTRUCTION DATA SHEET 7 OVERLAY PLACEMENT OPERATIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [03]
--	---

1. DATE SURFACE PREPARATION BEGAN (Month-Day-Year) [07-10-97]
2. DATE SURFACE PREPARATION COMPLETED [07-10-97]
3. SURFACE PREPARATION PRIOR TO PLACEMENT OF OVERLAY
 None..... 1 Broomed..... 2 Broomed + Asphaltic Tack Coat.... 3
 Asphaltic Tack Coat (only).... 4 Binder [3]
4. TACK COAT
 Layer Numbers [05] []
 Material Type None..... 1 SS-1.... 2 SS-1H.... 3 CRS-1.... 4 [02]
 CRS-2.... 5 CMS-2.... 6 CMS-2H.. 7 CSS-1.... 8 CSS-1H... 9
 Other.... 10 (Specify) _____
5. TACK COAT DILUTION
 (Percent) [50]
 Mixing Rate Parts Diluent 1 TO Parts Asphalt 1
6. TACK COAT APPLICATION RATE (Gal/Sq. Yd.) [0.03]
7. ASPHALT CONCRETE PLANT AND HAUL

Plant	Type	Name	Haul Distance (Mi)	Time (Min)	Layer Numbers
Plant 1	[2]	Aztec	[] [] [7]	[10]	[6] [7] []
Plant 2	[]	_____	[] [] []	[] [] []	[] [] []
Plant 3	[]	_____	[] [] []	[] [] []	[] [] []

 Plant Type: Batch..... 1 Drum Mix.... 2 Other... 3 Specify _____
8. MANUFACTURER OF ASPHALT CONCRETE PAVER Blaw-knox
9. MODEL DESIGNATION OF ASPHALT CONCRETE PAVER PF-510
10. SINGLE PASS LAYDOWN WIDTH (Feet) [22.0]
11. AC BINDER COURSE LIFT
 Layer Number [06]
 Nominal First Lift Placement Thickness (Inches) [3.5]
 Nominal Second Lift Placement Thickness (Inches) []
12. AC SURFACE COURSE LIFT
 Layer Number [07]
 Nominal First Lift Placement Thickness (Inches) [2.5]
 Nominal Second Lift Placement Thickness (Inches) []
13. SURFACE FRICTION COURSE
 Layer Number []
 Nominal Placement Thickness (Inches) []
14. TEST SECTION STATION OF TRANSVERSE JOINTS (within test section)
 Binder Course [] + [] []
 Surface Course [] + [] []
 Surface Friction Course [] + [] []
15. LOCATION OF LONGITUDINAL SURFACE JOINT
 Between lanes.. 1 Within lane.. 2 (specify offset from O/S feet) [1] [2.0]
16. SIGNIFICANT EVENTS DURING CONSTRUCTION (disruptions, rain, equip. problems, etc.)

PREPARER

Justin J. Parks

EMPLOYER

BREDATE 11/19/97

ENHANCED MAY 18 1998

 24
 11/21/98

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA	* STATE CODE	[40]
SHEET 8	* SPS PROJECT CODE	[05]
OVERLAY COMPACTION DATA	* TEST SECTION NO.	[03]

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) [07-10-97]
 2. DATE PAVING OPERATIONS COMPLETED [07-11-97]
 3. LAYER NUMBER Binder [6]
 4. MIXING TEMPERATURE (°F) [315]
 5. LAYDOWN TEMPERATURES (°F)
 Mean..... 305.
 Minimum.....
 Standard Deviation...
 Number of Tests
 Maximum.....

ROLLER DATA

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	12.0				
7	B	Steel-Whl Tandem	—				
8	C	Steel-Whl Tandem	—				
9	D	Steel-Whl Tandem	—				
10	E	Pneumatic-Tired	18.0	120			
11	F	Pneumatic-Tired	—				
12	G	Pneumatic-Tired	—				
13	H	Pneumatic-Tired	—				
14	I	Single-Drum Vibr.	—				
15	J	Single-Drum Vibr.	—				
16	K	Single-Drum Vibr.	—				
17	L	Single-Drum Vibr.	—				
18	M	Double-Drum Vibr.	11.2		3200	02	
19	N	Double-Drum Vibr.	—				
20	O	Double-Drum Vibr.	—				
21	P	Double-Drum Vibr.	—				
22	Q	Other					

	COMPACTION DATA	First Lift	Second Lift	Third Lift	Fourth Lift
23	BREAKDOWN				
24	Roller Code (A-Q)	M	—	—	—
24	Coverages	— 1.	— —.	— —.	— —.
25	INTERMEDIATE				
26	Roller Code (A-Q)	E	—	—	—
26	Coverages	— 3.	— —.	— —.	— —.
27	FINAL				
28	Roller Code (A-Q)	A	—	—	—
28	Coverages	— 1.	— —.	— —.	— —.
29	Air Temperature (°F)	— 85.	— — —.	— — —.	— — —.
30	Compacted Thickness (In)	— 3.0	— —.	— —.	— —.
31	Curing Period (Days)	— 3.0	— —.	— —.	— —.

PREPARER Ernest J. Martin EMPLOYER BRE DATE 11/19/97

SPS-5 CONSTRUCTION DATA	* STATE CODE	[4 0]
SHEET 8	* SPS PROJECT CODE	[0 5]
OVERLAY COMPACTION DATA	* TEST SECTION NO.	[0 3]

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) [0 7 - 1 4 - 9 7]
 2. DATE PAVING OPERATIONS COMPLETED [0 7 - 1 6 - 9 7]
 3. LAYER NUMBER [7]
 4. MIXING TEMPERATURE (°F) [3 1 5.]
 5. LAYDOWN TEMPERATURES (°F)
 Mean..... 3 0 5.
 Minimum..... — — —.
 Standard Deviation... — — —.

Number of Tests — — .

Maximum..... — — —.

ROLLER DATA

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	1 2.0				
7	B	Steel-Whl Tandem	— — .				
8	C	Steel-Whl Tandem	— — .				
9	D	Steel-Whl Tandem	— — .				
10	E	Pneumatic-Tired	1 8.0	1 2 0.			
11	F	Pneumatic-Tired	— — .	— — — .			
12	G	Pneumatic-Tired	— — .	— — — .			
13	H	Pneumatic-Tired	— — .	— — — .			
14	I	Single-Drum Vibr.	— — .		— — — .	— — — .	— — .
15	J	Single-Drum Vibr.	— — .		— — — .	— — — .	— — .
16	K	Single-Drum Vibr.	— — .		— — — .	— — — .	— — .
17	L	Single-Drum Vibr.	— — .		— — — .	— — — .	— — .
18	M	Double-Drum Vibr.	1 1.2		3 2 0 0.	0 2	— — .
19	N	Double-Drum Vibr.	— — .		— — — .	— — — .	— — .
20	O	Double-Drum Vibr.	— — .		— — — .	— — — .	— — .
21	P	Double-Drum Vibr.	— — .		— — — .	— — — .	— — .
22	Q	Other					
COMPACTION DATA			First Lift	Second Lift	Third Lift	Fourth Lift	
BREAKDOWN							
23	Roller Code (A-Q)		M	—	—	—	
24	Coverages		— 1.	— — .	— — .	— — .	
INTERMEDIATE							
25	Roller Code (A-Q)		E	—	—	—	
26	Coverages		— 2.	— — .	— — .	— — .	
FINAL							
27	Roller Code (A-Q)		A	—	—	—	
28	Coverages		— 1.	— — .	— — .	— — .	
29	Air Temperature (°F)		— 8 5.	— — — .	— — — .	— — — .	
30	Compacted Thickness (In)		2.0	— — .	— — .	— — .	
31	Curing Period (Days)		— — .	— — — .	— — — .	— — — .	

PREPARER

Jonathan J. Marks

EMPLOYER

BRE

DATE 11/19/97

 EMULATED
 MAY 18 1998 J
 B

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE <u>[4 0]</u> * SPS PROJECT CODE <u>[0 5]</u> * TEST SECTION NO. <u>[0 3]</u>
---	---

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 1 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCITION LAYER
<u>0+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — . —	— — . —	<u>2 .4</u> <u>2 .9</u> <u>3 .0</u> <u>3 .7</u> <u>3 .6</u>	<u>1 .0</u> <u>1 .2</u> <u>1 .3</u> <u>1 .2</u> <u>1 .0</u>	— — . —
<u>0+5 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — . —	— — . —	<u>2 .4</u> <u>2 .6</u> <u>2 .6</u> <u>3 .1</u> <u>3 .0</u>	<u>1 .2</u> <u>1 .3</u> <u>1 .4</u> <u>1 .3</u> <u>1 .2</u>	— — . —
<u>1+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — . —	— — . —	<u>2 .8</u> <u>2 .9</u> <u>3 .1</u> <u>3 .7</u> <u>3 .1</u>	<u>1 .3</u> <u>1 .7</u> <u>1 .8</u> <u>1 .7</u> <u>1 .4</u>	— — . —
<u>1+5 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — . —	— — . —	<u>3 .0</u> <u>2 .8</u> <u>2 .8</u> <u>3 .2</u> <u>2 .8</u>	<u>1 .2</u> <u>1 .6</u> <u>1 .7</u> <u>1 .7</u> <u>2 .2</u>	— — . —
<u>2+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — . —	— — . —	<u>1 .7</u> <u>2 .3</u> <u>2 .4</u> <u>2 .8</u> <u>2 .8</u>	<u>1 .9</u> <u>1 .9</u> <u>2 .0</u> <u>2 .0</u> <u>1 .9</u>	— — . —
<u>2+5 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — . —	— — . —	<u>2 .0</u> <u>2 .2</u> <u>2 .2</u> <u>2 .6</u> <u>2 .8</u>	<u>1 .6</u> <u>1 .9</u> <u>2 .2</u> <u>2 .0</u> <u>1 .8</u>	— — . —
<u>3+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — . —	— — . —	<u>2 .0</u> <u>2 .4</u> <u>2 .4</u> <u>3 .0</u> <u>2 .9</u>	<u>2 .2</u> <u>2 .2</u> <u>2 .3</u> <u>1 .9</u> <u>1 .9</u>	— — . —
LAYER NUMBER		— —	— —	<u>0 6</u>	<u>0 7</u>	— —

PREPARER

Y. J. M. Jr.

EMPLOYER

BREDATE 10/27/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [03]
---	---

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 2 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCCTION LAYER
<u>3+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>2.3</u> <u>2.6</u> <u>2.6</u> <u>3.2</u> <u>3.2</u>	<u>2.3</u> <u>2.3</u> <u>2.5</u> <u>2.3</u> <u>1.9</u>	— — . — — — . — — — . — — — . — — — . —
<u>4+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>1.7</u> <u>1.9</u> <u>2.0</u> <u>2.6</u> <u>2.6</u>	<u>2.2</u> <u>2.4</u> <u>2.6</u> <u>2.4</u> <u>2.2</u>	— — . — — — . — — — . — — — . — — — . —
<u>4+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>1.1</u> <u>1.4</u> <u>1.7</u> <u>2.4</u> <u>2.4</u>	<u>2.0</u> <u>2.2</u> <u>2.4</u> <u>2.2</u> <u>2.3</u>	— — . — — — . — — — . — — — . — — — . —
<u>5+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>1.2</u> <u>1.4</u> <u>1.7</u> <u>2.4</u> <u>2.4</u>	<u>2.2</u> <u>2.3</u> <u>2.5</u> <u>2.4</u> <u>2.4</u>	— — . — — — . — — — . — — — . — — — . —
<u>+ — —</u>	— — — — — — — — — — — — — — —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —
<u>+ — —</u>	— — — — — — — — — — — — — — —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —
<u>+ — —</u>	— — — — — — — — — — — — — — —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —
LAYER NUMBER	— — —	— — —	— — —	<u>06</u>	<u>07</u>	— — —

PREPARER Lindsay WhiteEMPLOYER BREDATE 10/27/97

Revised December 15, 1989

SHEET 1
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]

*STATE CODE [4 0]

*SHRP SECTION ID [0 5 0 3]

IMPROVEMENT LISTING

* 1. DATE COMPLETED (MO/DAY/YR)	* 2. WORK ¹ TYPE CODE (TABLE A.17)	* 3. WORK QUANTITY (UNITS FROM (TABLE A.17))	4. THICKNESS (INCHES)	5. COST ² (THOUSANDS OF DOLLARS PER LANE-MILE)
[0 7 / 1 6 / 9 7]	[4 3]	[_ 2 2 0 0 .]	_ 5 . 0	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ . _	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ . _	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ . _	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ . _	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ . _	_ _ _ .

NOTES:

1. For each specific work type, the appropriate set of sheets should be completed (as indexed in Table 7.1). It is recognized that parts of both Chapter 6 (Maintenance Data Collection) and Chapter 7 (Rehabilitation Data Collection) may be required to adequately record a given set of improvements for a test section.
2. Cost includes only pavement structure cost. Non-pavement costs such as cut and fill work, work on bridges, culverts, lighting, and guard rails are to be excluded.

G.M. ENTERED JUN 16 1998

Revised December 15, 1989

SHEET 2
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]
*STATE CODE [4 0]
*SHRP SECTION ID [0 5 0 3]

C.M. ENTERED JUN 16 1998

REVISED LAYER DESCRIPTIONS

1.	*2.	*3.	*4.			
LAYER ¹ NUMBER	LAYER ² DESCRIP- TION	MATERIAL ^{3,4} TYPE CLASSIFICATION	LAYER THICKNESS (IN)			
			<----- MEAN	MIN.	MAX.	STD. DEV.
1	SUBGRADE(7)	[5 6]				
2	[0 5]	[4 6]	[_ 8.0]	_ _ . _	_ _ . _	_ _ . _
3	[0 4]	[0 1]	[_ 3.0]	_ _ . _	_ _ . _	_ _ . _
4	[0 3]	[0 1]	[_ 1.5]	_ _ . _	_ _ . _	_ _ . _
5	[0 2]	[7 3]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
6	[0 4]	[1 3]	[_ 2.5]	_ 1.1	_ 3.7	_ 0.6
7	[0 1]	[1 3]	[_ 1.9]	_ 1.0	_ 2.6	_ 0.4
8	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _
9	[_ _]	[_ _]	[_ . _]	_ _ . _	_ _ . _	_ _ . _

NOTES:

- Layer 1 is subgrade soil, last layer is existing surface.
- Layer description codes:

Overlay.....01	Base Layer.....05	Porous Friction
Seal/Tack Coat....02	Subbase Layer.....06	Course.....09
Original Surface...03	Subgrade.....07	Surface Treatment....10
HMAC Layer (Below	Interlayer.....08	Embankment (Fill)....11
Surface Layer)...04		Recycled Layer.....12
- The material type classification codes for surface, base or subbase, subgrade, and seal coat or interlayer materials appear in Tables A.5, A.6, A.7 and A.8, respectively.
- If the materials or thicknesses of a layer has not changed during the rehabilitation, enter "99" as the material type classification and leave the layer thicknesses for that layer blank. If a layer has changed, enter the appropriate codes and thicknesses.

SPS-5 CONSTRUCTION DATA SHEET 2 REVISED LAYER DESCRIPTIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [04]
--	---

ENCLOSURE MAY 18 1998 J B

1. LAYER NUMBER	2. LAYER DESCRIPTION	3. MATERIAL TYPE CLASS	4. LAYER THICKNESSES (Inches)			
			AVERAGE	MINIMUM	MAXIMUM	STD. DEV.
1	SUBGRADE(7)	[56]				
2	[05]	[46]	[8.0]	---	---	---
3	[04]	[01]	[3.0]	---	---	---
4	[03]	[01]	[1.5]	---	---	---
5	[02]	[73]	[.]	---	---	---
6	[04]	[01]	[2.9]	1.7	3.8	0.4
7	[01]	[01]	[1.8]	1.0	2.3	0.4
8	[]	[]	[.]	---	---	---
9	[]	[]	[.]	---	---	---
10	[]	[]	[.]	---	---	---
11	[]	[]	[.]	---	---	---
12	[]	[]	[.]	---	---	---
13	[]	[]	[.]	---	---	---
14	[]	[]	[.]	---	---	---
15	[]	[]	[.]	---	---	---

NOTES:

- Layer 1 is subgrade soil, the highest numbered layer is the pavement surface.
- Layer description codes:
 Overlay.....01 Base Layer.....05 Porous Friction Course...09
 Seal/Tack Coat.....02 Subbase Layer.....06 Surface Treatment.....10
 Original Surface.....03 Subgrade.....07 Embankment (Fill).....11
 HMA Layer (Subsurface).04 Interlayer.....08
 If milling was performed, the layers which were milled shall be assigned their previous layer number and material type. If the layer was completely removed by milling, it shall still be shown as a layer with a zero thickness.
- Enter the material type classification codes from Tables A.5, A.6, A.7 and A.8 which best describes the material in each layer. If the layer was milled, enter the material classification code corresponding to the type material which was removed.
- Enter the average thickness of each layer and the maximum, minimum, and standard deviation of the thickness measurements, if known. If a layer was partially milled, the remaining thickness of the layer shall be indicated.

PREPARER *Tracy J. Mark* EMPLOYER ERE DATE 11/18/97

October 1990 (Heading revised October 1992)

ENTERED MAY 13 1998 J B

SPS-5 CONSTRUCTION DATA SHEET 7 OVERLAY PLACEMENT OPERATIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [04]
--	---

1. DATE SURFACE PREPARATION BEGAN (Month-Day-Year) [07-02-97]
2. DATE SURFACE PREPARATION COMPLETED [07-02-97]
3. SURFACE PREPARATION PRIOR TO PLACEMENT OF OVERLAY Binder [3]
None..... 1 Broomed..... 2 Broomed + Asphaltic Tack Coat.... 3
Asphaltic Tack Coat (only).... 4
4. TACK COAT
Layer Numbers [05] []
Material Type None..... 1 SS-1.... 2 SS-1H.... 3 CRS-1.... 4 [02]
CRS-2.... 5 CMS-2.... 6 CMS-2H.. 7 CSS-1.... 8 CSS-1H... 9
Other.... 10 (Specify) _____
5. TACK COAT DILUTION [50]
(Percent)
Mixing Rate Parts Diluent 1 TO Parts Asphalt 1
6. TACK COAT APPLICATION RATE (Gal/Sq. Yd.) [0.03]
7. ASPHALT CONCRETE PLANT AND HAUL

	Type	Name	Haul Distance (Mi)	Time (Min)	Layer Numbers
Plant 1	[2]	Aztec	[] [] [7]	[1] [0]	[6] [7] []
Plant 2	[]	_____	[] [] []	[] []	[] [] []
Plant 3	[]	_____	[] [] []	[] []	[] [] []

 Plant Type: Batch..... 1 Drum Mix.... 2 Other... 3 Specify _____
8. MANUFACTURER OF ASPHALT CONCRETE PAVER Blaw - knew
9. MODEL DESIGNATION OF ASPHALT CONCRETE PAVER PF-510
10. SINGLE PASS LAYDOWN WIDTH (Feet) [22.0]
11. AC BINDER COURSE LIFT [06]
 Layer Number [3.5]
 Nominal First Lift Placement Thickness (Inches) []
 Nominal Second Lift Placement Thickness (Inches)
12. AC SURFACE COURSE LIFT [07]
 Layer Number [2.5]
 Nominal First Lift Placement Thickness (Inches) []
 Nominal Second Lift Placement Thickness (Inches)
13. SURFACE FRICTION COURSE []
 Layer Number []
 Nominal Placement Thickness (Inches)
14. TEST SECTION STATION OF TRANSVERSE JOINTS (within test section)
 Binder Course [] + []
 Surface Course [] + []
 Surface Friction Course [] + []
15. LOCATION OF LONGITUDINAL SURFACE JOINT [1]
 Between lanes.. 1 Within lane.. 2 (specify offset from O/S feet) [72.0]
16. SIGNIFICANT EVENTS DURING CONSTRUCTION (disruptions, rain, equip. problems, etc.)

PREPARER Shirley J. Martin EMPLOYER BRE DATE 11/19/97

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 8 OVERLAY COMPACTION DATA	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [04]
---	---

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) [07-02-97]
 2. DATE PAVING OPERATIONS COMPLETED [07-03-97]
 3. LAYER NUMBER Binder [6]
 4. MIXING TEMPERATURE (°F) [328]
 5. LAYDOWN TEMPERATURES (°F)
 Mean..... 315
 Minimum.....
 Standard Deviation...
 Number of Tests
 Maximum.....

ROLLER DATA

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	12.0				
7	B	Steel-Whl Tandem					
8	C	Steel-Whl Tandem					
9	D	Steel-Whl Tandem					
10	E	Pneumatic-Tired	18.0	120			
11	F	Pneumatic-Tired					
12	G	Pneumatic-Tired					
13	H	Pneumatic-Tired					
14	I	Single-Drum Vibr.					
15	J	Single-Drum Vibr.					
16	K	Single-Drum Vibr.					
17	L	Single-Drum Vibr.					
18	M	Double-Drum Vibr.	11.2		3200	02	
19	N	Double-Drum Vibr.					
20	O	Double-Drum Vibr.					
21	P	Double-Drum Vibr.					
22	Q	Other					

	COMPACTION DATA	First Lift	Second Lift	Third Lift	Fourth Lift
23	BREAKDOWN				
24	Roller Code (A-Q)	M			
24	Coverages	1			
25	INTERMEDIATE				
26	Roller Code (A-Q)	E			
26	Coverages	3			
27	FINAL				
28	Roller Code (A-Q)	A			
28	Coverages	1			
29	Air Temperature (°F)	85			
30	Compacted Thickness (In)	3.0			
31	Curing Period (Days)	4.0			

PREPARED Sanjay J. Gupta EMPLOYER BRE DATE 11/18/97

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 8 OVERLAY COMPACTION DATA	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [04]
---	---

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) [07-07-97]
 2. DATE PAVING OPERATIONS COMPLETED [07-08-97]
 3. LAYER NUMBER Surface [7]
 4. MIXING TEMPERATURE (°F) [328]
 5. LAYDOWN TEMPERATURES (°F)
 Mean..... 315
 Minimum.....
 Standard Deviation...
 Number of Tests
 Maximum.....

ROLLER DATA

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	12.0				
7	B	Steel-Whl Tandem					
8	C	Steel-Whl Tandem					
9	D	Steel-Whl Tandem					
10	E	Pneumatic-Tired	18.0	120			
11	F	Pneumatic-Tired					
12	G	Pneumatic-Tired					
13	H	Pneumatic-Tired					
14	I	Single-Drum Vibr.					
15	J	Single-Drum Vibr.					
16	K	Single-Drum Vibr.					
17	L	Single-Drum Vibr.					
18	M	Double-Drum Vibr.	11.2		3200	02	
19	N	Double-Drum Vibr.					
20	O	Double-Drum Vibr.					
21	P	Double-Drum Vibr.					
22	Q	Other					

	COMPACTION DATA	First Lift	Second Lift	Third Lift	Fourth Lift
23	BREAKDOWN Roller Code (A-Q)	M			
24	Coverages	1			
25	INTERMEDIATE Roller Code (A-Q)	E			
26	Coverages	2			
27	FINAL Roller Code (A-Q)	A			
28	Coverages	1			
29	Air Temperature (°F)	85			
30	Compacted Thickness (In)	20			
31	Curing Period (Days)				

PREPARER Anthony J. M... EMPLOYER BRE DATE 11/19/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE <u>[4 0]</u> * SPS PROJECT CODE <u>[0 5]</u> * TEST SECTION NO. <u>[0 4]</u>
---	---

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 1 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCITION LAYER
<u>0+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>1 . 7</u> <u>2 . 5</u> <u>3 . 0</u> <u>2 . 8</u> <u>2 . 2</u>	<u>1 . 4</u> <u>1 . 1</u> <u>1 . 2</u> <u>1 . 3</u> <u>1 . 7</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>
<u>0+5 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>3 . 1</u> <u>3 . 8</u> <u>3 . 5</u> <u>3 . 6</u> <u>2 . 3</u>	<u>1 . 4</u> <u>1 . 1</u> <u>1 . 2</u> <u>1 . 4</u> <u>2 . 0</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>
<u>1+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>2 . 4</u> <u>2 . 6</u> <u>3 . 1</u> <u>3 . 2</u> <u>2 . 4</u>	<u>1 . 4</u> <u>1 . 8</u> <u>1 . 1</u> <u>1 . 4</u> <u>1 . 9</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>
<u>1+5 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>2 . 3</u> <u>3 . 0</u> <u>2 . 9</u> <u>3 . 4</u> <u>2 . 4</u>	<u>1 . 2</u> <u>1 . 0</u> <u>1 . 1</u> <u>1 . 3</u> <u>2 . 0</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>
<u>2+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>2 . 8</u> <u>3 . 5</u> <u>3 . 5</u> <u>3 . 6</u> <u>3 . 2</u>	<u>2 . 2</u> <u>2 . 0</u> <u>1 . 9</u> <u>2 . 0</u> <u>2 . 2</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>
<u>2+5 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>2 . 5</u> <u>2 . 9</u> <u>2 . 9</u> <u>3 . 1</u> <u>2 . 4</u>	<u>2 . 0</u> <u>1 . 9</u> <u>1 . 9</u> <u>1 . 9</u> <u>2 . 2</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>
<u>3+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>	<u>2 . 5</u> <u>3 . 1</u> <u>3 . 1</u> <u>3 . 5</u> <u>2 . 4</u>	<u>2 . 0</u> <u>1 . 9</u> <u>1 . 7</u> <u>1 . 8</u> <u>2 . 2</u>	<u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u> <u>— — . —</u>
LAYER NUMBER				<u>0 6</u>	<u>0 7</u>	

PREPARER Jimmy / M.D.EMPLOYER BREDATE 10/31/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE <u>[40]</u> * SPS PROJECT CODE <u>[05]</u> * TEST SECTION NO. <u>[04]</u>
---	--

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 2 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCION LAYER
<u>3+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>2.6</u> <u>3.1</u> <u>2.9</u> <u>3.2</u> <u>2.9</u>	<u>2.0</u> <u>2.0</u> <u>1.8</u> <u>1.9</u> <u>2.0</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
<u>4+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>2.3</u> <u>3.0</u> <u>2.9</u> <u>3.0</u> <u>2.5</u>	<u>2.3</u> <u>2.2</u> <u>2.0</u> <u>2.0</u> <u>2.2</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
<u>4+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>2.5</u> <u>3.2</u> <u>3.2</u> <u>3.6</u> <u>2.6</u>	<u>2.2</u> <u>1.9</u> <u>1.8</u> <u>1.8</u> <u>2.2</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
<u>5+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>2.3</u> <u>2.9</u> <u>3.0</u> <u>3.4</u> <u>2.6</u>	<u>2.3</u> <u>2.2</u> <u>2.0</u> <u>2.0</u> <u>2.2</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
<u>—+—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
<u>—+—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
<u>—+—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
LAYER NUMBER	<u>—</u>	<u>—</u>	<u>—</u>	<u>06</u>	<u>07</u>	<u>—</u>

ENTERED MAY 18 1993

PREPARER Timothy J. MartinEMPLOYER BREDATE 10/31/97

Revised December 15, 1989

SHEET 1
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]
*STATE CODE [4 0]
*SHRP SECTION ID [0 5 0 4]

IMPROVEMENT LISTING

* 1. DATE COMPLETED (MO/DAY/YR)	* 2. WORK ¹ TYPE CODE (TABLE A.17)	* 3. WORK QUANTITY (UNITS FROM (TABLE A.17))	4. THICKNESS (INCHES)	5. COST ² (THOUSANDS OF DOLLARS PER LANE-MILE)
[0 7 / 0 8 / 9 7]	[1 9]	[_ 2 2 0 0 .]	_ 5 . 0	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ . _	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ . _	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ . _	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ . _	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ . _	_ _ _ .

NOTES:

1. For each specific work type, the appropriate set of sheets should be completed (as indexed in Table 7.1). It is recognized that parts of both Chapter 6 (Maintenance Data Collection) and Chapter 7 (Rehabilitation Data Collection) may be required to adequately record a given set of improvements for a test section.
2. Cost includes only pavement structure cost. Non-pavement costs such as cut and fill work, work on bridges, culverts, lighting, and guard rails are to be excluded.

GW ENTERED JUN 16 1998

Revised December 15, 1989

SHEET 2
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]
*STATE CODE [4 0]
*SHRP SECTION ID [0 5 0 4]

REVISED LAYER DESCRIPTIONS

1.	*2.	*3.	*4.			
LAYER ¹ NUMBER	LAYER ² DESCRIP- TION	MATERIAL ^{3,4} TYPE CLASSIFICATION	LAYER THICKNESS (IN)			
			<----- MEAN	MIN.	MAX.	STD. DEV.
1	SUBGRADE(7)	[5 6]				
2	[0 5]	[4 6]	[_ 8.0]	---	---	---
3	[0 4]	[0 1]	[_ 3.0]	---	---	---
4	[0 3]	[0 1]	[_ 1.5]	---	---	---
5	[0 2]	[7 3]	[_ .]	---	---	---
6	[0 4]	[0 1]	[_ 2.9]	1.7	3.8	0.4
7	[0 1]	[0 1]	[_ 1.8]	1.0	2.3	0.4
8	[_ _]	[_ _]	[_ .]	---	---	---
9	[_ _]	[_ _]	[_ .]	---	---	---

GW ENTERED JUN 16 1998

NOTES:

- Layer 1 is subgrade soil, last layer is existing surface.
- Layer description codes:

Overlay.....01	Base Layer.....05	Porous Friction
Seal/Tack Coat.....02	Subbase Layer.....06	Course.....09
Original Surface...03	Subgrade.....07	Surface Treatment....10
HMAC Layer (Below	Interlayer.....08	Embankment (Fill)....11
Surface Layer)...04		Recycled Layer.....12
- The material type classification codes for surface, base or subbase, subgrade, and seal coat or interlayer materials appear in Tables A.5, A.6, A.7 and A.8, respectively.
- If the materials or thicknesses of a layer has not changed during the rehabilitation, enter "99" as the material type classification and leave the layer thicknesses for that layer blank. If a layer has changed, enter the appropriate codes and thicknesses.

October 1990 (Heading revised October 1992)

ENT-1 MAY 18 1998 J R

SPS-5 CONSTRUCTION DATA SHEET 7 OVERLAY PLACEMENT OPERATIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [05]
--	---

1. DATE SURFACE PREPARATION BEGAN (Month-Day-Year) [07-07-97]
2. DATE SURFACE PREPARATION COMPLETED [07-07-97]
3. SURFACE PREPARATION PRIOR TO PLACEMENT OF OVERLAY [3]
None..... 1 Broomed..... 2 Broomed + Asphaltic Tack Coat.... 3
Asphaltic Tack Coat (only).... 4
4. TACK COAT
Layer Numbers [05] []
Material Type None..... 1 SS-1.... 2 SS-1H.... 3 CRS-1.... 4 [02]
CRS-2.... 5 CMS-2.... 6 CMS-2H.. 7 CSS-1.... 8 CSS-1H... 9
Other.... 10 (Specify) _____
5. TACK COAT DILUTION [50]
(Percent)
Mixing Rate Parts Diluent 1 TO Parts Asphalt 1
6. TACK COAT APPLICATION RATE (Gal/Sq. Yd.) [0.03]
7. ASPHALT CONCRETE PLANT AND HAUL

Type	Name	Haul Distance (Mi)	Time (Min)	Layer Numbers
Plant 1 [2]	Aztec	[] [] [7]	[10]	[6] [] []
Plant 2 []	_____	[] [] []	[] []	[] [] []
Plant 3 []	_____	[] [] []	[] []	[] [] []

 Plant Type: Batch..... 1 Drum Mix.... 2 Other... 3 Specify _____
8. MANUFACTURER OF ASPHALT CONCRETE PAVER Blaw-Knox
9. MODEL DESIGNATION OF ASPHALT CONCRETE PAVER PF-510
10. SINGLE PASS LAYDOWN WIDTH (Feet) [22.0]
11. AC BINDER COURSE LIFT []
Layer Number []
Nominal First Lift Placement Thickness (Inches) []
Nominal Second Lift Placement Thickness (Inches) []
12. AC SURFACE COURSE LIFT [06]
Layer Number [2.5]
Nominal First Lift Placement Thickness (Inches) []
Nominal Second Lift Placement Thickness (Inches) []
13. SURFACE FRICTION COURSE []
Layer Number []
Nominal Placement Thickness (Inches) []
14. TEST SECTION STATION OF TRANSVERSE JOINTS (within test section)
Binder Course [] + []
Surface Course [] + []
Surface Friction Course [] + []
15. LOCATION OF LONGITUDINAL SURFACE JOINT [1]
Between lanes.. 1 Within lane.. 2 (specify offset from O/S feet) [2.0] ⁴¹¹ 9/2/98
16. SIGNIFICANT EVENTS DURING CONSTRUCTION (disruptions, rain, equip. problems, etc.) _____

PREPARER Jonathan J. [Signature]

EMPLOYER BRE

DATE 11/19/97

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 8 OVERLAY COMPACTION DATA	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [05]
---	---

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) [07-07-97]
 2. DATE PAVING OPERATIONS COMPLETED [07-08-97]
 3. LAYER NUMBER [6]
 4. MIXING TEMPERATURE (°F) [322]
 5. LAYDOWN TEMPERATURES (°F)
 Mean..... 315. Number of Tests
 Minimum..... Maximum.....
 Standard Deviation... ..

ROLLER DATA

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	12.0				
7	B	Steel-Whl Tandem					
8	C	Steel-Whl Tandem					
9	D	Steel-Whl Tandem					
10	E	Pneumatic-Tired	18.0	120			
11	F	Pneumatic-Tired					
12	G	Pneumatic-Tired					
13	H	Pneumatic-Tired					
14	I	Single-Drum Vibr.					
15	J	Single-Drum Vibr.					
16	K	Single-Drum Vibr.					
17	L	Single-Drum Vibr.					
18	M	Double-Drum Vibr.	11.2		3200	02	
19	N	Double-Drum Vibr.					
20	O	Double-Drum Vibr.					
21	P	Double-Drum Vibr.					
22	Q	Other					

	COMPACTION DATA	First Lift	Second Lift	Third Lift	Fourth Lift
23	BREAKDOWN Roller Code (A-Q)	M			
24	Coverages	1			
25	INTERMEDIATE Roller Code (A-Q)	E			
26	Coverages	2			
27	FINAL Roller Code (A-Q)	A			
28	Coverages	1			
29	Air Temperature (°F)	85			
30	Compacted Thickness (In)	2.0			
31	Curing Period (Days)				

PREPARER

Samuel J. Pluta

EMPLOYER

BRE

DATE

11/19/97

EN. 10 MAY 13 1998 J B

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE <u>40</u> * SPS PROJECT CODE <u>05</u> * TEST SECTION NO. <u>05</u>
---	--

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 1 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCITION LAYER
<u>0+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.7</u> <u>2.2</u> <u>1.8</u> <u>1.9</u> <u>1.6</u>	
<u>0+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.6</u> <u>1.8</u> <u>1.6</u> <u>1.8</u> <u>1.3</u>	
<u>1+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.7</u> <u>2.0</u> <u>1.7</u> <u>2.0</u> <u>1.8</u>	
<u>1+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.3</u> <u>1.6</u> <u>1.6</u> <u>1.9</u> <u>1.7</u>	
<u>2+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.0</u> <u>1.3</u> <u>1.4</u> <u>1.7</u> <u>1.6</u>	
<u>2+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>0.8</u> <u>1.2</u> <u>1.3</u> <u>1.7</u> <u>1.4</u>	
<u>3+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.3</u> <u>1.6</u> <u>1.7</u> <u>1.8</u> <u>1.6</u>	
LAYER NUMBER					<u>06</u>	

PREPARER

Timothy J. Miller

EMPLOYER

BSR

DATE

10/31/97

FILED MAY 18 1998 J B

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [05]
---	---

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 2 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCION LAYER
<u>3+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.8</u> <u>1.7</u> <u>1.4</u> <u>1.7</u> <u>1.6</u>	
<u>4+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.9</u> <u>2.0</u> <u>1.9</u> <u>2.0</u> <u>1.8</u>	
<u>4+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.8</u> <u>2.0</u> <u>1.9</u> <u>1.9</u> <u>1.6</u>	
<u>5+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.9</u> <u>2.2</u> <u>1.9</u> <u>1.9</u> <u>2.2</u>	
<u>+ - -</u>						
<u>+ - -</u>						
<u>+ - -</u>						
LAYER NUMBER					<u>C 6</u>	

EMPLOYER

BRE

DATE 10/31/97

ENLINED MAY 18 1998 J R

October 1990 (Heading revised October 1992)

RECEIVED MAY 13 1998 J B

SPS-5 CONSTRUCTION DATA SHEET 8 OVERLAY COMPACTION DATA	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [06]
---	---

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) [07-07-97]
 2. DATE PAVING OPERATIONS COMPLETED [07-08-97]
 3. LAYER NUMBER overlay [6]
 4. MIXING TEMPERATURE (°F) [328]
 5. LAYDOWN TEMPERATURES (°F)
 Mean..... 315
 Minimum.....
 Standard Deviation...
 Number of Tests
 Maximum.....

ROLLER DATA

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	12.0				
7	B	Steel-Whl Tandem					
8	C	Steel-Whl Tandem					
9	D	Steel-Whl Tandem					
10	E	Pneumatic-Tired	18.0	120			
11	F	Pneumatic-Tired					
12	G	Pneumatic-Tired					
13	H	Pneumatic-Tired					
14	I	Single-Drum Vibr.					
15	J	Single-Drum Vibr.					
16	K	Single-Drum Vibr.					
17	L	Single-Drum Vibr.					
18	M	Double-Drum Vibr.	11.2		3200	02	
19	N	Double-Drum Vibr.					
20	O	Double-Drum Vibr.					
21	P	Double-Drum Vibr.					
22	Q	Other					
	COMPACTION DATA		First Lift	Second Lift	Third Lift	Fourth Lift	
23	BREAKDOWN						
24	Roller Code (A-Q)		M				
24	Coverages		1				
25	INTERMEDIATE						
26	Roller Code (A-Q)		E				
26	Coverages		3				
27	FINAL						
28	Roller Code (A-Q)		A				
28	Coverages		2				
29	Air Temperature (°F)		85				
30	Compacted Thickness (In)		3.5				
31	Curing Period (Days)						

PREPARER

Timothy J. Mark

EMPLOYER

BRE

DATE

11/19/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE <u>[4 0]</u> * SPS PROJECT CODE <u>[0 5]</u> * TEST SECTION NO. <u>[0 6]</u>
---	---

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 1 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCITION LAYER
<u>0+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — —	— — —	— — —	<u>3 0</u> <u>3 4</u> <u>3 4</u> <u>3 7</u> <u>3 6</u>	— — —
<u>0+5 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — —	— — —	— — —	<u>3 0</u> <u>3 1</u> <u>2 9</u> <u>3 4</u> <u>3 7</u>	— — —
<u>1+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — —	— — —	— — —	<u>3 2</u> <u>3 2</u> <u>3 1</u> <u>3 3</u> <u>3 8</u>	— — —
<u>1+5 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — —	— — —	— — —	<u>4 0</u> <u>3 7</u> <u>3 5</u> <u>3 7</u> <u>4 1</u>	— — —
<u>2+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — —	— — —	— — —	<u>4 1</u> <u>3 7</u> <u>3 7</u> <u>4 0</u> <u>4 1</u>	— — —
<u>2+5 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — —	— — —	— — —	<u>3 7</u> <u>3 6</u> <u>3 5</u> <u>3 7</u> <u>4 0</u>	— — —
<u>3+0 0</u>	<u>0</u> <u>5 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — —	— — —	— — —	<u>3 8</u> <u>3 7</u> <u>3 7</u> <u>4 1</u> <u>4 4</u>	— — —
LAYER NUMBER					<u>0 6</u>	— — —

ENTERED MAY 18 1993 J R

 PREPARED *Kimberly J. Muth* EMPLOYER ISRE DATE 10/31/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE 40 * SPS PROJECT CODE 05 * TEST SECTION NO. 06
---	---

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 2 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCION LAYER
<u>3+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	<u>4.0</u> <u>4.1</u> <u>4.0</u> <u>4.2</u> <u>4.3</u>	— — — — — — — — — — — — — — — — — — — —
<u>4+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	<u>4.1</u> <u>3.7</u> <u>4.0</u> <u>4.3</u> <u>4.5</u>	— — — — — — — — — — — — — — — — — — — —
<u>4+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	<u>4.7</u> <u>4.6</u> <u>4.4</u> <u>4.6</u> <u>4.7</u>	— — — — — — — — — — — — — — — — — — — —
<u>5+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	<u>4.9</u> <u>4.4</u> <u>4.4</u> <u>4.6</u> <u>4.9</u>	— — — — — — — — — — — — — — — — — — — —
<u>+ — —</u>	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —
<u>+ — —</u>	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —
<u>+ — —</u>	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —	— — — — — — — — — — — — — — — — — — — —
LAYER NUMBER	— — — —	— — — —	— — — —	— — — —	<u>06</u>	— — — —

PREPARER

Ginethy J. [Signature]

EMPLOYER

BRE

DATE

10/31/97

Revised December 15, 1989

SHEET 1
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]

*STATE CODE [4 0]

*SHRP SECTION ID [0 5 0 6]

IMPROVEMENT LISTING

* 1. DATE COMPLETED (MO/DAY/YR)	* 2. WORK ¹ TYPE CODE (TABLE A.17)	* 3. WORK QUANTITY (UNITS FROM (TABLE A.17))	4. THICKNESS (INCHES)	5. COST ² (THOUSANDS OF DOLLARS PER LANE-MILE)
[0 7 / 0 8 / 9 7]	[5 1]	[_ 2 2 0 0 .]	_ 3.5	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .

NOTES:

1. For each specific work type, the appropriate set of sheets should be completed (as indexed in Table 7.1). It is recognized that parts of both Chapter 6 (Maintenance Data Collection) and Chapter 7 (Rehabilitation Data Collection) may be required to adequately record a given set of improvements for a test section.
2. Cost includes only pavement structure cost. Non-pavement costs such as cut and fill work, work on bridges, culverts, lighting, and guard rails are to be excluded.

G.W. ENTERED JUN 17 1998

Revised December 15, 1989

SHEET 2
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]

*STATE CODE [4 0]

*SHRP SECTION ID [0 5 0 6]

REVISED LAYER DESCRIPTIONS

1.	*2.	*3.	*4.			
LAYER ¹ NUMBER	LAYER ² DESCRIP- TION	MATERIAL ^{3,4} TYPE CLASSIFICATION	<----- LAYER THICKNESS (IN) ----->			
			MEAN	MIN.	MAX.	STD. DEV.
1	SUBGRADE(7)	[5 6]				
2	[0 5]	[4 6]	[_ _ 8.0]	---	---	---
3	[0 4]	[0 1]	[_ _ 3.0]	---	---	---
4	[0 3]	[0 1]	[_ _ 0.0]	---	---	---
5	[0 2]	[7 3]	[_ _ _]	---	---	---
6	[0 1]	[0 1]	[_ _ 3.9]	2.9	4.9	0.5
7	[_ _]	[_ _]	[_ _ _]	---	---	---
8	[_ _]	[_ _]	[_ _ _]	---	---	---
9	[_ _]	[_ _]	[_ _ _]	---	---	---

NOTES:

- Layer 1 is subgrade soil, last layer is existing surface.
- Layer description codes:

Overlay.....01	Base Layer.....05	Porous Friction
Seal/Tack Coat....02	Subbase Layer.....06	Course.....09
Original Surface...03	Subgrade.....07	Surface Treatment....10
HMAC Layer (Below	Interlayer.....08	Embankment (Fill)....11
Surface Layer)...04		Recycled Layer.....12
- The material type classification codes for surface, base or subbase, subgrade, and seal coat or interlayer materials appear in Tables A.5, A.6, A.7 and A.8, respectively.
- If the materials or thicknesses of a layer has not changed during the rehabilitation, enter "99" as the material type classification and leave the layer thicknesses for that layer blank. If a layer has changed, enter the appropriate codes and thicknesses.

G.W. ENTERED JUN 17 1998

RECEIVED NOV 20 1997

SPS-5 CONSTRUCTION DATA SHEET 2 REVISED LAYER DESCRIPTIONS	* STATE CODE <u>(40)</u> * SPS PROJECT CODE <u>(05)</u> * TEST SECTION NO. <u>(07)</u>
--	--

1. LAYER NUMBER	2. LAYER DESCRIPTION	3. MATERIAL TYPE CLASS	4. LAYER THICKNESSES (Inches)			
			AVERAGE	MINIMUM	MAXIMUM	STD. DEV.
1	SUBGRADE(7)	[56]				
2	[05]	[46]	[8.0]	---	---	---
3	[04]	[01]	[3.0]	---	---	---
4	[03]	[01]	[0.0]	---	---	---
5	[02]	[73]	[.]	---	---	---
6	[04]	[01]	[2.9]	2.4	3.8	0.3
7	[01]	[01]	[3.5]	2.8	4.3	0.4
8	[]	[]	[.]	---	---	---
9	[]	[]	[.]	---	---	---
10	[]	[]	[.]	---	---	---
11	[]	[]	[.]	---	---	---
12	[]	[]	[.]	---	---	---
13	[]	[]	[.]	---	---	---
14	[]	[]	[.]	---	---	---
15	[]	[]	[.]	---	---	---

NOTES:

- Layer 1 is subgrade soil, the highest numbered layer is the pavement surface.
- Layer description codes:
 Overlay.....01 Base Layer.....05 Porous Friction Course..09
 Seal/Tack Coat.....02 Subbase Layer.....06 Surface Treatment.....10
 Original Surface.....03 Subgrade.....07 Embankment (Fill).....11
 HMA Layer (Subsurface).04 Interlayer.....08
 If milling was performed, the layers which were milled shall be assigned their previous layer number and material type. If the layer was completely removed by milling, it shall still be shown as a layer with a zero thickness.
- Enter the material type classification codes from Tables A.5, A.6, A.7 and A.8 which best describes the material in each layer. If the layer was milled, enter the material classification code corresponding to the type material which was removed.
- Enter the average thickness of each layer and the maximum, minimum, and standard deviation of the thickness measurements, if known. If a layer was partially milled, the remaining thickness of the layer shall be indicated.

PREPARER

Janet J. [Signature]

EMPLOYER

BRE

DATE

11/19/97

SPS-5 CONSTRUCTION DATA SHEET 6 PREPARATION OF MILLED TEST SECTIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [07]
---	---

1. DATE OF MILLING OPERATION [06-26-97]
2. MANUFACTURER OF MILLING MACHINE (Specify) Destrol, Inc. (owner)
3. MILLING MACHINE MODEL DESIGNATION (Specify) D1100 SMI
4. WIDTH OF CUTTING HEAD (Inches) [144]
5. TOTAL MILLED DEPTH (Inches)

Location	No. Measrmnts	Maximum	Minimum	Std. Dev.	Average
Inside lane edge	11.	2.3	0.0	0.7	1.2
Outside lane edge	11.	2.3	0.0	0.7	1.2

MILLED SURFACE CHARACTERISTICS

6. Macro Texture
Fine Macro Texture ($\leq \frac{1}{8}$ inch)... 1 Coarse Macro Texture ($> \frac{1}{8}$ inch)... 2 [2]
7. Estimate of extent of test section surface area delaminated (Percent) [0]
8. Height of Ridge Between Parallel Passes? (Inches) [.]
9. Other Comments? (Yes, No) []
Comments _____
10. WHERE PATCHES PLACED AFTER MILLING? (Yes, No) [No]
(If yes complete Construction Data Sheet 3)
11. LENGTH OF TIME MILLED SURFACE WAS OPENED TO TRAFFIC? (Hrs.) 6 days [144]
12. WAS MILL REPLACEMENT LAYER THICKER THAN MILL DEPTH (Yes, No) [Yes]
13. LAYER NUMBER OF MILL REPLACEMENT [6]
14. NOMINAL THICKNESS OF MILL REPLACEMENT MATERIAL (Inches) [3.5]
15. TYPE OF MILL REPLACEMENT LAYER MATERIAL [1]
"Virgin" Asphalt Concrete 1 Recycled Asphalt Concrete.... 2
Other... 3 (Specify) _____
16. WAS ADJACENT TRAVEL LANE MILLED TO SAME DEPTH AS TEST LANE? (Yes, No) [Yes]
IF NO, WIDTH MILLED SAME DEPTH AS TEST LANE (Feet) [.]
17. COMMENTS _____

PREPARER

Brent J. Martin

EMPLOYER

BRE

DATE

11/19/97

SPS-5 CONSTRUCTION DATA SHEET 7 OVERLAY PLACEMENT OPERATIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [07]
--	---

1. DATE SURFACE PREPARATION BEGAN (Month-Day-Year) [07-02-97]
2. DATE SURFACE PREPARATION COMPLETED [07-02-97]
3. SURFACE PREPARATION PRIOR TO PLACEMENT OF OVERLAY [3]
None..... 1 Broomed..... 2 Broomed + Asphaltic Tack Coat.... 3
Asphaltic Tack Coat (only).... 4
4. TACK COAT
Layer Numbers [05] []
Material Type None..... 1 SS-1.... 2 SS-1H.... 3 CRS-1.... 4 [02]
CRS-2.... 5 CMS-2.... 6 CMS-2H.. 7 CSS-1.... 8 CSS-1H... 9
Other.... 10 (Specify) _____
5. TACK COAT DILUTION
(Percent) [50]
Mixing Rate Parts Diluent 1 TO Parts Asphalt 1
6. TACK COAT APPLICATION RATE (Gal/Sq. Yd.) [0.03]
7. ASPHALT CONCRETE PLANT AND HAUL

Plant	Type	Name	Haul Distance (Mi)	Time (Min)	Layer Numbers
Plant 1	[2]	Aztec	[] [] [7]	[1] [0]	[6] [7] []
Plant 2	[]	_____	[] [] []	[] []	[] [] []
Plant 3	[]	_____	[] [] []	[] []	[] [] []

Plant Type: Batch..... 1 Drum Mix.... 2 Other... 3 Specify _____
8. MANUFACTURER OF ASPHALT CONCRETE PAVER Blaw-Knox
9. MODEL DESIGNATION OF ASPHALT CONCRETE PAVER PF-510
10. SINGLE PASS LAYDOWN WIDTH (Feet) [220]
11. AC BINDER COURSE LIFT
Layer Number [06]
Nominal First Lift Placement Thickness (Inches) [3.5]
Nominal Second Lift Placement Thickness (Inches) []
12. AC SURFACE COURSE LIFT
Layer Number [07]
Nominal First Lift Placement Thickness (Inches) [4.0]
Nominal Second Lift Placement Thickness (Inches) []
13. SURFACE FRICTION COURSE
Layer Number []
Nominal Placement Thickness (Inches) []
14. TEST SECTION STATION OF TRANSVERSE JOINTS (within test section)
Binder Course [] + []
Surface Course [] + []
Surface Friction Course [] + []
15. LOCATION OF LONGITUDINAL SURFACE JOINT
Between lanes.. 1 Within lane.. 2 (specify offset from O/S feet) [2.0] 241
7/2/98
16. SIGNIFICANT EVENTS DURING CONSTRUCTION (disruptions, rain, equip. problems, etc.)

PREPARER

Gimothy J. Porto

EMPLOYER

BAE

DATE

11/12/97

SPS-5 CONSTRUCTION DATA SHEET 8 OVERLAY COMPACTION DATA	* STATE CODE [4 0] * SPS PROJECT CODE [0 5] * TEST SECTION NO. [0 7]
---	--

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) [0 7-0 2-9 7]
 2. DATE PAVING OPERATIONS COMPLETED [0 7-0 3-9 7]
 3. LAYER NUMBER inlay [6]
 4. MIXING TEMPERATURE (°F) [3 2 8.]
 5. LAYDOWN TEMPERATURES (°F)
 Mean..... 3 1 5.
 Minimum.....
 Standard Deviation...
 Number of Tests
 Maximum.....

ROLLER DATA

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	1 2.0				
7	B	Steel-Whl Tandem	— —.				
8	C	Steel-Whl Tandem	— —.				
9	D	Steel-Whl Tandem	— —.				
10	E	Pneumatic-Tired	1 8.0	1 2 0.			
11	F	Pneumatic-Tired	— —.	— —.			
12	G	Pneumatic-Tired	— —.	— —.			
13	H	Pneumatic-Tired	— —.	— —.			
14	I	Single-Drum Vibr.	— —.				
15	J	Single-Drum Vibr.	— —.				
16	K	Single-Drum Vibr.	— —.				
17	L	Single-Drum Vibr.	— —.				
18	M	Double-Drum Vibr.	1 1.2		3 2 0 0.	0 2	
19	N	Double-Drum Vibr.	— —.				
20	O	Double-Drum Vibr.	— —.				
21	P	Double-Drum Vibr.	— —.				
22	Q	Other					
	COMPACTION DATA		First Lift	Second Lift	Third Lift	Fourth Lift	
23	BREAKDOWN						
	Roller Code (A-Q)		M	—	—	—	—
24	Coverages		— 1.	— —.	— —.	— —.	— —.
25	INTERMEDIATE						
	Roller Code (A-Q)		E	—	—	—	—
26	Coverages		— 3.	— —.	— —.	— —.	— —.
27	FINAL						
	Roller Code (A-Q)		A	—	—	—	—
28	Coverages		— 2.	— —.	— —.	— —.	— —.
29	Air Temperature (°F)		— 8 5.	— —.	— —.	— —.	— —.
30	Compacted Thickness (In)		— 3.0	— —.	— —.	— —.	— —.
31	Curing Period (Days)		— 4.0	— —.	— —.	— —.	— —.

PREPARER Samuel J. Martin EMPLOYER BRE DATE 11/19/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE <u>40</u> * SPS PROJECT CODE <u>05</u> * TEST SECTION NO. <u>05</u>
---	--

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 2 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCION LAYER
<u>3+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.8</u> <u>1.7</u> <u>1.4</u> <u>1.7</u> <u>1.6</u>	
<u>4+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.9</u> <u>2.0</u> <u>1.9</u> <u>2.0</u> <u>1.8</u>	
<u>4+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.8</u> <u>2.0</u> <u>1.9</u> <u>1.9</u> <u>1.6</u>	
<u>5+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>1.9</u> <u>2.2</u> <u>1.9</u> <u>1.9</u> <u>2.2</u>	
<u>+ - -</u>						
<u>+ - -</u>						
<u>+ - -</u>						
LAYER NUMBER					<u>06</u>	

PREPARED

Birney J. Martin

EMPLOYER

BRE

DATE

10/31/97

ENLISHED MAY 13 1998 J R

SPS-5 CONSTRUCTION DATA SHEET 11 MISCELLANEOUS CONSTRUCTION NOTES AND COMMENTS	<table> <tr> <td>* STATE CODE</td> <td>[4][0]</td> </tr> <tr> <td>* SPS PROJECT CODE</td> <td>[0][5]</td> </tr> <tr> <td>* TEST SECTION NO.</td> <td>[0][5]</td> </tr> </table>	* STATE CODE	[4][0]	* SPS PROJECT CODE	[0][5]	* TEST SECTION NO.	[0][5]
* STATE CODE	[4][0]						
* SPS PROJECT CODE	[0][5]						
* TEST SECTION NO.	[0][5]						

Provide any miscellaneous comments and notes concerning construction operations which may have an influence on the ultimate performance of the test sections or which may cause undesired performance differences to occur between test sections. Also include any quality control measurements or data for which space is not provided on other forms. Provide an indication of the basis for such measurements, such as an ASTM, AASHTO, or Agency standard test designation.

Patching was used to seal 6 large depressed transverse cracks. This was done using an HMAC level-up and rolling w/ pneumatic roller.

ENCLOSURE MAY 18 1998 J B

PREPARER Smithy J. Monte EMPLOYER BRE DATE 11/19/97

Revised December 15, 1989

SHEET 1
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]

*STATE CODE [4 0]

*SHRP SECTION ID [0 5 0 5]

IMPROVEMENT LISTING

* 1. DATE COMPLETED (MO/DAY/YR)	* 2. WORK ¹ TYPE CODE (TABLE A.17)	* 3. WORK QUANTITY (UNITS FROM (TABLE A.17)	4. THICKNESS (INCHES)	5. COST ² (THOUSANDS OF DOLLARS PER LANE-MILE)
[0 7 / 0 8 / 9 7]	[1 9]	[_ 2 2 0 0 .]	_ 2 . 0	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .

NOTES:

1. For each specific work type, the appropriate set of sheets should be completed (as indexed in Table 7.1). It is recognized that parts of both Chapter 6 (Maintenance Data Collection) and Chapter 7 (Rehabilitation Data Collection) may be required to adequately record a given set of improvements for a test section.
2. Cost includes only pavement structure cost. Non-pavement costs such as cut and fill work, work on bridges, culverts, lighting, and guard rails are to be excluded.

G.W. ENTERED JUN 16 1998

Revised December 15, 1989

SHEET 2
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _]

*STATE CODE [4 0]

*SHRP SECTION ID [0 5 0 5]

REVISED LAYER DESCRIPTIONS

1.	*2.	*3.	*4.			
LAYER ¹ NUMBER	LAYER ² DESCRIP- TION	MATERIAL ^{3,4} TYPE CLASSIFICATION	<----- LAYER THICKNESS (IN) ----->			
			MEAN	MIN.	MAX.	STD. DEV.
1	SUBGRADE(7)	[5 6]				
2	[0 5]	[4 6]	[_ 8.0]	----	----	----
3	[0 4]	[0 1]	[_ 3.0]	----	----	----
4	[0 3]	[0 1]	[_ 1.5]	----	----	----
5	[0 2]	[7 3]	[_ .]	----	----	----
6	[0 1]	[0 1]	[_ 1.7]	0.8	2.2	0.3
7	[_]	[_]	[_ .]	----	----	----
8	[_]	[_]	[_ .]	----	----	----
9	[_]	[_]	[_ .]	----	----	----

NOTES:

- Layer 1 is subgrade soil, last layer is existing surface.
- Layer description codes:

Overlay.....01	Base Layer.....05	Porous Friction
Seal/Tack Coat.....02	Subbase Layer.....06	Course.....09
Original Surface...03	Subgrade.....07	Surface Treatment....10
HMAC Layer (Below	Interlayer.....08	Embankment (Fill)....11
Surface Layer)...04		Recycled Layer.....12
- The material type classification codes for surface, base or subbase, subgrade, and seal coat or interlayer materials appear in Tables A.5, A.6, A.7 and A.8, respectively.
- If the materials or thicknesses of a layer has not changed during the rehabilitation, enter "99" as the material type classification and leave the layer thicknesses for that layer blank. If a layer has changed, enter the appropriate codes and thicknesses.

G.W. ENTERED JUN 16 1998

RECEIVED NOV 20 1997

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 2 REVISED LAYER DESCRIPTIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [06]
--	---

1. LAYER NUMBER	2. LAYER DESCRIPTION	3. MATERIAL TYPE CLASS	4. LAYER THICKNESSES (Inches)			
			AVERAGE	MINIMUM	MAXIMUM	STD. DEV.
1	SUBGRADE(7)	[56]				
2	[05]	[46]	[8.0]	---	---	---
3	[04]	[01]	[3.0]	---	---	---
4	[03]	[01]	[0.0]	---	---	---
5	[02]	[73]	[]	---	---	---
6	[01]	[01]	[3.9]	2.9	4.9	0.5
7	[]	[]	[]	---	---	---
8	[]	[]	[]	---	---	---
9	[]	[]	[]	---	---	---
10	[]	[]	[]	---	---	---
11	[]	[]	[]	---	---	---
12	[]	[]	[]	---	---	---
13	[]	[]	[]	---	---	---
14	[]	[]	[]	---	---	---
15	[]	[]	[]	---	---	---

NOTES:

- Layer 1 is subgrade soil, the highest numbered layer is the pavement surface.
- Layer description codes:

Overlay.....01	Base Layer.....05	Porous Friction Course..09
Seal/Tack Coat.....02	Subbase Layer.....06	Surface Treatment.....10
Original Surface.....03	Subgrade.....07	Embankment (Fill).....11
HMAC Layer (Subsurface).04	Interlayer.....08	

If milling was performed, the layers which were milled shall be assigned their previous layer number and material type. If the layer was completely removed by milling, it shall still be shown as a layer with a zero thickness.
- Enter the material type classification codes from Tables A.5, A.6, A.7 and A.8 which best describes the material in each layer. If the layer was milled, enter the material classification code corresponding to the type material which was removed.
- Enter the average thickness of each layer and the maximum, minimum, and standard deviation of the thickness measurements, if known. If a layer was partially milled, the remaining thickness of the layer shall be indicated.

PREPARER

Swick & Smith

EMPLOYER

BRE

DATE

11/18/97

RECEIVED NOV 10 1998

SPS-5 CONSTRUCTION DATA SHEET 6 PREPARATION OF MILLED TEST SECTIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [06]
---	---

1. DATE OF MILLING OPERATION [06-26-97]
2. MANUFACTURER OF MILLING MACHINE (Specify) Destrol, Inc. (owner)
3. MILLING MACHINE MODEL DESIGNATION (Specify) D1100 SMI
4. WIDTH OF CUTTING HEAD (Inches) [144]
5. TOTAL MILLED DEPTH (Inches)

Location	No. Measurements	Maximum	Minimum	Std. Dev.	Average
Inside lane edge	11	2.5	0.6	0.5	1.6
Outside lane edge	11	2.5	0.6	0.5	1.6

MILLED SURFACE CHARACTERISTICS

6. Macro Texture
Fine Macro Texture ($\leq 1/8$ inch)... 1 Coarse Macro Texture ($> 1/8$ inch)... 2 [2]
7. Estimate of extent of test section surface area delaminated (Percent) [0]
8. Height of Ridge Between Parallel Passes? (Inches) []
9. Other Comments? (Yes, No) []
Comments _____
10. WHERE PATCHES PLACED AFTER MILLING? (Yes, No) [No]
(If yes complete Construction Data Sheet 3)
11. LENGTH OF TIME MILLED SURFACE WAS OPENED TO TRAFFIC? (Hrs.) 11 days [264]
12. WAS MILL REPLACEMENT LAYER THICKER THAN MILL DEPTH (YES, NO) [Yes]
13. LAYER NUMBER OF MILL REPLACEMENT [6]
14. NOMINAL THICKNESS OF MILL REPLACEMENT MATERIAL (Inches) [4.0]
15. TYPE OF MILL REPLACEMENT LAYER MATERIAL [1]
"Virgin" Asphalt Concrete 1 Recycled Asphalt Concrete.... 2
Other... 3 (Specify) _____
16. WAS ADJACENT TRAVEL LANE MILLED TO SAME DEPTH AS TEST LANE? (Yes, No) [Yes]
IF NO, WIDTH MILLED SAME DEPTH AS TEST LANE (Feet) []
17. COMMENTS _____

PREPARER

Sanjay G. Mehta

EMPLOYER

BAE

DATE

11/19/97

SPS-5 CONSTRUCTION DATA SHEET 7 OVERLAY PLACEMENT OPERATIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [06]
--	---

1. DATE SURFACE PREPARATION BEGAN (Month-Day-Year) [07-07-97]
2. DATE SURFACE PREPARATION COMPLETED [07-07-97]
3. SURFACE PREPARATION PRIOR TO PLACEMENT OF OVERLAY [3]
None..... 1 Broomed..... 2 Broomed + Asphaltic Tack Coat.... 3
Asphaltic Tack Coat (only).... 4
4. TACK COAT
Layer Numbers [05] []
Material Type None..... 1 SS-1.... 2 SS-1H.... 3 CRS-1.... 4 [02]
CRS-2.... 5 CMS-2.... 6 CMS-2H.. 7 CSS-1.... 8 CSS-1H... 9
Other.... 10 (Specify) _____
5. TACK COAT DILUTION
(Percent) [50]
Mixing Rate Parts Diluent 1 TO Parts Asphalt 1
6. TACK COAT APPLICATION RATE (Gal/Sq. Yd.) [0.03]
7. ASPHALT CONCRETE PLANT AND HAUL

Plant	Type	Name	Haul Distance (Mi)	Time (Min)	Layer Numbers
Plant 1	[2]	Aspha	[7]	[10]	[6] [] []
Plant 2	[]		[]	[]	[] [] []
Plant 3	[]		[]	[]	[] [] []

Plant Type: Batch..... 1 Drum Mix.... 2 Other... 3 Specify _____
8. MANUFACTURER OF ASPHALT CONCRETE PAVER Blaw Knox
9. MODEL DESIGNATION OF ASPHALT CONCRETE PAVER PF-510
10. SINGLE PASS LAYDOWN WIDTH (Feet) [22.0]
11. AC BINDER COURSE LIFT
Layer Number []
Nominal First Lift Placement Thickness (Inches) []
Nominal Second Lift Placement Thickness (Inches) []
12. AC SURFACE COURSE LIFT
Layer Number [06]
Nominal First Lift Placement Thickness (Inches) [4.0]
Nominal Second Lift Placement Thickness (Inches) []
13. SURFACE FRICTION COURSE
Layer Number []
Nominal Placement Thickness (Inches) []
14. TEST SECTION STATION OF TRANSVERSE JOINTS (within test section)
Binder Course [+ -]
Surface Course [+ -]
Surface Friction Course [+ -]
15. LOCATION OF LONGITUDINAL SURFACE JOINT [1] 4/12/98
Between lanes.. 1 Within lane.. 2 (specify offset from O/S feet) [72.0]
16. SIGNIFICANT EVENTS DURING CONSTRUCTION (disruptions, rain, equip. problems, etc.)

PREPARER

Smithy Mark

EMPLOYER

BRE

DATE

11/19/97

ENHANCED MAY 18 1998 J B

SPS-5 CONSTRUCTION DATA SHEET 8 OVERLAY COMPACTION DATA	* STATE CODE [40] * SPS PROJECT CODE [03] * TEST SECTION NO. [06]
---	---

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) [07-07-97]
 2. DATE PAVING OPERATIONS COMPLETED [07-08-97]
 3. LAYER NUMBER overlay [6]
 4. MIXING TEMPERATURE (*F) [328.]
 5. LAYDOWN TEMPERATURES (*F)
 Mean..... 315.
 Minimum.....
 Standard Deviation...
 Number of Tests
 Maximum.....

ROLLER DATA

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	12.0				
7	B	Steel-Whl Tandem					
8	C	Steel-Whl Tandem					
9	D	Steel-Whl Tandem					
10	E	Pneumatic-Tired	18.0	120.			
11	F	Pneumatic-Tired					
12	G	Pneumatic-Tired					
13	H	Pneumatic-Tired					
14	I	Single-Drum Vibr.					
15	J	Single-Drum Vibr.					
16	K	Single-Drum Vibr.					
17	L	Single-Drum Vibr.					
18	M	Double-Drum Vibr.	17.2		3200.	02	
19	N	Double-Drum Vibr.					
20	O	Double-Drum Vibr.					
21	P	Double-Drum Vibr.					
22	Q	Other					
	COMPACTION DATA		First Lift	Second Lift	Third Lift	Fourth Lift	
23	BREAKDOWN						
24	Roller Code (A-Q)		M				
24	Coverages		1.				
25	INTERMEDIATE						
26	Roller Code (A-Q)		E				
26	Coverages		3.				
27	FINAL						
28	Roller Code (A-Q)		A				
28	Coverages		2.				
29	Air Temperature (*F)		85.				
30	Compacted Thickness (In)		3.5				
31	Curing Period (Days)						

PREPARER

Justin J. Tinto

EMPLOYER

BRE

DATE

11/17/97

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) [0 7 - 0 7 - 97]

2. DATE PAVING OPERATIONS COMPLETED [0 7 - 0 8 - 97]

3. LAYER NUMBER overlay [7]

4. MIXING TEMPERATURE (°F) [3 2 8]

5. LAYDOWN TEMPERATURES (°F)

Mean.....	<u>3</u> <u>1</u> <u>5</u> .	Number of Tests	— — .
Minimum.....	— — .	Maximum.....	— — .
Standard Deviation...	— — .		

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	<u>1 2.0</u>				
7	B	Steel-Whl Tandem	— —.				
8	C	Steel-Whl Tandem	— —.				
9	D	Steel-Whl Tandem	— —.				
10	E	Pneumatic-Tired	<u>1 8.0</u>	<u>1 2 0.</u>			
11	F	Pneumatic-Tired	— —.	— —.			
12	G	Pneumatic-Tired	— —.	— —.			
13	H	Pneumatic-Tired	— —.	— —.			
14	I	Single-Drum Vibr.	— —.		— —.	— —.	— —.
15	J	Single-Drum Vibr.	— —.		— —.	— —.	— —.
16	K	Single-Drum Vibr.	— —.		— —.	— —.	— —.
17	L	Single-Drum Vibr.	— —.		— —.	— —.	— —.
18	M	Double-Drum Vibr.	<u>1 1.2</u>	— —.	<u>3 2 0 0.</u>	<u>0 2</u>	— —.
19	N	Double-Drum Vibr.	— —.	— —.	— —.	— —.	— —.
20	O	Double-Drum Vibr.	— —.	— —.	— —.	— —.	— —.
21	P	Double-Drum Vibr.	— —.	— —.	— —.	— —.	— —.
22	Q	Other					

PREPARED Smith & Partners EMPLOYER BRE DATE 11/19/97

SPS-5 CONSTRUCTION DATA
SHEET 10
LAYER THICKNESS MEASUREMENTS

* STATE CODE (40)
* SPS PROJECT CODE (05)
* TEST SECTION NO. (07)

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 1 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCITION LAYER
<u>0+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>3.1</u> <u>2.9</u> <u>2.9</u> <u>2.8</u> <u>2.6</u>	<u>3.1</u> <u>3.1</u> <u>2.9</u> <u>3.2</u> <u>3.7</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>0+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>2.5</u> <u>2.6</u> <u>2.8</u> <u>2.4</u> <u>2.6</u>	<u>3.6</u> <u>3.4</u> <u>3.1</u> <u>3.7</u> <u>3.7</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>1+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>2.5</u> <u>2.8</u> <u>3.2</u> <u>2.8</u> <u>2.4</u>	<u>3.8</u> <u>3.6</u> <u>3.4</u> <u>3.7</u> <u>3.8</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>1+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>3.0</u> <u>2.6</u> <u>2.8</u> <u>2.6</u> <u>2.5</u>	<u>3.6</u> <u>3.1</u> <u>3.1</u> <u>3.2</u> <u>3.7</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>2+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>3.5</u> <u>3.7</u> <u>2.9</u> <u>3.1</u> <u>3.0</u>	<u>3.8</u> <u>3.5</u> <u>3.8</u> <u>3.6</u> <u>4.0</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>2+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>3.6</u> <u>3.1</u> <u>3.1</u> <u>3.0</u> <u>2.8</u>	<u>3.8</u> <u>3.6</u> <u>3.4</u> <u>3.7</u> <u>4.2</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>3+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>3.4</u> <u>3.8</u> <u>3.0</u> <u>2.8</u> <u>2.6</u>	<u>3.6</u> <u>3.1</u> <u>3.2</u> <u>3.5</u> <u>3.8</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
LAYER NUMBER				<u>06</u>	<u>07</u>	

ENTERED MAY 13 1998 J R

PREPARED Santhya J. Martin

EMPLOYER BRE

DATE 10/31/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE <u>(40)</u> * SPS PROJECT CODE <u>(05)</u> * TEST SECTION NO. <u>(07)</u>
---	--

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 2 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCION LAYER
<u>3+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>2.6</u> <u>3.0</u> <u>3.0</u> <u>3.0</u> <u>2.6</u>	<u>3.1</u> <u>2.8</u> <u>2.8</u> <u>3.0</u> <u>3.6</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
<u>4+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>2.6</u> <u>2.8</u> <u>3.1</u> <u>3.0</u> <u>2.6</u>	<u>3.7</u> <u>3.4</u> <u>3.0</u> <u>3.4</u> <u>4.1</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
<u>4+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>2.4</u> <u>2.9</u> <u>3.1</u> <u>2.9</u> <u>2.3</u>	<u>3.5</u> <u>3.2</u> <u>3.2</u> <u>3.6</u> <u>4.0</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
<u>5+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>2.9</u> <u>3.5</u> <u>3.2</u> <u>2.8</u> <u>2.8</u>	<u>3.8</u> <u>3.4</u> <u>3.4</u> <u>4.1</u> <u>4.3</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
<u>+ —</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
<u>+ —</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
<u>+ —</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>	<u>—</u> <u>—</u> <u>—</u> <u>—</u> <u>—</u>
LAYER NUMBER	<u>—</u>	<u>—</u>	<u>—</u>	<u>06</u>	<u>07</u>	<u>—</u>

PREPARED

Timothy J. Martin

EMPLOYER

BREDATE 10/31/97

Revised December 15, 1989

SHEET 1
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]

*STATE CODE [4 0]

*SHRP SECTION ID [0 5 0 7]

IMPROVEMENT LISTING

* 1. DATE COMPLETED (MO/DAY/YR)	* 2. WORK ¹ TYPE CODE (TABLE A.17)	* 3. WORK QUANTITY (UNITS FROM (TABLE A.17)	4. THICKNESS (INCHES)	5. COST ² (THOUSANDS OF DOLLARS PER LANE-MILE)
[0 7 / 0 8 / 9 7]	[5 1]	[_ 2 2 0 0 .]	_ 6.5	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .

NOTES:

1. For each specific work type, the appropriate set of sheets should be completed (as indexed in Table 7.1). It is recognized that parts of both Chapter 6 (Maintenance Data Collection) and Chapter 7 (Rehabilitation Data Collection) may be required to adequately record a given set of improvements for a test section.
2. Cost includes only pavement structure cost. Non-pavement costs such as cut and fill work, work on bridges, culverts, lighting, and guard rails are to be excluded.

G.W. ENTERED JUN 17 1998

Revised December 15, 1989

G.W. ENTIN JUN 17 1998

SHEET 2
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]
*STATE CODE [4 0]
*SHRP SECTION ID [0 5 0 7]

REVISED LAYER DESCRIPTIONS

1.	*2.	*3.	*4.			
LAYER ¹ NUMBER	LAYER ² DESCRIP- TION	MATERIAL ^{3,4} TYPE CLASSIFICATION	LAYER THICKNESS (IN)			
			MEAN	MIN.	MAX.	STD. DEV.
1	SUBGRADE(7)	[5 6]				
2	[0 5]	[4 6]	[_ 8.0]	---	---	---
3	[0 4]	[0 1]	[_ 3.0]	---	---	---
4	[0 3]	[0 1]	[_ 0.0]	---	---	---
5	[0 2]	[7 3]	[_ _ _]	---	---	---
6	[0 4]	[0 1]	[_ 2.9]	2.4	3.8	0.3
7	[0 1]	[0 1]	[_ 3.5]	2.8	4.3	0.4
8	[_ _]	[_ _]	[_ _ _]	---	---	---
9	[_ _]	[_ _]	[_ _ _]	---	---	---

NOTES:

- Layer 1 is subgrade soil, last layer is existing surface.
- Layer description codes:

Overlay.....01	Base Layer.....05	Porous Friction
Seal/Tack Coat.....02	Subbase Layer.....06	Course.....09
Original Surface...03	Subgrade.....07	Surface Treatment....10
HMAC Layer (Below	Interlayer.....08	Embankment (Fill)....11
Surface Layer)...04		Recycled Layer.....12
- The material type classification codes for surface, base or subbase, subgrade, and seal coat or interlayer materials appear in Tables A.5, A.6, A.7 and A.8, respectively.
- If the materials or thicknesses of a layer has not changed during the rehabilitation, enter "99" as the material type classification and leave the layer thicknesses for that layer blank. If a layer has changed, enter the appropriate codes and thicknesses.

SPS-5 CONSTRUCTION DATA SHEET 2 REVISED LAYER DESCRIPTIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [08]
--	---

1. LAYER NUMBER	2. LAYER DESCRIPTION	3. MATERIAL TYPE CLASS	4. LAYER THICKNESSES (Inches)			
			AVERAGE	MINIMUM	MAXIMUM	STD. DEV.
1	SUBGRADE(7)	[56]				
2	[05]	[46]	[_ 8.0]	---	---	---
3	[04]	[01]	[_ 3.0]	---	---	---
4	[03]	[01]	[_ 0.0]	---	---	---
5	[02]	[73]	[_ _ _]	---	---	---
6	[04]	[13]	[_ 2.9]	--2.0	--3.5	--0.4
7	[01]	[13]	[_ 2.9]	--1.8	--3.5	--0.5
8	[_]	[_]	[_ _ _]	---	---	---
9	[_]	[_]	[_ _ _]	---	---	---
10	[_]	[_]	[_ _ _]	---	---	---
11	[_]	[_]	[_ _ _]	---	---	---
12	[_]	[_]	[_ _ _]	---	---	---
13	[_]	[_]	[_ _ _]	---	---	---
14	[_]	[_]	[_ _ _]	---	---	---
15	[_]	[_]	[_ _ _]	---	---	---

NOTES:

- Layer 1 is subgrade soil, the highest numbered layer is the pavement surface.
- Layer description codes:

Overlay.....01	Base Layer.....05	Porous Friction Course..09
Seal/Tack Coat.....02	Subbase Layer.....06	Surface Treatment.....10
Original Surface.....03	Subgrade.....07	Embankment (Fill).....11
HMAC Layer (Subsurface).04	Interlayer.....08	

If milling was performed, the layers which were milled shall be assigned their previous layer number and material type. If the layer was completely removed by milling, it shall still be shown as a layer with a zero thickness.
- Enter the material type classification codes from Tables A.5, A.6, A.7 and A.8 which best describes the material in each layer. If the layer was milled, enter the material classification code corresponding to the type material which was removed.
- Enter the average thickness of each layer and the maximum, minimum, and standard deviation of the thickness measurements, if known. If a layer was partially milled, the remaining thickness of the layer shall be indicated.

PREPARER

Smiley J. Martin

EMPLOYER

BRE

DATE 11/18/97

SPS-5 CONSTRUCTION DATA SHEET 6 PREPARATION OF MILLED TEST SECTIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [08]
---	---

1. DATE OF MILLING OPERATION [06-26-97]
2. MANUFACTURER OF MILLING MACHINE (Specify) Deere, Inc (owner)
3. MILLING MACHINE MODEL DESIGNATION (Specify) D1100 SME
4. WIDTH OF CUTTING HEAD (Inches) [144]
5. TOTAL MILLED DEPTH (Inches)

Location	No. Measrmnts	Maximum	Minimum	Std. Dev.	Average
Inside lane edge	11.	2.8	0.4	0.6	1.4
Outside lane edge	11.	2.8	0.4	0.6	1.4

MILLED SURFACE CHARACTERISTICS

6. Macro Texture
Fine Macro Texture ($\leq 1/8$ inch)... 1 Coarse Macro Texture ($> 1/8$ inch)... 2 [2]
7. Estimate of extent of test section surface area delaminated (Percent) [0]
8. Height of Ridge Between Parallel Passes? (Inches) []
9. Other Comments? (Yes, No) []
Comments _____
10. WHERE PATCHES PLACED AFTER MILLING? (Yes, No) [No]
(If yes complete Construction Data Sheet 3)
11. LENGTH OF TIME MILLED SURFACE WAS OPENED TO TRAFFIC? (Hrs.) 14 days [336]
12. WAS MILL REPLACEMENT LAYER THICKER THAN MILL DEPTH (YES, NO) [Yes]
13. LAYER NUMBER OF MILL REPLACEMENT [6]
14. NOMINAL THICKNESS OF MILL REPLACEMENT MATERIAL (Inches) [3.5]
15. TYPE OF MILL REPLACEMENT LAYER MATERIAL [2]
"Virgin" Asphalt Concrete 1 Recycled Asphalt Concrete.... 2
Other... 3 (Specify) _____
16. WAS ADJACENT TRAVEL LANE MILLED TO SAME DEPTH AS TEST LANE? (Yes, No) [Yes]
IF NO, WIDTH MILLED SAME DEPTH AS TEST LANE (Feet) []
17. COMMENTS _____

PREPARER

Shirley J. Hild

EMPLOYER

BRE

DATE

11/19/97

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 7 OVERLAY PLACEMENT OPERATIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [08]
--	---

1. DATE SURFACE PREPARATION BEGAN (Month-Day-Year) [07-10-97]
2. DATE SURFACE PREPARATION COMPLETED [07-10-97]
3. SURFACE PREPARATION PRIOR TO PLACEMENT OF OVERLAY [3]
None..... 1 Broomed..... 2 Broomed + Asphaltic Tack Coat.... 3
Asphaltic Tack Coat (only).... 4
4. TACK COAT
Layer Numbers [05] []
Material Type None..... 1 SS-1.... 2 SS-1H.... 3 CRS-1.... 4 [02]
CRS-2.... 5 CMS-2.... 6 CMS-2H.. 7 CSS-1.... 8 CSS-1H... 9
Other.... 10 (Specify) _____
5. TACK COAT DILUTION
(Percent) [50]
Mixing Rate Parts Diluent 1 TO Parts Asphalt 1
6. TACK COAT APPLICATION RATE (Gal/Sq. Yd.) [0.03]
7. ASPHALT CONCRETE PLANT AND HAUL
Type Name Haul Distance (Mi) Time (Min) Layer Numbers
Plant 1 [2] Aztec [7] [10] [6] [7] []
Plant 2 [] [] [] [] [] [] []
Plant 3 [] [] [] [] [] [] []
Plant Type: Batch..... 1 Drum Mix.... 2 Other... 3 Specify _____
8. MANUFACTURER OF ASPHALT CONCRETE PAVER Blaw - Knox
9. MODEL DESIGNATION OF ASPHALT CONCRETE PAVER PF-510
10. SINGLE PASS LAYDOWN WIDTH (Feet) [22.0]
11. AC BINDER COURSE LIFT
Layer Number [06]
Nominal First Lift Placement Thickness (Inches) [3.5]
Nominal Second Lift Placement Thickness (Inches) []
12. AC SURFACE COURSE LIFT
Layer Number [07]
Nominal First Lift Placement Thickness (Inches) [4.0]
Nominal Second Lift Placement Thickness (Inches) []
13. SURFACE FRICTION COURSE
Layer Number []
Nominal Placement Thickness (Inches) []
14. TEST SECTION STATION OF TRANSVERSE JOINTS (within test section)
Binder Course [] + []
Surface Course [] + []
Surface Friction Course [] + []
15. LOCATION OF LONGITUDINAL SURFACE JOINT [1]
Between lanes.. 1 Within lane.. 2 (specify offset from O/S feet) [2.0] 2m 9/2/98
16. SIGNIFICANT EVENTS DURING CONSTRUCTION (disruptions, rain, equip. problems, etc.)

PREPARER Joseph M. Pardo EMPLOYER BRE DATE 11/19/97

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 8 OVERLAY COMPACTION DATA	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [08]
---	---

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) [07-10-97]
 2. DATE PAVING OPERATIONS COMPLETED [07-11-97]
 3. LAYER NUMBER inlay [6]
 4. MIXING TEMPERATURE (°F) [315]
 5. LAYDOWN TEMPERATURES (°F)
 Mean..... 310
 Minimum.....
 Standard Deviation...
 Number of Tests
 Maximum.....

ROLLER DATA

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	12.0				
7	B	Steel-Whl Tandem					
8	C	Steel-Whl Tandem					
9	D	Steel-Whl Tandem					
10	E	Pneumatic-Tired	18.0	120			
11	F	Pneumatic-Tired					
12	G	Pneumatic-Tired					
13	H	Pneumatic-Tired					
14	I	Single-Drum Vibr.					
15	J	Single-Drum Vibr.					
16	K	Single-Drum Vibr.					
17	L	Single-Drum Vibr.					
18	M	Double-Drum Vibr.	11.2		3200	02	
19	N	Double-Drum Vibr.					
20	O	Double-Drum Vibr.					
21	P	Double-Drum Vibr.					
22	Q	Other					

	COMPACTION DATA	First Lift	Second Lift	Third Lift	Fourth Lift
23	BREAKDOWN Roller Code (A-Q)	M			
24	Coverages	1			
25	INTERMEDIATE Roller Code (A-Q)	E			
26	Coverages	3			
27	FINAL Roller Code (A-Q)	A			
28	Coverages	1			
29	Air Temperature (°F)	85			
30	Compacted Thickness (In)	3.0			
31	Curing Period (Days)	3.0			

PREPARER [Signature]

EMPLOYER BRE

DATE 11/19/97

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 8 OVERLAY COMPACTION DATA	* STATE CODE <u>40</u> * SPS PROJECT CODE <u>05</u> * TEST SECTION NO. <u>08</u>
---	--

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) 07-14-97
2. DATE PAVING OPERATIONS COMPLETED 07-16-97
3. LAYER NUMBER overlay [7]
4. MIXING TEMPERATURE (°F) [315.]
5. LAYDOWN TEMPERATURES (°F)
- | | | | |
|-----------------------|-------------|-----------------------|-----|
| Mean..... | <u>305.</u> | Number of Tests | --- |
| Minimum..... | --- | Maximum..... | --- |
| Standard Deviation... | --- | | |

ROLLER DATA

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	<u>12.0</u>				
7	B	Steel-Whl Tandem	---				
8	C	Steel-Whl Tandem	---				
9	D	Steel-Whl Tandem	---				
10	E	Pneumatic-Tired	<u>18.0</u>	<u>120.</u>			
11	F	Pneumatic-Tired	---	---			
12	G	Pneumatic-Tired	---	---			
13	H	Pneumatic-Tired	---	---			
14	I	Single-Drum Vibr.	---				
15	J	Single-Drum Vibr.	---				
16	K	Single-Drum Vibr.	---				
17	L	Single-Drum Vibr.	---				
18	M	Double-Drum Vibr.	<u>11.2</u>		<u>3200.</u>	<u>02</u>	
19	N	Double-Drum Vibr.	---				
20	O	Double-Drum Vibr.	---				
21	P	Double-Drum Vibr.	---				
22	Q	Other					

	COMPACTION DATA	First Lift	Second Lift	Third Lift	Fourth Lift
23	BREAKDOWN Roller Code (A-Q)	<u>M</u>	---	---	---
24	Coverages	<u>1.</u>	---	---	---
25	INTERMEDIATE Roller Code (A-Q)	<u>E</u>	---	---	---
26	Coverages	<u>3.</u>	---	---	---
27	FINAL Roller Code (A-Q)	<u>A</u>	---	---	---
28	Coverages	<u>1.</u>	---	---	---
29	Air Temperature (°F)	<u>85.</u>	---	---	---
30	Compacted Thickness (In)	<u>3.5</u>	---	---	---
31	Curing Period (Days)	---	---	---	---

PREPARER Timothy J. Martin EMPLOYER BRE DATE 11/19/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE <u>40</u> * SPS PROJECT CODE <u>05</u> * TEST SECTION NO. <u>08</u>
---	--

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 1 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRICTION LAYER
<u>0+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>3.0</u> <u>3.0</u> <u>3.0</u> <u>3.1</u> <u>3.2</u>	<u>1.9</u> <u>1.9</u> <u>1.9</u> <u>1.8</u> <u>1.9</u>	— — . — — — . — — — . — — — . — — — . —
<u>0+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>3.5</u> <u>2.9</u> <u>2.9</u> <u>3.4</u> <u>3.5</u>	<u>2.4</u> <u>2.3</u> <u>2.2</u> <u>2.0</u> <u>2.2</u>	— — . — — — . — — — . — — — . — — — . —
<u>1+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>2.6</u> <u>3.0</u> <u>2.3</u> <u>2.6</u> <u>2.8</u>	<u>2.7</u> <u>2.6</u> <u>2.6</u> <u>2.5</u> <u>2.4</u>	— — . — — — . — — — . — — — . — — — . —
<u>1+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>2.9</u> <u>3.4</u> <u>2.9</u> <u>3.1</u> <u>3.4</u>	<u>3.4</u> <u>2.9</u> <u>2.9</u> <u>2.8</u> <u>2.6</u>	— — . — — — . — — — . — — — . — — — . —
<u>2+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>2.8</u> <u>2.3</u> <u>2.6</u> <u>2.9</u> <u>3.1</u>	<u>3.0</u> <u>3.0</u> <u>3.0</u> <u>2.9</u> <u>3.0</u>	— — . — — — . — — — . — — — . — — — . —
<u>2+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>3.5</u> <u>3.0</u> <u>2.9</u> <u>3.1</u> <u>3.4</u>	<u>3.2</u> <u>3.2</u> <u>3.2</u> <u>3.1</u> <u>3.1</u>	— — . — — — . — — — . — — — . — — — . —
<u>3+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	— — . — — — . — — — . — — — . — — — . —	— — . — — — . — — — . — — — . — — — . —	<u>2.4</u> <u>2.2</u> <u>2.0</u> <u>2.5</u> <u>2.9</u>	<u>3.4</u> <u>3.2</u> <u>3.2</u> <u>2.9</u> <u>2.9</u>	— — . — — — . — — — . — — — . — — — . —
LAYER NUMBER		— —	— —	<u>06</u>	<u>07</u>	— —

PREPARER Ginny J. MartinEMPLOYER BREDATE 10/31/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE <u>[40]</u> * SPS PROJECT CODE <u>[05]</u> * TEST SECTION NO. <u>[08]</u>
---	--

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 2 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCION LAYER
<u>3+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>			<u>2.0</u> <u>2.5</u> <u>2.2</u> <u>2.6</u> <u>2.9</u>	<u>3.4</u> <u>3.2</u> <u>3.4</u> <u>3.2</u> <u>3.4</u>	
<u>4+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>			<u>2.0</u> <u>2.4</u> <u>2.4</u> <u>2.6</u> <u>3.0</u>	<u>3.1</u> <u>3.2</u> <u>3.1</u> <u>3.1</u> <u>3.1</u>	
<u>4+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>			<u>2.5</u> <u>3.1</u> <u>3.0</u> <u>3.0</u> <u>3.4</u>	<u>3.4</u> <u>3.0</u> <u>2.9</u> <u>3.0</u> <u>2.9</u>	
<u>5+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>			<u>3.0</u> <u>3.5</u> <u>2.8</u> <u>3.1</u> <u>3.1</u>	<u>3.5</u> <u>3.0</u> <u>3.2</u> <u>3.2</u> <u>3.5</u>	
<u>+ --</u>						
<u>+ --</u>						
<u>+ --</u>						
LAYER NUMBER				<u>06</u>	<u>07</u>	

PREPARER

Timothy J. Mark

EMPLOYER

BREDATE 10/31/97

Revised December 15, 1989

SHEET 1
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]

*STATE CODE [4 0]

*SHRP SECTION ID [0 5 0 8]

IMPROVEMENT LISTING

* 1. DATE COMPLETED (MO/DAY/YR)	* 2. WORK ¹ TYPE CODE (TABLE A.17)	* 3. WORK QUANTITY (UNITS FROM (TABLE A.17))	4. THICKNESS (INCHES)	5. COST ² (THOUSANDS OF DOLLARS PER LANE-MILE)
[0 7 / 1 6 / 9 8]	[5 5]	[_ 2 2 0 0 .]	_ 6.5	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ .	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ .	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ .	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ .	_ _ _ .
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_ _ .	_ _ _ .

NOTES:

1. For each specific work type, the appropriate set of sheets should be completed (as indexed in Table 7.1). It is recognized that parts of both Chapter 6 (Maintenance Data Collection) and Chapter 7 (Rehabilitation Data Collection) may be required to adequately record a given set of improvements for a test section.
2. Cost includes only pavement structure cost. Non-pavement costs such as cut and fill work, work on bridges, culverts, lighting, and guard rails are to be excluded.

SHR. ENTERED JUN 17 1998

Revised December 15, 1989

SHEET 2
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]
*STATE CODE [4 0]
*SHRP SECTION ID [0 5 0 8]

REVISED LAYER DESCRIPTIONS

1.	*2.	*3.	*4.			
LAYER ¹ NUMBER	LAYER ² DESCRIP- TION	MATERIAL ^{3,4} TYPE CLASSIFICATION	LAYER THICKNESS (IN)			
			<----- MEAN	MIN.	MAX.	STD. DEV.
1	SUBGRADE(7)	[5 6]				
2	[0 5]	[4 6]	[_ 8.0]	---	---	---
3	[0 4]	[0 1]	[_ 3.0]	---	---	---
4	[0 3]	[0 1]	[_ 0.0]	---	---	---
5	[0 2]	[7 3]	[_ .]	---	---	---
6	[0 4]	[1 3]	[_ 2.9]	2.0	3.5	0.4
7	[0 1]	[1 3]	[_ 2.9]	1.8	3.5	0.5
8	[_ _]	[_ _]	[_ .]	---	---	---
9	[_ _]	[_ _]	[_ .]	---	---	---

NOTES:

- Layer 1 is subgrade soil, last layer is existing surface.
- Layer description codes:

Overlay.....01	Base Layer.....05	Porous Friction
Seal/Tack Coat....02	Subbase Layer.....06	Course.....09
Original Surface...03	Subgrade.....07	Surface Treatment....10
HMAC Layer (Below	Interlayer.....08	Embankment (Fill)....11
Surface Layer)...04		Recycled Layer.....12
- The material type classification codes for surface, base or subbase, subgrade, and seal coat or interlayer materials appear in Tables A.5, A.6, A.7 and A.8, respectively.
- If the materials or thicknesses of a layer has not changed during the rehabilitation, enter "99" as the material type classification and leave the layer thicknesses for that layer blank. If a layer has changed, enter the appropriate codes and thicknesses.

G.W. ENTERED JUN 17 1990

SPS-5 CONSTRUCTION DATA SHEET 2 REVISED LAYER DESCRIPTIONS	* STATE CODE (40) * SPS PROJECT CODE (05) * TEST SECTION NO. (09)
--	---

1. LAYER NUMBER	2. LAYER DESCRIPTION	3. MATERIAL TYPE CLASS	4. LAYER THICKNESSES (Inches)			
			AVERAGE	MINIMUM	MAXIMUM	STD. DEV.
1	SUBGRADE(7)	(56)				
2	(05)	(46)	(8.0)			
3	(04)	(01)	(3.0)			
4	(03)	(01)	(0.0)			
5	(02)	(73)				
6	(01)	(13)	(3.)	2.2	3.8	0.4
7	()	()				
8	()	()				
9	()	()				
10	()	()				
11	()	()				
12	()	()				
13	()	()				
14	()	()				
15	()	()				

NOTES:

- Layer 1 is subgrade soil, the highest numbered layer is the pavement surface.
- Layer description codes:

Overlay.....01	Base Layer.....05	Porous Friction Course..09
Seal/Tack Coat.....02	Subbase Layer.....06	Surface Treatment.....10
Original Surface.....03	Subgrade.....07	Embankment (Fill).....11
HMAC Layer (Subsurface).04	Interlayer.....08	

If milling was performed, the layers which were milled shall be assigned their previous layer number and material type. If the layer was completely removed by milling, it shall still be shown as a layer with a zero thickness.
- Enter the material type classification codes from Tables A.5, A.6, A.7 and A.8 which best describes the material in each layer. If the layer was milled, enter the material classification code corresponding to the type material which was removed.
- Enter the average thickness of each layer and the maximum, minimum, and standard deviation of the thickness measurements, if known. If a layer was partially milled, the remaining thickness of the layer shall be indicated.

PREPARER

[Signature]

EMPLOYER

BRE

DATE

11/18/97

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 6 PREPARATION OF MILLED TEST SECTIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [09]
---	---

1. DATE OF MILLING OPERATION 106-26-97
2. MANUFACTURER OF MILLING MACHINE (Specify) Destrol, Inc. (owner)
3. MILLING MACHINE MODEL DESIGNATION (Specify) D1100 SMS
4. WIDTH OF CUTTING HEAD (Inches) 144
5. TOTAL MILLED DEPTH (Inches)

Location	No. Measurements	Maximum	Minimum	Std. Dev.	Average
Inside lane edge	<u>11</u>	<u>2.8</u>	<u>0.6</u>	<u>0.5</u>	<u>1.7</u>
Outside lane edge	<u>11</u>	<u>2.8</u>	<u>0.6</u>	<u>0.5</u>	<u>1.7</u>

MILLED SURFACE CHARACTERISTICS

6. Macro Texture 2
 Fine Macro Texture ($\leq \frac{1}{8}$ inch)... 1 Coarse Macro Texture ($> \frac{1}{8}$ inch)... 2
7. Estimate of extent of test section surface area delaminated (Percent) 0
8. Height of Ridge Between Parallel Passes? (Inches) —
9. Other Comments? (Yes, No) —
 Comments _____
10. WHERE PATCHES PLACED AFTER MILLING? (Yes, No) No
 (If yes complete Construction Data Sheet 3)
11. LENGTH OF TIME MILLED SURFACE WAS OPENED TO TRAFFIC? (Hrs.) 18 days 432
12. WAS MILL REPLACEMENT LAYER THICKER THAN MILL DEPTH (Yes, No) Yes
13. LAYER NUMBER OF MILL REPLACEMENT 6
14. NOMINAL THICKNESS OF MILL REPLACEMENT MATERIAL (Inches) 4.0
15. TYPE OF MILL REPLACEMENT LAYER MATERIAL 2
 "Virgin" Asphalt Concrete 1 Recycled Asphalt Concrete.... 2
 Other... 3 (Specify) _____
16. WAS ADJACENT TRAVEL LANE MILLED TO SAME DEPTH AS TEST LANE? (Yes, No) Yes
 IF NO, WIDTH MILLED SAME DEPTH AS TEST LANE (Feet) —
17. COMMENTS _____

PREPARER Kimberly J. Porter EMPLOYER BRE DATE 11/19/97

SPS-5 CONSTRUCTION DATA SHEET 7 OVERLAY PLACEMENT OPERATIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [09]
--	---

1. DATE SURFACE PREPARATION BEGAN (Month-Day-Year) [07-14-97]
 2. DATE SURFACE PREPARATION COMPLETED [07-14-97]
 3. SURFACE PREPARATION PRIOR TO PLACEMENT OF OVERLAY overlay [3]
 None..... 1 Broomed..... 2 Broomed + Asphaltic Tack Coat.... 3
 Asphaltic Tack Coat (only).... 4
 4. TACK COAT
 Layer Numbers [05] []
 Material Type None..... 1 SS-1.... 2 SS-1H.... 3 CRS-1.... 4 [02]
 CRS-2.... 5 CMS-2.... 6 CMS-2H.. 7 CSS-1.... 8 CSS-1H... 9
 Other.... 10 (Specify) _____
 5. TACK COAT DILUTION [50]
 (Percent) _____
 Mixing Rate _____ Parts Diluent 1 TO Parts Asphalt 1
 6. TACK COAT APPLICATION RATE (Gal/Sq. Yd.) [0.03]
 7. ASPHALT CONCRETE PLANT AND HAUL

Plant	Type	Name	Haul Distance (Mi)	Time (Min)	Layer Numbers
Plant 1	[Z]	Aztec	[7]	[10]	[6] [] []
Plant 2	[]		[]	[]	[] [] []
Plant 3	[]		[]	[]	[] [] []

 Plant Type: Batch..... 1 Drum Mix.... 2 Other... 3 Specify _____
 8. MANUFACTURER OF ASPHALT CONCRETE PAVER Blankex
 9. MODEL DESIGNATION OF ASPHALT CONCRETE PAVER PF-510
 10. SINGLE PASS LAYDOWN WIDTH (Feet) [22.0]
 11. AC BINDER COURSE LIFT
 Layer Number []
 Nominal First Lift Placement Thickness (Inches) []
 Nominal Second Lift Placement Thickness (Inches) []
 12. AC SURFACE COURSE LIFT
 Layer Number [06]
 Nominal First Lift Placement Thickness (Inches) [4.0]
 Nominal Second Lift Placement Thickness (Inches) []
 13. SURFACE FRICTION COURSE
 Layer Number []
 Nominal Placement Thickness (Inches) []
 14. TEST SECTION STATION OF TRANSVERSE JOINTS (within test section)
 Binder Course [+ -]
 Surface Course [+ -]
 Surface Friction Course [+ -]
 15. LOCATION OF LONGITUDINAL SURFACE JOINT [1]
 Between lanes.. 1 Within lane.. 2 (specify offset from O/S feet) [2.0] 21/11/98
 16. SIGNIFICANT EVENTS DURING CONSTRUCTION (disruptions, rain, equip. problems, etc.)

PREPARER

Smith, Mark

EMPLOYER

BRE

DATE

11/19/97

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 8 OVERLAY COMPACTION DATA	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [09]
---	---

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) [07-14-97]
2. DATE PAVING OPERATIONS COMPLETED [07-16-97]
3. LAYER NUMBER overlay [6]
4. MIXING TEMPERATURE (°F) [131.5]
5. LAYDOWN TEMPERATURES (°F)

Mean.....	[305]	Number of Tests	---
Minimum.....	---	Maximum.....	---
Standard Deviation...	---		

ROLLER DATA

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	12.0				
7	B	Steel-Whl Tandem	---				
8	C	Steel-Whl Tandem	---				
9	D	Steel-Whl Tandem	---				
10	E	Pneumatic-Tired	18.0	120			
11	F	Pneumatic-Tired	---	---			
12	G	Pneumatic-Tired	---	---			
13	H	Pneumatic-Tired	---	---			
14	I	Single-Drum Vibr.	---				
15	J	Single-Drum Vibr.	---				
16	K	Single-Drum Vibr.	---				
17	L	Single-Drum Vibr.	---				
18	M	Double-Drum Vibr.	11.2		3200	02	
19	N	Double-Drum Vibr.	---				
20	O	Double-Drum Vibr.	---				
21	P	Double-Drum Vibr.	---				
22	Q	Other					

	COMPACTION DATA	First Lift	Second Lift	Third Lift	Fourth Lift
23	BREAKDOWN Roller Code (A-Q)	M	---	---	---
24	Coverages	1	---	---	---
25	INTERMEDIATE Roller Code (A-Q)	E	---	---	---
26	Coverages	3	---	---	---
27	FINAL Roller Code (A-Q)	A	---	---	---
28	Coverages	2	---	---	---
29	Air Temperature (°F)	85	---	---	---
30	Compacted Thickness (In)	3.5	---	---	---
31	Curing Period (Days)	---	---	---	---

PREPARED Emily J. Costa EMPLOYER BRE DATE 11/19/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE <u>(4 0)</u> * SPS PROJECT CODE <u>(0 5)</u> * TEST SECTION NO. <u>(0 9)</u>
---	---

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 1 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCITION LAYER
<u>0+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — — . —	— — — . —	— — — . —	<u>2 9</u> <u>2 6</u> <u>2 6</u> <u>2 9</u> <u>3 2</u>	— — — . —
<u>0+5 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — — . —	— — — . —	— — — . —	<u>2 5</u> <u>2 5</u> <u>2 5</u> <u>2 7</u> <u>3 0</u>	— — — . —
<u>1+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — — . —	— — — . —	— — — . —	<u>2 2</u> <u>2 3</u> <u>2 3</u> <u>2 6</u> <u>3 0</u>	— — — . —
<u>1+5 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — — . —	— — — . —	— — — . —	<u>3 0</u> <u>3 1</u> <u>3 1</u> <u>3 1</u> <u>3 6</u>	— — — . —
<u>2+0 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — — . —	— — — . —	— — — . —	<u>3 1</u> <u>3 2</u> <u>3 1</u> <u>3 2</u> <u>3 6</u>	— — — . —
<u>2+5 0</u>	<u>0</u> <u>3 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — — . —	— — — . —	— — — . —	<u>3 2</u> <u>3 4</u> <u>3 2</u> <u>3 5</u> <u>3 7</u>	— — — . —
<u>3+0 0</u>	<u>0</u> <u>5 6</u> <u>7 2</u> <u>1 0 8</u> <u>1 4 4</u>	— — — . —	— — — . —	— — — . —	<u>3 0</u> <u>2 9</u> <u>2 7</u> <u>3 1</u> <u>3 5</u>	— — — . —
LAYER NUMBER		— — —	— — —	— — —	<u>0 6</u>	— — —

PREPARER

Jimmy J. Potts

EMPLOYER

BRE

DATE

10/31/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE <u>[40]</u> * SPS PROJECT CODE <u>[05]</u> * TEST SECTION NO. <u>[09]</u>
---	--

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 2 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCION LAYER
<u>3+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>2.9</u> <u>3.0</u> <u>2.9</u> <u>3.1</u> <u>3.4</u>	
<u>4+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>3.1</u> <u>3.2</u> <u>3.1</u> <u>3.5</u> <u>3.8</u>	
<u>4+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>3.1</u> <u>3.4</u> <u>3.2</u> <u>3.5</u> <u>3.7</u>	
<u>5+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>				<u>3.0</u> <u>3.0</u> <u>2.9</u> <u>3.2</u> <u>3.5</u>	
<u>+ - -</u>						
<u>+ - -</u>						
<u>+ - -</u>						
LAYER NUMBER					<u>6</u>	

PREPARER *Timothy J. Martin*EMPLOYER BREDATE 10/31/97

Revised December 15, 1989

SHEET 1
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _]

*STATE CODE [4 0]

*SHRP SECTION ID [0 5 0 9]

IMPROVEMENT LISTING

* 1. DATE COMPLETED (MO/DAY/YR)	* 2. WORK ¹ TYPE CODE (TABLE A.17)	* 3. WORK QUANTITY (UNITS FROM (TABLE A.17))	4. THICKNESS (INCHES)	5. COST ² (THOUSANDS OF DOLLARS PER LANE-MILE)
[0 7 / 1 6 / 9 7]	[5 5]	[_ 2 2 0 0 .]	_ 3 . 5	_____
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_____	_____
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_____	_____
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_____	_____
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_____	_____
[_ _ / _ _ / _ _]	[_ _]	[_ _ _ _ _ .]	_____	_____

NOTES:

1. For each specific work type, the appropriate set of sheets should be completed (as indexed in Table 7.1). It is recognized that parts of both Chapter 6 (Maintenance Data Collection) and Chapter 7 (Rehabilitation Data Collection) may be required to adequately record a given set of improvements for a test section.
2. Cost includes only pavement structure cost. Non-pavement costs such as cut and fill work, work on bridges, culverts, lighting, and guard rails are to be excluded.

G.W. ENTERED JUN 17 1998

Revised December 15, 1989

SHEET 2
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _]

*STATE CODE [4 0]

*SHRP SECTION ID [0 5 0 9]

REVISED LAYER DESCRIPTIONS

1.	*2.	*3.	*4.			
LAYER ¹ NUMBER	LAYER ² DESCRIP- TION	MATERIAL ^{3,4} TYPE CLASSIFICATION	LAYER THICKNESS (IN)			
			<----- MEAN	MIN.	MAX.	STD. DEV.
1	SUBGRADE(7)	[5 6]				
2	[0 5]	[4 6]	[_ 8.0]	---	---	---
3	[0 4]	[0 1]	[_ 3.0]	---	---	---
4	[0 3]	[0 1]	[_ 0.0]	---	---	---
5	[0 2]	[7 3]	[_ .]	---	---	---
6	[0 1]	[1 3]	[_ 3.1]	2.2	3.8	0.4
7	[_]	[_]	[_ .]	---	---	---
8	[_]	[_]	[_ .]	---	---	---
9	[_]	[_]	[_ .]	---	---	---

NOTES:

- Layer 1 is subgrade soil, last layer is existing surface.
- Layer description codes:

Overlay.....01	Base Layer.....05	Porous Friction
Seal/Tack Coat.....02	Subbase Layer.....06	Course.....09
Original Surface...03	Subgrade.....07	Surface Treatment....10
HMAC Layer (Below	Interlayer.....08	Embankment (Fill)....11
Surface Layer)...04		Recycled Layer.....12
- The material type classification codes for surface, base or subbase, subgrade, and seal coat or interlayer materials appear in Tables A.5, A.6, A.7 and A.8, respectively.
- If the materials or thicknesses of a layer has not changed during the rehabilitation, enter "99" as the material type classification and leave the layer thicknesses for that layer blank. If a layer has changed, enter the appropriate codes and thicknesses.

G.W. ENTERED JUN 17 1998

RECEIVED NOV 20 1997

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 2 REVISED LAYER DESCRIPTIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [60]
--	---

1. LAYER NUMBER	2. LAYER DESCRIPTION	3. MATERIAL TYPE CLASS	4. LAYER THICKNESSES (Inches)			
			AVERAGE	MINIMUM	MAXIMUM	STD. DEV.
1	SUBGRADE(7)	[56]				
2	[05]	[46]	[8.0]	----	----	----
3	[04]	[01]	[3.0]	----	----	----
4	[03]	[01]	[0.5]	----	----	----
5	[02]	[73]	[.]	----	----	----
6	[01]	[01]	[4.0]	2.8	5.3	0.6
7	[]	[]	[.]	----	----	----
8	[]	[]	[.]	----	----	----
9	[]	[]	[.]	----	----	----
10	[]	[]	[.]	----	----	----
11	[]	[]	[.]	----	----	----
12	[]	[]	[.]	----	----	----
13	[]	[]	[.]	----	----	----
14	[]	[]	[.]	----	----	----
15	[]	[]	[.]	----	----	----

NOTES:

- Layer 1 is subgrade soil, the highest numbered layer is the pavement surface.
- Layer description codes:

Overlay.....01	Base Layer.....05	Porous Friction Course..09
Seal/Tack Coat.....02	Subbase Layer.....06	Surface Treatment.....10
Original Surface.....03	Subgrade.....07	Embankment (Fill).....11
HMAC Layer (Subsurface).04	Interlayer.....08	

If milling was performed, the layers which were milled shall be assigned their previous layer number and material type. If the layer was completely removed by milling, it shall still be shown as a layer with a zero thickness.
- Enter the material type classification codes from Tables A.5, A.6, A.7 and A.8 which best describes the material in each layer. If the layer was milled, enter the material classification code corresponding to the type material which was removed.
- Enter the average thickness of each layer and the maximum, minimum, and standard deviation of the thickness measurements, if known. If a layer was partially milled, the remaining thickness of the layer shall be indicated.

PREPARER Smith, J. M. EMPLOYER BRE DATE 11/18/97

October 1990 (Heading revised October 1992)

SPS-5 CONSTRUCTION DATA SHEET 7 OVERLAY PLACEMENT OPERATIONS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [60]
--	---

1. DATE SURFACE PREPARATION BEGAN (Month-Day-Year) [07-07-97]
2. DATE SURFACE PREPARATION COMPLETED [07-07-97]
3. SURFACE PREPARATION PRIOR TO PLACEMENT OF OVERLAY [3]
None..... 1 Broomed..... 2 Broomed + Asphaltic Tack Coat.... 3
Asphaltic Tack Coat (only).... 4
4. TACK COAT
Layer Numbers [05] [02]
Material Type None..... 1 SS-1.... 2 SS-1H.... 3 CRS-1.... 4
CRS-2.... 5 CMS-2.... 6 CMS-2H.. 7 CSS-1.... 8 CSS-1H... 9
Other.... 10 (Specify) _____
5. TACK COAT DILUTION
(Percent) [50]
Mixing Rate Parts Diluent 1 TO Parts Asphalt 1
6. TACK COAT APPLICATION RATE (Gal/Sq. Yd.) [0.03]
7. ASPHALT CONCRETE PLANT AND HAUL
Type Name Haul Distance (Mi) Time (Min) Layer Numbers
Plant 1 [2] Aztec [7] [10] [6] [] []
Plant 2 [] [] [] [] [] []
Plant 3 [] [] [] [] [] []
Plant Type: Batch..... 1 Drum Mix.... 2 Other... 3 Specify _____
8. MANUFACTURER OF ASPHALT CONCRETE PAVER Blaw-knox
9. MODEL DESIGNATION OF ASPHALT CONCRETE PAVER PF-510
10. SINGLE PASS LAYDOWN WIDTH (Feet) [22.0]
11. AC BINDER COURSE LIFT
Layer Number [] []
Nominal First Lift Placement Thickness (Inches) [] []
Nominal Second Lift Placement Thickness (Inches) [] []
12. AC SURFACE COURSE LIFT
Layer Number [06]
Nominal First Lift Placement Thickness (Inches) [4.0]
Nominal Second Lift Placement Thickness (Inches) [] []
13. SURFACE FRICTION COURSE
Layer Number [] []
Nominal Placement Thickness (Inches) [] []
14. TEST SECTION STATION OF TRANSVERSE JOINTS (within test section)
Binder Course [] + []
Surface Course [] + []
Surface Friction Course [] + []
15. LOCATION OF LONGITUDINAL SURFACE JOINT
Between lanes.. 1 Within lane.. 2 (specify offset from O/S feet) [2.0] ^{4M} 7/2/98
16. SIGNIFICANT EVENTS DURING CONSTRUCTION (disruptions, rain, equip. problems, etc.)

PREPARER

Jonathan J. Martin

EMPLOYER

BRE

DATE 11/19/97

SPS-5 CONSTRUCTION DATA SHEET 8 OVERLAY COMPACTION DATA	* STATE CODE <u>(40)</u> * SPS PROJECT CODE <u>(05)</u> * TEST SECTION NO. <u>(60)</u>
---	--

1. DATE PAVING OPERATIONS BEGAN (Month-Day-Year) (07-07-97)
2. DATE PAVING OPERATIONS COMPLETED (07-08-97)
3. LAYER NUMBER (6)
4. MIXING TEMPERATURE (°F) (328)
5. LAYDOWN TEMPERATURES (°F)
- | | | | |
|-----------------------|------------|-----------------------|-----|
| Mean..... | <u>315</u> | Number of Tests | --- |
| Minimum..... | --- | Maximum..... | --- |
| Standard Deviation... | --- | | |

ROLLER DATA

	Roller Code #	Roller Description	Gross Wt (Tons)	Tire Press. (psi)	Frequency (Vibr./Min)	Amplitude (Inches)	Speed (mph)
6	A	Steel-Whl Tandem	<u>12.0</u>				
7	B	Steel-Whl Tandem	---				
8	C	Steel-Whl Tandem	---				
9	D	Steel-Whl Tandem	---				
10	E	Pneumatic-Tired	<u>18.0</u>	<u>120</u>			
11	F	Pneumatic-Tired	---	---			
12	G	Pneumatic-Tired	---	---			
13	H	Pneumatic-Tired	---	---			
14	I	Single-Drum Vibr.	---				
15	J	Single-Drum Vibr.	---				
16	K	Single-Drum Vibr.	---				
17	L	Single-Drum Vibr.	---				
18	M	Double-Drum Vibr.	<u>11.2</u>		<u>3200</u>	<u>02</u>	
19	N	Double-Drum Vibr.	---				
20	O	Double-Drum Vibr.	---				
21	P	Double-Drum Vibr.	---				
22	Q	Other					
COMPACTION DATA			First Lift	Second Lift	Third Lift	Fourth Lift	
BREAKDOWN							
23	Roller Code (A-Q)		<u>M</u>	---	---	---	---
24	Coverages		<u>1</u>	---	---	---	---
INTERMEDIATE							
25	Roller Code (A-Q)		<u>E</u>	---	---	---	---
26	Coverages		<u>3</u>	---	---	---	---
FINAL							
27	Roller Code (A-Q)		<u>A</u>	---	---	---	---
28	Coverages		<u>2</u>	---	---	---	---
29	Air Temperature (°F)		<u>85</u>	---	---	---	---
30	Compacted Thickness (In)		<u>3.3</u>	---	---	---	---
31	Curing Period (Days)		---	---	---	---	---

PREPARER Sanjay P. Patel EMPLOYER BRE DATE 11/14/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE <u>[40]</u> * SPS PROJECT CODE <u>[05]</u> * TEST SECTION NO. <u>[60]</u>
---	--

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 1 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCITION LAYER
<u>0+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>2.8</u> <u>2.9</u> <u>3.1</u> <u>3.2</u> <u>3.7</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>0+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>4.0</u> <u>3.8</u> <u>4.0</u> <u>4.0</u> <u>4.2</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>1+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>3.5</u> <u>3.4</u> <u>3.8</u> <u>3.9</u> <u>4.2</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>1+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>2+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>2+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>3+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>4.1</u> <u>3.8</u> <u>4.0</u> <u>4.3</u> <u>4.8</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
LAYER NUMBER					<u>06</u>	

PREPARED

Donally J. Hester

EMPLOYER

BRE

DATE

10/31/97

SPS-5 CONSTRUCTION DATA SHEET 10 LAYER THICKNESS MEASUREMENTS	* STATE CODE [40] * SPS PROJECT CODE [05] * TEST SECTION NO. [60]
---	---

LAYER THICKNESS MEASUREMENTS (Inches)

SHEET 2 OF 2

STATION NUMBER	OFFSET (Inches)	RUT LEVEL-UP	MILL REPLACEMENT	BINDER COURSE	SURFACE COURSE	SURFACE FRCION LAYER
<u>3+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>4.2</u> <u>4.4</u> <u>4.2</u> <u>4.4</u> <u>4.8</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>4+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>3.5</u> <u>3.7</u> <u>3.7</u> <u>4.1</u> <u>4.5</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>4+50</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>3.7</u> <u>3.7</u> <u>3.6</u> <u>4.1</u> <u>4.7</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>5+00</u>	<u>0</u> <u>36</u> <u>72</u> <u>108</u> <u>144</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>4.4</u> <u>4.4</u> <u>4.9</u> <u>4.9</u> <u>5.3</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>+</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>+</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
<u>+</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>	<u>---</u> <u>---</u> <u>---</u> <u>---</u> <u>---</u>
LAYER NUMBER	<u>---</u>	<u>---</u>	<u>---</u>	<u>---</u>	<u>06</u>	<u>---</u>

PREPARED

Joseph M. M...

EMPLOYER

BRE

DATE

10/31/97

ENTERED MAY 18 1998 J B

Revised December 15, 1989

SHEET 1
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]
*STATE CODE [4 0]
*SHRP SECTION ID [0 5 6 0]

IMPROVEMENT LISTING

* 1. DATE COMPLETED (MO/DAY/YR)	* 2. WORK ¹ TYPE CODE (TABLE A.17)	* 3. WORK QUANTITY (UNITS FROM (TABLE A.17))	4. THICKNESS (INCHES)	5. COST ² (THOUSANDS OF DOLLARS PER LANE-MILE)
[0 7 / 0 8 / 9 7]	[1 9]	[_ 2 2 0 0 .]	_ 3.5	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .
[_ / _ / _]	[_]	[_ _ _ _ .]	_ _ .	_ _ _ .

NOTES:

1. For each specific work type, the appropriate set of sheets should be completed (as indexed in Table 7.1). It is recognized that parts of both Chapter 6 (Maintenance Data Collection) and Chapter 7 (Rehabilitation Data Collection) may be required to adequately record a given set of improvements for a test section.
2. Cost includes only pavement structure cost. Non-pavement costs such as cut and fill work, work on bridges, culverts, lighting, and guard rails are to be excluded.

G.W. ENTERED JUN 17 1998

Revised December 15, 1989

SHEET 2
REHABILITATION DATA
LTPP PROGRAM

*STATE ASSIGNED ID [_ _ _ _]
*STATE CODE [4 0]
*SHRP SECTION ID [0 5 6 0]

REVISED LAYER DESCRIPTIONS

1.	*2.	*3.	*4.			
LAYER ¹ NUMBER	LAYER ² DESCRIP- TION	MATERIAL ^{3,4} TYPE CLASSIFICATION	LAYER THICKNESS (IN)			
			<----- MEAN	MIN.	MAX.	STD. DEV.
1	SUBGRADE(7)	[5 6]				
2	[0 5]	[4 6]	[_ 8.0]	---	---	---
3	[0 4]	[0 1]	[_ 3.0]	---	---	---
4	[0 3]	[0 1]	[_ 0.5]	---	---	---
5	[0 2]	[7 3]	[_ .]	---	---	---
6	[0 1]	[0 1]	[_ 4.0]	2.8	5.3	0.6
7	[_]	[_]	[_ .]	---	---	---
8	[_]	[_]	[_ .]	---	---	---
9	[_]	[_]	[_ .]	---	---	---

NOTES:

- Layer 1 is subgrade soil, last layer is existing surface.
- Layer description codes:





Overlay.....01	Base Layer.....05	Porous Friction
Seal/Tack Coat.....02	Subbase Layer.....06	Course.....09
Original Surface...03	Subgrade.....07	Surface Treatment....10
HMAC Layer (Below	Interlayer.....08	Embankment (Fill)....11
Surface Layer)...04		Recycled Layer.....12
- The material type classification codes for surface, base or subbase, subgrade, and seal coat or interlayer materials appear in Tables A.5, A.6, A.7 and A.8, respectively.
- If the materials or thicknesses of a layer has not changed during the rehabilitation, enter "99" as the material type classification and leave the layer thicknesses for that layer blank. If a layer has changed, enter the appropriate codes and thicknesses.

G.W. ENTERED JUN 17 1998





APPENDIX F

TRANSVERSE PROFILE DATA




Oklahoma SPS-5 (400501)

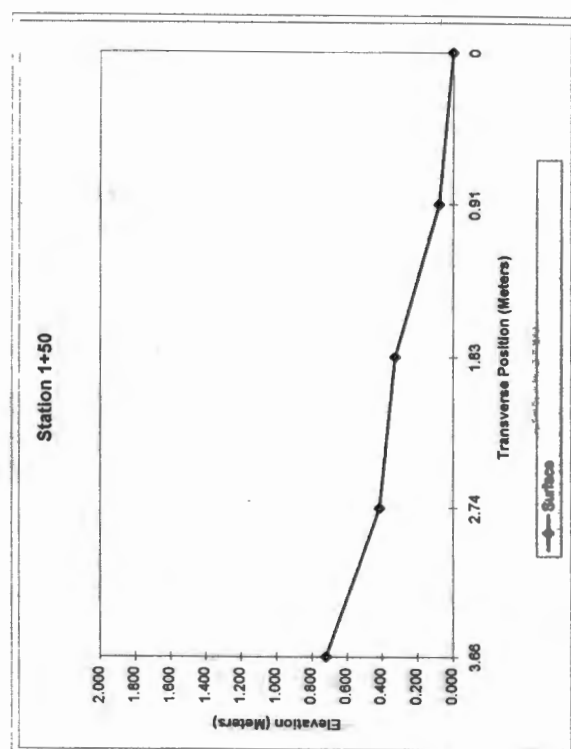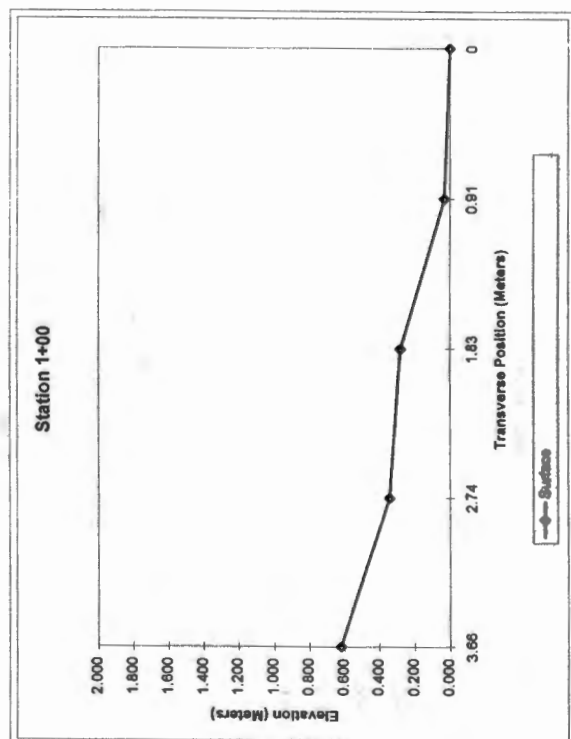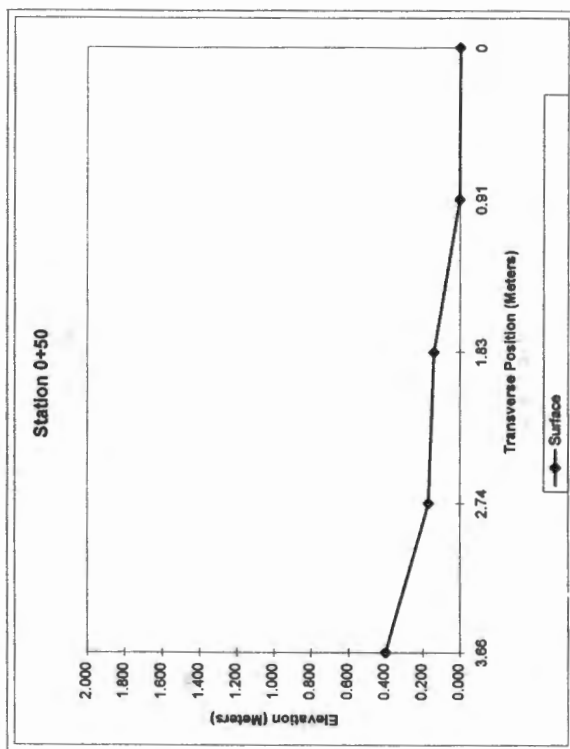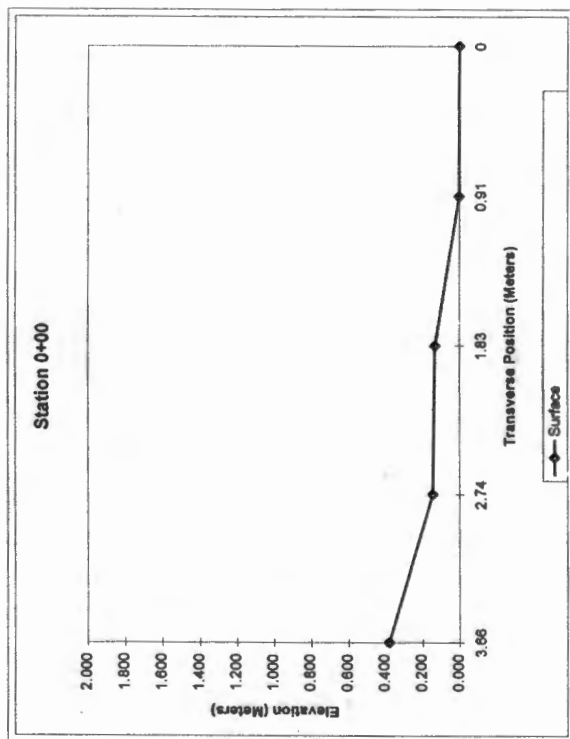

Oklahoma SPS-5 (400501)

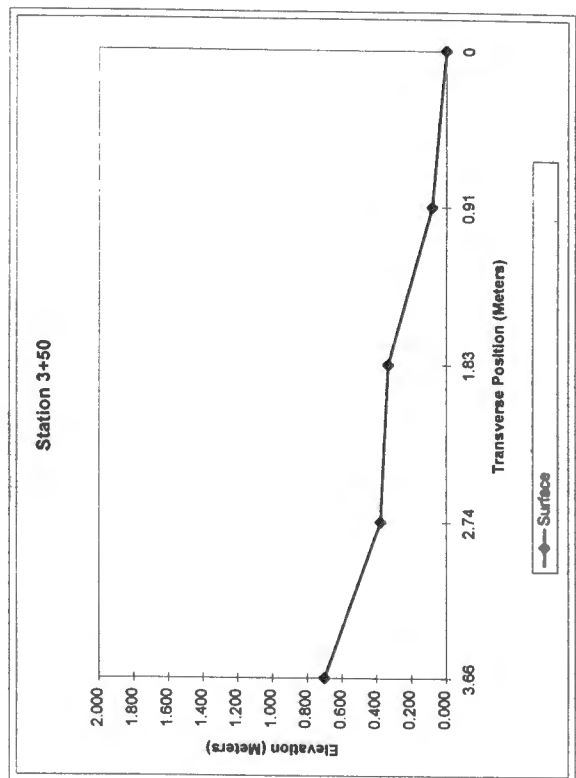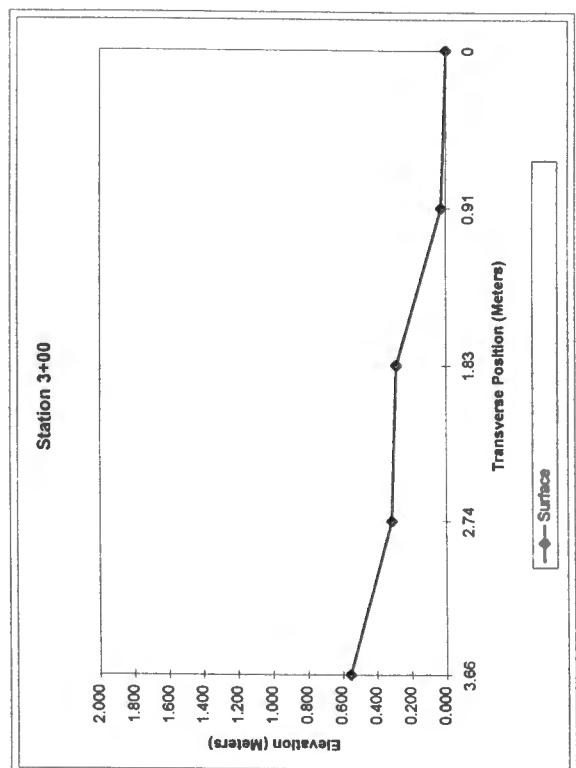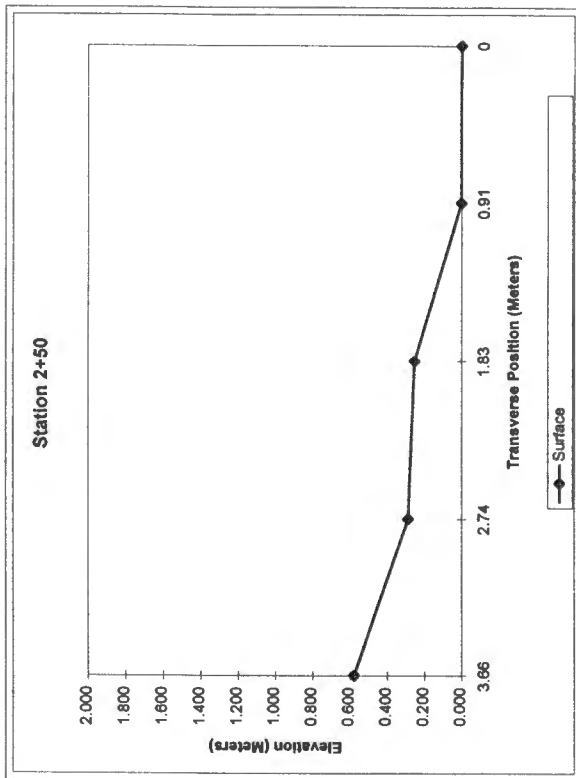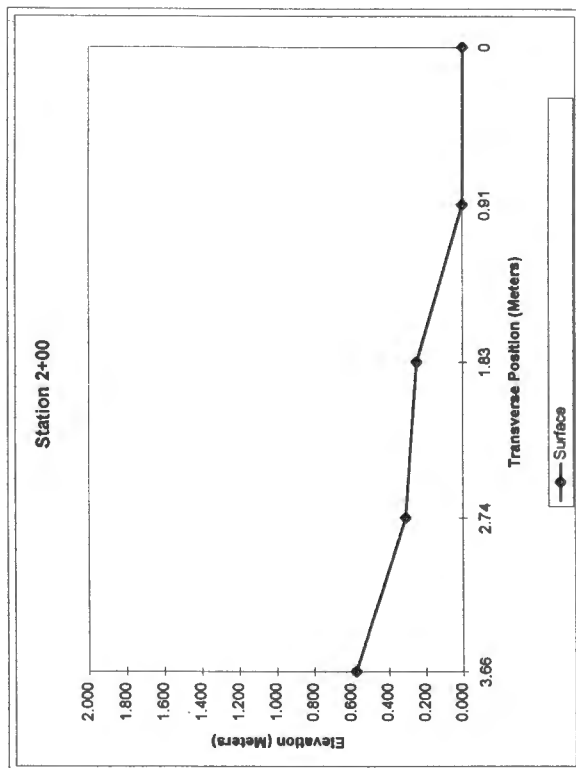

Oklahoma SPS-5 (400501)

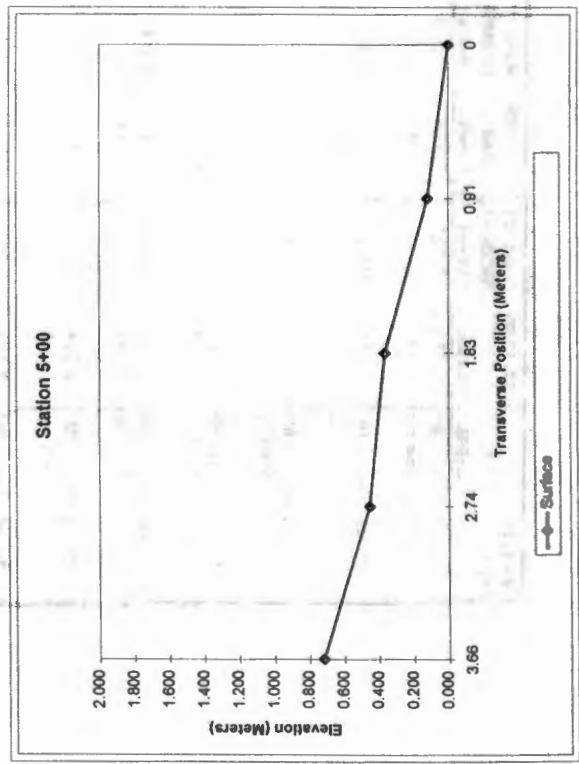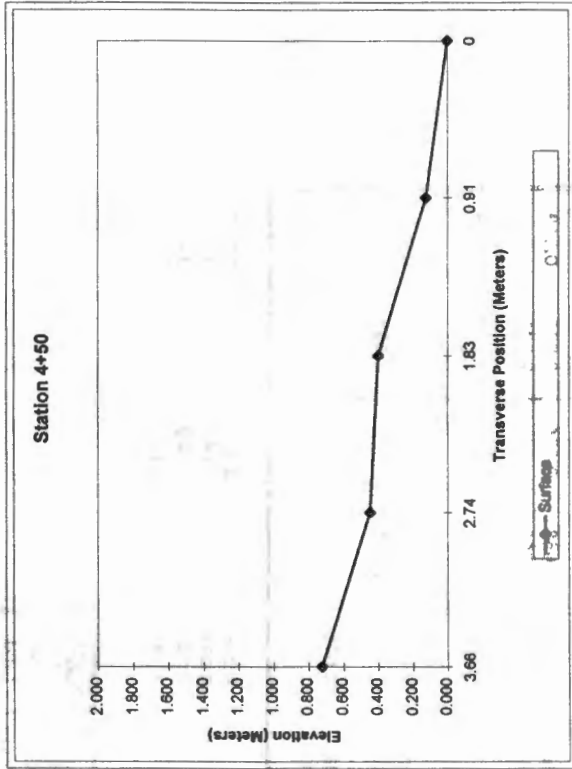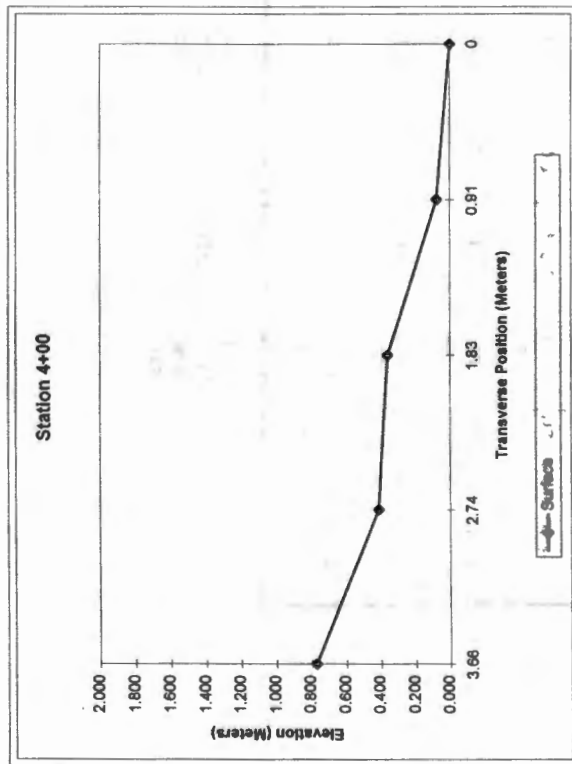





Oklahoma SPS-5 (400502)

Transverse Offset	2 LAYERS	ELEVATION 0		ELEVATION 0.91		ELEVATION 1.83		ELEVATION 2.74		ELEVATION 3.66	
		Meters	Recyc. BH THICKNESS	Meters	Recyc. BH THICKNESS	Meters	Recyc. BH THICKNESS	Meters	Recyc. BH THICKNESS	Meters	Recyc. BH THICKNESS
0+00	Recyc. BH Existing	1.366 1.338	0.027	1.384 1.341	0.043	1.396 1.353	0.043	1.408 1.359	0.049	1.420 1.378	0.043
0+50	Recyc. BH Existing	1.561 1.536	0.024	1.576 1.539	0.037	1.591 1.558	0.034	1.603 1.564	0.040	1.615 1.588	0.027
1+00	Recyc. BH Existing	1.743 1.707	0.037	1.759 1.713	0.046	1.774 1.734	0.040	1.786 1.740	0.046	1.801 1.762	0.040
1+50	Recyc. BH Existing	1.920 1.878	0.043	1.935 1.893	0.043	1.954 1.908	0.046	1.966 1.917	0.049	1.978 1.942	0.037
2+00	Recyc. BH Existing	2.124 2.085	0.040	2.137 2.094	0.043	2.152 2.112	0.040	2.164 2.118	0.046	2.179 2.140	0.040
2+50	Recyc. BH Existing	2.304 2.265	0.040	2.320 2.274	0.046	2.335 2.289	0.046	2.350 2.301	0.049	2.368 2.323	0.046
3+00	Recyc. BH Existing	2.460 2.408	0.052	2.472 2.417	0.055	2.487 2.432	0.055	2.496 2.438	0.058	2.512 2.448	0.064
3+50	Recyc. BH Existing	2.618 2.563	0.055	2.630 2.579	0.052	2.646 2.594	0.052	2.658 2.603	0.055	2.670 2.621	0.049
4+00	Recyc. BH Existing	2.780 2.740	0.040	2.798 2.749	0.049	2.813 2.761	0.052	2.822 2.771	0.052	2.835 2.786	0.049
4+50	Recyc. BH Existing	2.963 2.914	0.049	2.981 2.926	0.055	2.993 2.938	0.055	3.005 2.944	0.061	3.018 2.969	0.049
5+00	Recyc. BH Existing	3.161 3.121	0.040	3.176 3.127	0.049	3.188 3.133	0.055	3.197 3.139	0.058	3.210 3.155	0.055





AVG	0.040	0.047	0.048	0.052	0.046
MAX	0.055	0.055	0.055	0.061	0.064
MIN	0.024	0.037	0.034	0.040	0.027
STD	0.009	0.005	0.007	0.006	0.010

Recyc. BH	
SECTION AVG	0.046
SECTION MAX	0.064
SECTION MIN	0.024
SECTION STD	0.008




Oklahoma SPS-5 (400502)

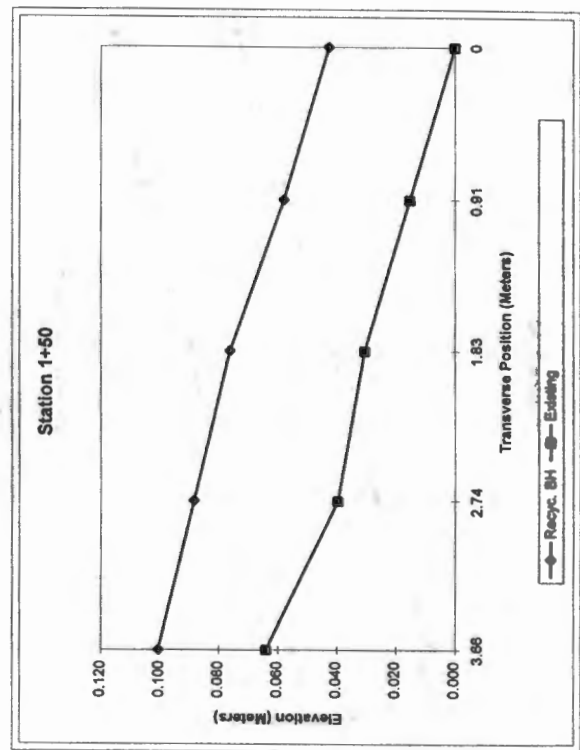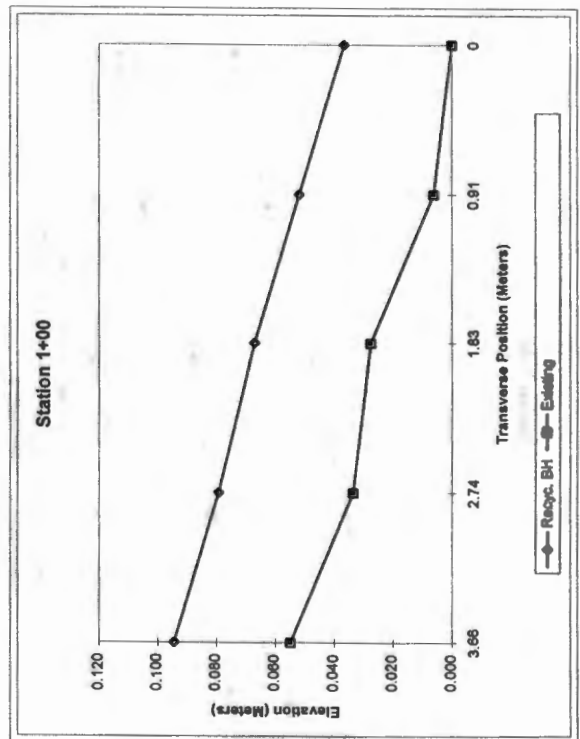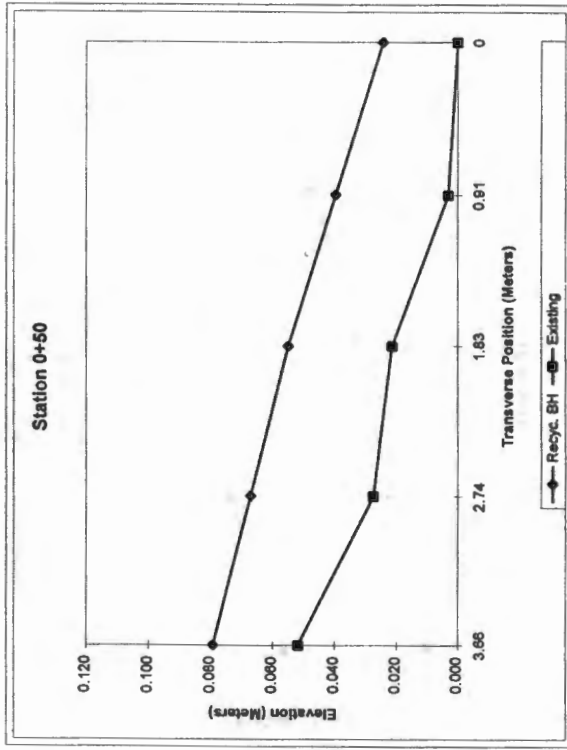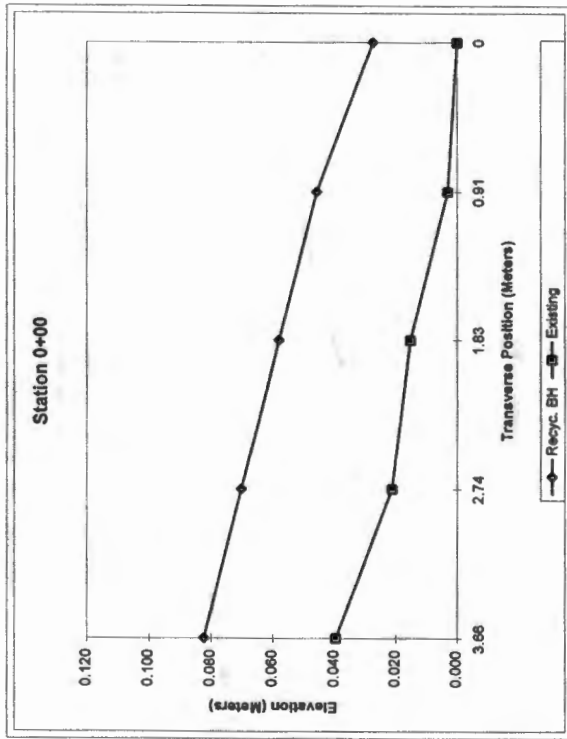

Oklahoma SPS-5 (400502)

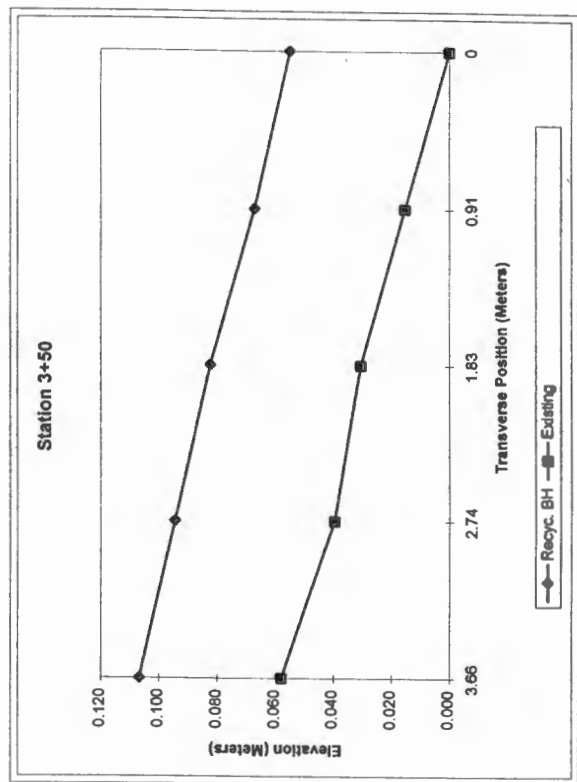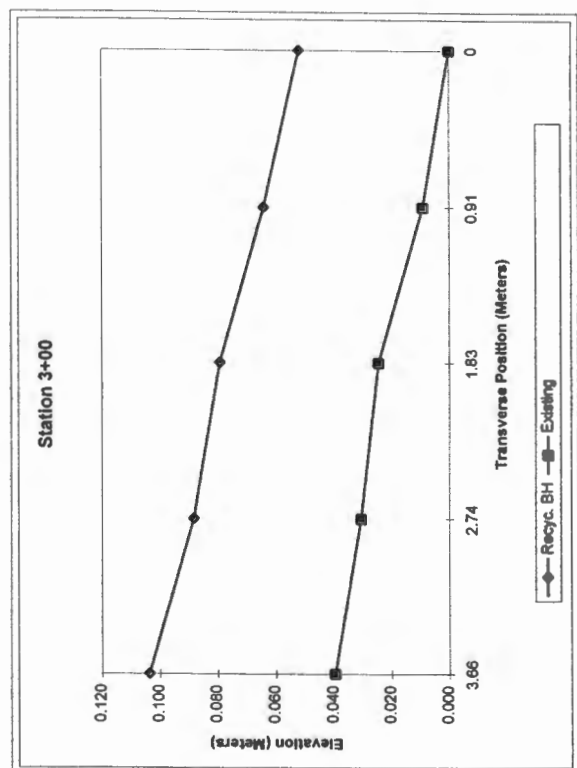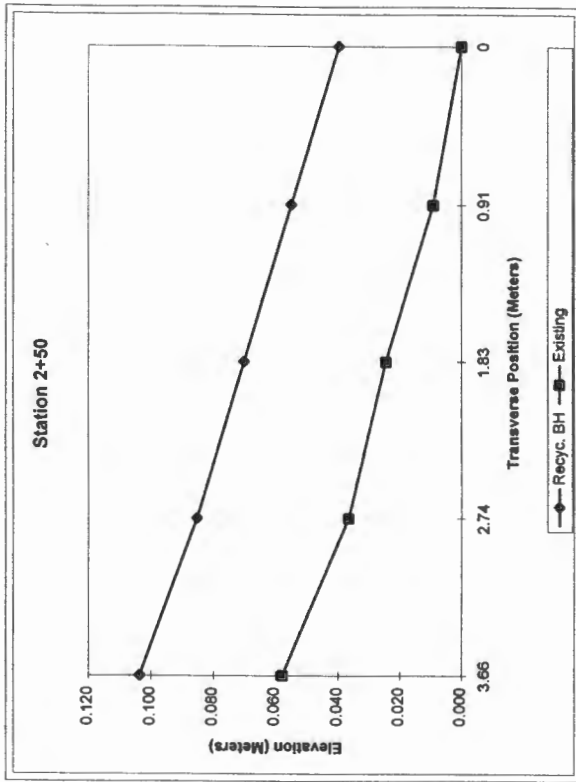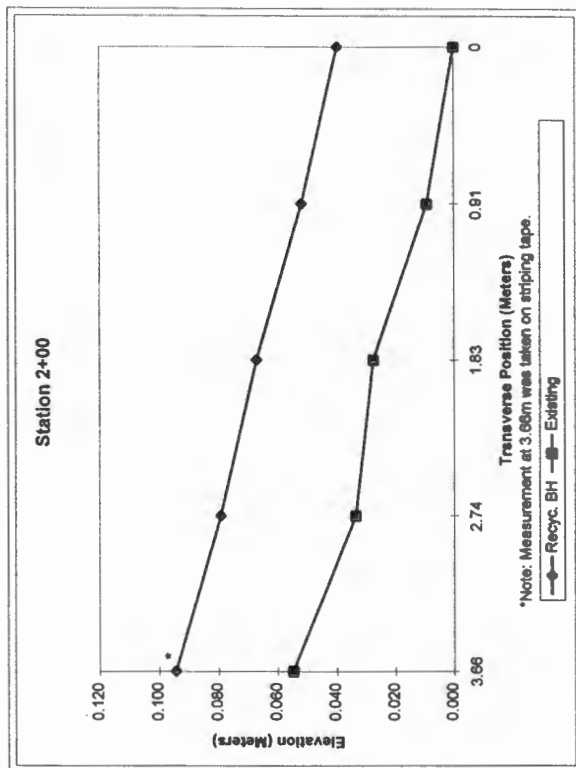

Oklahoma SPS-5 (400502)

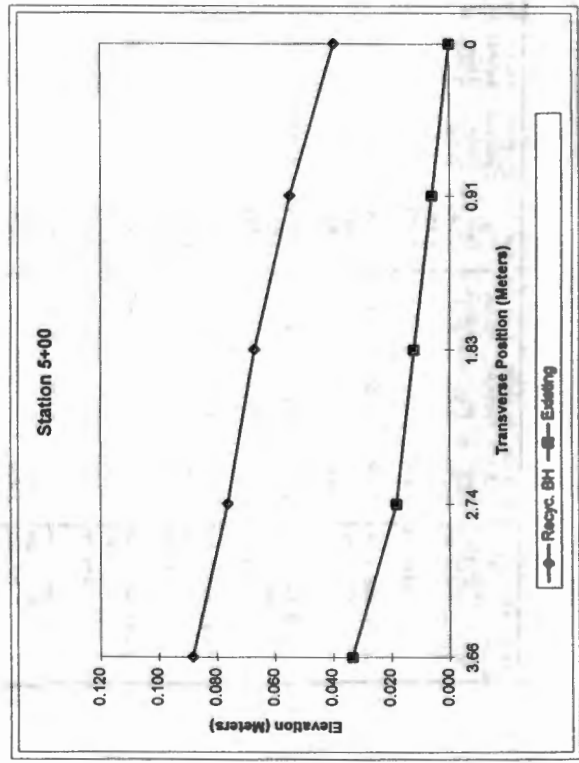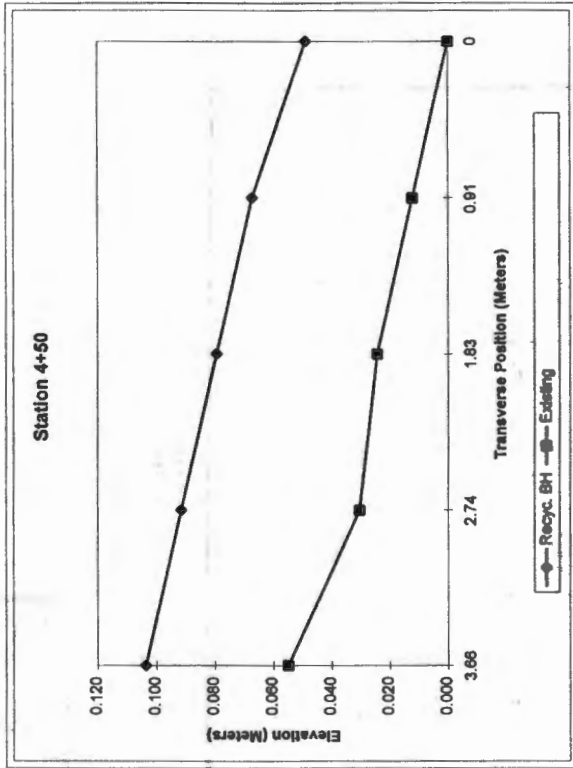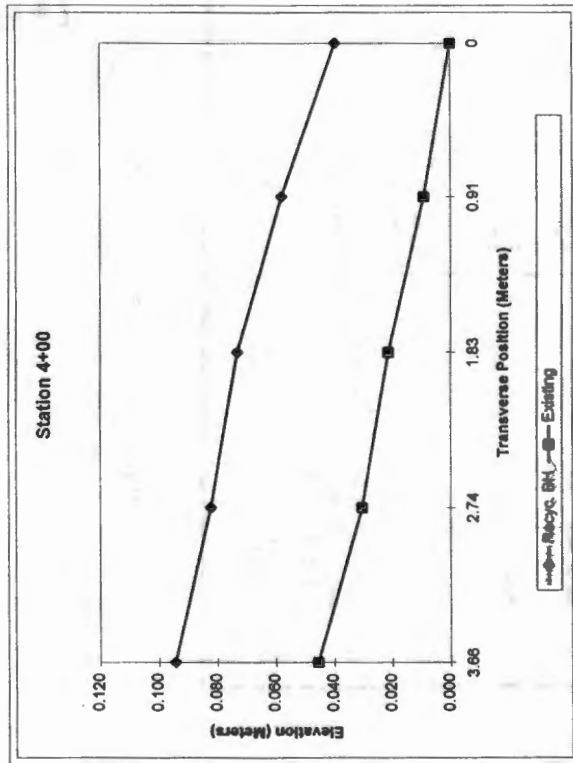





Oklahoma SPS-5 (400503)

Transverse Offset	3 LAYERS	ELEVATION 0 Meters	Recyc. BH THICKNESS Meters	Recyc. AH THICKNESS Meters	ELEVATION 0.91 Meters	Recyc. BH THICKNESS Meters	Recyc. AH THICKNESS Meters	ELEVATION 1.83 Meters	Recyc. BH THICKNESS Meters	Recyc. AH THICKNESS Meters	ELEVATION 2.74 Meters	Recyc. BH THICKNESS Meters	Recyc. AH THICKNESS Meters	ELEVATION 3.66 Meters	Recyc. BH THICKNESS Meters	Recyc. AH THICKNESS Meters
0+00	Recyc. BH Existing	1.765	0.024	0.061	1.780	0.030	0.073	1.795	0.034	0.076	1.811	0.030	0.094	1.823	0.024	0.091
	Recyc. AH Existing	1.740			1.750			1.762			1.780			1.798		
	Existing	1.679			1.676			1.686			1.686			1.707		
0+50	Recyc. BH Existing	1.908	0.030	0.081	1.920	0.034	0.067	1.939	0.037	0.067	1.954	0.034	0.079	1.969	0.030	0.076
	Recyc. AH Existing	1.878			1.887			1.902			1.920			1.939		
	Existing	1.817			1.820			1.835			1.841			1.862		
1+00	Recyc. BH Existing	2.045	0.034	0.070	2.063	0.043	0.073	2.082	0.046	0.079	2.097	0.043	0.094	2.109	0.037	0.079
	Recyc. AH Existing	2.012			2.021			2.036			2.054			2.073		
	Existing	1.942			1.948			1.957			1.960			1.993		
1+50	Recyc. BH Existing	2.188	0.030	0.076	2.207	0.040	0.070	2.225	0.043	0.070	2.240	0.043	0.082	2.259	0.055	0.070
	Recyc. AH Existing	2.158			2.167			2.182			2.198			2.204		
	Existing	2.082			2.097			2.112			2.115			2.134		
2+00	Recyc. BH Existing	2.362	0.049	0.043	2.377	0.049	0.058	2.396	0.052	0.061	2.411	0.052	0.070	2.426	0.049	0.070
	Recyc. AH Existing	2.313			2.329			2.344			2.359			2.377		
	Existing	2.271			2.271			2.283			2.289			2.307		
2+50	Recyc. BH Existing	2.521	0.040	0.052	2.539	0.049	0.055	2.557	0.055	0.055	2.573	0.052	0.067	2.588	0.046	0.070
	Recyc. AH Existing	2.481			2.490			2.502			2.521			2.542		
	Existing	2.429			2.435			2.448			2.454			2.472		
3+00	Recyc. BH Existing	2.637	0.055	0.052	2.652	0.055	0.061	2.670	0.058	0.061	2.682	0.049	0.076	2.701	0.049	0.073
	Recyc. AH Existing	2.582			2.597			2.612			2.633			2.652		
	Existing	2.530			2.536			2.551			2.557			2.579		
3+50	Recyc. BH Existing	2.719	0.058	0.058	2.737	0.058	0.067	2.758	0.064	0.067	2.774	0.058	0.082	2.786	0.049	0.082
	Recyc. AH Existing	2.681			2.679			2.694			2.716			2.737		
	Existing	2.603			2.612			2.627			2.633			2.655		
4+00	Recyc. BH Existing	2.835	0.055	0.043	2.850	0.061	0.049	2.871	0.067	0.052	2.883	0.061	0.067	2.899	0.055	0.067
	Recyc. AH Existing	2.780			2.789			2.804			2.822			2.844		
	Existing	2.737			2.740			2.752			2.755			2.777		
4+50	Recyc. BH Existing	2.966	0.052	0.027	2.981	0.055	0.037	2.999	0.061	0.043	3.014	0.055	0.061	3.033	0.058	0.061
	Recyc. AH Existing	2.914			2.926			2.938			2.960			2.975		
	Existing	2.866			2.890			2.896			2.899			2.914		
5+00	Recyc. BH Existing	3.100	0.055	0.030	3.112	0.058	0.037	3.130	0.064	0.043	3.146	0.061	0.061	3.161	0.061	0.061
	Recyc. AH Existing	3.045			3.054			3.066			3.085			3.100		
	Existing	3.014			3.018			3.024			3.024			3.039		





AVG	0.044	0.053	0.048	0.059	0.053	0.061	0.077	0.046	0.073
MAX	0.058	0.076	0.061	0.073	0.067	0.079	0.094	0.061	0.091
MIN	0.024	0.027	0.030	0.037	0.034	0.043	0.061	0.030	0.024
STD	0.012	0.015	0.010	0.013	0.012	0.012	0.012	0.010	0.009

SECTION AVG	Recyc. BH	Recyc. AH
0.048	0.048	0.064
SECTION MAX	0.067	0.094
SECTION MIN	0.024	0.027
SECTION STD	0.011	0.015




Oklahoma SPS-5 (400503)

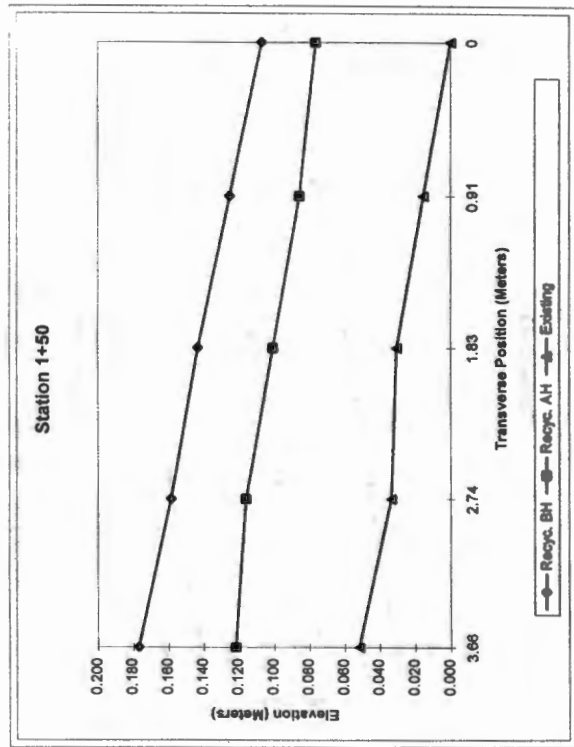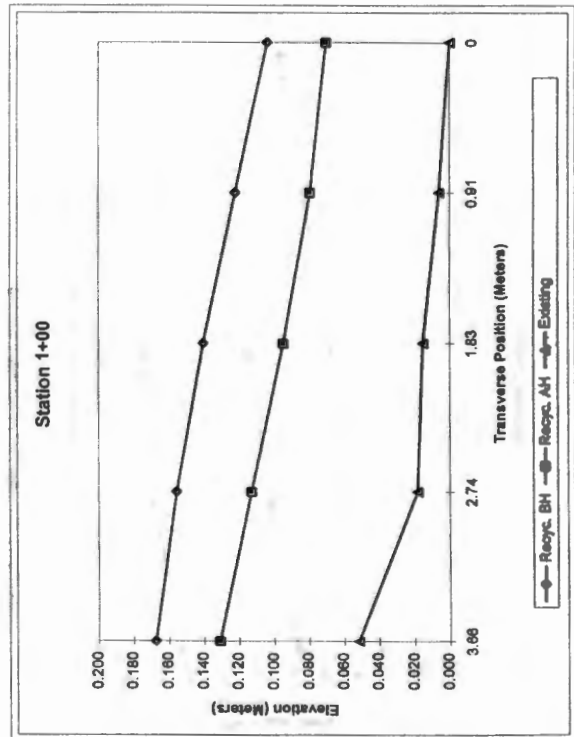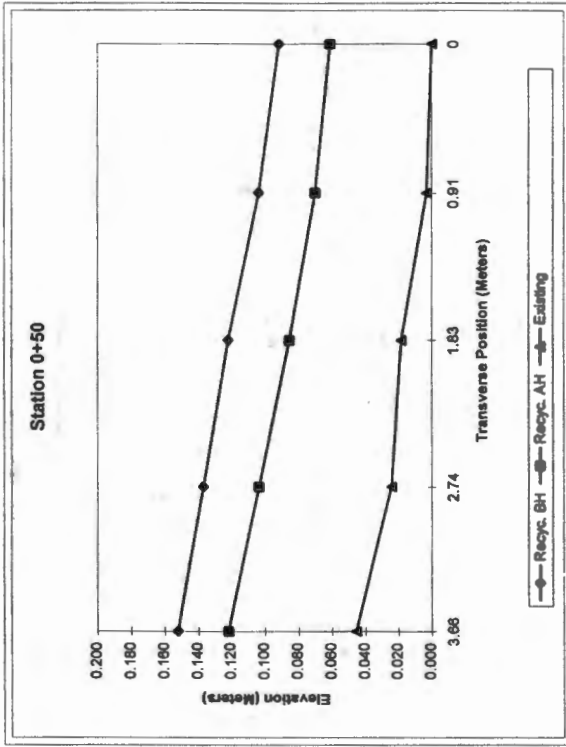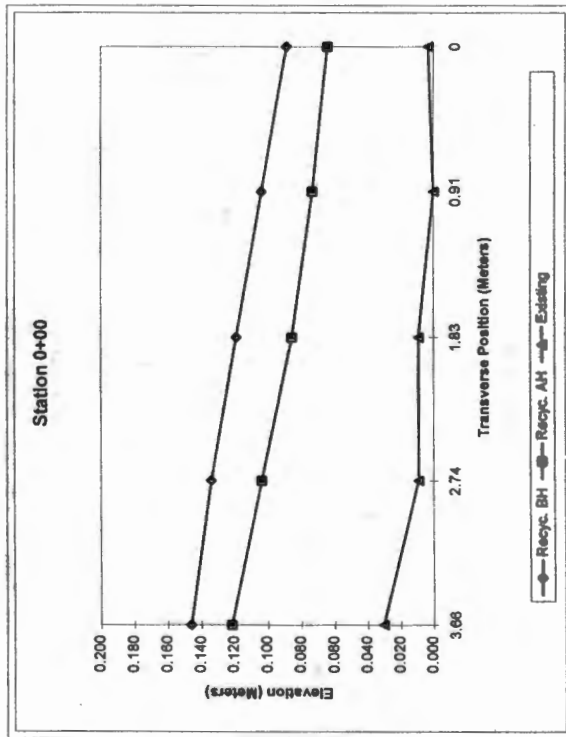

Oklahoma SPS-5 (400503)

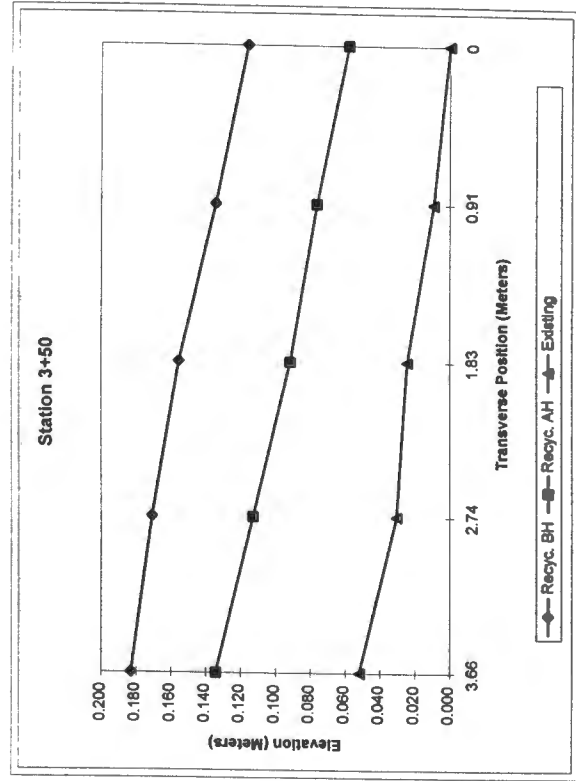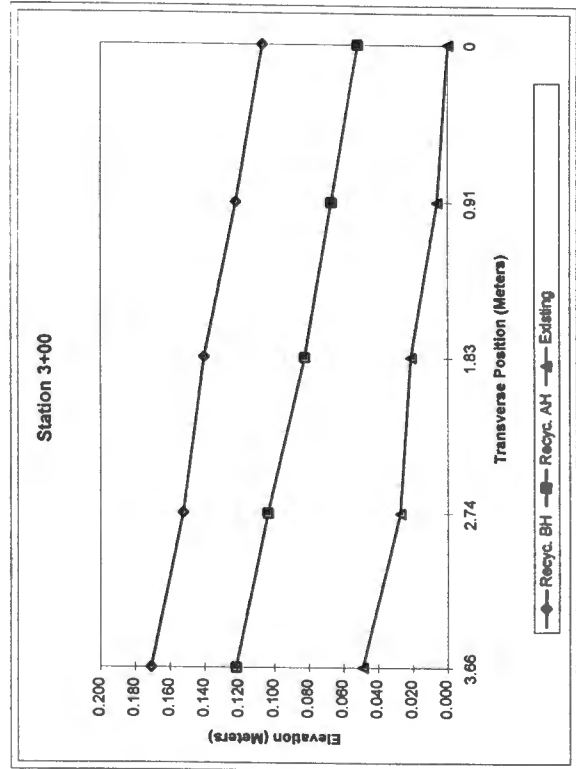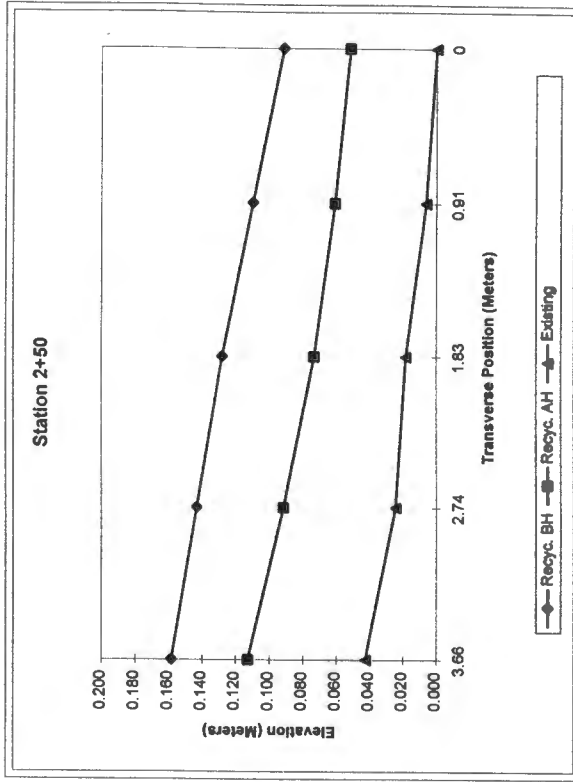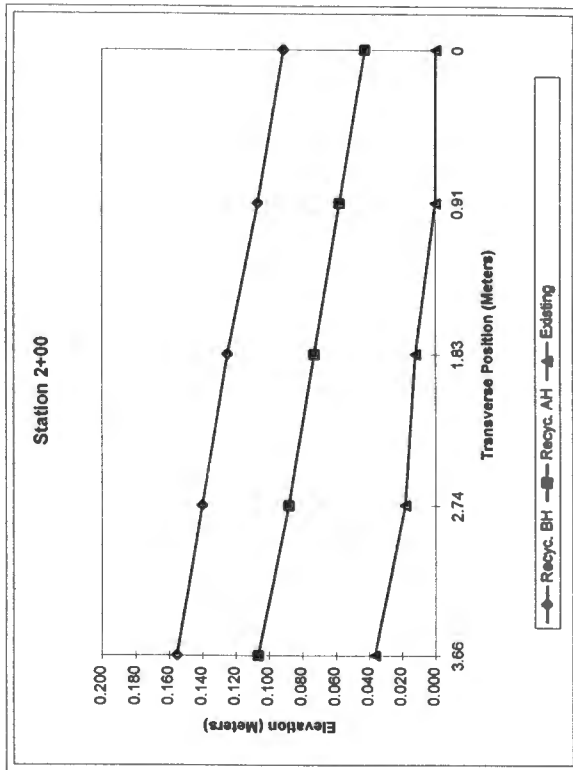

Oklahoma SPS-5 (400503)


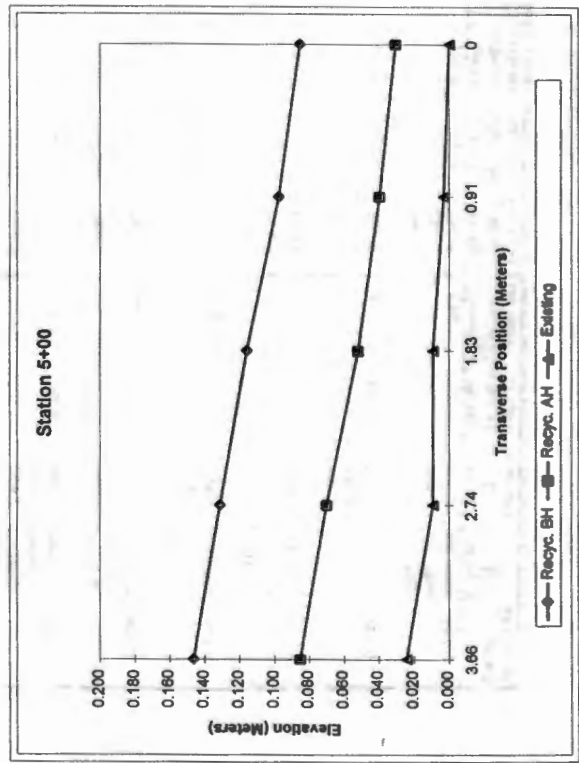
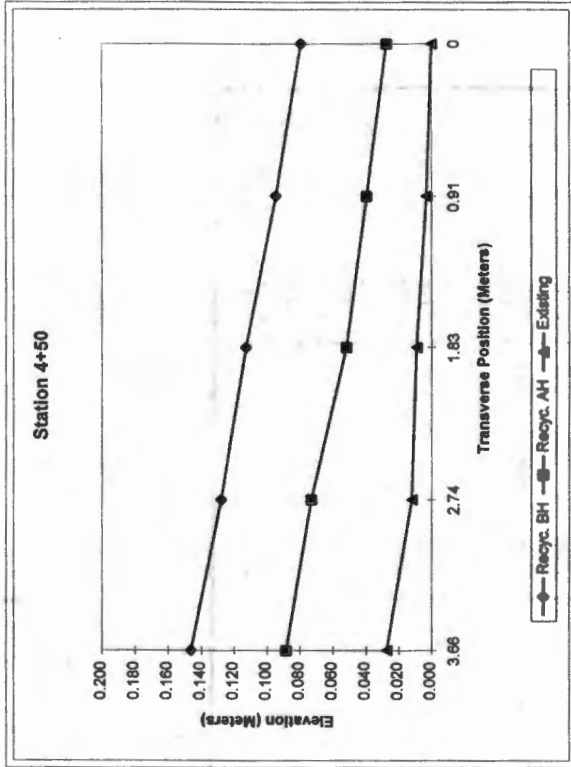
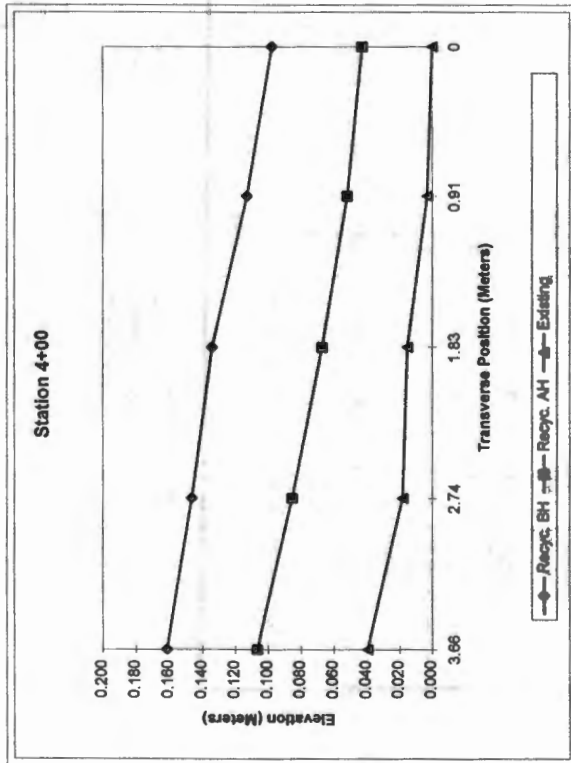


Oklahoma SPS-5 (400504)





Transverse Offset	LAYERS	ELEVATION		Virgin BH THICKNESS		Virgin AH THICKNESS		ELEVATION		Virgin BH THICKNESS		Virgin AH THICKNESS		ELEVATION		Virgin BH THICKNESS		Virgin AH THICKNESS	
		Meters	Feet	Meters	Feet	Meters	Feet	Meters	Feet	Meters	Feet	Meters	Feet	Meters	Feet	Meters	Feet	Meters	Feet
0 + 00	Virgin BH Virgin AH Existing	2.374	7.79	0.037	0.043	2.390	7.86	0.027	0.089	2.408	7.92	0.030	0.098	2.420	7.94	0.034	0.112	2.432	7.98
		2.338	7.67			2.382	7.83			2.377	7.81			2.387	7.85			2.390	7.86
		2.295	7.53			2.298	7.54			2.301	7.55			2.316	7.59			2.335	7.67
0 + 50	Virgin BH Virgin AH Existing	2.420	7.94	0.037	0.079	2.432	7.98	0.027	0.089	2.451	8.05	0.030	0.098	2.463	8.08	0.037	0.121	2.472	8.12
		2.384	7.82			2.405	7.89			2.420	7.92			2.426	7.96			2.420	7.92
		2.304	7.56			2.307	7.58			2.332	7.66			2.335	7.67			2.382	7.82
1 + 00	Virgin BH Virgin AH Existing	2.448	8.03	0.037	0.061	2.463	8.08	0.046	0.151	2.475	8.12	0.027	0.079	2.490	8.16	0.037	0.121	2.499	8.20
		2.411	7.90			2.417	7.93			2.448	8.02			2.454	8.05			2.451	8.04
		2.350	7.71			2.350	7.71			2.368	7.77			2.371	7.78			2.390	7.90
1 + 50	Virgin BH Virgin AH Existing	2.466	8.11	0.030	0.058	2.481	8.15	0.024	0.076	2.496	8.20	0.027	0.073	2.515	8.26	0.034	0.112	2.533	8.32
		2.435	7.97			2.457	8.05			2.469	8.08			2.481	8.14			2.481	8.14
		2.377	7.80			2.380	7.83			2.396	7.89			2.396	7.89			2.420	7.90
2 + 00	Virgin BH Virgin AH Existing	2.515	8.25	0.055	0.070	2.530	8.30	0.052	0.172	2.542	8.35	0.049	0.161	2.551	8.38	0.052	0.172	2.554	8.40
		2.480	8.13			2.478	8.12			2.493	8.18			2.499	8.20			2.499	8.20
		2.390	7.85			2.390	7.85			2.405	7.90			2.408	7.92			2.417	7.97
2 + 50	Virgin BH Virgin AH Existing	2.536	8.33	0.052	0.064	2.551	8.37	0.049	0.161	2.566	8.42	0.043	0.141	2.579	8.46	0.048	0.157	2.597	8.52
		2.484	8.15			2.502	8.23			2.518	8.28			2.536	8.34			2.542	8.36
		2.420	7.90			2.429	7.98			2.444	8.03			2.457	8.07			2.481	7.97
3 + 00	Virgin BH Virgin AH Existing	2.548	8.38	0.052	0.064	2.566	8.42	0.049	0.161	2.579	8.46	0.043	0.141	2.591	8.50	0.048	0.157	2.597	8.52
		2.496	8.18			2.518	8.23			2.536	8.28			2.545	8.31			2.542	8.36
		2.432	7.94			2.438	7.98			2.457	8.07			2.467	8.11			2.481	7.97
3 + 50	Virgin BH Virgin AH Existing	2.582	8.47	0.052	0.067	2.597	8.51	0.052	0.172	2.609	8.56	0.046	0.151	2.621	8.60	0.049	0.161	2.630	8.63
		2.530	8.28			2.545	8.35			2.583	8.47			2.573	8.45			2.579	8.46
		2.463	8.08			2.466	8.09			2.490	8.17			2.490	8.17			2.505	8.21
4 + 00	Virgin BH Virgin AH Existing	2.609	8.56	0.058	0.058	2.627	8.63	0.055	0.182	2.640	8.68	0.052	0.173	2.646	8.70	0.052	0.172	2.655	8.73
		2.551	8.37			2.573	8.45			2.588	8.49			2.594	8.51			2.600	8.53
		2.493	8.18			2.496	8.19			2.515	8.26			2.518	8.27			2.536	8.36
4 + 50	Virgin BH Virgin AH Existing	2.633	8.63	0.055	0.064	2.652	8.69	0.049	0.161	2.664	8.73	0.046	0.151	2.673	8.77	0.046	0.151	2.682	8.80
		2.579	8.45			2.603	8.53			2.618	8.57			2.627	8.60			2.627	8.60
		2.515	8.25			2.521	8.26			2.536	8.31			2.536	8.31			2.560	8.38
5 + 00	Virgin BH Virgin AH Existing	2.658	8.72	0.058	0.058	2.676	8.79	0.055	0.182	2.688	8.84	0.052	0.173	2.701	8.88	0.052	0.172	2.707	8.90
		2.600	8.53			2.621	8.61			2.637	8.66			2.649	8.69			2.652	8.70
		2.542	8.34			2.548	8.37			2.560	8.41			2.563	8.42			2.585	8.50
AVG				0.047	0.062			0.043	0.077			0.040	0.077			0.043	0.083		
MAX				0.058	0.079			0.055	0.098			0.052	0.088			0.052	0.091		
MIN				0.030	0.043			0.024	0.064			0.020	0.073			0.034	0.070		
STD				0.010	0.009			0.011	0.009			0.010	0.005			0.007	0.006		

SECTION AVG		Virgin BH	Virgin AH
SECTION MAX		0.046	0.073
SECTION MIN		0.024	0.043
SECTION STD		0.009	0.011




Oklahoma SPS-5 (400504)

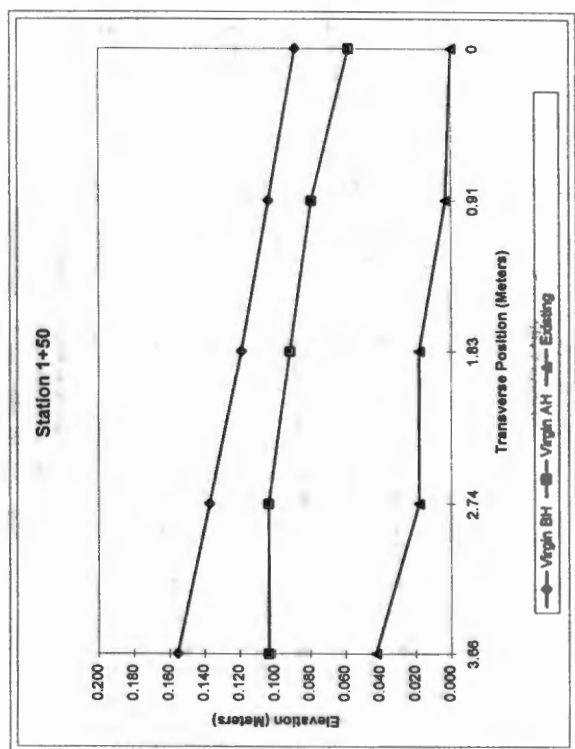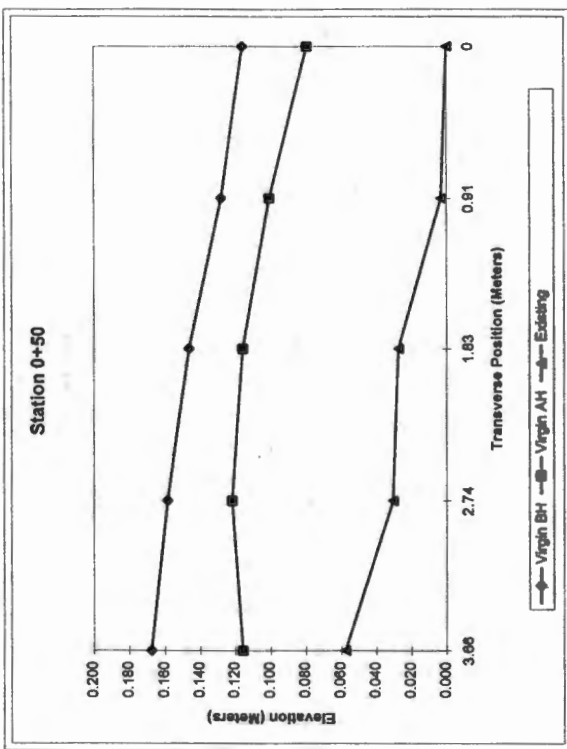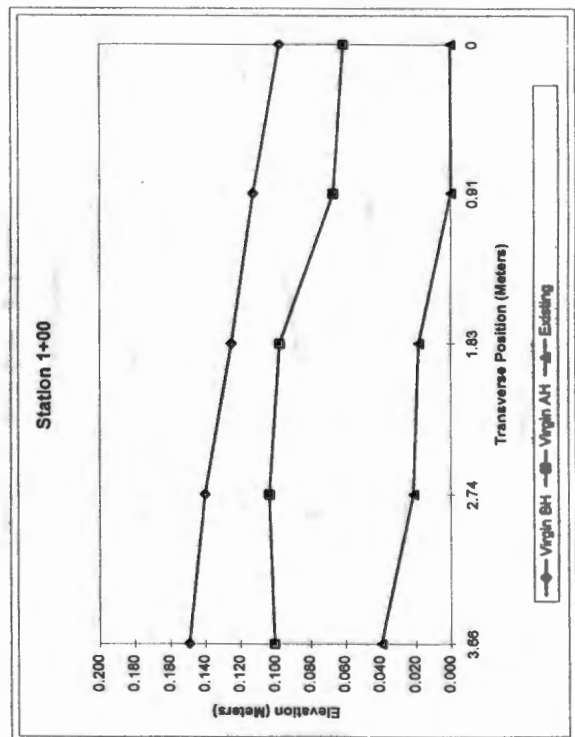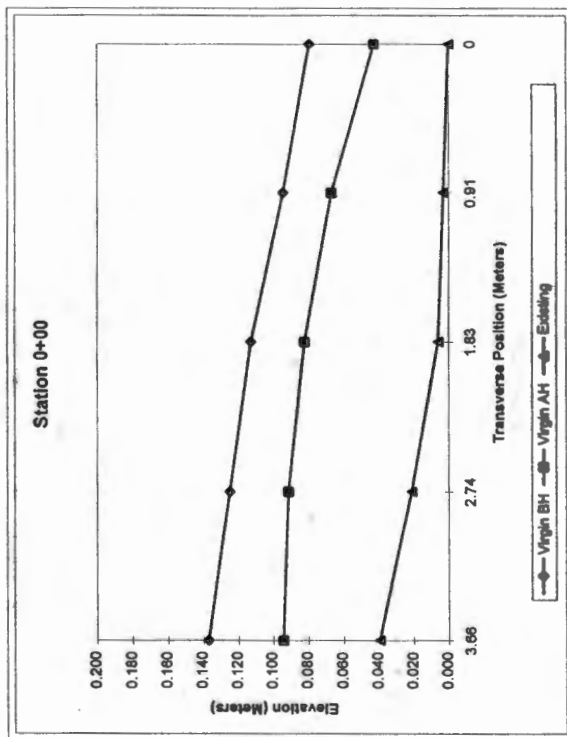

Oklahoma SPS-5 (400504)

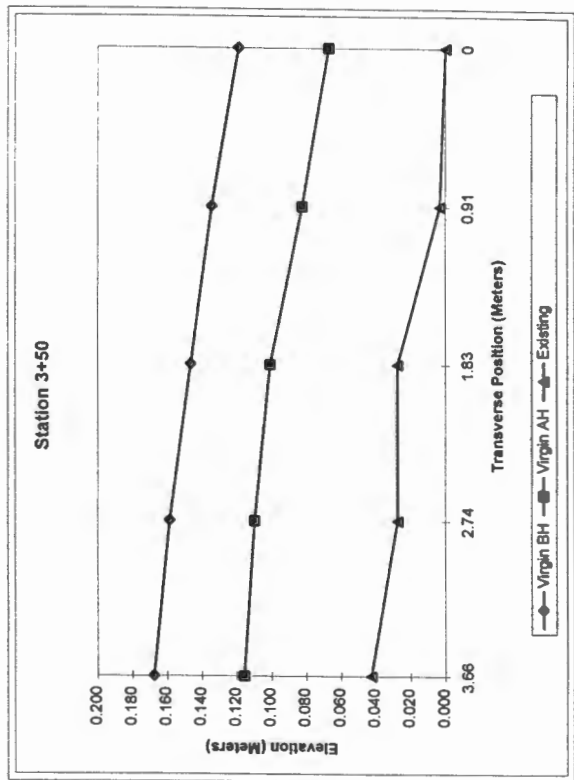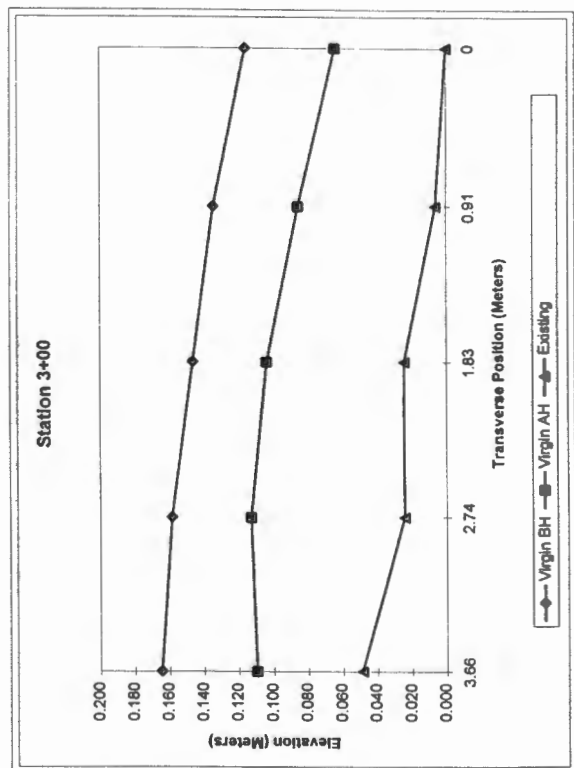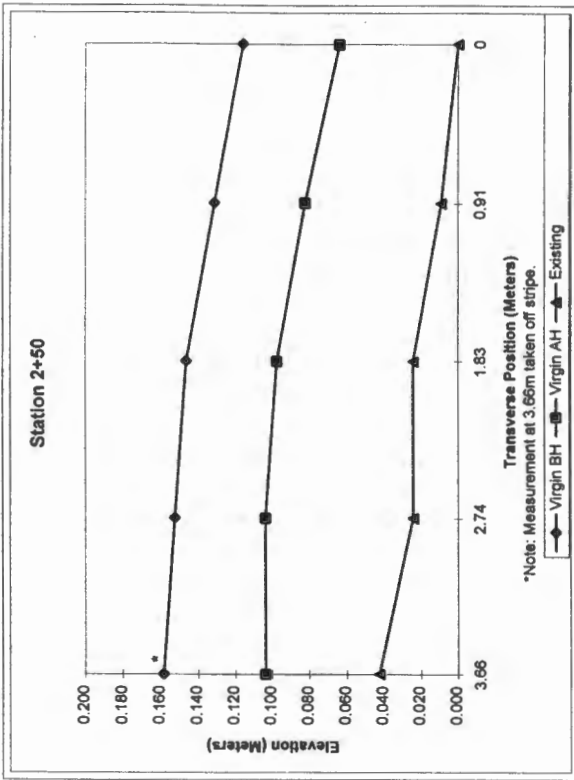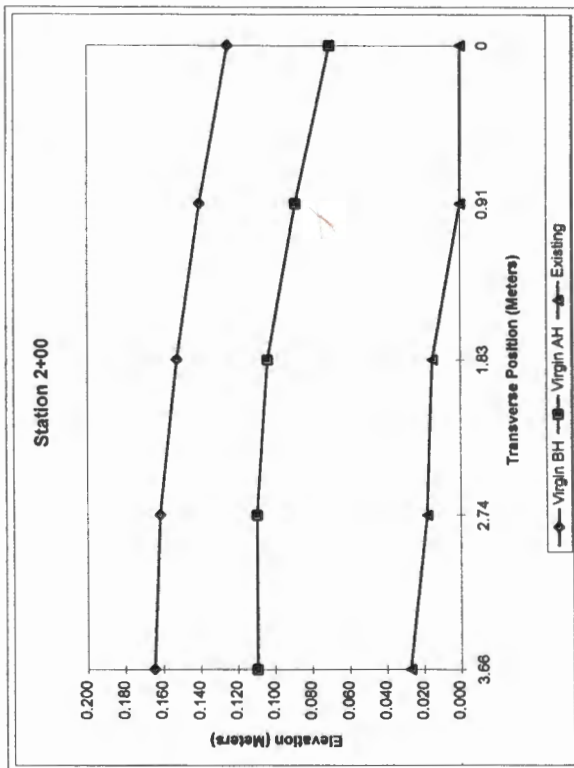

Oklahoma SPS-5 (400504)

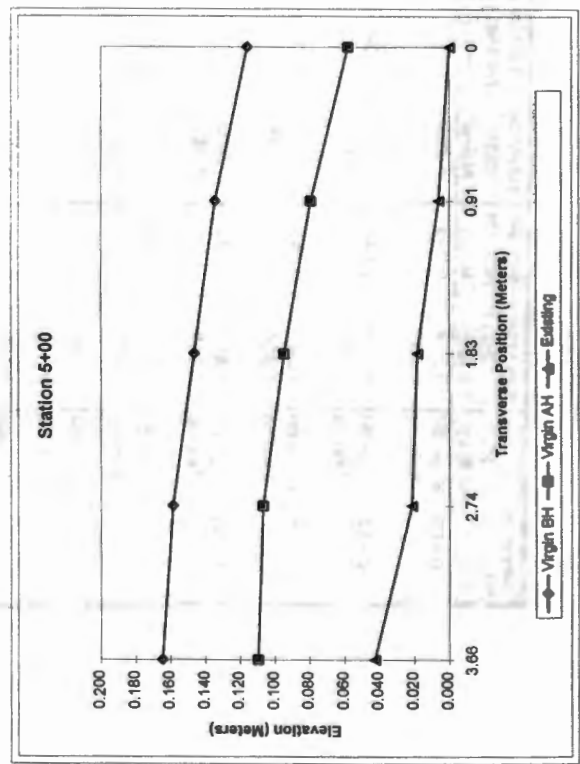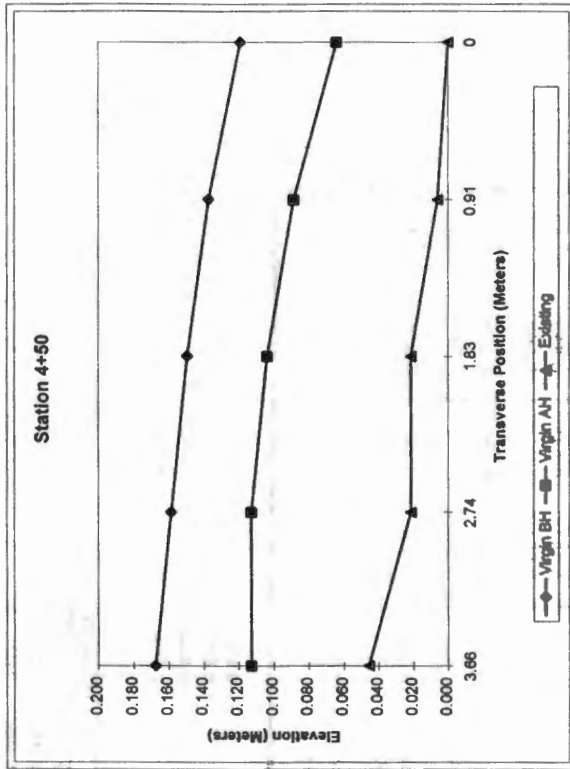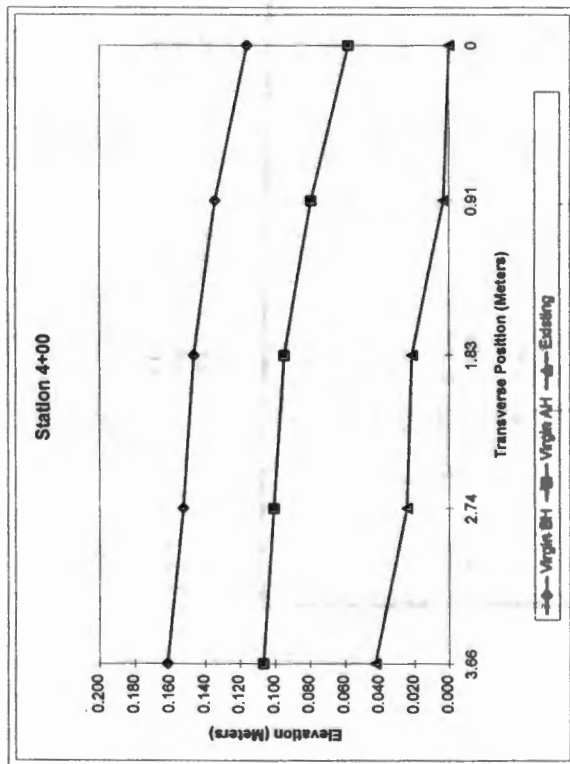





Oklahoma SPS-5 (400505)

Transverse Offset	2 LAYERS	ELEVATION 0 Meters	Virgin BH THICKNESS Meters	ELEVATION 0.91 Meters	Virgin BH THICKNESS Meters	ELEVATION 1.83 Meters	Virgin BH THICKNESS Meters	ELEVATION 2.74 Meters	Virgin BH THICKNESS Meters	ELEVATION 3.66 Meters	Virgin BH THICKNESS Meters
0+00	Virgin BH Existing	1.274 1.231	0.043	1.292 1.237	0.055	1.308 1.262	0.046	1.323 1.274	0.049	1.335 1.295	0.040
0+50	Virgin BH Existing	1.149 1.109	0.040	1.167 1.122	0.046	1.186 1.146	0.040	1.201 1.155	0.046	1.216 1.183	0.034
1+00	Virgin BH Existing	1.049 1.006	0.043	1.070 1.018	0.052	1.085 1.042	0.043	1.100 1.049	0.052	1.119 1.073	0.046
1+50	Virgin BH Existing	0.981 0.948	0.034	1.000 0.960	0.040	1.012 0.972	0.040	1.030 0.981	0.049	1.047 1.003	0.044
2+00	Virgin BH Existing	0.902 0.878	0.024	0.920 0.887	0.034	0.933 0.896	0.037	0.951 0.908	0.043	0.966 0.927	0.040
2+50	Virgin BH Existing	0.796 0.774	0.021	0.811 0.780	0.030	0.826 0.792	0.034	0.841 0.799	0.043	0.860 0.823	0.037
3+00	Virgin BH Existing	0.655 0.622	0.034	0.671 0.631	0.040	0.689 0.646	0.043	0.704 0.658	0.046	0.719 0.680	0.040
3+50	Virgin BH Existing	0.521 0.475	0.046	0.536 0.494	0.043	0.549 0.512	0.037	0.567 0.524	0.043	0.585 0.546	0.040
4+00	Virgin BH Existing	0.402 0.354	0.049	0.421 0.369	0.052	0.439 0.390	0.049	0.454 0.402	0.052	0.472 0.427	0.046
4+50	Virgin BH Existing	0.311 0.265	0.046	0.329 0.277	0.052	0.344 0.296	0.049	0.354 0.305	0.049	0.366 0.326	0.040
5+00	Virgin BH Existing	0.223 0.174	0.049	0.238 0.183	0.055	0.250 0.201	0.049	0.259 0.210	0.049	0.274 0.219	0.055





AVG	0.039	0.046	0.043	0.048	0.042
MAX	0.049	0.055	0.049	0.052	0.055
MIN	0.021	0.030	0.034	0.043	0.034
STD	0.009	0.008	0.005	0.003	0.006

Virgin BH	
SECTION AVG	0.043
SECTION MAX	0.055
SECTION MIN	0.021
SECTION STD	0.007




Oklahoma SPS-5 (400505)

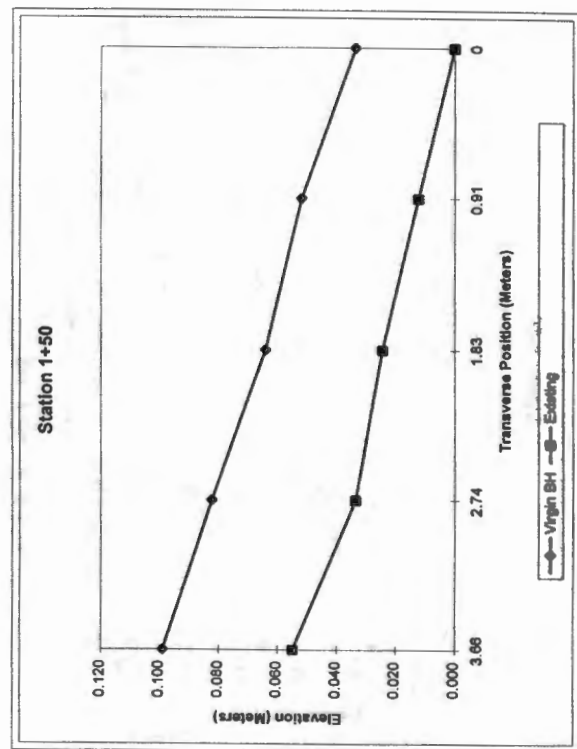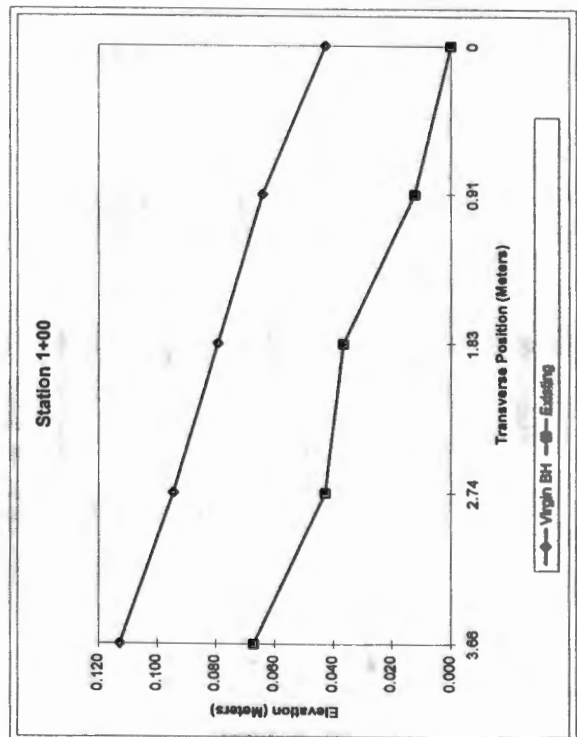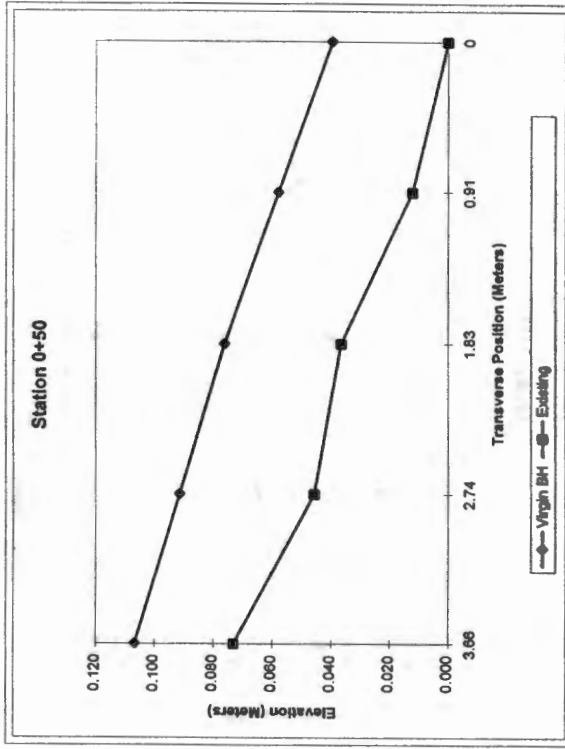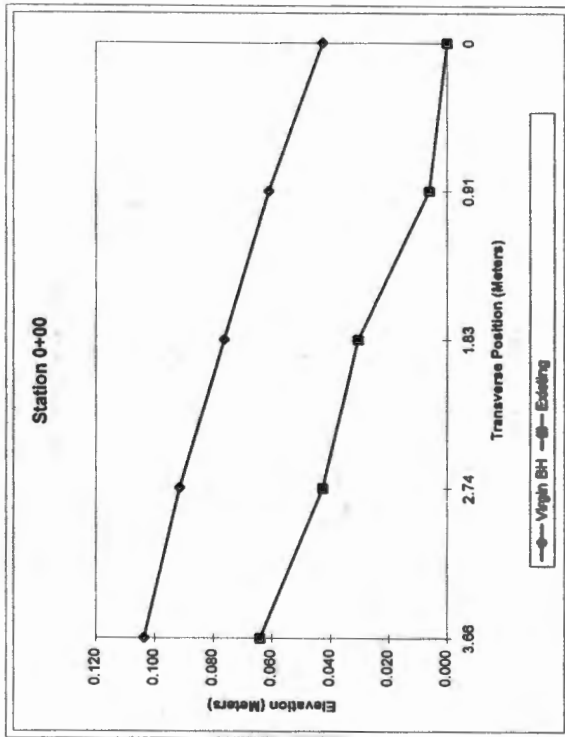

Oklahoma SPS-5 (400505)

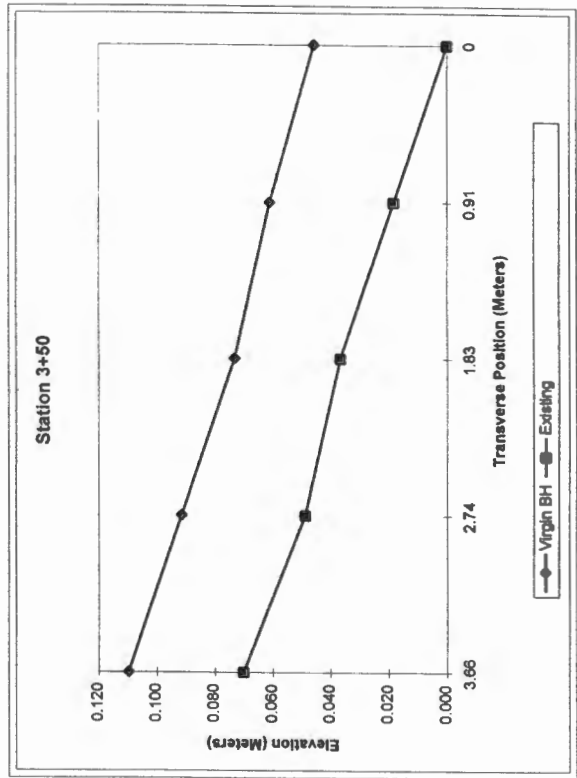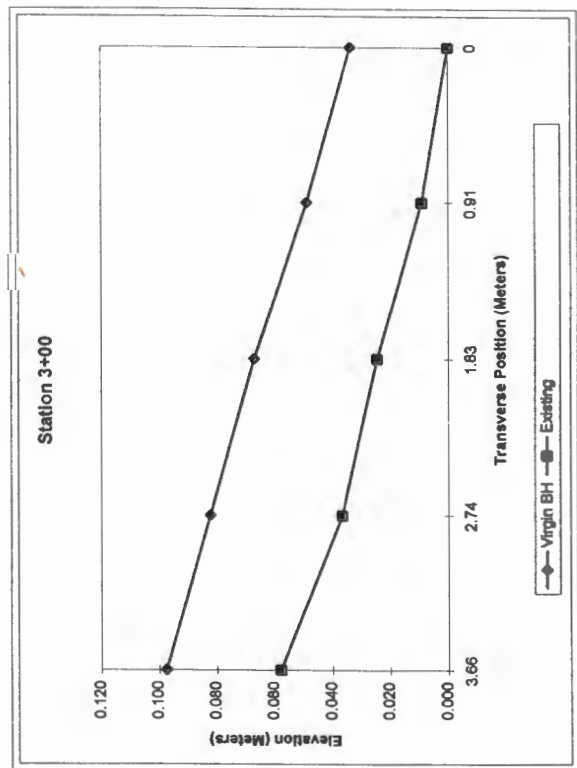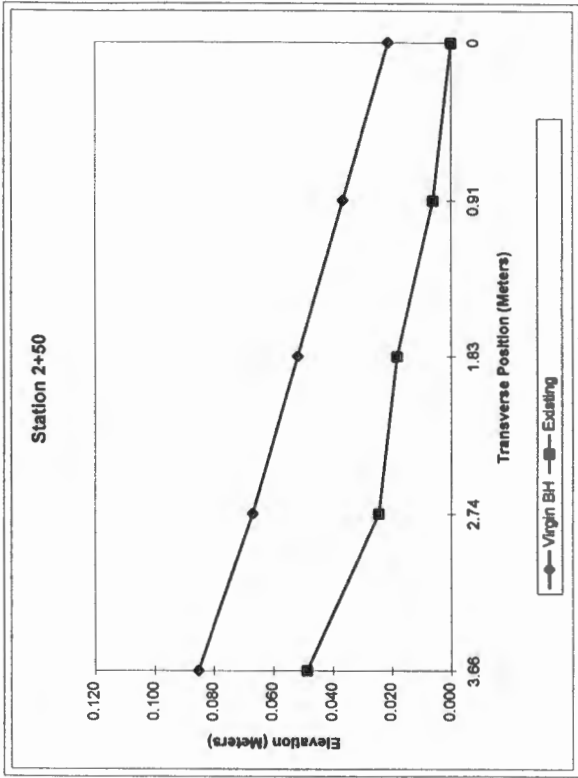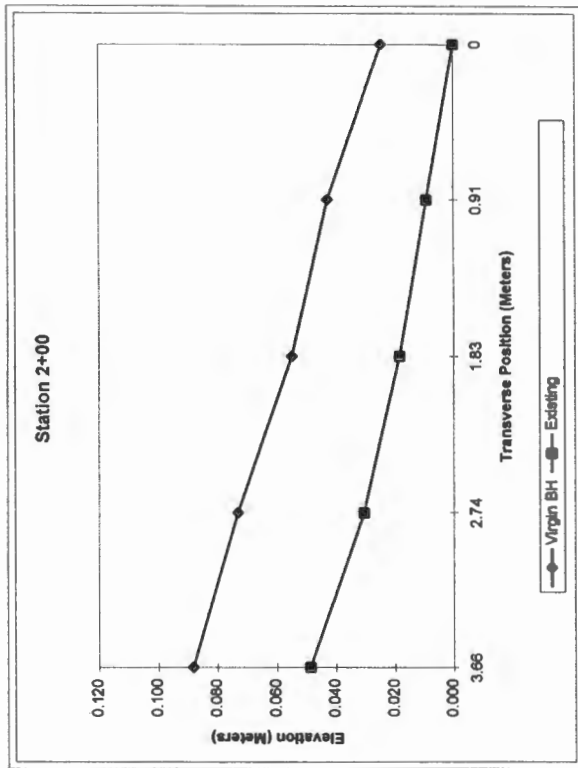

Oklahoma SPS-5 (400505)


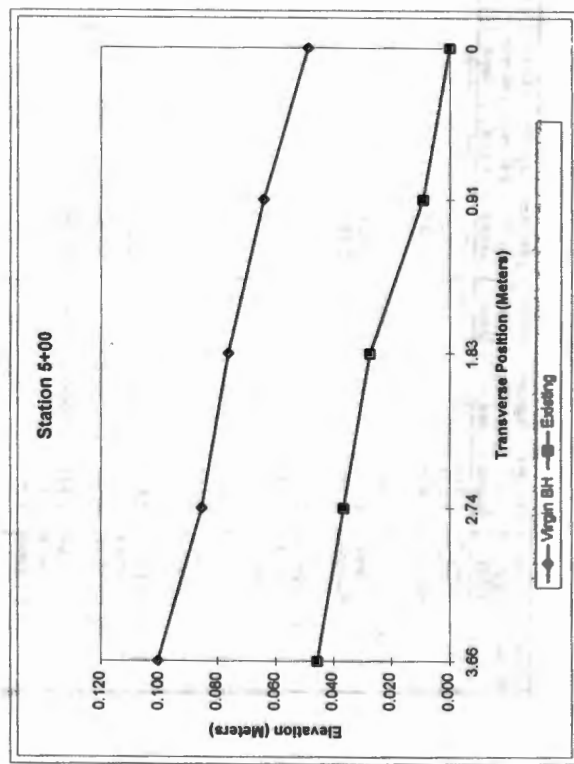
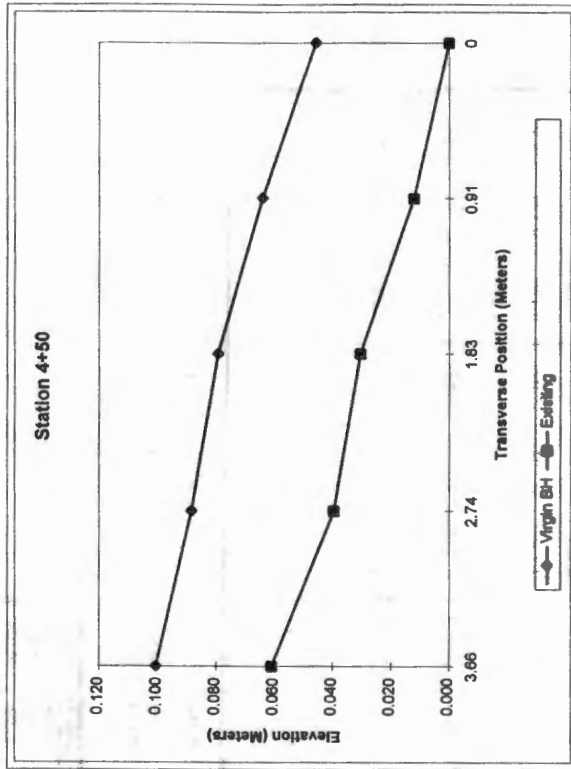
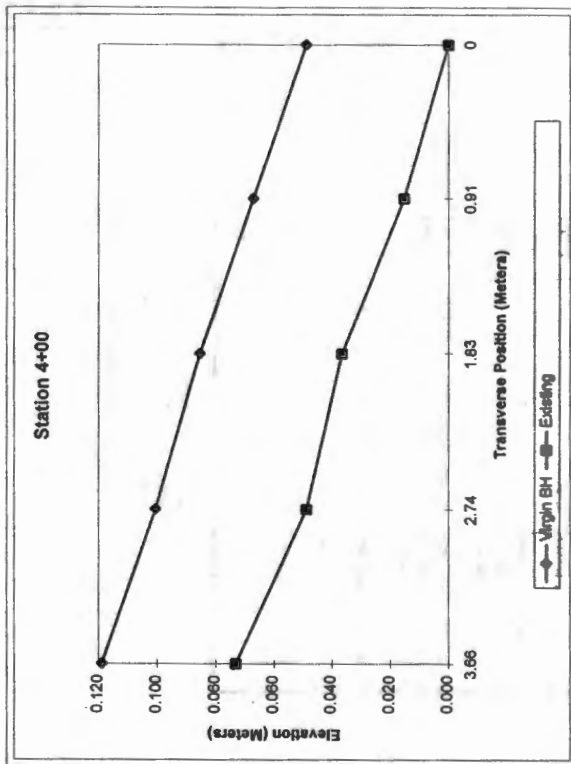


Oklahoma SPS-5 (400506)





Transverse Offset	LAYERS	ELEVATION			Virgin BH			Milled			ELEVATION			Virgin BH			Milled			ELEVATION			Virgin BH			Milled		
		0	THICKNESS	THICKNESS	0.91	THICKNESS	THICKNESS	1.83	THICKNESS	THICKNESS	2.74	THICKNESS	THICKNESS	3.66	THICKNESS	THICKNESS	4.58	THICKNESS	THICKNESS	5.50	THICKNESS	THICKNESS	6.42	THICKNESS	THICKNESS	7.34	THICKNESS	THICKNESS
0 + 00	Virgin BH Milled	2.499 2.423 2.487	0.076	-0.064	2.512 2.426 2.487	0.085	-0.061	2.530 2.444 2.496	0.085	-0.052	2.545 2.451 2.493	0.094	-0.043	2.560 2.469 2.512	0.091	-0.043	2.575 2.478 2.520	0.098	-0.037	2.590 2.491 2.534	0.098	-0.034	2.605 2.506 2.550	0.098	-0.034	2.620 2.521 2.564	0.098	-0.034
0 + 50	Virgin BH Milled	2.588 2.512 2.566	0.078	-0.055	2.603 2.524 2.566	0.079	-0.043	2.618 2.545 2.579	0.073	-0.034	2.633 2.551 2.579	0.087	-0.027	2.648 2.569 2.612	0.093	-0.037	2.663 2.584 2.627	0.098	-0.034	2.678 2.599 2.643	0.098	-0.034	2.693 2.614 2.658	0.098	-0.034	2.708 2.629 2.673	0.098	-0.034
1 + 00	Virgin BH Milled	2.670 2.588 2.649	0.082	-0.081	2.685 2.603 2.649	0.082	-0.046	2.701 2.621 2.655	0.078	-0.034	2.717 2.633 2.655	0.084	-0.021	2.734 2.657 2.670	0.098	-0.034	2.749 2.670 2.713	0.098	-0.034	2.764 2.685 2.728	0.098	-0.034	2.779 2.700 2.744	0.098	-0.034	2.794 2.715 2.759	0.098	-0.034
1 + 50	Virgin BH Milled	2.749 2.649 2.710	0.101	-0.061	2.766 2.673 2.713	0.093	-0.040	2.783 2.694 2.728	0.088	-0.034	2.801 2.707 2.728	0.094	-0.021	2.816 2.713 2.749	0.104	-0.037	2.831 2.738 2.782	0.104	-0.037	2.846 2.753 2.797	0.104	-0.037	2.861 2.768 2.812	0.104	-0.037	2.876 2.783 2.827	0.104	-0.037
2 + 00	Virgin BH Milled	2.841 2.737 2.792	0.104	-0.055	2.854 2.761 2.798	0.093	-0.037	2.871 2.777 2.816	0.094	-0.040	2.889 2.795 2.822	0.101	-0.034	2.903 2.809 2.841	0.105	-0.043	2.918 2.825 2.867	0.105	-0.043	2.933 2.840 2.882	0.105	-0.043	2.948 2.855 2.897	0.105	-0.043	2.963 2.870 2.912	0.105	-0.043
2 + 50	Virgin BH Milled	2.923 2.829 2.890	0.094	-0.061	2.938 2.847 2.893	0.091	-0.046	2.955 2.865 2.914	0.090	-0.049	2.972 2.877 2.914	0.094	-0.037	2.987 2.894 2.935	0.101	-0.049	3.002 2.909 2.950	0.101	-0.049	3.017 2.924 2.965	0.101	-0.049	3.032 2.939 2.980	0.101	-0.049	3.047 2.954 2.995	0.101	-0.049
3 + 00	Virgin BH Milled	2.999 2.902 2.963	0.098	-0.061	3.011 2.917 2.963	0.094	-0.048	3.030 2.935 2.981	0.094	-0.048	3.048 2.944 2.981	0.104	-0.037	3.066 2.962 3.002	0.113	-0.049	3.084 2.980 3.020	0.113	-0.049	3.102 2.998 3.038	0.113	-0.049	3.120 3.016 3.052	0.113	-0.049	3.138 3.034 3.070	0.113	-0.049
3 + 50	Virgin BH Milled	3.075 2.975 3.024	0.101	-0.049	3.091 2.987 3.024	0.104	-0.037	3.106 3.005 3.042	0.101	-0.037	3.124 3.018 3.045	0.107	-0.027	3.139 3.030 3.072	0.110	-0.043	3.157 3.048 3.084	0.110	-0.043	3.172 3.063 3.100	0.110	-0.043	3.187 3.078 3.112	0.110	-0.043	3.202 3.093 3.128	0.110	-0.043
4 + 00	Virgin BH Milled	3.146 3.042 3.072	0.104	-0.030	3.161 3.068 3.082	0.094	-0.015	3.179 3.078 3.103	0.101	-0.024	3.197 3.088 3.112	0.110	-0.024	3.211 3.097 3.139	0.114	-0.043	3.226 3.117 3.153	0.114	-0.043	3.241 3.132 3.168	0.114	-0.043	3.256 3.147 3.183	0.114	-0.043	3.271 3.162 3.198	0.114	-0.043
4 + 50	Virgin BH Milled	3.218 3.097 3.139	0.119	-0.043	3.231 3.115 3.146	0.116	-0.030	3.246 3.133 3.167	0.113	-0.034	3.268 3.149 3.170	0.117	-0.021	3.277 3.158 3.197	0.119	-0.040	3.292 3.173 3.209	0.119	-0.040	3.307 3.188 3.224	0.119	-0.040	3.322 3.203 3.240	0.119	-0.040	3.337 3.218 3.255	0.119	-0.040
5 + 00	Virgin BH Milled	3.277 3.152 3.197	0.125	-0.046	3.292 3.179 3.203	0.113	-0.024	3.310 3.197 3.218	0.113	-0.021	3.325 3.210 3.231	0.116	-0.021	3.341 3.216 3.255	0.125	-0.040	3.356 3.241 3.277	0.125	-0.040	3.371 3.256 3.292	0.125	-0.040	3.386 3.271 3.308	0.125	-0.040	3.401 3.286 3.323	0.125	-0.040
		AVG	0.098	-0.053		0.095	-0.039		0.094	-0.036		0.101	-0.028		0.107	-0.041		0.107	-0.041		0.107	-0.041		0.107	-0.041		0.107	-0.041
		MAX	0.125	-0.030		0.116	-0.015		0.113	-0.021		0.117	-0.021		0.125	-0.034		0.125	-0.034		0.125	-0.034		0.125	-0.034		0.125	-0.034
		MIN	0.076	-0.064		0.079	-0.061		0.073	-0.052		0.084	-0.043		0.091	-0.049		0.091	-0.049		0.091	-0.049		0.091	-0.049		0.091	-0.049
		STD	0.015	0.010		0.012	0.012		0.013	0.009		0.011	0.007		0.011	0.005		0.011	0.005		0.011	0.005		0.011	0.005		0.011	0.005

SECTION AVG		Virgin BH	Milled
SECTION MAX	0.125	0.125	-0.015
SECTION MIN	0.073	0.073	-0.064
SECTION STD	0.013	0.013	0.012




Oklahoma SPS-5 (400506)

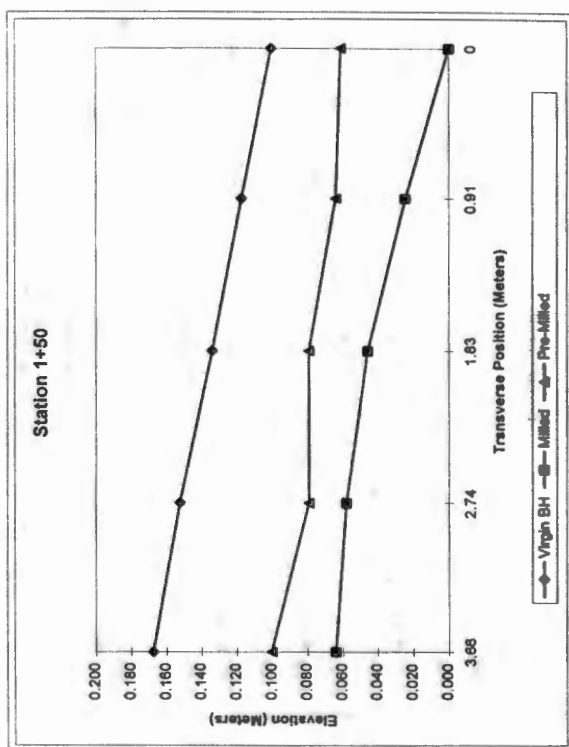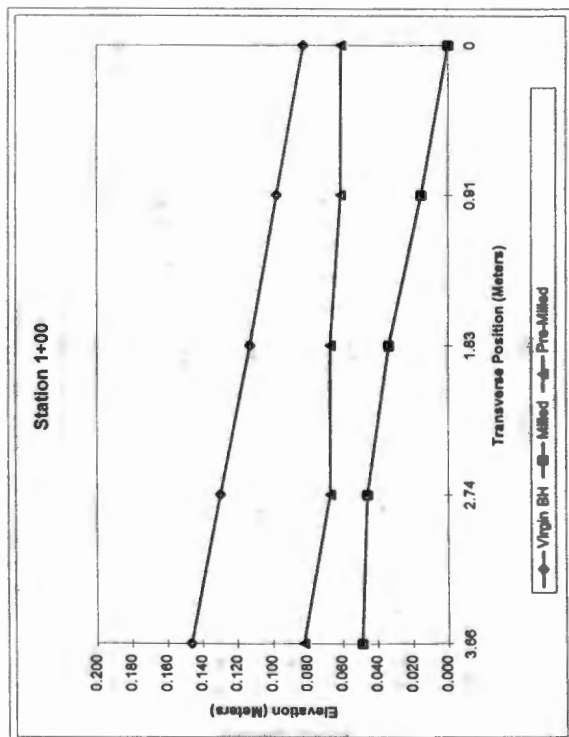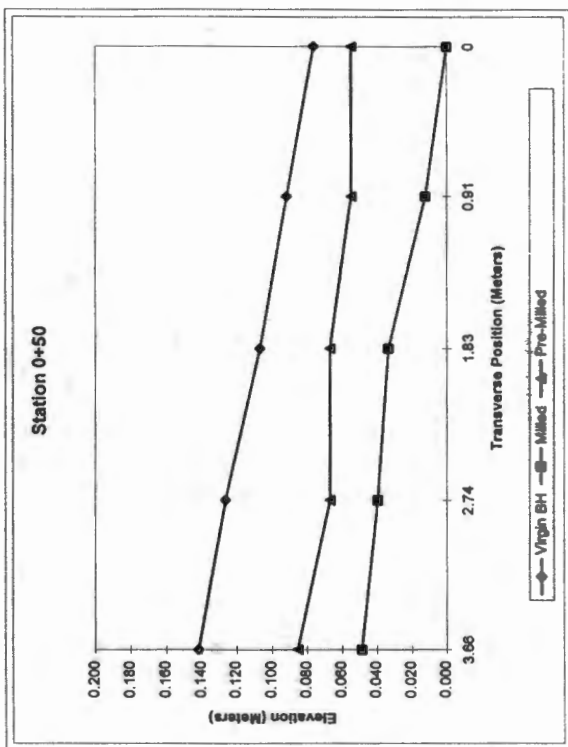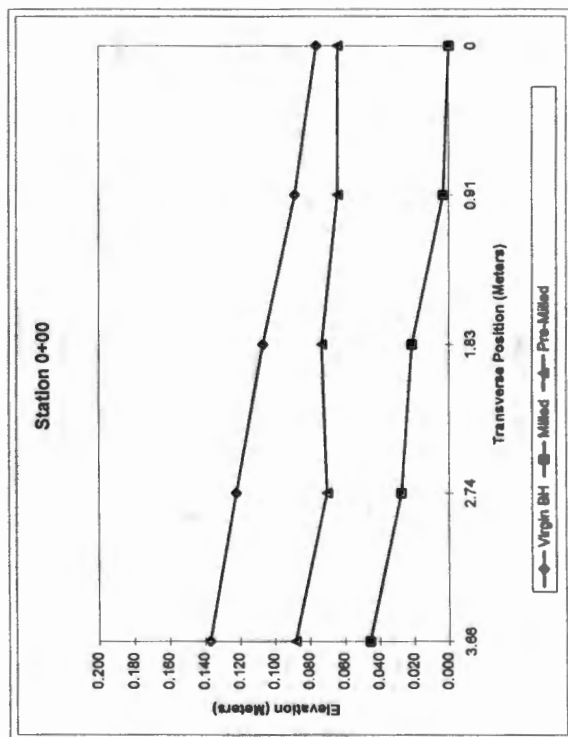

Oklahoma SPS-5 (400506)

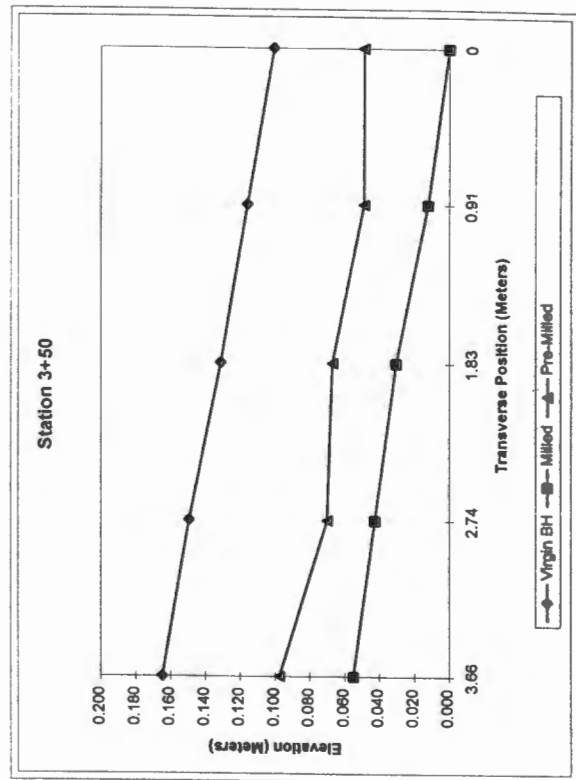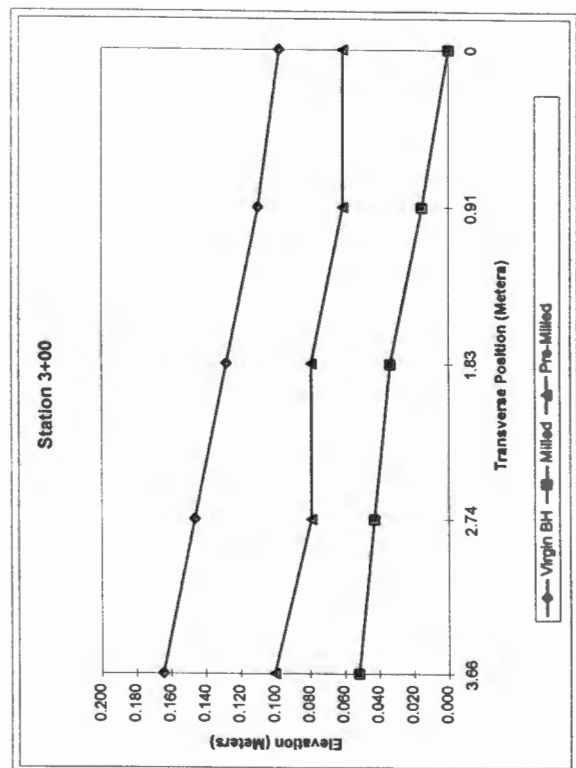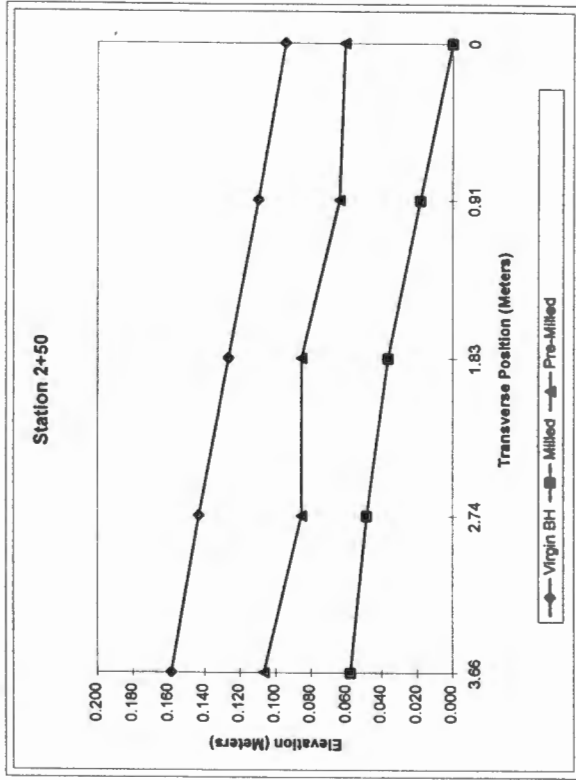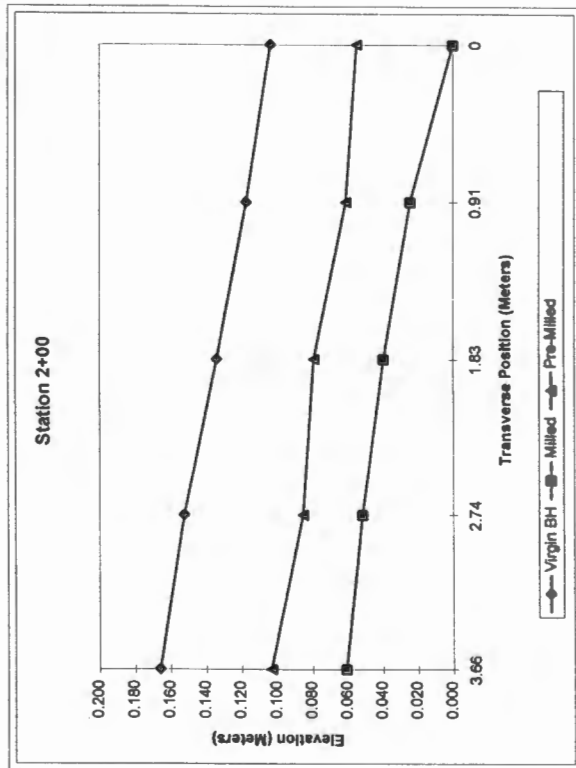

Oklahoma SPS-5 (400506)

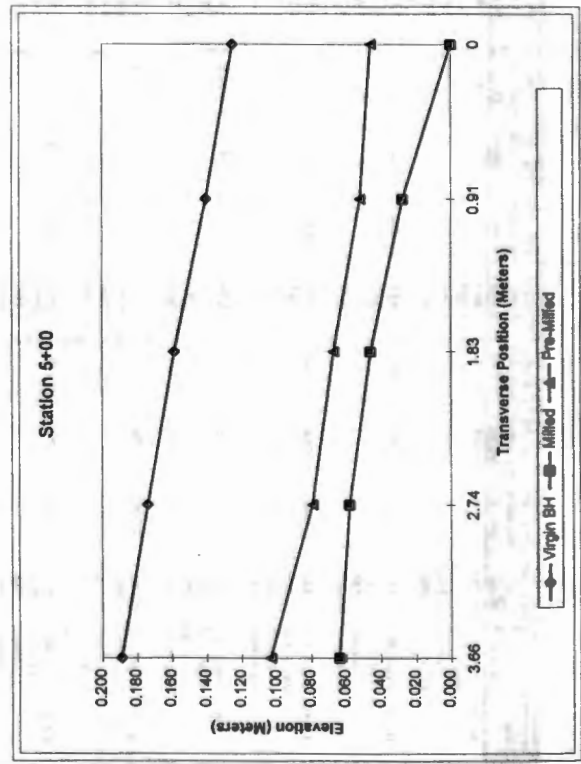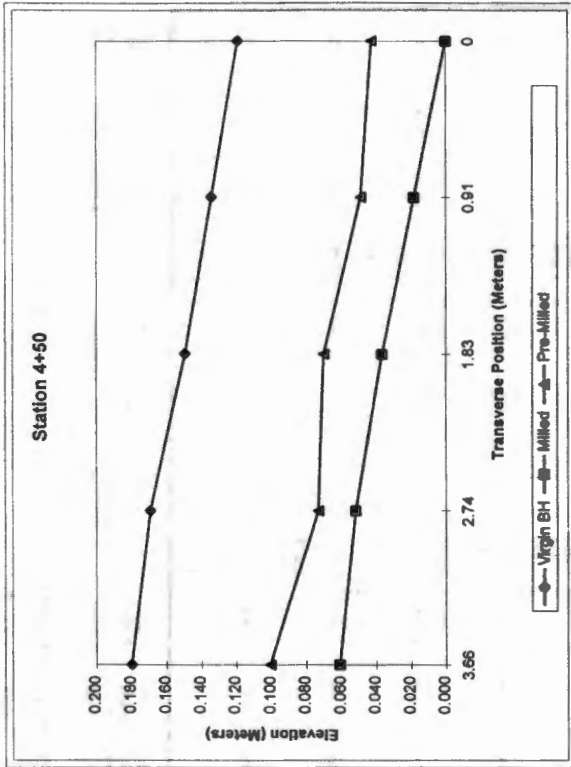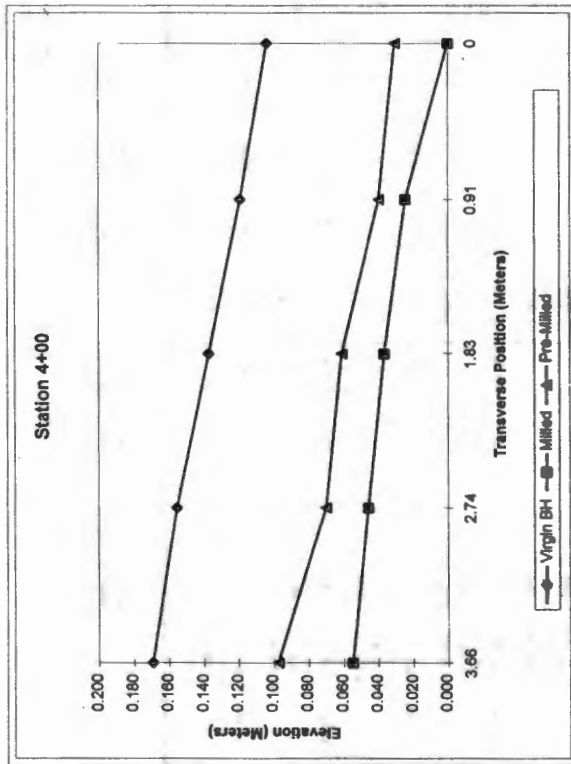





Oklahoma SPS-5 (400507)

Transverse Offset	4 LAYERS	ELEVATION Meters	Virgin BH THICKNESS Meters	Virgin AH THICKNESS Meters	Milled THICKNESS Meters	ELEVATION 0.91 Meters	Virgin BH THICKNESS Meters	Virgin AH THICKNESS Meters	Milled THICKNESS Meters	ELEVATION 1.83 Meters	Virgin BH THICKNESS Meters	Virgin AH THICKNESS Meters	Milled THICKNESS Meters	ELEVATION 2.74 Meters	Virgin BH THICKNESS Meters	Virgin AH THICKNESS Meters	Milled THICKNESS Meters	ELEVATION 3.66 Meters	Virgin BH THICKNESS Meters	Virgin AH THICKNESS Meters	Milled THICKNESS Meters
0+00	Virgin BH Virgin AH Milled Pre-Milled	1.792 1.713 1.634 1.664	0.079 0.079 0.079 0.079	0.079 0.079 0.079 0.079	-0.030 -0.030 -0.030 -0.030	1.807 1.728 1.855 1.870	0.079 0.079 0.079 0.079	0.073 0.073 0.073 0.073	-0.015 -0.015 -0.015 -0.015	1.823 1.750 1.878 1.886	0.073 0.073 0.073 0.073	0.073 0.073 0.073 0.073	-0.009 -0.009 -0.009 -0.009	1.841 1.759 1.889 1.889	0.082 0.082 0.082 0.082	0.070 0.070 0.070 0.070	0.000 0.000 0.000 0.000	1.856 1.782 1.685 1.713	0.094 0.094 0.094 0.094	0.067 0.067 0.067 0.067	-0.018 -0.018 -0.018 -0.018
0+50	Virgin BH Virgin AH Milled Pre-Milled	1.614 1.722 1.658 1.666	0.091 0.091 0.091 0.091	0.064 0.064 0.064 0.064	-0.027 -0.027 -0.027 -0.027	1.829 1.743 1.878 1.889	0.085 0.085 0.085 0.085	0.070 0.070 0.070 0.070	-0.012 -0.012 -0.012 -0.012	1.844 1.765 1.895 1.710	0.079 0.079 0.079 0.079	0.070 0.070 0.070 0.070	-0.015 -0.015 -0.015 -0.015	1.862 1.768 1.707 1.710	0.094 0.094 0.094 0.094	0.061 0.061 0.061 0.061	-0.003 -0.003 -0.003 -0.003	1.876 1.780 1.713 1.734	0.094 0.094 0.094 0.094	0.067 0.067 0.067 0.067	-0.021 -0.021 -0.021 -0.021
1+00	Virgin BH Virgin AH Milled Pre-Milled	1.644 1.747 1.682 1.713	0.098 0.098 0.098 0.098	0.064 0.064 0.064 0.064	-0.030 -0.030 -0.030 -0.030	1.858 1.765 1.895 1.716	0.091 0.091 0.091 0.091	0.070 0.070 0.070 0.070	-0.021 -0.021 -0.021 -0.021	1.871 1.788 1.704 1.731	0.085 0.085 0.085 0.085	0.082 0.082 0.082 0.082	-0.027 -0.027 -0.027 -0.027	1.887 1.792 1.722 1.734	0.094 0.094 0.094 0.094	0.070 0.070 0.070 0.070	-0.012 -0.012 -0.012 -0.012	1.896 1.798 1.737 1.763	0.098 0.098 0.098 0.098	0.061 0.061 0.061 0.061	-0.015 -0.015 -0.015 -0.015
1+50	Virgin BH Virgin AH Milled Pre-Milled	1.888 1.777 1.701 1.737	0.091 0.091 0.091 0.091	0.076 0.076 0.076 0.076	-0.037 -0.037 -0.037 -0.037	1.878 1.798 1.731 1.740	0.079 0.079 0.079 0.079	0.067 0.067 0.067 0.067	-0.009 -0.009 -0.009 -0.009	1.896 1.817 1.747 1.759	0.079 0.079 0.079 0.079	0.070 0.070 0.070 0.070	-0.012 -0.012 -0.012 -0.012	1.911 1.829 1.762 1.783	0.082 0.082 0.082 0.082	0.067 0.067 0.067 0.067	0.000 0.000 0.000 0.000	1.926 1.832 1.768 1.783	0.094 0.094 0.094 0.094	0.064 0.064 0.064 0.064	-0.015 -0.015 -0.015 -0.015
2+00	Virgin BH Virgin AH Milled Pre-Milled	1.906 1.807 1.719 1.762	0.098 0.098 0.098 0.098	0.088 0.088 0.088 0.088	-0.043 -0.043 -0.043 -0.043	1.917 1.829 1.734 1.768	0.088 0.088 0.088 0.088	0.073 0.073 0.073 0.073	-0.024 -0.024 -0.024 -0.024	1.936 1.838 1.785 1.789	0.088 0.088 0.088 0.088	0.073 0.073 0.073 0.073	-0.024 -0.024 -0.024 -0.024	1.951 1.859 1.780 1.792	0.091 0.091 0.091 0.091	0.079 0.079 0.079 0.079	-0.012 -0.012 -0.012 -0.012	1.963 1.862 1.786 1.817	0.101 0.101 0.101 0.101	0.076 0.076 0.076 0.076	-0.030 -0.030 -0.030 -0.030
2+50	Virgin BH Virgin AH Milled Pre-Milled	1.957 1.859 1.788 1.607	0.098 0.098 0.098 0.098	0.091 0.091 0.091 0.091	-0.040 -0.040 -0.040 -0.040	1.969 1.878 1.798 1.814	0.091 0.091 0.091 0.091	0.079 0.079 0.079 0.079	-0.016 -0.016 -0.016 -0.016	1.984 1.899 1.820 1.836	0.085 0.085 0.085 0.085	0.079 0.079 0.079 0.079	-0.016 -0.016 -0.016 -0.016	1.999 1.905 1.829 1.838	0.094 0.094 0.094 0.094	0.076 0.076 0.076 0.076	-0.009 -0.009 -0.009 -0.009	2.015 1.908 1.838 1.865	0.107 0.107 0.107 0.107	0.070 0.070 0.070 0.070	-0.027 -0.027 -0.027 -0.027
3+00	Virgin BH Virgin AH Milled Pre-Milled	2.030 1.939 1.853 1.896	0.091 0.091 0.091 0.091	0.085 0.085 0.085 0.085	-0.043 -0.043 -0.043 -0.043	2.039 1.960 1.882 1.899	0.079 0.079 0.079 0.079	0.098 0.098 0.098 0.098	-0.037 -0.037 -0.037 -0.037	2.057 1.976 1.899 1.920	0.082 0.082 0.082 0.082	0.076 0.076 0.076 0.076	-0.021 -0.021 -0.021 -0.021	2.073 1.984 1.914 1.923	0.088 0.088 0.088 0.088	0.070 0.070 0.070 0.070	-0.009 -0.009 -0.009 -0.009	2.085 1.987 1.920 1.935	0.098 0.098 0.098 0.098	0.067 0.067 0.067 0.067	-0.016 -0.016 -0.016 -0.016
3+50	Virgin BH Virgin AH Milled Pre-Milled	2.094 2.015 1.948 2.006	0.079 0.079 0.079 0.079	0.067 0.067 0.067 0.067	-0.056 -0.056 -0.056 -0.056	2.106 2.038 1.960 2.012	0.070 0.070 0.070 0.070	0.076 0.076 0.076 0.076	-0.052 -0.052 -0.052 -0.052	2.124 2.054 1.978 2.030	0.070 0.070 0.070 0.070	0.076 0.076 0.076 0.076	-0.052 -0.052 -0.052 -0.052	2.140 2.063 1.987 2.033	0.076 0.076 0.076 0.076	0.076 0.076 0.076 0.076	-0.046 -0.046 -0.046 -0.046	2.155 2.063 1.998 2.042	0.091 0.091 0.091 0.091	0.067 0.067 0.067 0.067	-0.046 -0.046 -0.046 -0.046
4+00	Virgin BH Virgin AH Milled Pre-Milled	2.124 2.030 1.983 2.008	0.094 0.094 0.094 0.094	0.067 0.067 0.067 0.067	-0.043 -0.043 -0.043 -0.043	2.137 2.051 1.981 2.021	0.065 0.065 0.065 0.065	0.070 0.070 0.070 0.070	-0.040 -0.040 -0.040 -0.040	2.155 2.079 1.999 2.045	0.076 0.076 0.076 0.076	0.079 0.079 0.079 0.079	-0.046 -0.046 -0.046 -0.046	2.170 2.085 2.009 2.051	0.085 0.085 0.085 0.085	0.076 0.076 0.076 0.076	-0.043 -0.043 -0.043 -0.043	2.188 2.085 2.018 2.073	0.104 0.104 0.104 0.104	0.067 0.067 0.067 0.067	-0.055 -0.055 -0.055 -0.055
4+50	Virgin BH Virgin AH Milled Pre-Milled	2.134 2.045 1.984 2.024	0.088 0.088 0.088 0.088	0.061 0.061 0.061 0.061	-0.040 -0.040 -0.040 -0.040	2.149 2.067 1.993 2.036	0.082 0.082 0.082 0.082	0.073 0.073 0.073 0.073	-0.043 -0.043 -0.043 -0.043	2.167 2.085 2.008 2.057	0.082 0.082 0.082 0.082	0.079 0.079 0.079 0.079	-0.052 -0.052 -0.052 -0.052	2.182 2.091 2.016 2.063	0.091 0.091 0.091 0.091	0.073 0.073 0.073 0.073	-0.046 -0.046 -0.046 -0.046	2.195 2.094 2.024 2.070	0.101 0.101 0.101 0.101	0.070 0.070 0.070 0.070	-0.046 -0.046 -0.046 -0.046
5+00	Virgin BH Virgin AH Milled Pre-Milled	2.146 2.048 1.975 2.030	0.098 0.098 0.098 0.098	0.073 0.073 0.073 0.073	-0.055 -0.055 -0.055 -0.055	2.156 2.073 1.984 2.036	0.085 0.085 0.085 0.085	0.088 0.088 0.088 0.088	-0.052 -0.052 -0.052 -0.052	2.176 2.091 2.009 2.057	0.085 0.085 0.085 0.085	0.082 0.082 0.082 0.082	-0.049 -0.049 -0.049 -0.049	2.195 2.091 2.021 2.070	0.104 0.104 0.104 0.104	0.070 0.070 0.070 0.070	-0.049 -0.049 -0.049 -0.049	2.207 2.097 2.027 2.082	0.110 0.110 0.110 0.110	0.070 0.070 0.070 0.070	-0.055 -0.055 -0.055 -0.055





AVG	0.091	0.073	-0.040	0.083	0.078	-0.030	0.080	0.077	-0.030	0.089	0.071	-0.022	0.089	0.067	-0.031
MAX	0.098	0.091	-0.027	0.091	0.098	-0.009	0.085	0.082	-0.009	0.104	0.076	0.000	0.110	0.070	-0.015
MIN	0.088	0.061	-0.056	0.070	0.067	-0.052	0.070	0.070	-0.052	0.076	0.061	-0.049	0.081	0.081	-0.055
STD	0.006	0.010	0.010	0.006	0.009	0.018	0.006	0.004	0.017	0.008	0.005	0.020	0.008	0.003	0.016

SECTION AVG	Virgin BH	Virgin AH	Milled
0.089	0.074	-0.030	
SECTION MAX	0.110	0.098	0.000
SECTION MIN	0.070	0.061	-0.058
SECTION STD	0.009	0.008	0.017




Oklahoma SPS-5 (400507)

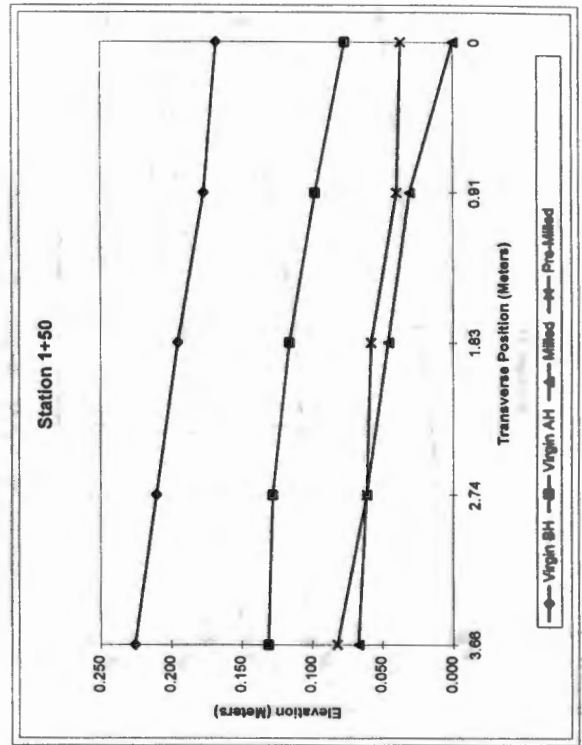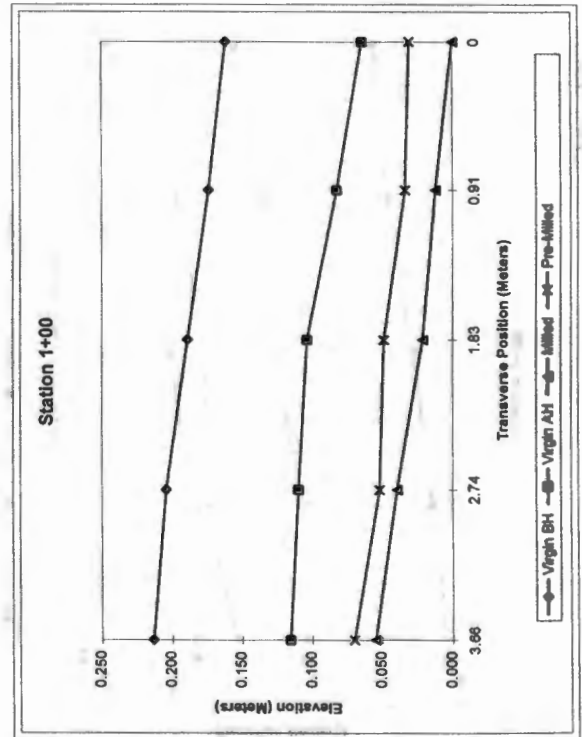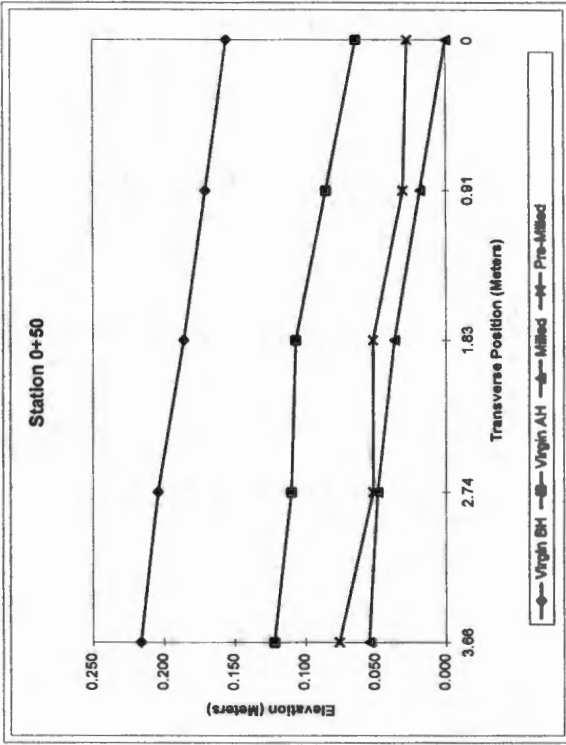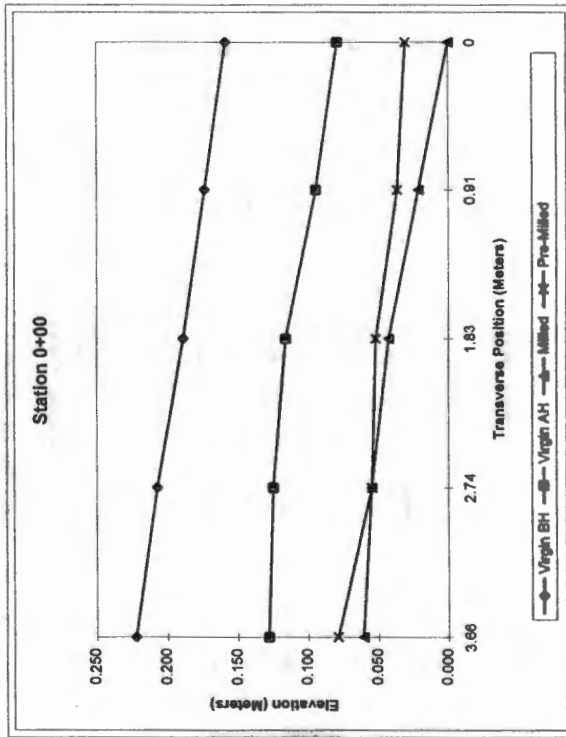

Oklahoma SPS-5 (400507)

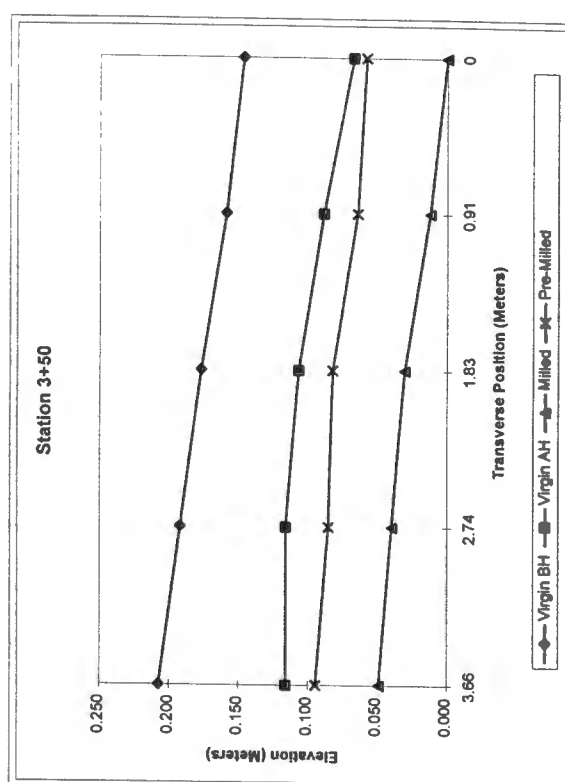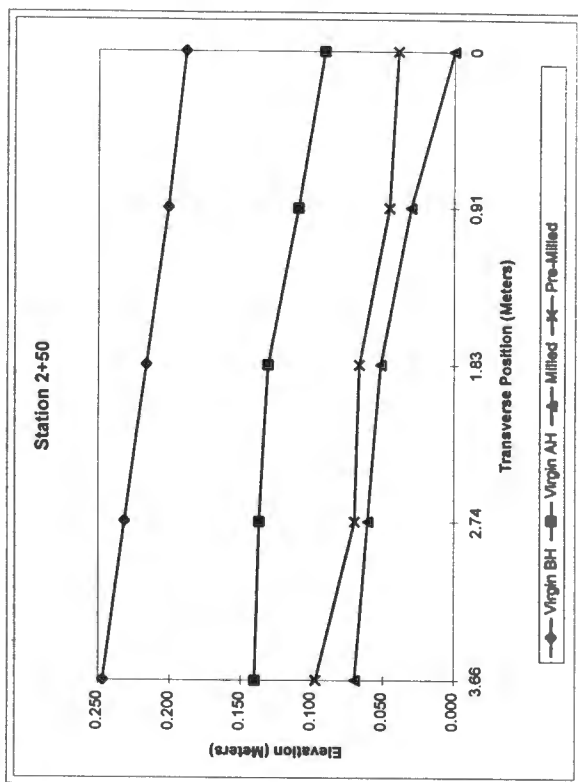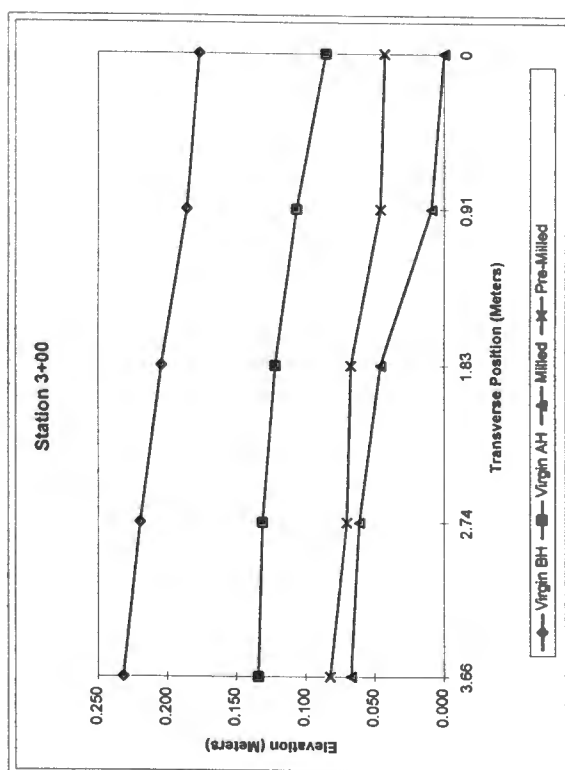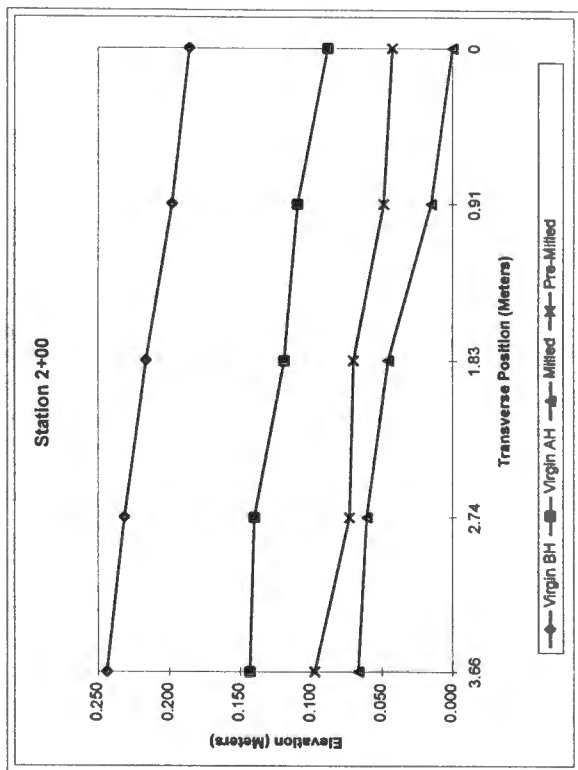

Oklahoma SPS-5 (400507)

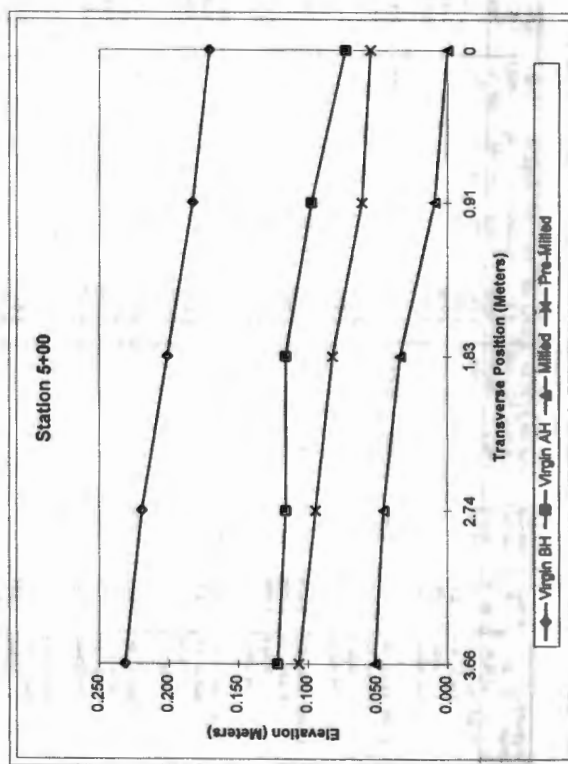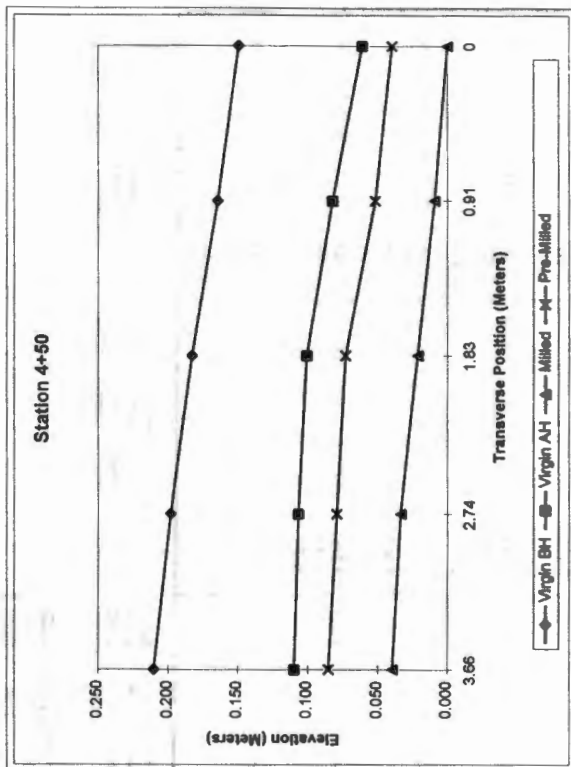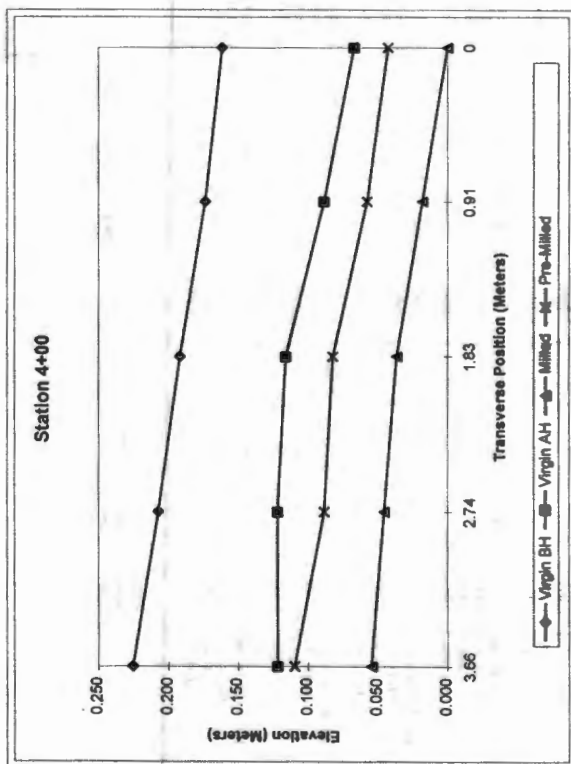





Oklahoma SPS-5 (400508)

Transverse Offset	4 LAYERS	ELEVATION Meters	Recyc. BH THICKNESS Meters	Recyc. AH THICKNESS Meters	Milled THICKNESS Meters	ELEVATION 0.91 Meters	Recyc. BH THICKNESS Meters	Recyc. AH THICKNESS Meters	Milled THICKNESS Meters	ELEVATION 1.33 Meters	Recyc. BH THICKNESS Meters	Recyc. AH THICKNESS Meters	Milled THICKNESS Meters	ELEVATION 2.74 Meters	Recyc. BH THICKNESS Meters	Recyc. AH THICKNESS Meters	Milled THICKNESS Meters	ELEVATION 3.66 Meters	Recyc. BH THICKNESS Meters	Recyc. AH THICKNESS Meters	Milled THICKNESS Meters
0+00	Recyc. BH 2.121 Recyc. AH 2.073 Milled 1.998 Pre-Milled 2.060	2.121	0.049	0.076	-0.064	2.091	0.049	0.076	-0.046	2.155	0.049	0.076	-0.046	2.140	0.046	0.079	-0.027	2.188	0.049	0.082	-0.034
0+60	Recyc. BH 2.260 Recyc. AH 2.219 Milled 2.131 Pre-Milled 2.201	2.260	0.061	0.088	-0.070	2.235	0.058	0.073	-0.046	2.310	0.055	0.073	-0.048	2.328	0.052	0.085	-0.034	2.344	0.055	0.088	-0.043
1+00	Recyc. BH 2.429 Recyc. AH 2.356 Milled 2.289 Pre-Milled 2.344	2.429	0.073	0.087	-0.055	2.448	0.067	0.076	-0.030	2.460	0.067	0.058	-0.027	2.475	0.064	0.067	-0.015	2.487	0.061	0.070	-0.037
1+60	Recyc. BH 2.557 Recyc. AH 2.472 Milled 2.399 Pre-Milled 2.444	2.557	0.085	0.073	-0.048	2.573	0.073	0.085	-0.043	2.588	0.073	0.073	-0.034	2.603	0.070	0.079	-0.021	2.615	0.067	0.085	-0.030
2+00	Recyc. BH 2.673 Recyc. AH 2.597 Milled 2.527 Pre-Milled 2.560	2.673	0.078	0.070	-0.034	2.688	0.076	0.058	-0.015	2.704	0.076	0.067	-0.030	2.719	0.073	0.073	-0.021	2.734	0.076	0.079	-0.037
2+60	Recyc. BH 2.795 Recyc. AH 2.713 Milled 2.624 Pre-Milled 2.658	2.795	0.082	0.068	-0.034	2.810	0.082	0.076	-0.024	2.825	0.082	0.073	-0.027	2.841	0.079	0.079	-0.018	2.853	0.079	0.085	-0.037
3+00	Recyc. BH 2.905 Recyc. AH 2.819 Milled 2.756 Pre-Milled 2.783	2.905	0.085	0.061	-0.024	2.920	0.082	0.055	-0.009	2.935	0.082	0.062	-0.015	2.950	0.073	0.064	-0.009	2.969	0.073	0.073	-0.030
3+60	Recyc. BH 3.038 Recyc. AH 2.950 Milled 2.899 Pre-Milled 2.928	3.038	0.085	0.052	-0.027	3.048	0.082	0.064	-0.030	3.063	0.085	0.065	-0.030	3.082	0.082	0.087	-0.024	3.100	0.085	0.073	-0.037
4+00	Recyc. BH 3.158 Recyc. AH 3.078 Milled 3.027 Pre-Milled 3.066	3.158	0.079	0.052	-0.040	3.173	0.082	0.061	-0.046	3.188	0.079	0.061	-0.037	3.208	0.079	0.067	-0.027	3.225	0.078	0.078	-0.037
4+60	Recyc. BH 3.292 Recyc. AH 3.206 Milled 3.142 Pre-Milled 3.200	3.292	0.085	0.064	-0.058	3.304	0.078	0.079	-0.058	3.319	0.073	0.076	-0.049	3.338	0.078	0.078	-0.037	3.353	0.073	0.085	-0.043
5+00	Recyc. BH 3.423 Recyc. AH 3.335 Milled 3.258 Pre-Milled 3.328	3.423	0.088	0.076	-0.070	3.438	0.076	0.088	-0.061	3.456	0.082	0.070	-0.048	3.475	0.082	0.079	-0.040	3.490	0.068	0.079	-0.049





AVG	0.077	0.070	-0.049	0.073	0.073	0.087	-0.038	0.070	0.074	-0.025	0.070	0.074	-0.025	0.070	0.074	-0.025	0.070	0.074	-0.025	0.070	0.074	-0.025
MAX	0.088	0.088	-0.024	0.082	0.088	0.076	-0.015	0.085	0.085	-0.009	0.085	0.085	-0.009	0.085	0.085	-0.009	0.085	0.085	-0.009	0.085	0.085	-0.009
MIN	0.049	0.052	-0.070	0.049	0.055	0.052	-0.049	0.049	0.052	-0.049	0.049	0.052	-0.049	0.049	0.052	-0.049	0.049	0.052	-0.049	0.049	0.052	-0.049
STD	0.012	0.012	0.018	0.011	0.010	0.010	0.010	0.012	0.009	0.010	0.012	0.007	0.009	0.012	0.007	0.009	0.012	0.007	0.009	0.012	0.006	0.005

SECTION AVG	Recyc. BH	Recyc. AH	Milled
0.073	0.073	0.073	-0.037
SECTION MAX	0.088	0.088	-0.009
SECTION MIN	0.049	0.052	-0.070
SECTION STD	0.012	0.010	0.014




Oklahoma SPS-5 (400508)

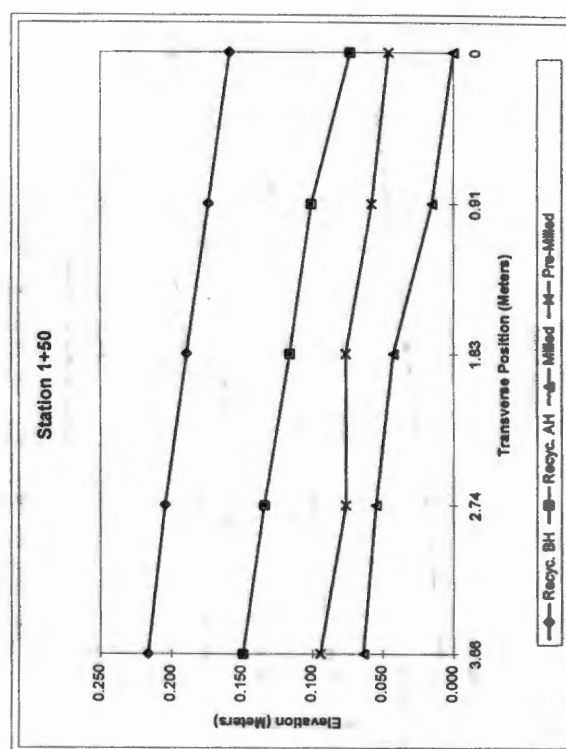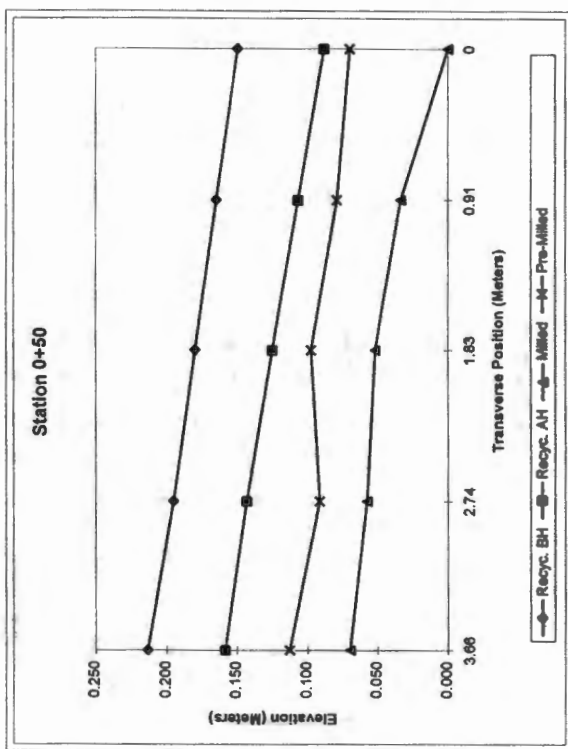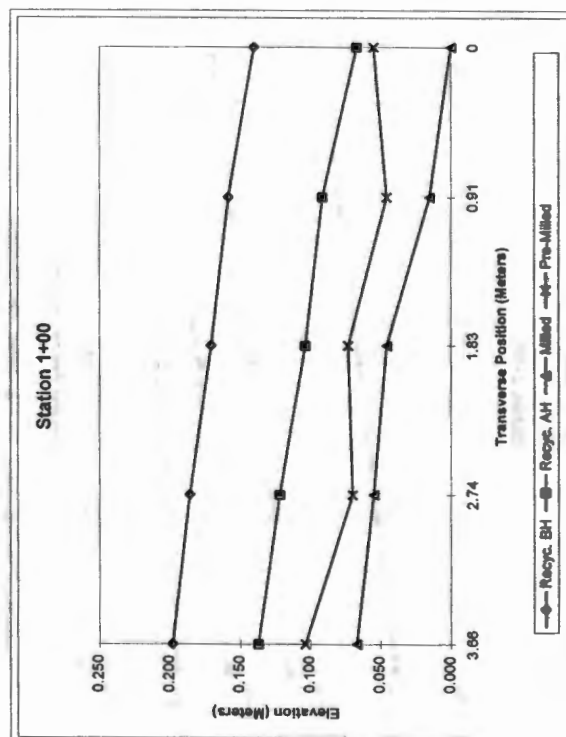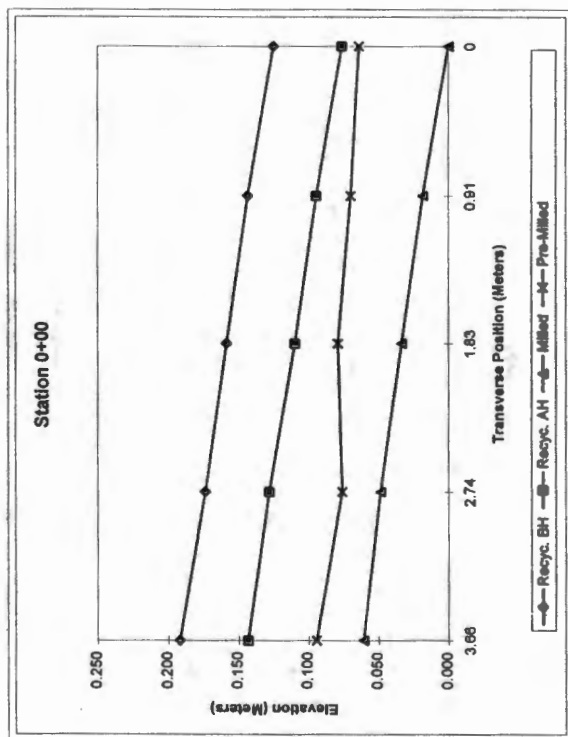

Oklahoma SPS-5 (400508)

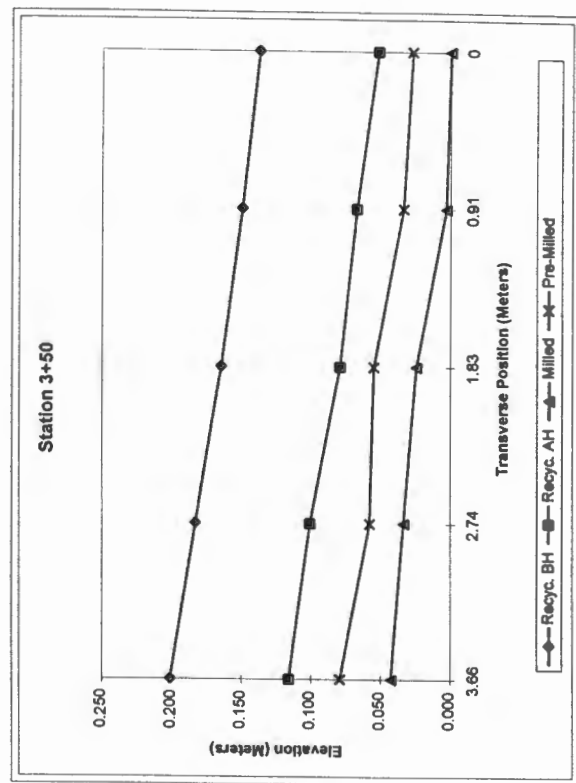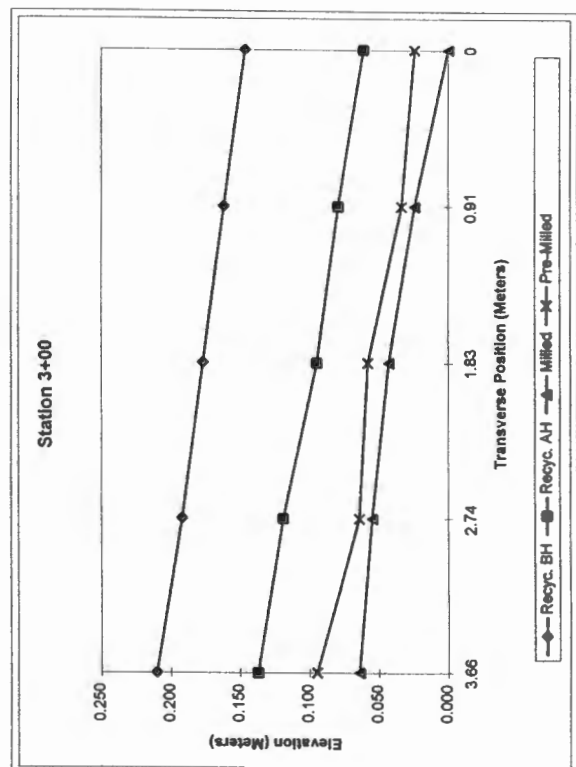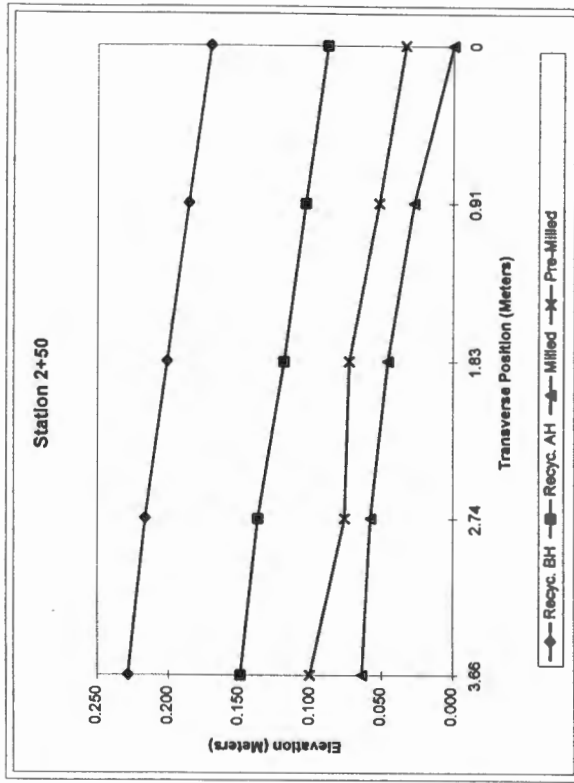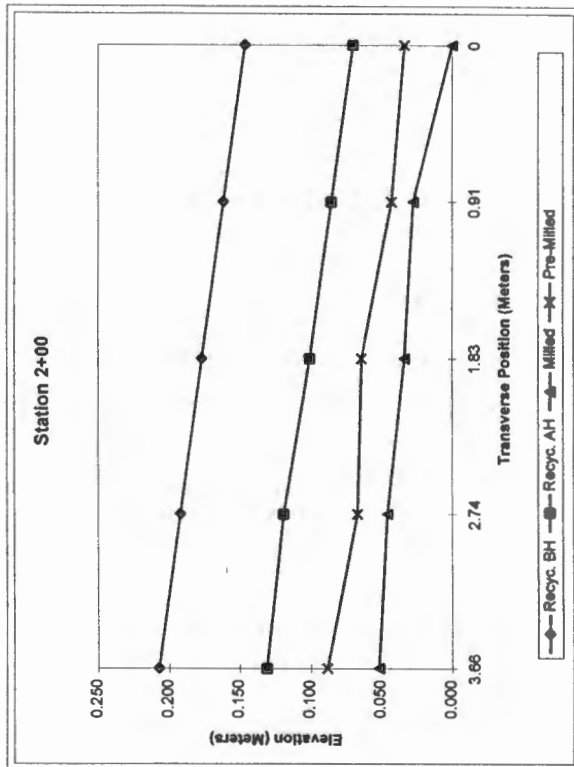

Oklahoma SPS-5 (400508)

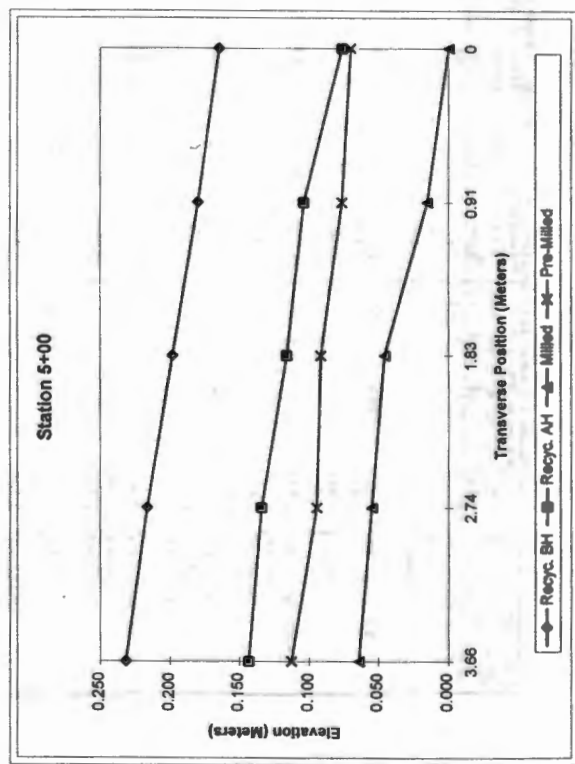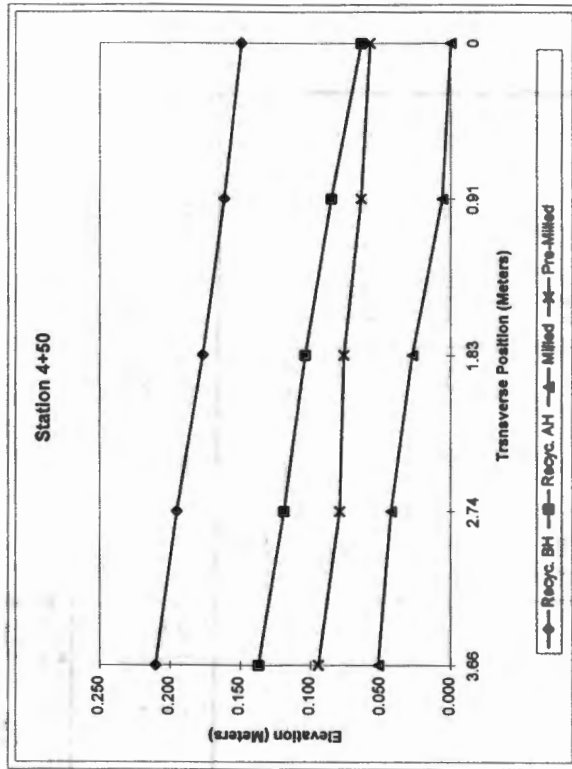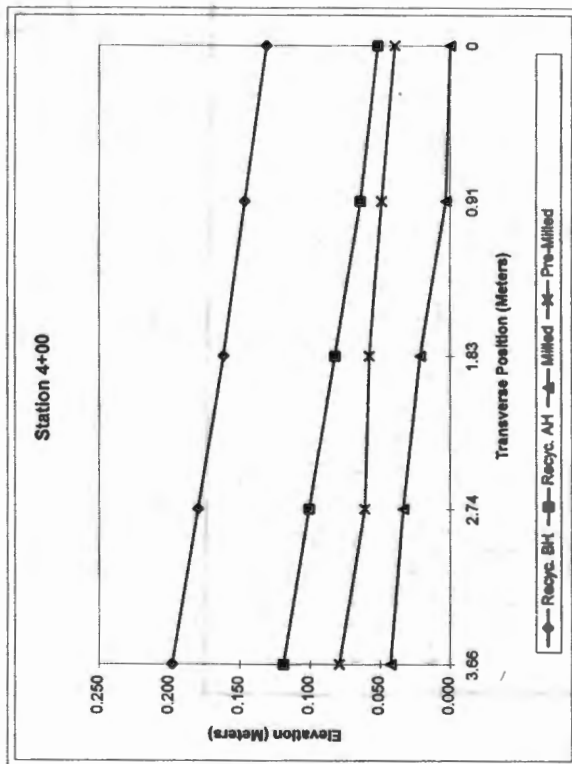





Oklahoma SPS-5 (400509)

Transverse Offset	3 LAYERS	ELEVATION			Recyc. BH			Milled			ELEVATION			Recyc. BH			Milled		
		0	THICKNESS	Meters	0.91	THICKNESS	Meters	1.83	THICKNESS	Meters	2.74	THICKNESS	Meters	3.66	THICKNESS	Meters	4.58	THICKNESS	Meters
0+00	Recyc. BH	2.259	-0.052	0.073	2.274	0.067	-0.034	2.274	0.067	-0.024	2.307	0.073	-0.015	2.320	0.082	-0.021	2.332	0.082	-0.021
	Milled	2.185			2.207			2.222			2.234			2.237			2.259		
	Pre-Milled	2.237			2.240			2.248			2.249								
0+50	Recyc. BH	2.457	-0.058	0.064	2.470	0.062	-0.043	2.487	0.064	-0.037	2.509	0.073	-0.024	2.521	0.076	-0.034	2.544	0.076	-0.034
	Milled	2.393			2.408			2.423			2.435			2.444			2.478		
	Pre-Milled	2.451			2.451			2.460			2.460								
1+00	Recyc. BH	2.643	-0.052	0.055	2.655	0.058	-0.043	2.673	0.058	-0.037	2.693	0.066	-0.024	2.710	0.076	-0.037	2.733	0.076	-0.037
	Milled	2.588			2.597			2.615			2.627			2.633			2.670		
	Pre-Milled	2.640			2.640			2.652			2.652								
1+50	Recyc. BH	2.810	-0.061	0.076	2.825	0.079	-0.052	2.844	0.079	-0.040	2.859	0.079	-0.024	2.874	0.091	-0.043	2.893	0.091	-0.043
	Milled	2.734			2.748			2.765			2.780			2.783			2.825		
	Pre-Milled	2.795			2.798			2.804			2.804								
2+00	Recyc. BH	2.987	-0.052	0.079	2.999	0.082	-0.049	3.014	0.079	-0.040	3.030	0.082	-0.034	3.045	0.091	-0.043	3.064	0.091	-0.043
	Milled	2.908			2.917			2.935			2.947			2.954			2.996		
	Pre-Milled	2.960			2.966			2.975			2.981								
2+50	Recyc. BH	3.178	-0.052	0.082	3.191	0.085	-0.048	3.206	0.082	-0.040	3.225	0.088	-0.027	3.240	0.094	-0.037	3.264	0.094	-0.037
	Milled	3.094			3.106			3.124			3.138			3.146			3.182		
	Pre-Milled	3.146			3.152			3.164			3.164								
3+00	Recyc. BH	3.365	-0.058	0.076	3.380	0.073	-0.043	3.395	0.073	-0.043	3.417	0.079	-0.027	3.432	0.088	-0.040	3.454	0.088	-0.040
	Milled	3.289			3.307			3.322			3.338			3.344			3.383		
	Pre-Milled	3.347			3.350			3.365			3.365								
3+50	Recyc. BH	3.548	-0.061	0.073	3.563	0.078	-0.052	3.578	0.073	-0.049	3.597	0.079	-0.043	3.612	0.085	-0.052	3.637	0.085	-0.052
	Milled	3.475			3.487			3.505			3.517			3.527			3.578		
	Pre-Milled	3.536			3.539			3.554			3.560								
4+00	Recyc. BH	3.719	-0.064	0.079	3.731	0.082	-0.058	3.749	0.079	-0.049	3.767	0.088	-0.040	3.786	0.098	-0.049	3.811	0.098	-0.049
	Milled	3.639			3.648			3.670			3.679			3.688			3.737		
	Pre-Milled	3.703			3.706			3.719			3.719								
4+50	Recyc. BH	3.908	-0.081	0.079	3.920	0.085	-0.055	3.938	0.082	-0.052	3.953	0.088	-0.043	3.968	0.094	-0.052	3.994	0.094	-0.052
	Milled	3.828			3.834			3.856			3.885			3.874			3.926		
	Pre-Milled	3.889			3.889			3.908			3.908								
5+00	Recyc. BH	4.103	-0.070	0.076	4.118	0.076	-0.055	4.133	0.073	-0.049	4.151	0.082	-0.037	4.167	0.088	-0.048	4.194	0.088	-0.048
	Milled	4.026			4.042			4.060			4.069			4.078			4.124		
	Pre-Milled	4.097			4.097			4.109			4.108								





AVG	0.074	-0.059	0.075	-0.048	0.073	-0.042	0.080	-0.030	0.087	-0.041
MAX	0.082	-0.052	0.085	-0.034	0.082	-0.024	0.088	-0.015	0.096	-0.021
MIN	0.055	-0.070	0.058	-0.058	0.058	-0.052	0.066	-0.043	0.076	-0.052
STD	0.008	0.006	0.009	0.007	0.008	0.008	0.007	0.009	0.007	0.009

Recyc. BH		Milled	
SECTION AVG	0.078	SECTION MAX	-0.044
SECTION MIN	0.058	SECTION MIN	-0.015
SECTION STD	0.009	SECTION STD	0.012




Oklahoma SPS-5 (400509)

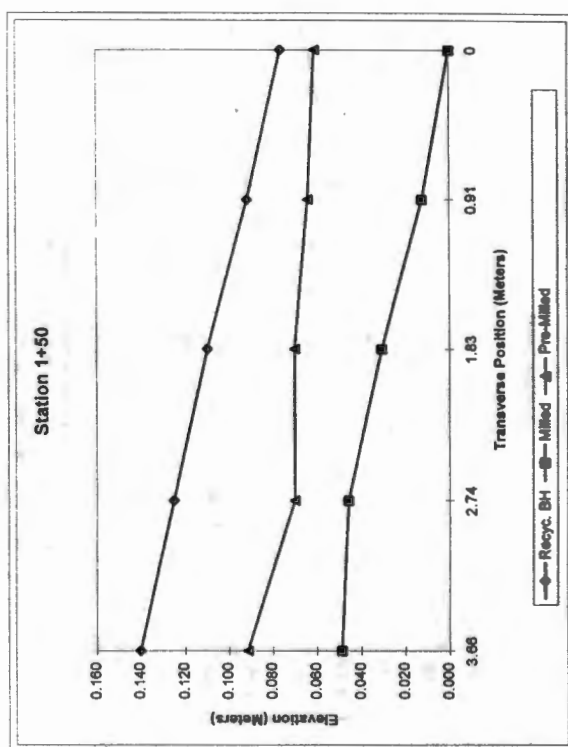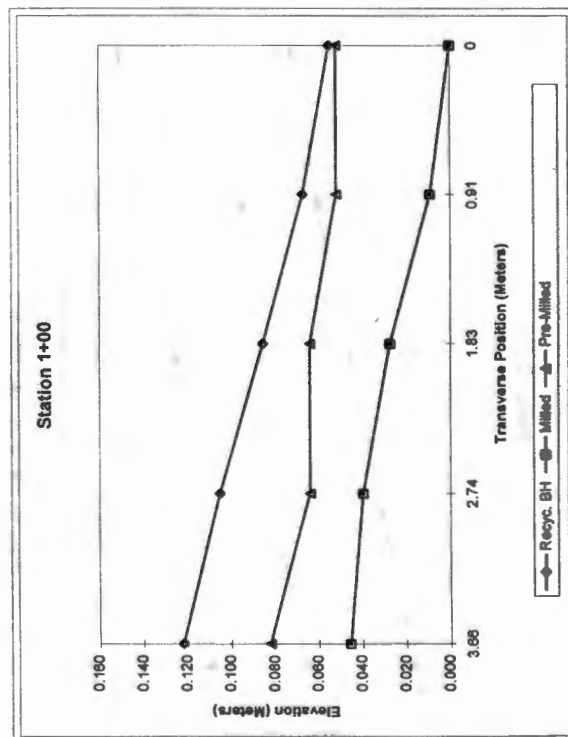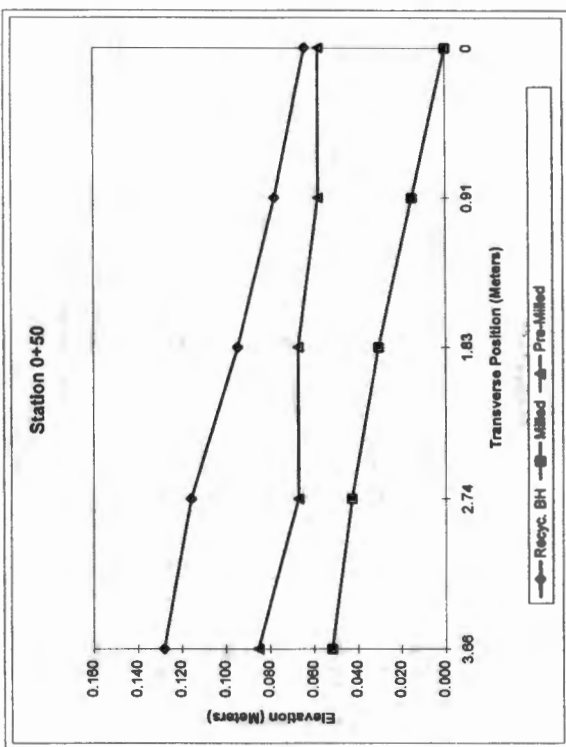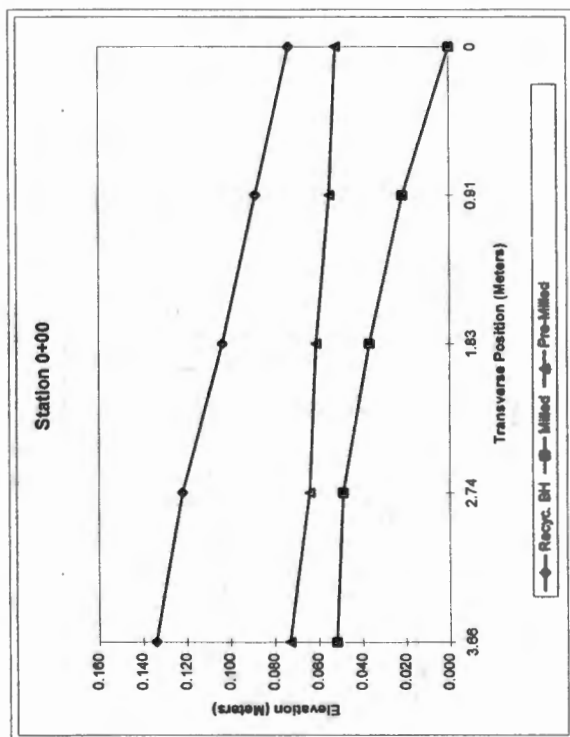

Oklahoma SPS-5 (400509)

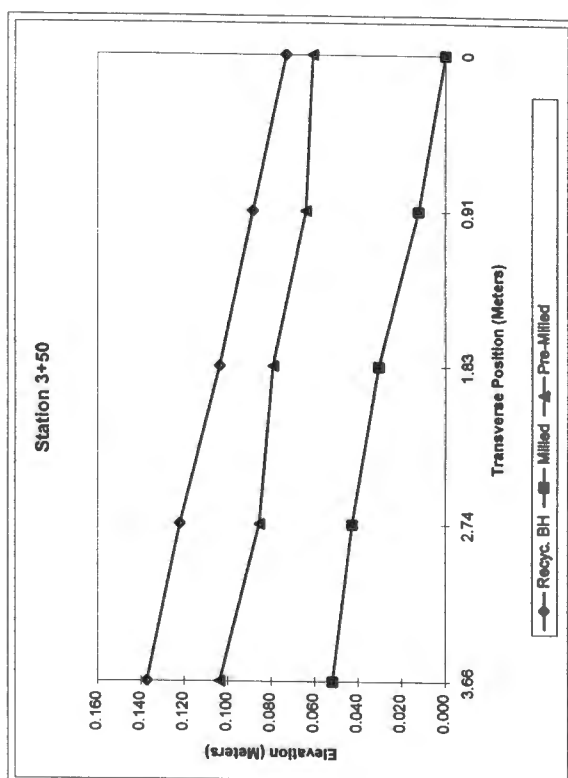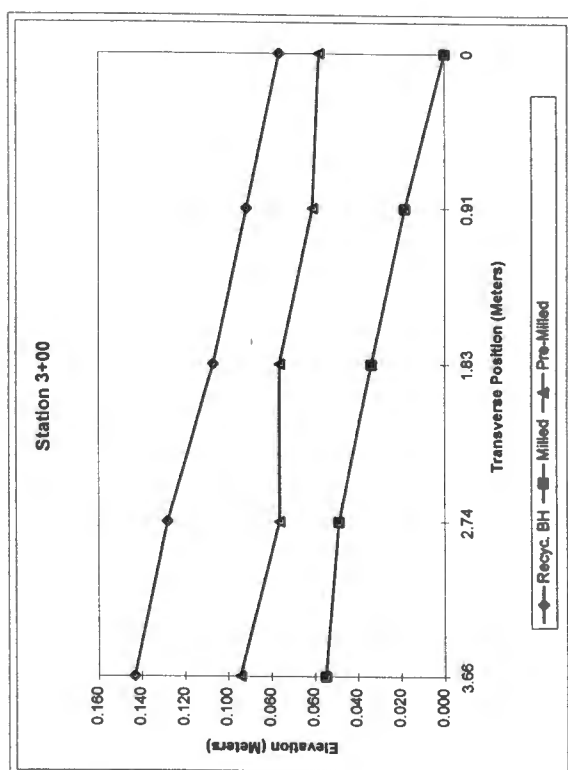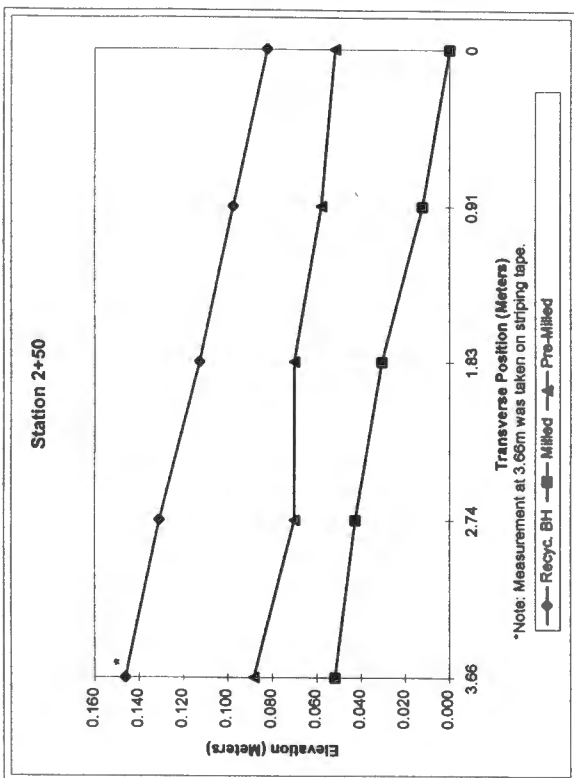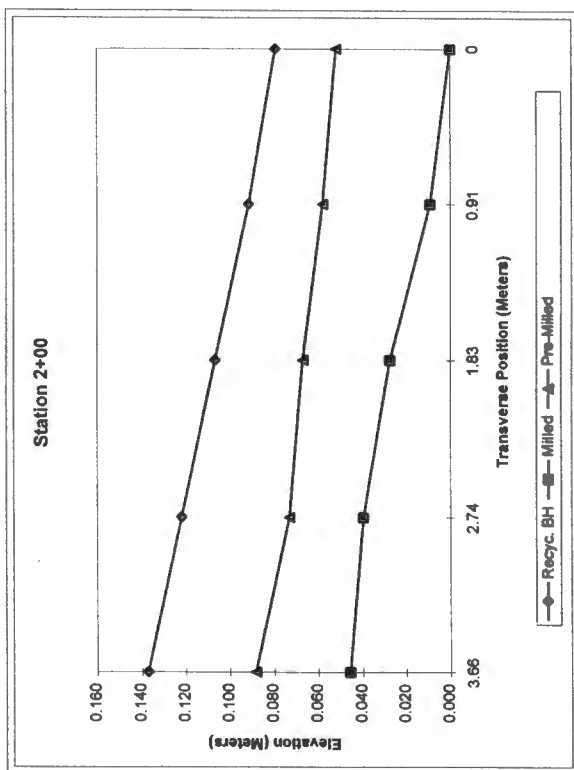

Oklahoma SPS-5 (400509)

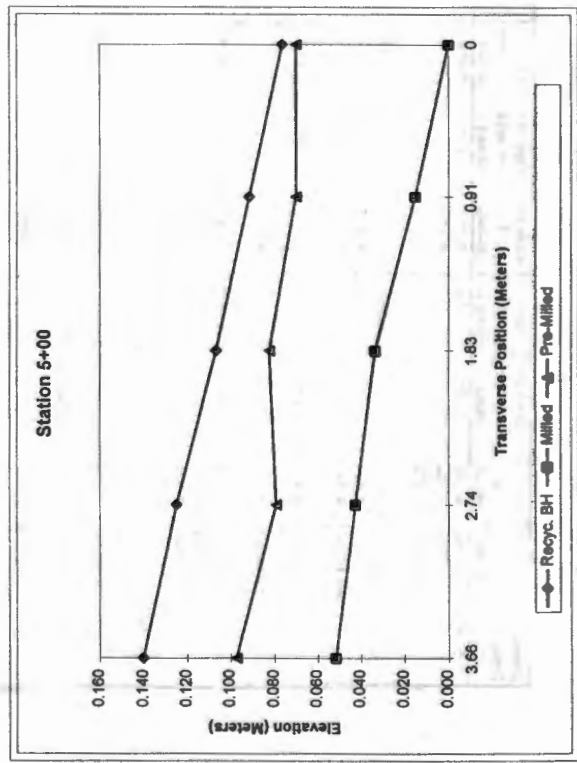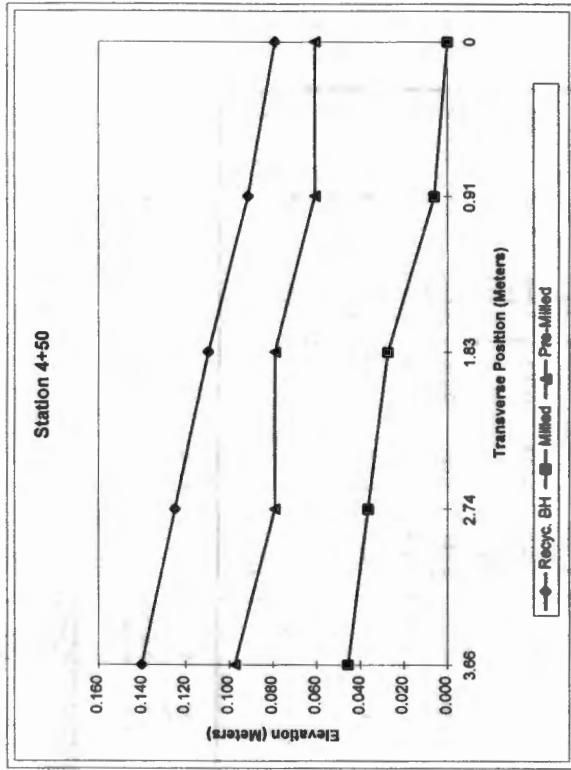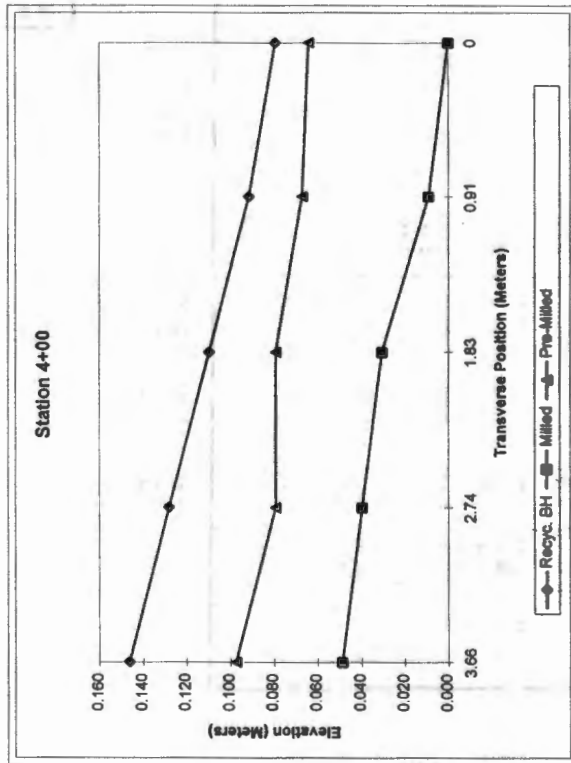





Oklahoma SPS-5 (400560)

Transverse Offset	3 LAYERS	ELEVATION Meters	Virgin BH THICKNESS Meters	Milled THICKNESS Meters	ELEVATION Meters	Virgin BH THICKNESS Meters	Milled THICKNESS Meters	ELEVATION Meters	Virgin BH THICKNESS Meters	Milled THICKNESS Meters
0+00	Virgin BH Milled Pre-Milled	4.666 4.596 4.615	0.070 0.101 0.088	-0.018 -0.040 -0.043	4.685 4.612 4.618	0.073 0.096 0.087	-0.006 -0.027 -0.024	4.697 4.618 4.639	0.079 0.101 0.090	-0.021 -0.015 -0.027
0+50	Virgin BH Milled Pre-Milled	4.502 4.401 4.441	0.101 0.088 0.088	-0.040 -0.043 -0.043	4.519 4.423 4.450	0.096 0.087 0.087	-0.027 -0.024 -0.024	4.535 4.435 4.450	0.101 0.090 0.090	-0.015 -0.027 -0.027
1+00	Virgin BH Milled Pre-Milled	4.304 4.215 4.258	0.088 0.088 0.088	-0.043 -0.043 -0.043	4.324 4.237 4.261	0.087 0.087 0.087	-0.024 -0.024 -0.024	4.342 4.252 4.279	0.090 0.090 0.090	-0.027 -0.027 -0.027
1+50	Virgin BH Milled Pre-Milled	4.078 0.000 3.996	Unknown Unknown Unknown	Unknown Unknown Unknown	4.098 0.000 4.005	Unknown Unknown Unknown	Unknown Unknown Unknown	4.115 0.000 4.023	Unknown Unknown Unknown	Unknown Unknown Unknown
2+00	Virgin BH Milled Pre-Milled	3.821 0.000 3.743	Unknown Unknown Unknown	Unknown Unknown Unknown	3.840 0.000 3.749	Unknown Unknown Unknown	Unknown Unknown Unknown	3.856 0.000 3.773	Unknown Unknown Unknown	Unknown Unknown Unknown
2+50	Virgin BH Milled Pre-Milled	3.533 0.000 3.463	Unknown Unknown Unknown	Unknown Unknown Unknown	3.554 0.000 3.469	Unknown Unknown Unknown	Unknown Unknown Unknown	3.566 0.000 3.484	Unknown Unknown Unknown	Unknown Unknown Unknown
3+00	Virgin BH Milled Pre-Milled	3.231 3.127 3.181	0.104 0.107 0.107	-0.034 -0.034 -0.034	3.249 3.152 3.167	0.098 0.113 0.113	-0.015 -0.027 -0.027	3.264 3.164 3.182	0.101 0.107 0.107	-0.018 -0.021 -0.021
3+50	Virgin BH Milled Pre-Milled	2.896 2.789 2.822	0.088 0.088 0.088	-0.012 -0.012 -0.012	2.914 2.801 2.829	0.094 0.094 0.094	-0.009 -0.009 -0.009	2.929 2.822 2.844	0.093 0.093 0.093	-0.015 -0.015 -0.015
4+00	Virgin BH Milled Pre-Milled	2.533 2.444 2.457	0.088 0.088 0.088	-0.012 -0.012 -0.012	2.551 2.457 2.466	0.094 0.094 0.094	-0.009 -0.009 -0.009	2.568 2.475 2.490	0.093 0.093 0.093	-0.015 -0.015 -0.015
4+50	Virgin BH Milled Pre-Milled	2.170 2.076 2.094	0.094 0.094 0.094	-0.018 -0.018 -0.018	2.188 2.094 2.097	0.094 0.094 0.094	-0.003 -0.003 -0.003	2.204 2.112 2.118	0.091 0.091 0.091	-0.006 -0.006 -0.006
5+00	Virgin BH Milled Pre-Milled	1.771 1.658 1.698	0.113 0.113 0.113	-0.040 -0.040 -0.040	1.792 1.679 1.704	0.113 0.113 0.113	-0.024 -0.024 -0.024	1.807 1.682 1.722	0.125 0.125 0.125	-0.040 -0.040 -0.040





AVG	0.096	-0.030	0.096	-0.017	0.098	-0.021	0.105	-0.019	0.115	-0.035
MAX	0.113	-0.012	0.113	-0.003	0.125	-0.006	0.125	-0.009	0.134	-0.030
MIN	0.070	-0.043	0.073	-0.027	0.079	-0.040	0.082	-0.030	0.094	-0.043
STD	0.013	0.011	0.012	0.009	0.013	0.009	0.011	0.007	0.011	0.004

Virgin BH		Milled
SECTION AVG	0.102	-0.024
SECTION MAX	0.134	-0.003
SECTION MIN	0.070	-0.043
SECTION STD	0.014	0.011




Oklahoma SPS-5 (400560)

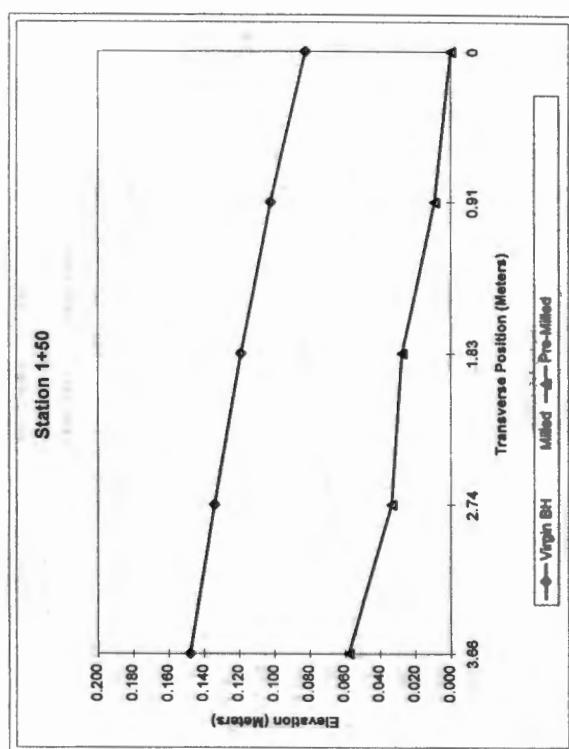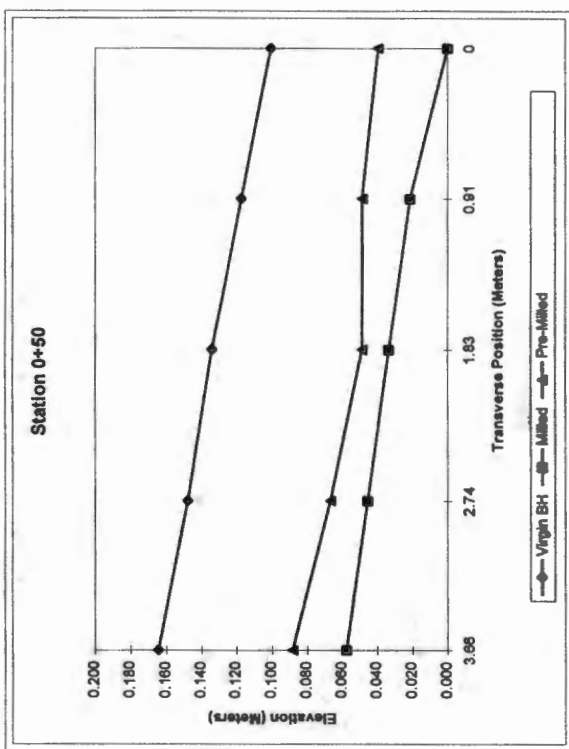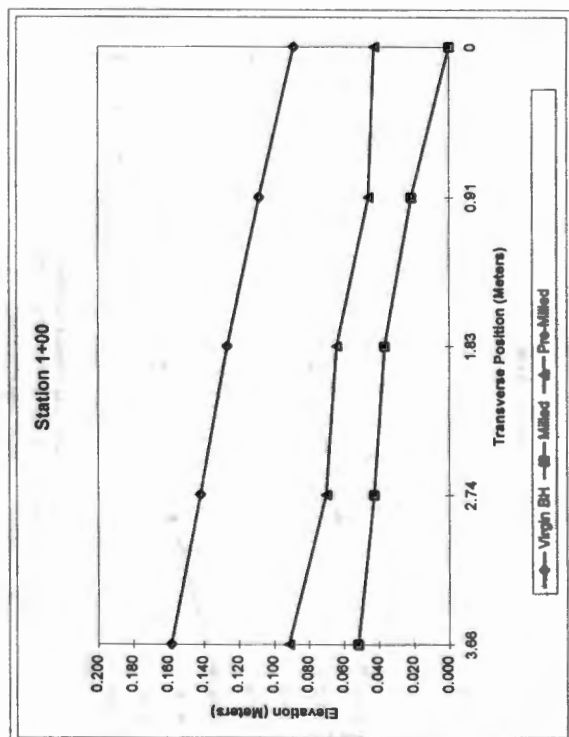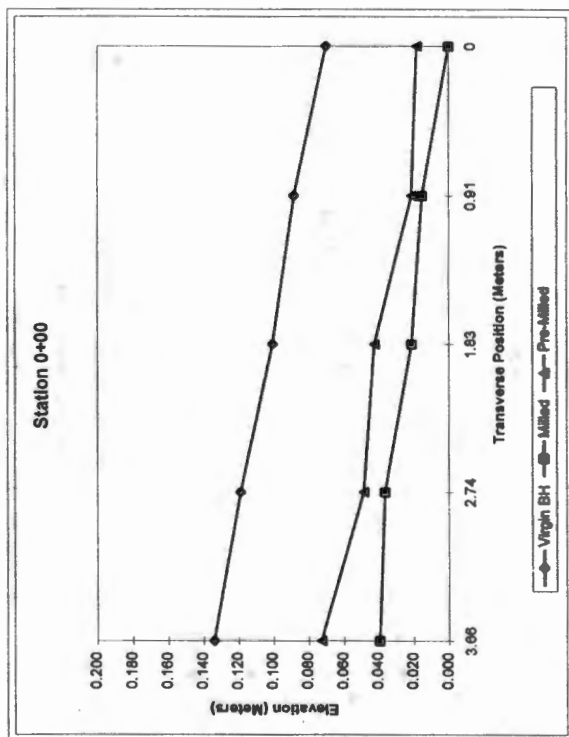

Oklahoma SPS-5 (400560)

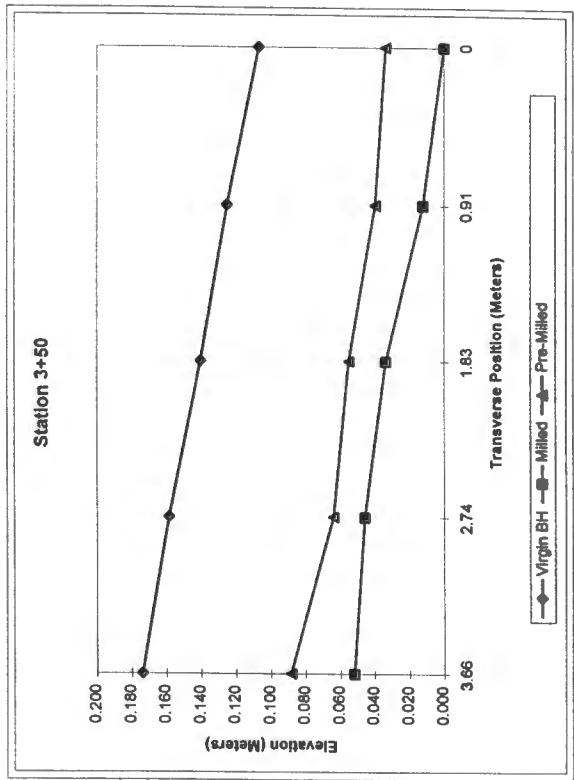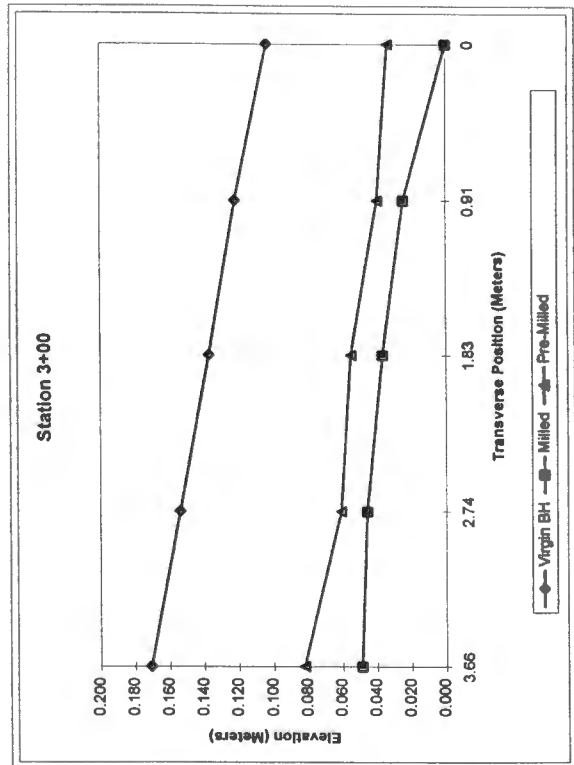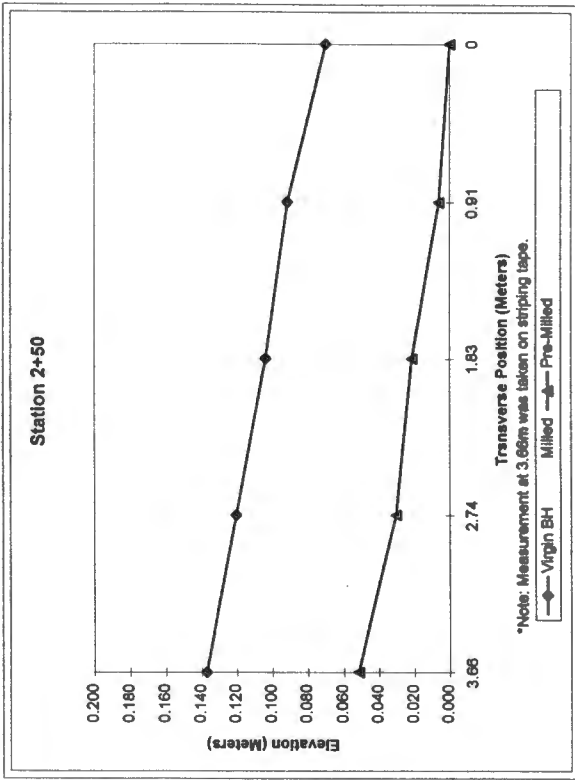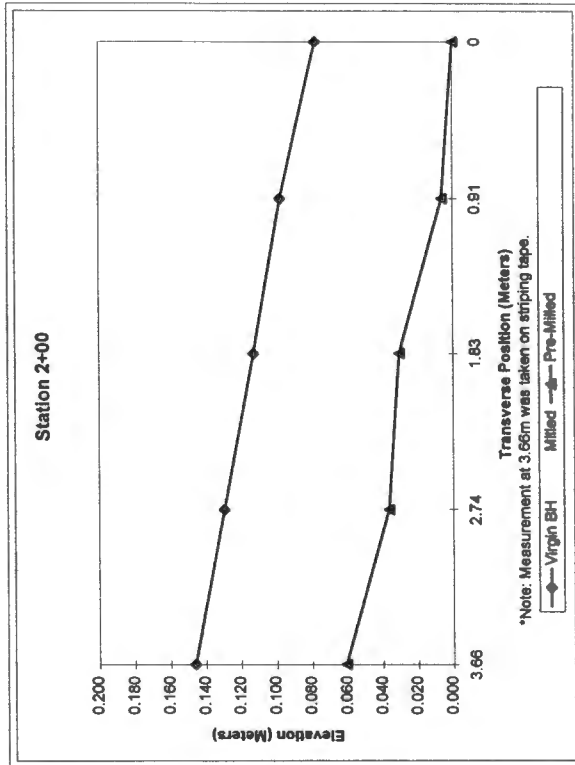

Oklahoma SPS-5 (400560)

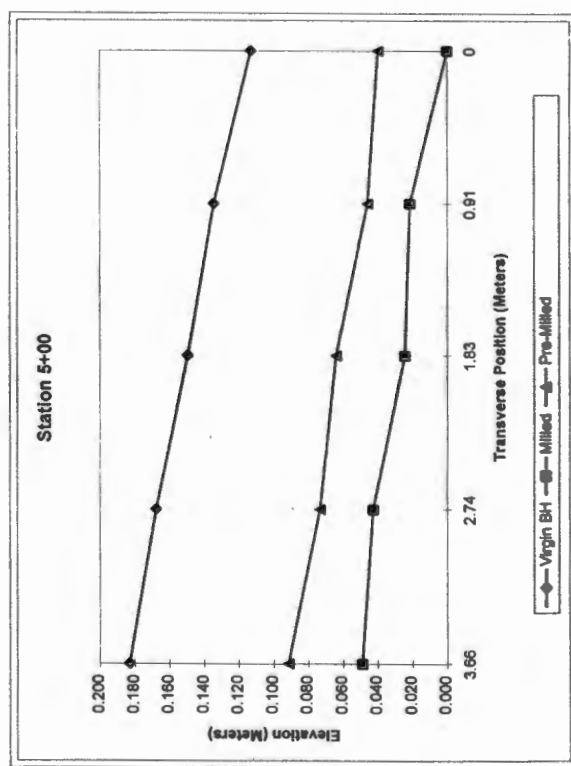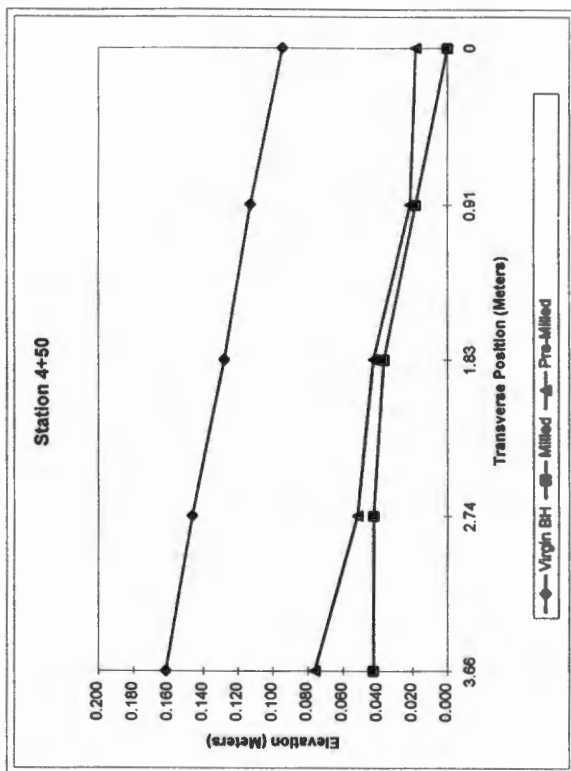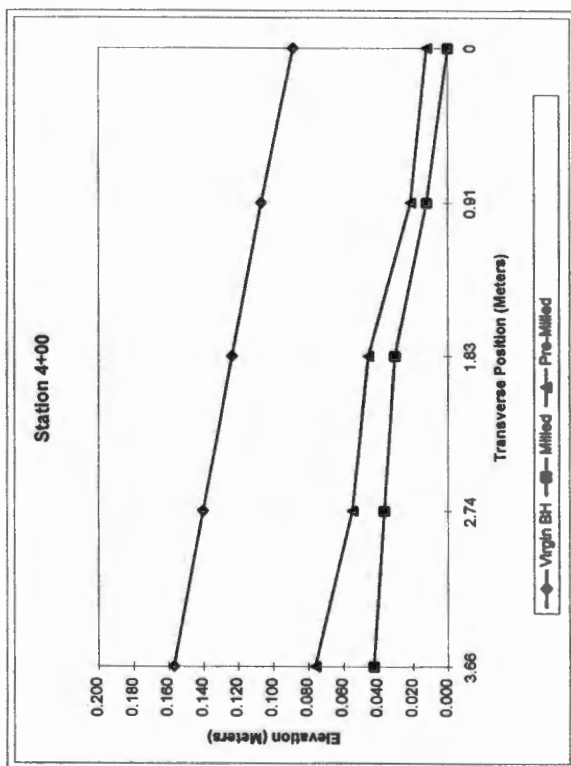

APPENDIX G
PHOTOGRAPHS

	<u>Page N^o.</u>
1 Preconstruction Sampling	G.2
2 Core Representing Existing Layer Thicknesses	G.2
3 Split-Spoon Sampling	G.3
4 Split-Spoon Sample	G.3
5 Transverse Crack	G.4
6 Milled Surface, Section 400508	G.4
7 Paving Operations	G.5
8 Compaction of 4005 Project	G.5



Photo 1. Preconstruction Sampling



Photo 2. Core Representing Existing Layer Thicknesses



Photo 3. Split-Spoon Sampling



Photo 4. Split-Spoon Sample



Photo 5. Transverse Crack



Photo 6. Milled Surface, Section 400508



Photo 7. Paving Operations



Photo 8. Compaction of 4005 Project

