

0-6985: Perform Feasibility Study on Use of Innovative Tools and Techniques to Accelerate Pavement Construction

Background

The Texas Department of Transportation is facing an increase in pavement reconstruction projects over the next several years. However, many roadways needing reconstruction and widening are in metro areas where traffic handling and user delay costs are a major expense. This project investigated innovative tools and techniques to accelerate pavement construction.

What the Researchers Did

The researchers identified four roadway projects scheduled for reconstruction as case studies. The case studies involved extensive evaluation of the pavement condition, pavement design, and traffic control options. Innovative tools and technologies, along with the advanced traffic control planning tool Construction Analysis for Pavement Rehabilitation Strategies (CA4PRS), were used in the evaluation. Figure 1 shows some of the tools, such as the falling weight deflectometer (FWD), portable weigh in motion (p-WIM), light detection and ranging equipment (LiDAR), ground-penetrating radar (GPR), electrical resistivity tomography (ERT), and total pavement acceptance device (TPAD). CA4PRS was used to estimate and document the optimal construction scheduling and identify time and cost savings. The researchers developed training materials and guidance that included the

methodology, testing procedures, and tools used in the selection and design of pavements. Recommendations on innovative approaches for pavement design and traffic control were presented for district consideration.

What They Found

There is potential for significant time and money savings when the existing pavement, proposed pavement design, and traffic control scenarios are evaluated and optimized. The reuse and incorporation of the existing pavement structure into the new pavement structure can save time, natural resources, and money.

What This Means

The training materials developed in this study are intended to provide guidance to designers on project evaluation. Evaluating the existing pavement and incorporating it into the new pavement design alongside traffic control scenarios can lead to time and money savings.

Research Performed by:

Texas A&M Transportation Institute

Research Supervisor:

Darlene Goehl, TTI

Researchers:

Tom Scullion, TTI

Kunhee (KC) Choi, TTI

Charles Gurganus, TTI

Bryan Wilson, TTI

Project Completed:

8-31-2021

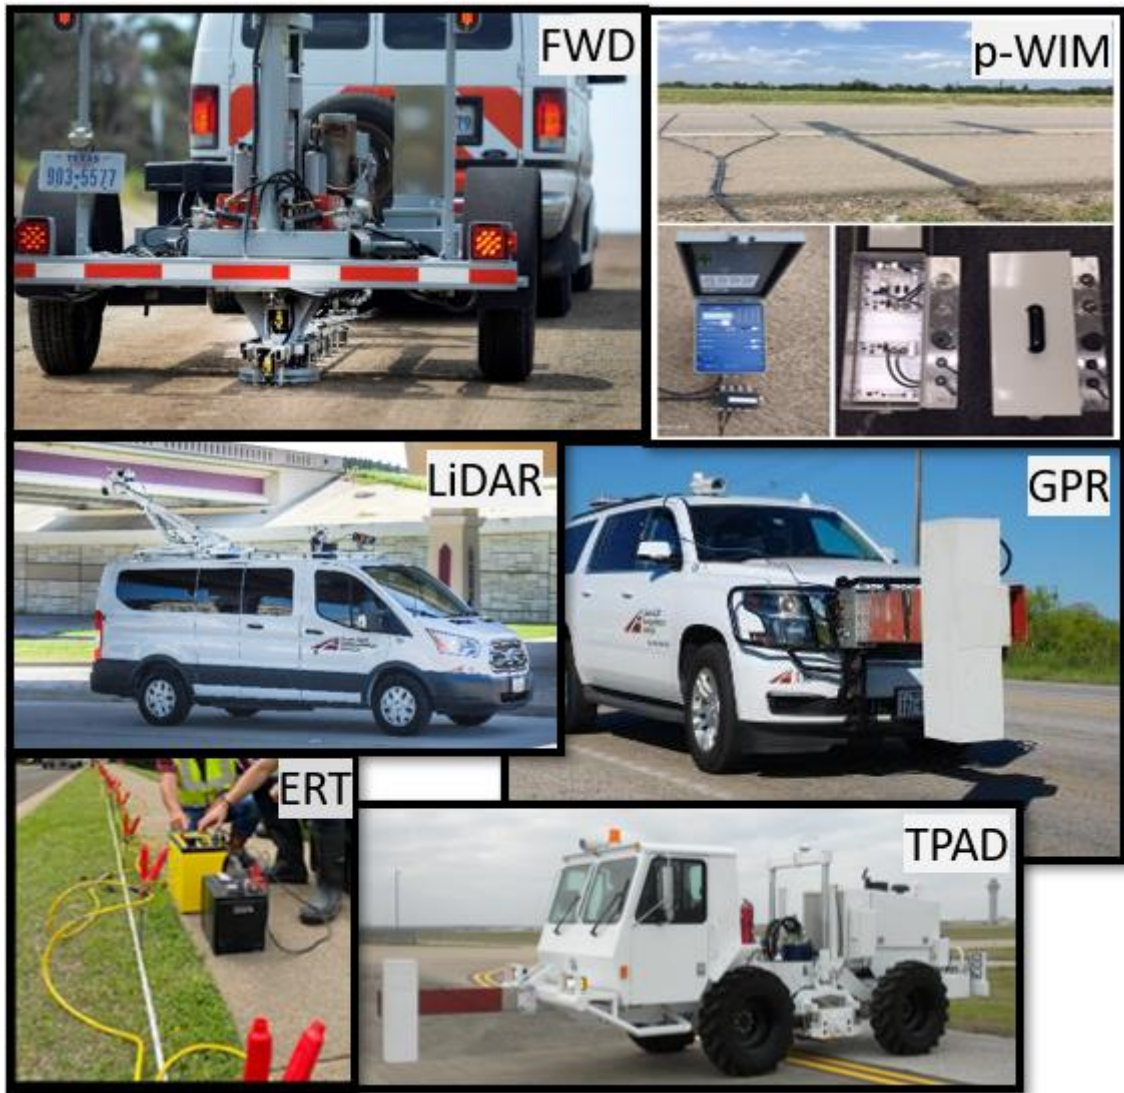


Figure 1. Innovative Testing Tools.

For More Information

Project Manager:

Shelley Pridgen, TxDOT, (512) 416-4728

Research Supervisor:

Darlene Goehl, TTI, (979) 317-2329

Technical reports when published are available at <http://library.ctr.utexas.edu>.

Research and Technology Implementation Office

Texas Department of Transportation

125 E. 11th Street

Austin, TX 78701-2483

www.txdot.gov

Keyword: Research

This research was performed in cooperation with the Texas Department of Transportation and the Federal Highway Administration. The contents of this report reflect the views of the authors, who are responsible for the facts and accuracy of the data presented here. The contents do not necessarily reflect the official view or policies of FHWA or TxDOT. This report does not constitute a standard, specification, or regulation, nor is it intended for construction, bidding, or permit purposes. Trade names were used solely for information and not for product endorsement.
